

Technical Site Visit Report

Prepared for: V Dorairaj_Sanjay Nagar_Non_Subsidy_13.3kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0180
Project ID	340FA364
Project Name	V Dorairaj_Sanjay Nagar_Non_Subsidy_13.3kWp_Hybrid
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Mahantayya
Site Address	V Dorairaj Site no.2, RMV II STAGE FURTHER EXTENSION BHOOPASANDRA BENGALURU 94 Land mark: opposite to shastri memorial hall.
Visit Date	2026-08-01
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	V Dorairaj
Contact	9886793068

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	13.3
Sanction Load (kW)	15
Module Make & Capacity	Waaree Non DCR Topcon, 700 Wp
Module Length (mm)	2384
Module Width (mm)	1303
Number of Panels	19

Inverter Type	Hybrid (String)
Inverter Brand	Deye: 15KW - 48V - LV - Three Phase
Number of Inverters	1
Battery	Needed
Number of Batteries	1
Capacity of each Battery (kWh)	11.8
Battery Model No.	Deye: SE-F12
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	A room is available on the ground floor to house the ACDB, DCDB, INVERTER & BATTERIES.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes. 3 Nos. of Spare earth pits already made available at the ground floor (entry basement) by the customer.	-
6	Where is the Internet Router located?	Not yet installed. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Other	On the same terrace, there exist two roofs for installation:

#	Question	Answer	Notes
			1) Roof 1: Upper headroom terrace – RCC flat roof. (The MS structure has to be fabricated.) 2) Roof 2: Lower terrace – RCC flat roof. (A corrugated sheet structure has to be fabricated.)
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	7	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	2	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	Roof 1: The MS structure with 8 Nos. of panels. Roof 2: A corrugated sheet structure with 11 Nos. of panels.
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	One can access the terrace floor via the inner staircase. But the headroom can be accessed with the help of a reliable ladder yet to be fabricated.
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	The following will be provided by the customer: 1) All earthings (including AC, DC & LA) up to the required termination points. 2) Conduits for DC cable from terrace level to the inverter room.
13	What is the height of the building and how many floors does it have?	15 meters. (G + 2 + Headroom)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	The building is under construction. The LT panel is not yet installed.
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	No	No access available at the moment. under construction.
4	Is the Termination Point easily visible or sealed?	Sealed	No access available at the moment. under construction.


#	Question	Answer	Notes
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	<i>The solar meter provision has been given in the customer LT panel.</i>
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>All earthings (including AC, DC & LA) up to the required termination points will be provided by the customer.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	No	<i>The lightning arrester has to be installed on the lift headroom terrace.</i>
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	<i>Open window available in the room.</i>
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	All accessories are wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	N/A	-
21	Provide the dimension for earth pits location (L x W of available space).	N/A	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend



Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA



Site Layout - Top View


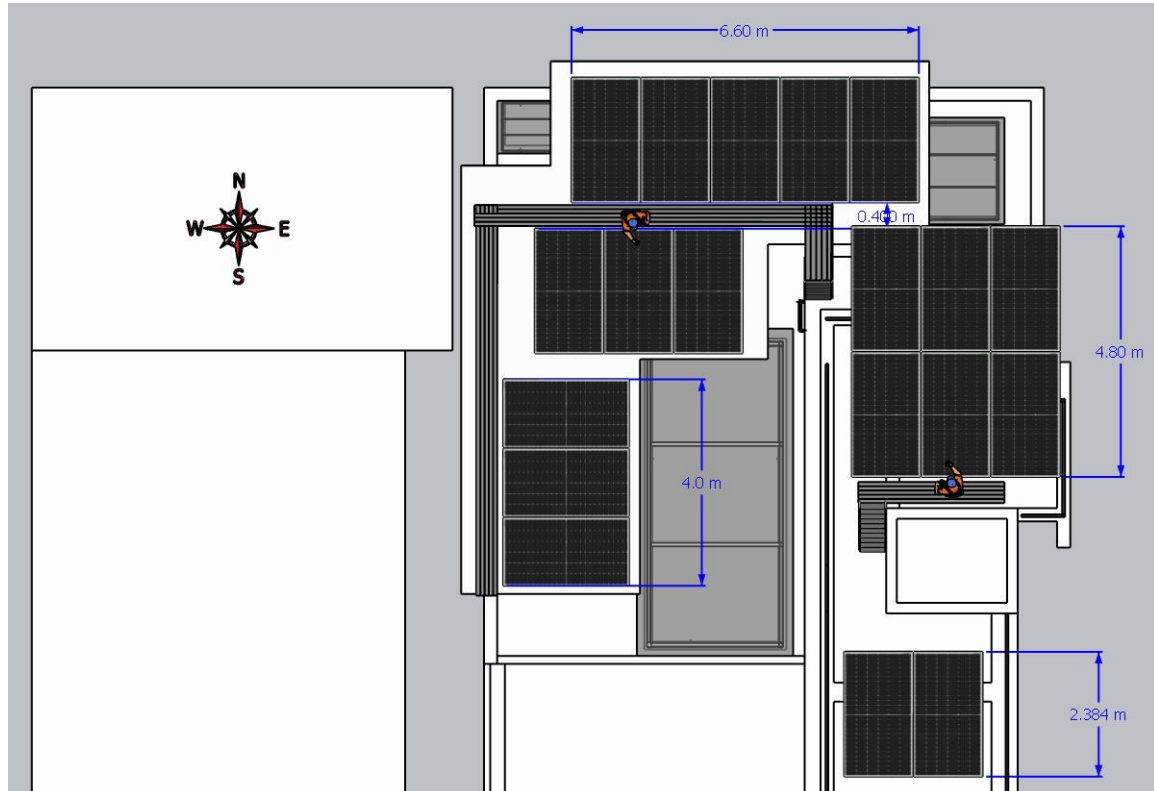


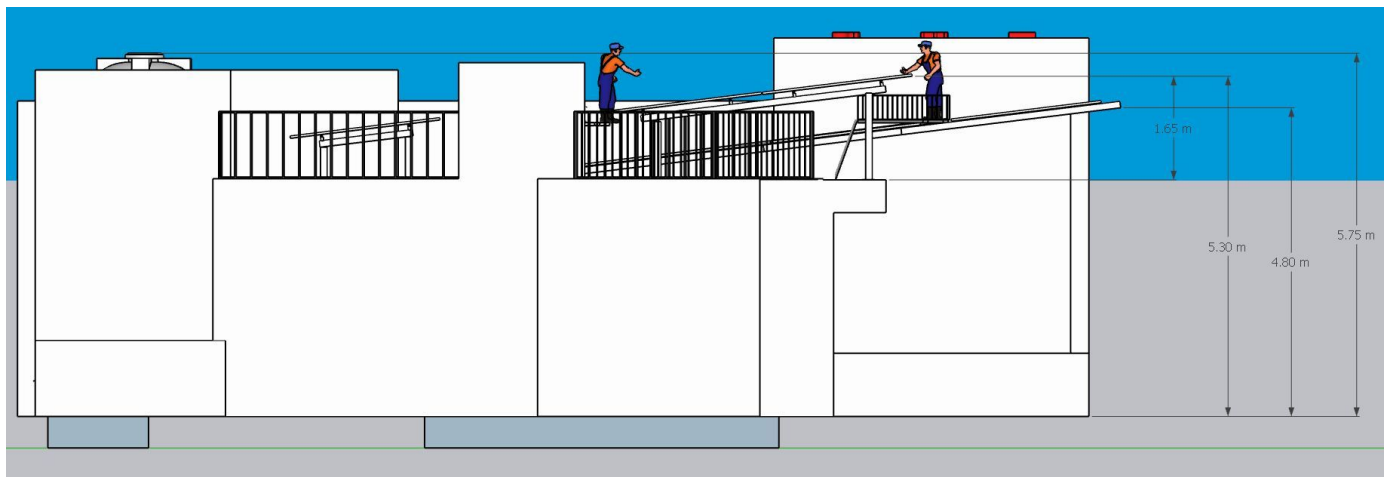
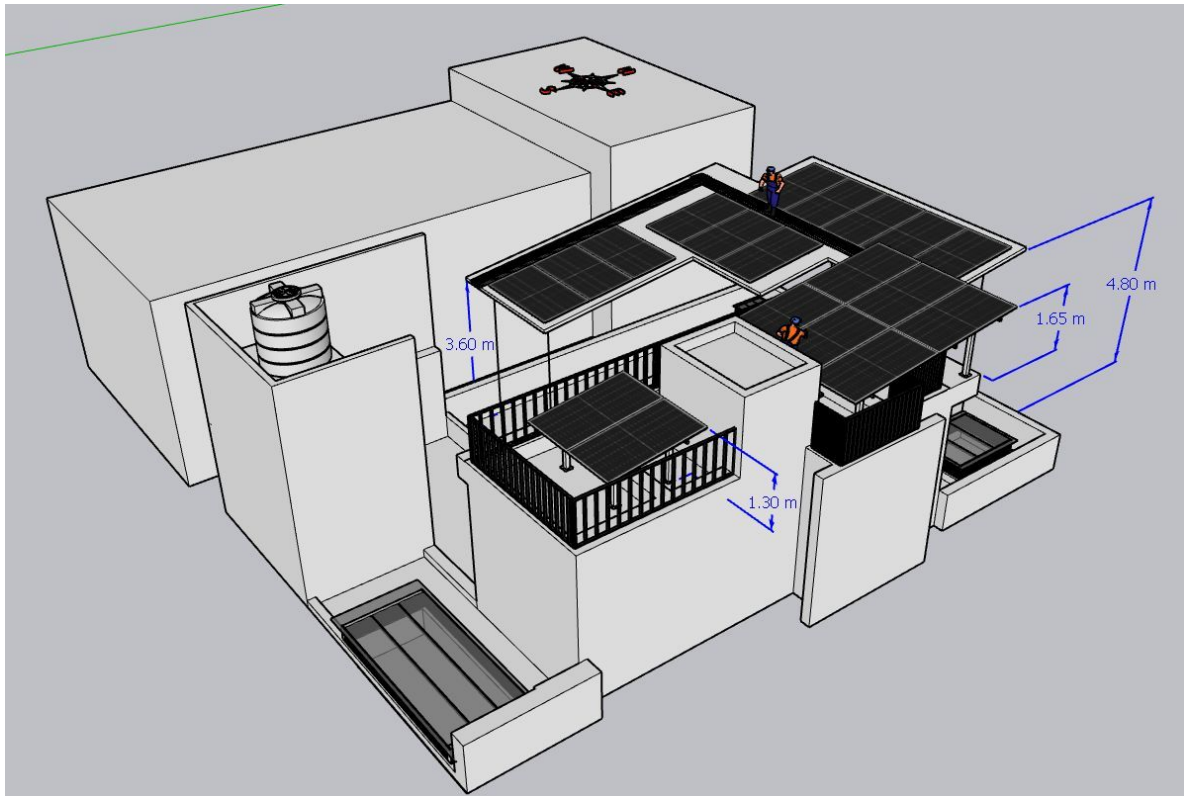


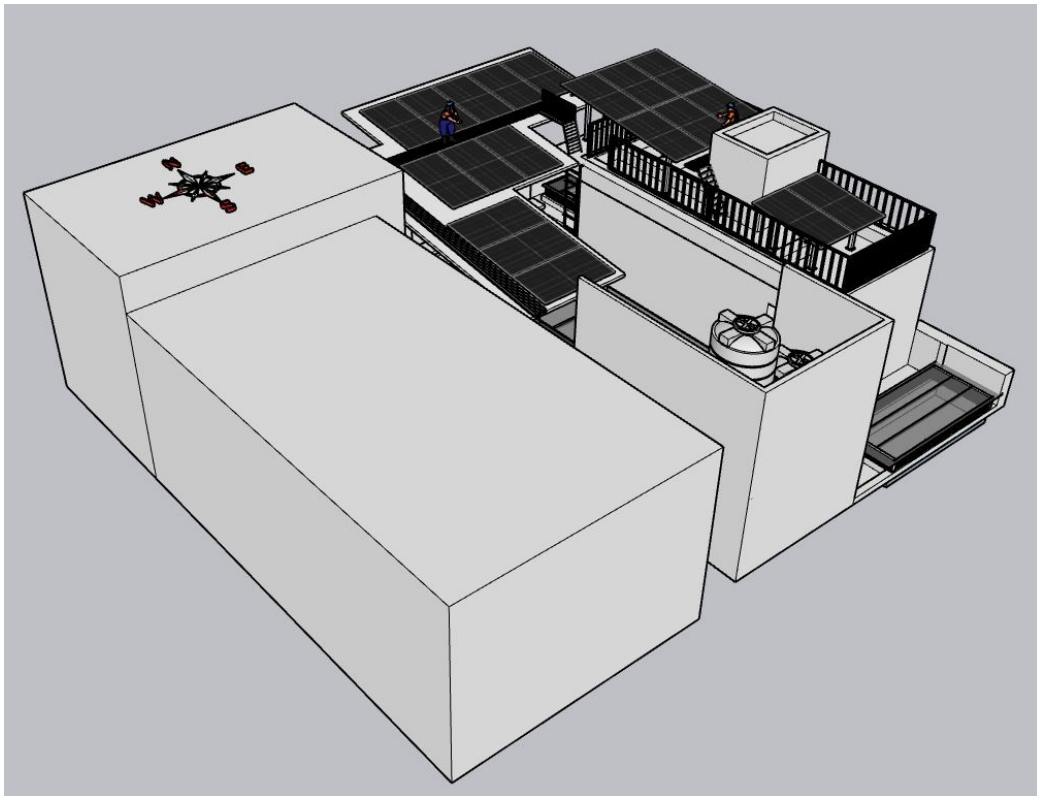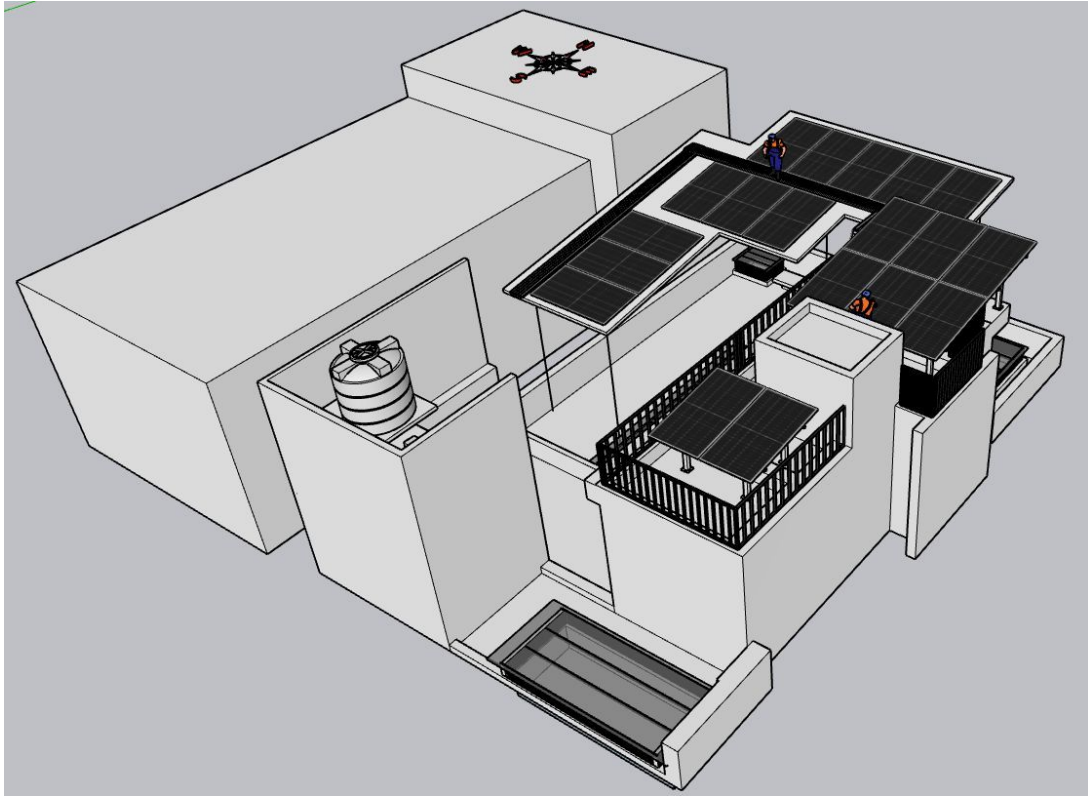


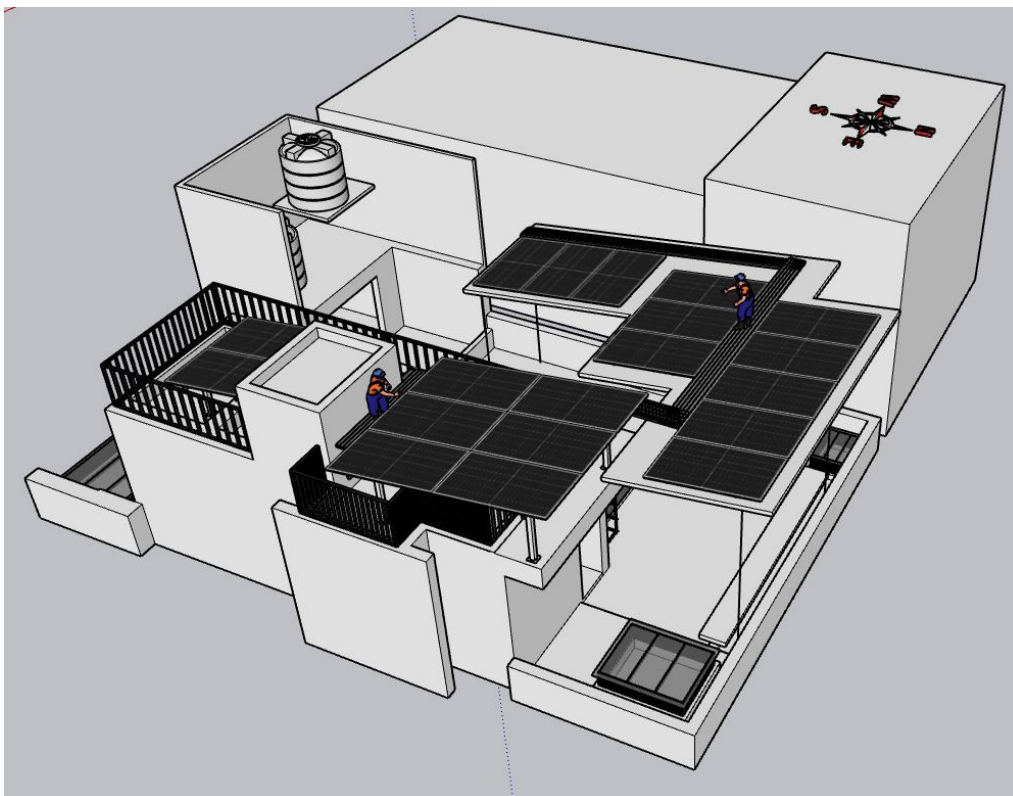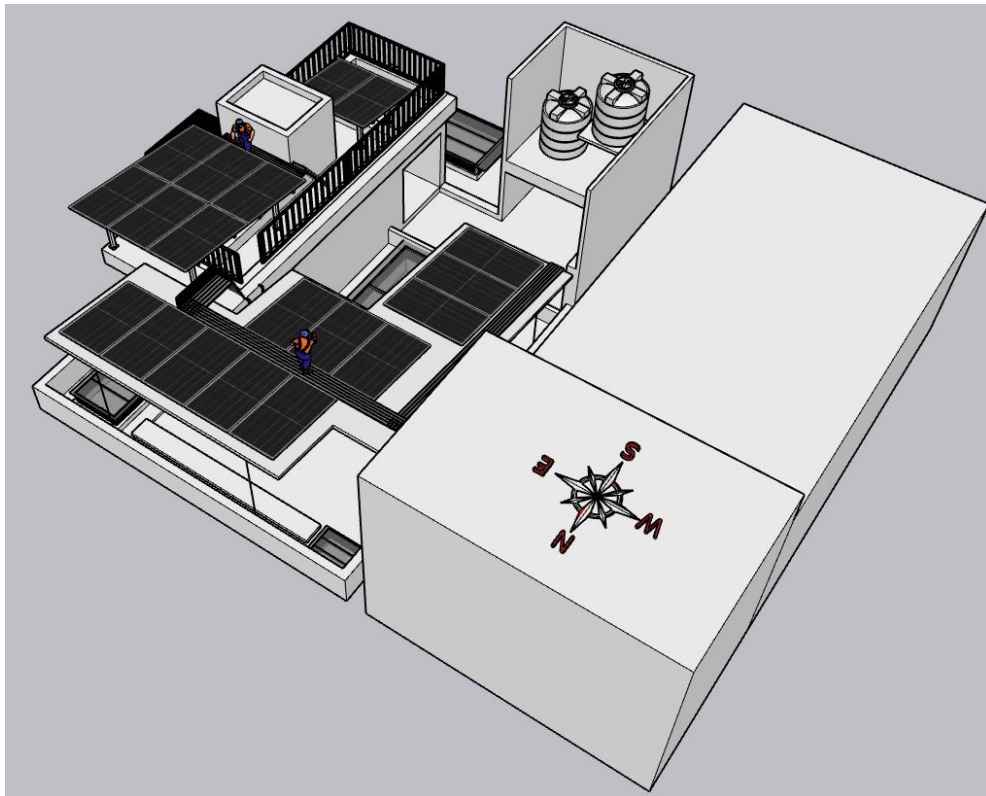

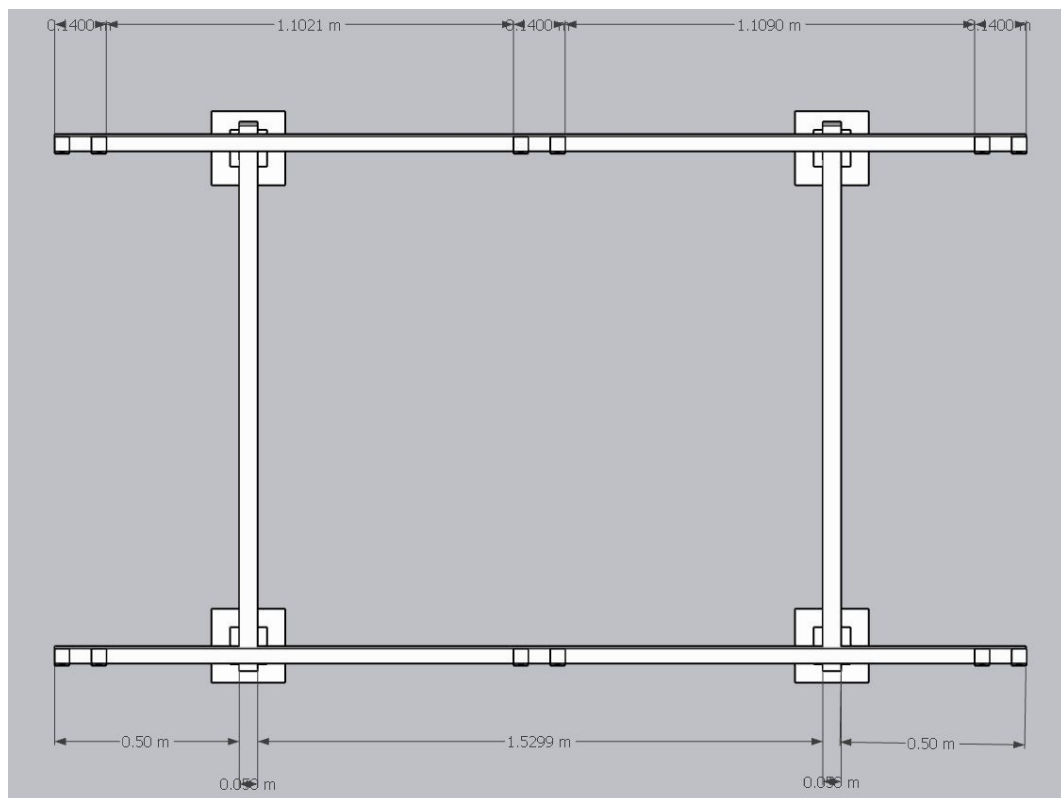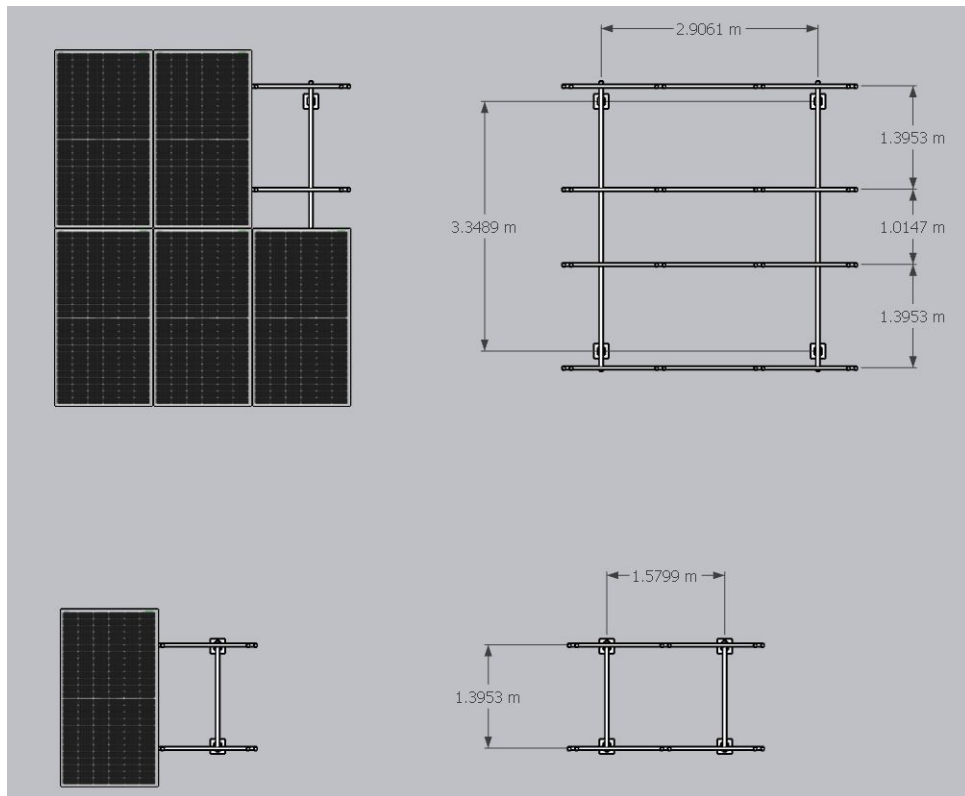

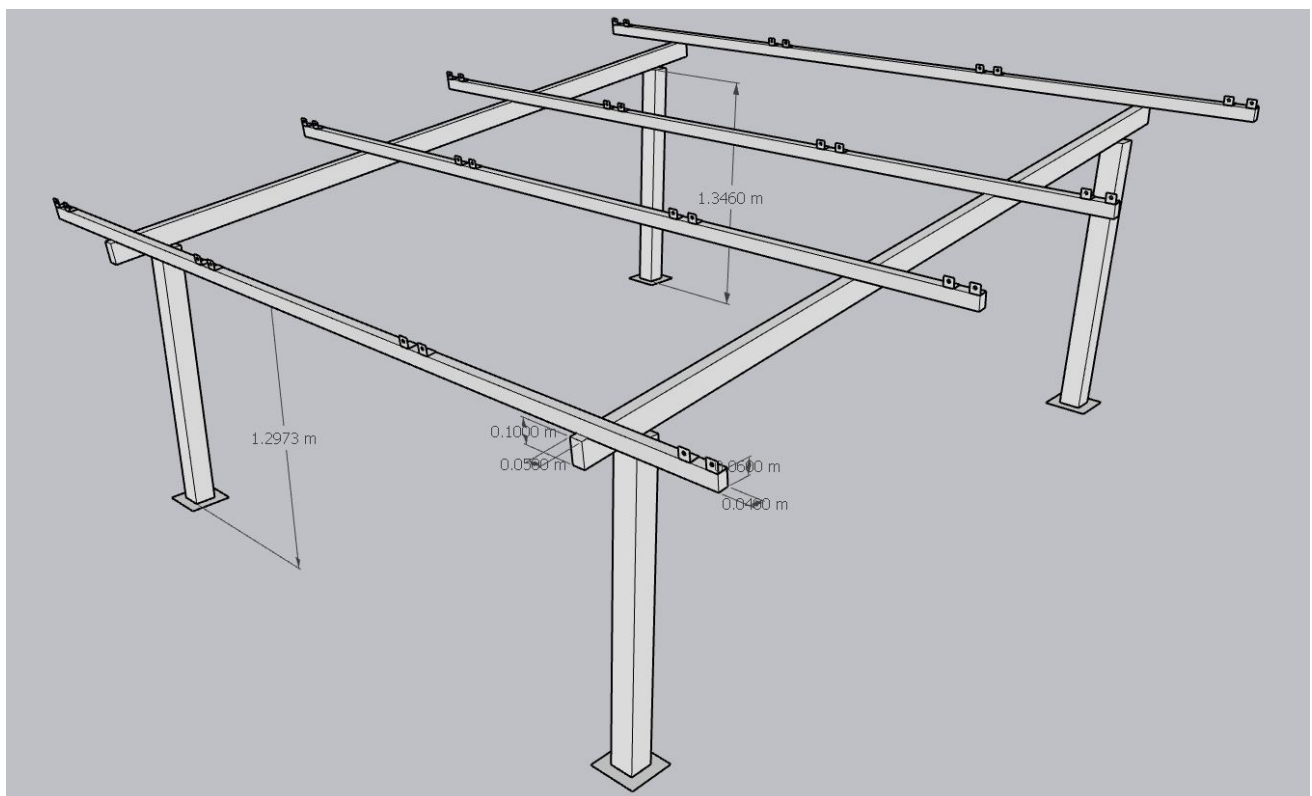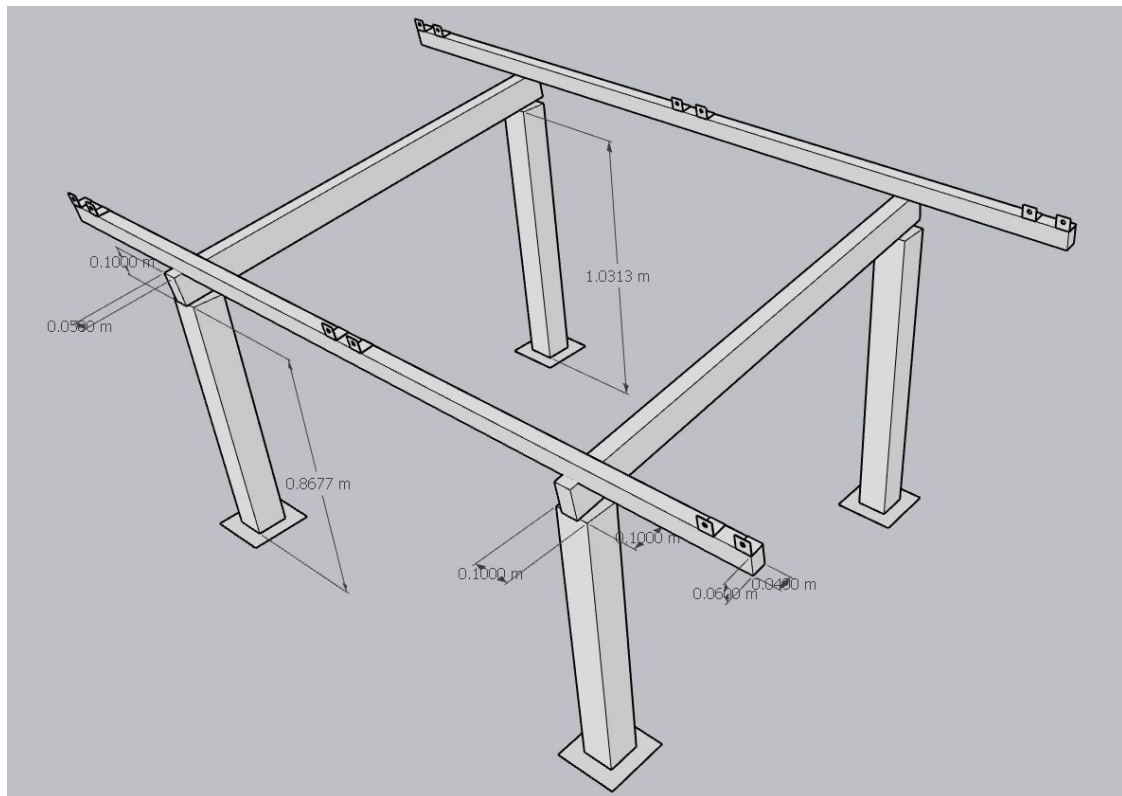

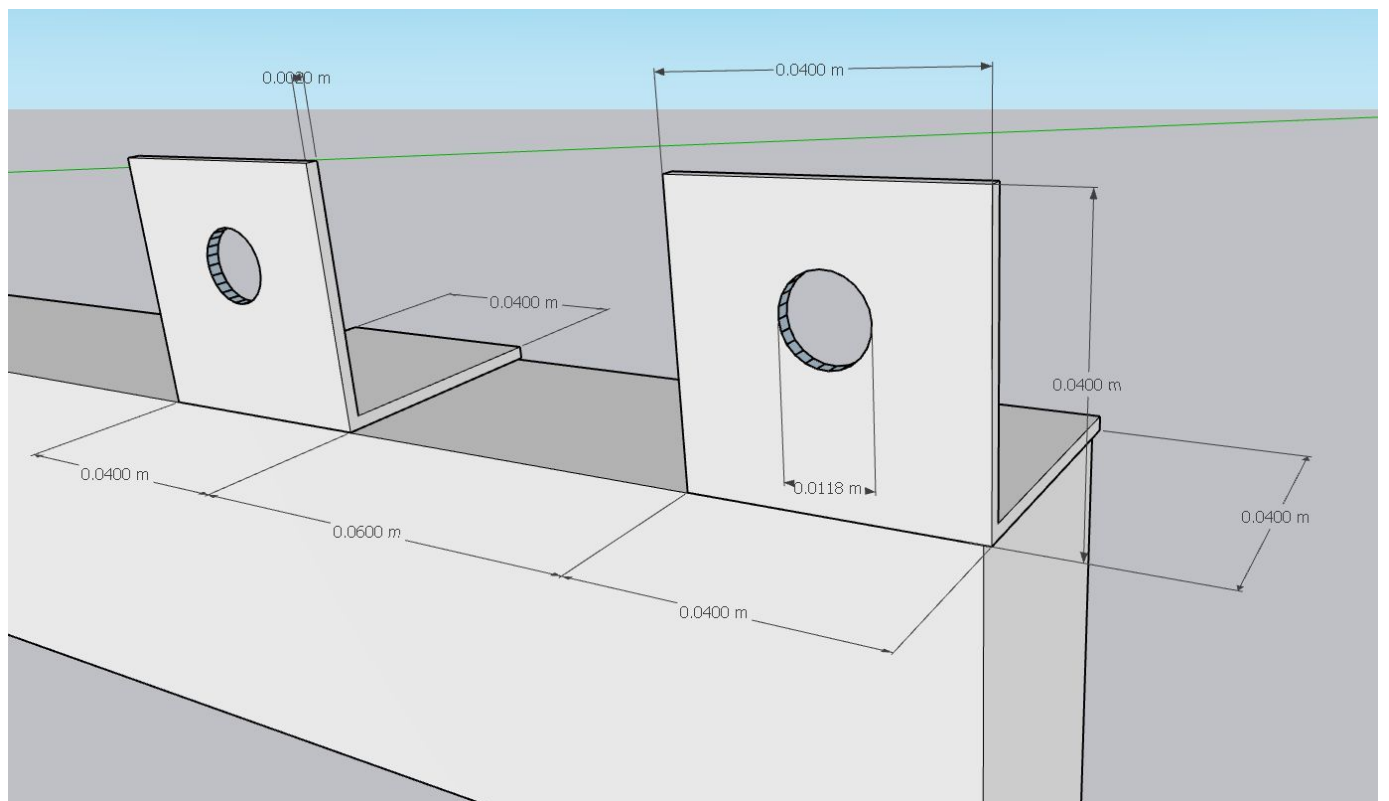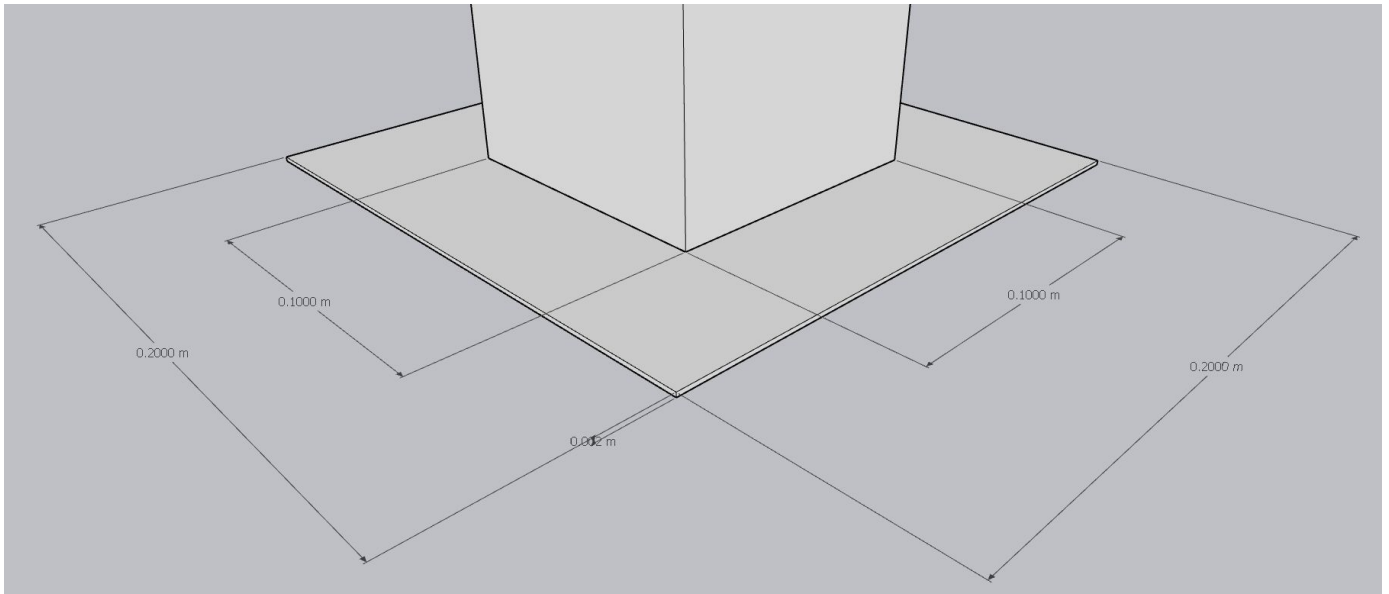

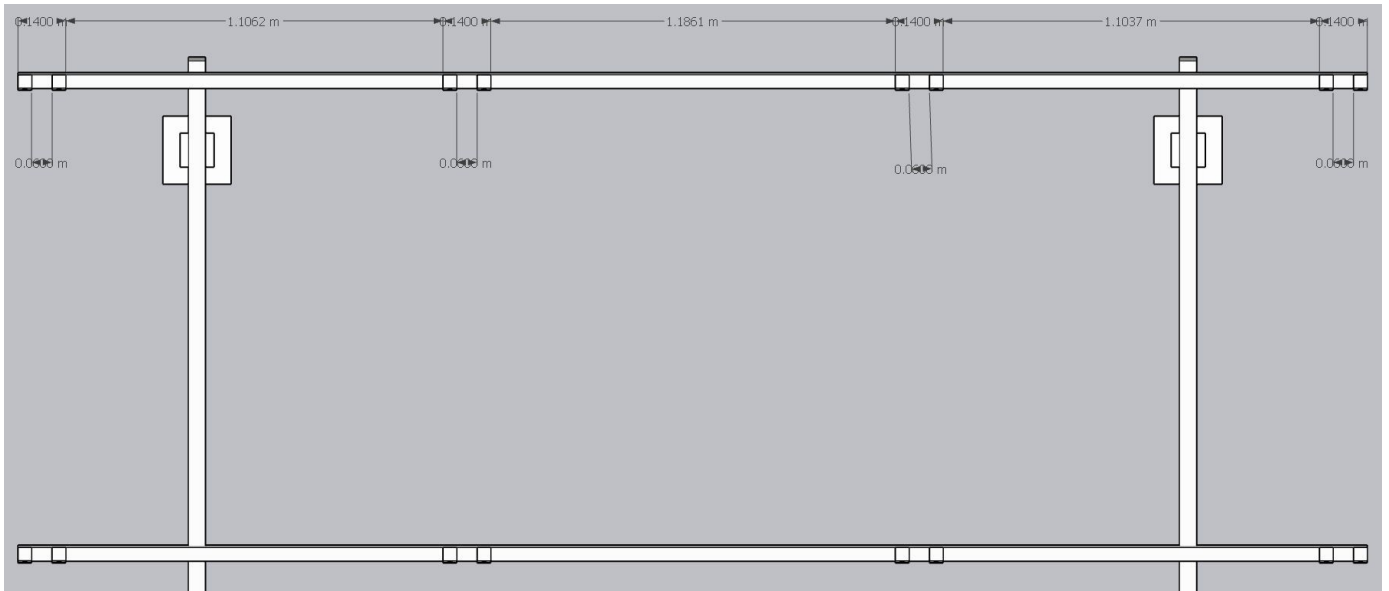

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



The materials can follow the stairs until reaching the terrace.



The materials can follow the stairs until reaching the terrace.



The materials are reaching the terrace floor of the 2nd floor.

Staircase Details



Material Storage




The materials can be stored inside this room available in the 2nd floor. (The panels can be stacked either vertically leaning on the wall or it can be stacked horizontally on the floor.

Proposed PV Area



Cable Routing

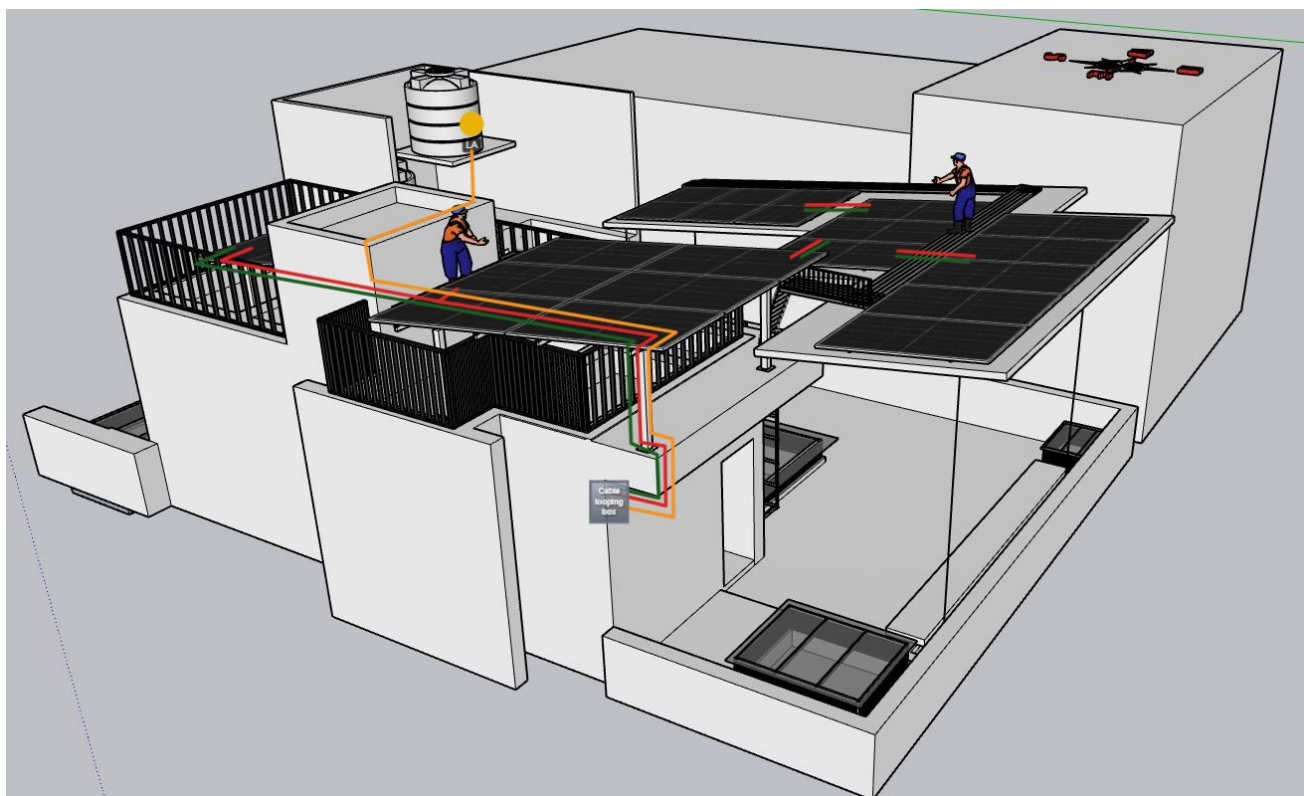



The customer will provide CONDUITS for DC cable, DC Earthing cable and LA earthing cable till the terrace level.



Three earth pits have already been done by the customer.



DC earthing cable and AC earthing cable can be terminated here at the earth bunch (provided by the customer.)



DC earthing cable and AC earthing cable can be terminated here at the earth bunch (provided by the customer.)




Meter Box




The LT panel is covered at the moment. (Under construction)

Shadow Analysis

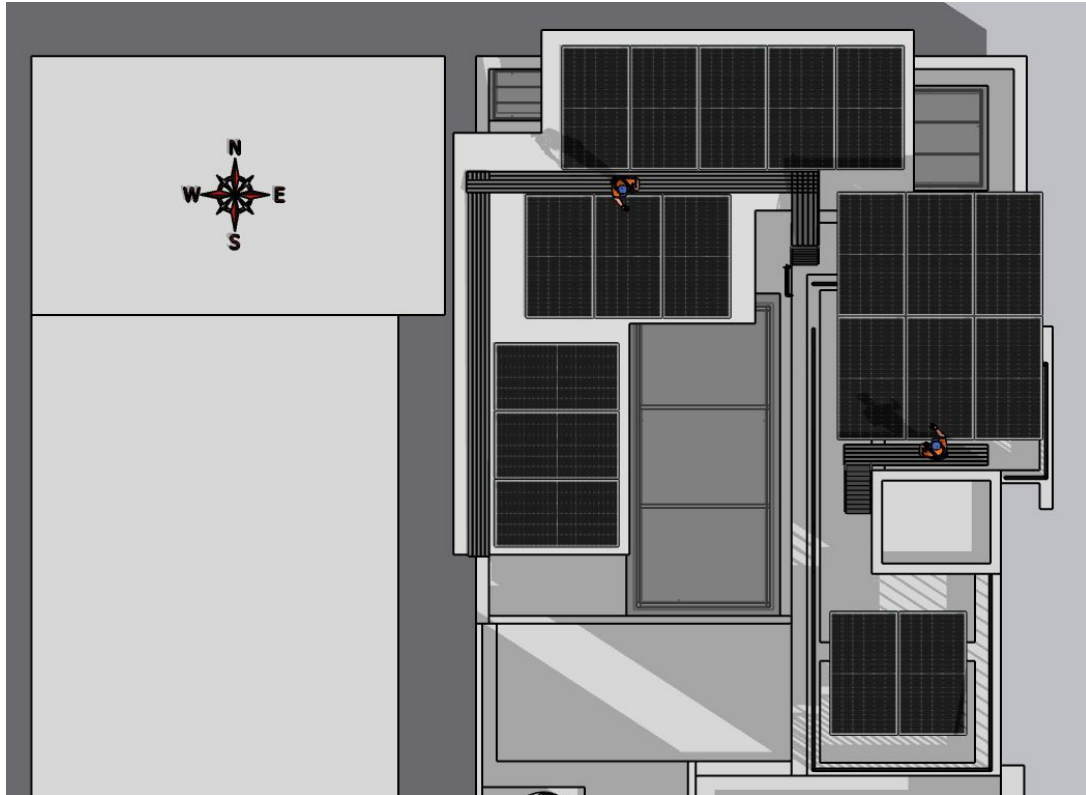

Shadow view (Nov - Jan) at 9 am

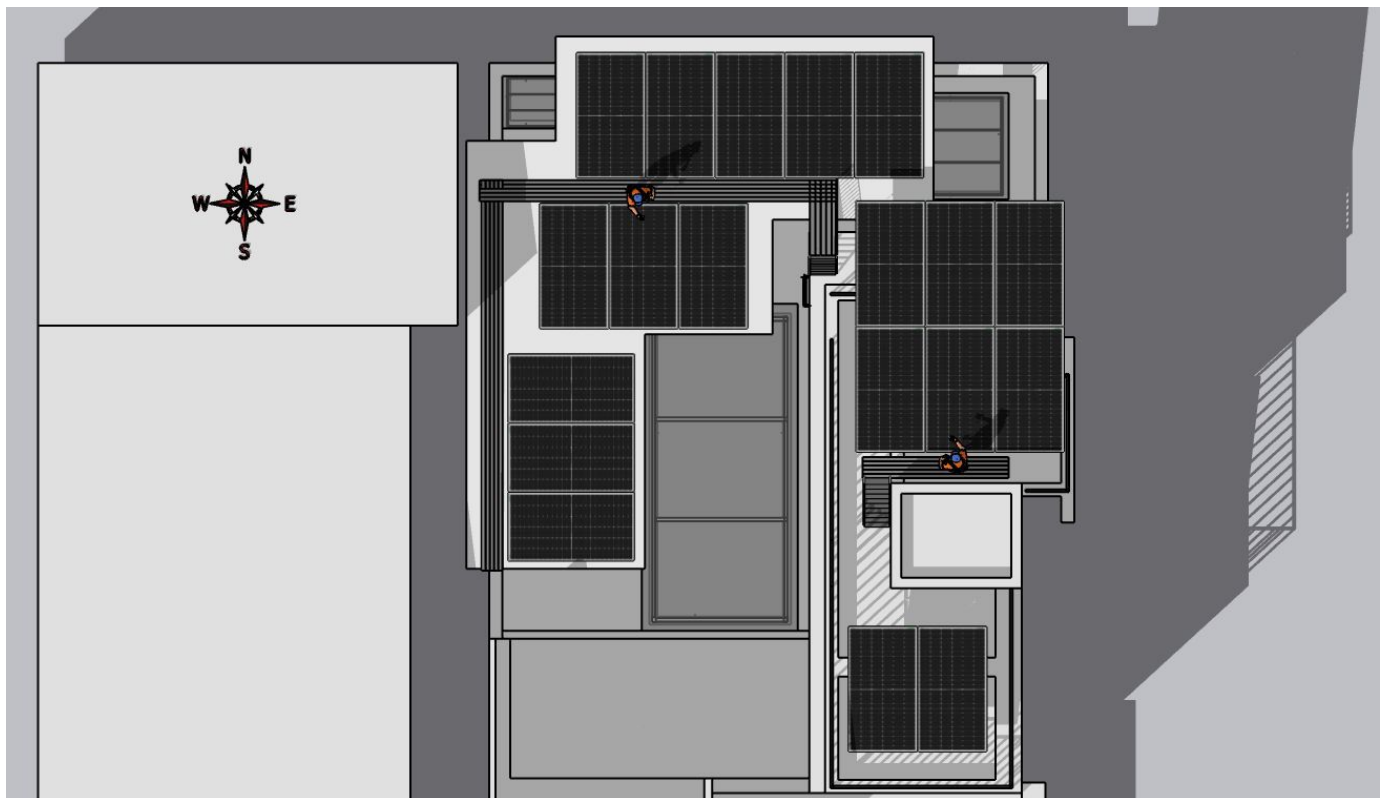

Shadow view (Nov - Jan) at 3 pm

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 13.3 kWp Hybrid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.
3	The customer will be providing all the earthing cables (3 set) from the earth pits to the respective termination points.

THANK YOU

Dear V Dorairaj,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
