

Technical Site Visit Report

Prepared for: Dr. Anisha Hari - 226/5

PROJECT INFORMATION

Report Number	ESV-2026-0141
Project ID	20510A31
Project Name	Dr. Anisha Hari
Building Name	226/5
Billing Name	Dr. Anisha Hari
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Mahantayya
Site Address	Dr. Anisha Hari plot # 226/5, 2nd street, Ferns Residency Kothanur Narayanapura 560077.
GPS Coordinates	13.0573797, 77.6382446
Google Maps	https://www.google.com/maps?q=13.0573797,77.6382446
Visit Date	2026-06-13
Visited By	K Naveen
Revision	Rev 1

CLIENT INFORMATION

Client Name	Dr. Anisha Hari
Contact	99169 53903

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	9.8
Module Make & Capacity	Waaree bifacial Non DCR - 700 Wp
Module Length (mm)	2382

Module Width (mm)	1303
Number of Panels	14
Inverter Type	Hybrid (String)
Inverter Brand	Deye 10 kW 3phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The elevation may be the obstacle to hinder the material lifting	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Below the water tank area inverter, DCDB, ACDB, Battery will be installed.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the ground floor.	-
6	Where is the Internet Router located?	Under construction	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-

#	Question	Answer	Notes
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstructions on the roof are lift headroom, water are the obstruction	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	HDGI - Elevated
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	The height of the building Basemen t+G+2+Headroom+approximately 15meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	Under construction
2	Is the Meter cubicle photo matching with the previous answer?	No	-
3	Has the termination point in the Main meter panel been identified?	No	-
4	Is the Termination Point easily visible or sealed?	-	Not Available
5	Is a Lightning Arrestor (LA) already available at the site?	No	Not Available
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Unser construction
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-

#	Question	Answer	Notes
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall Mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 1500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1000, width: 1000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).








This route (using Staircase) will be followed to carry Small items.



Staircase Details

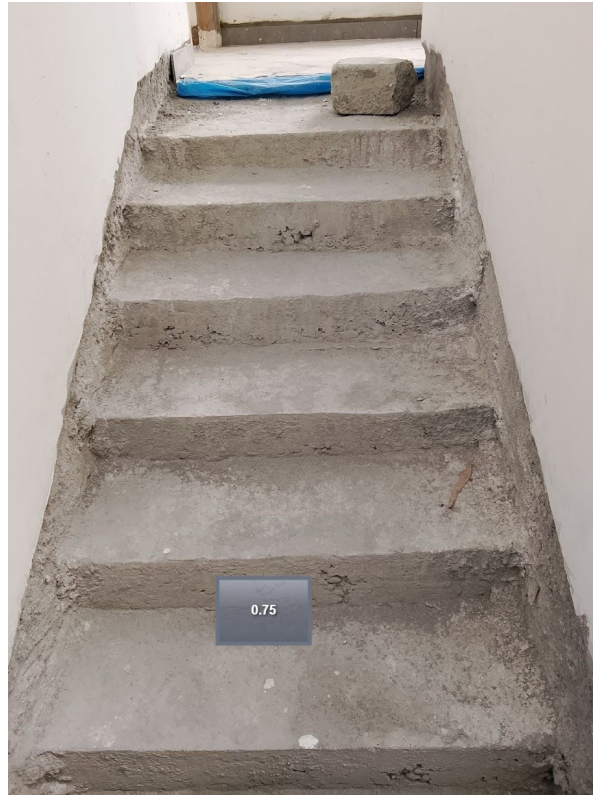

Meter Box




Material Storage



Proposed PV Area



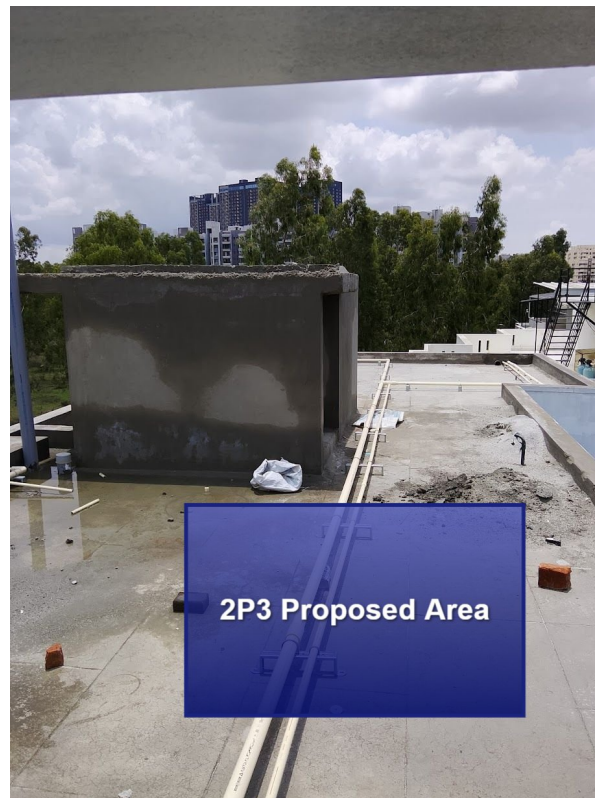


Cable Routing






Both 2P4 & 2P3 DC cable, DC earthing has been tapped here

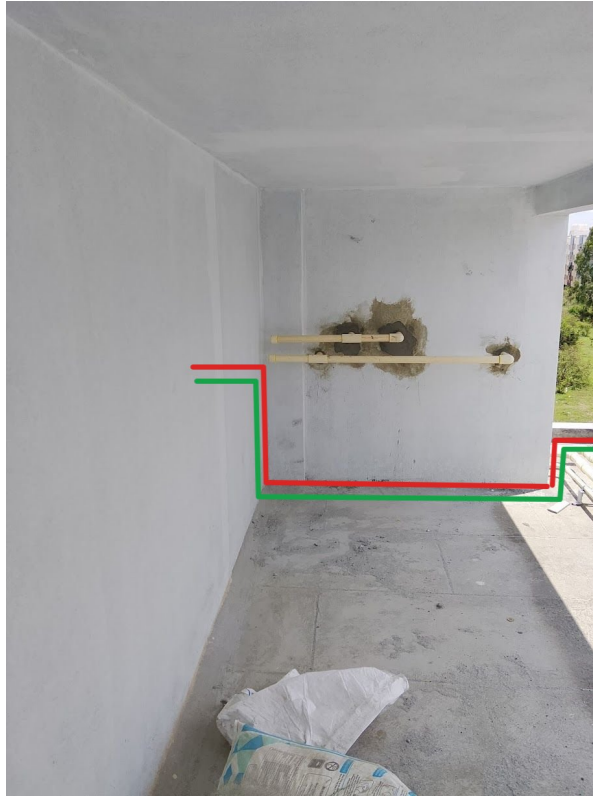



Equipment Location

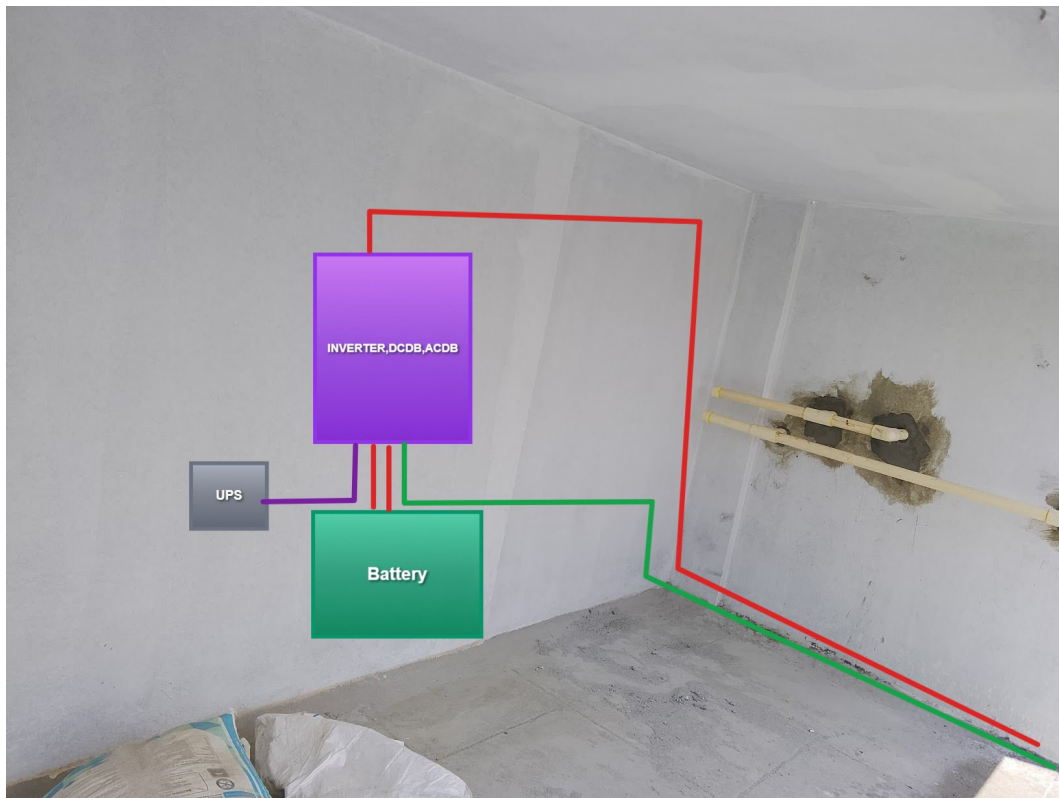

Client will made UPS near the inverter location






As per the client suggestions the electrical panel and main meter will be installed here.



Earth Pit Location







Site Layout - Top View

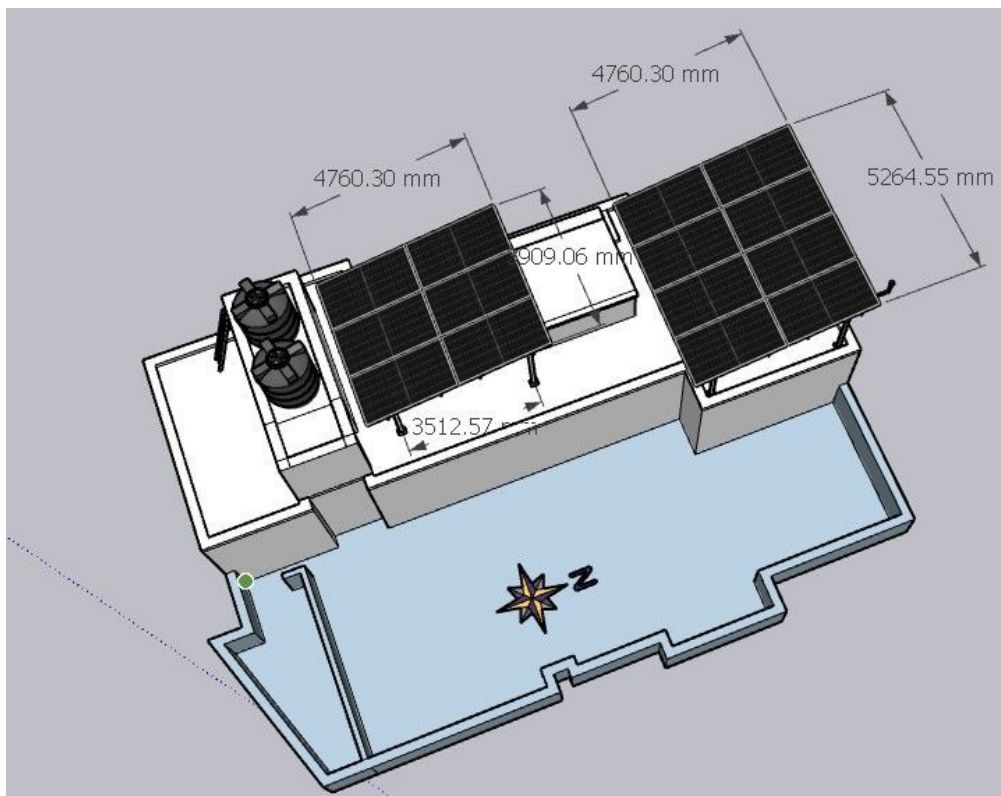

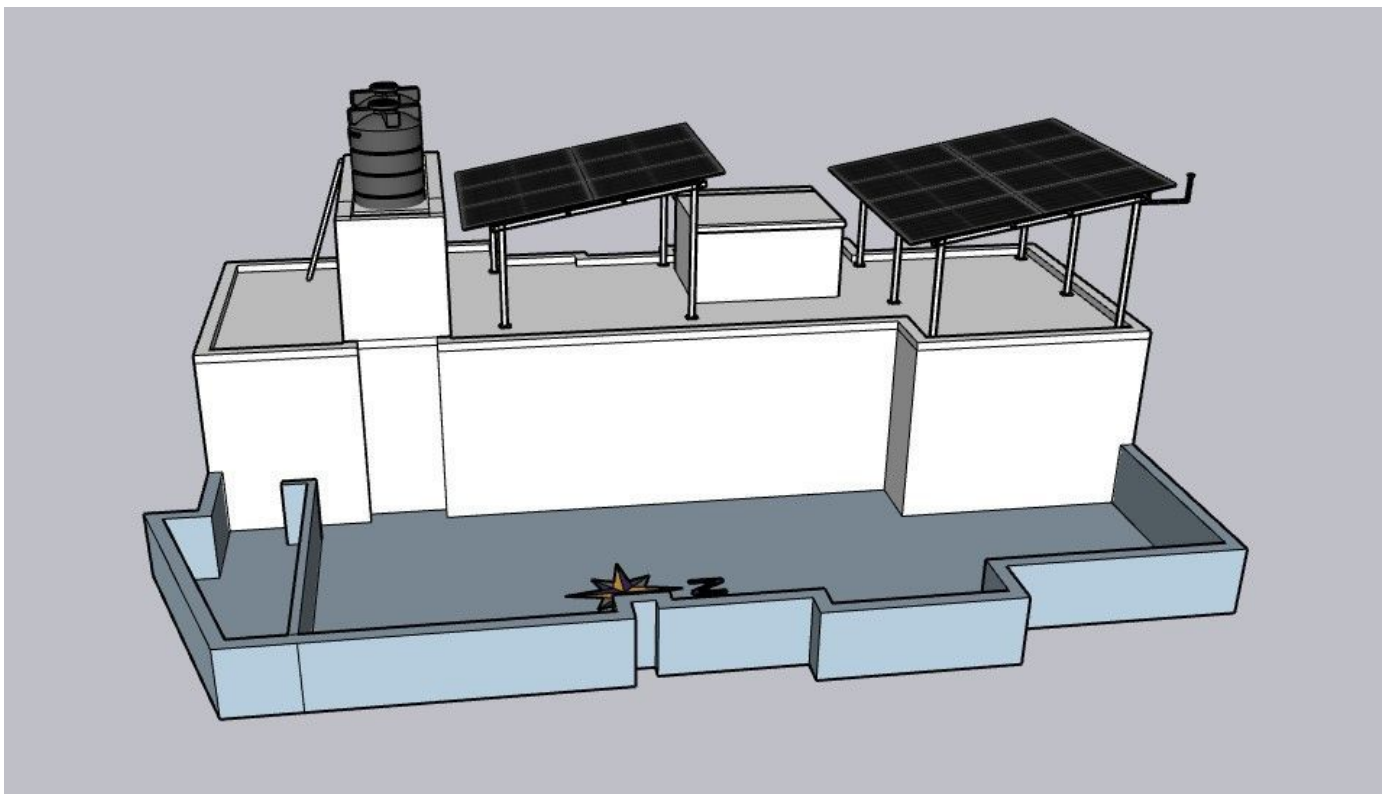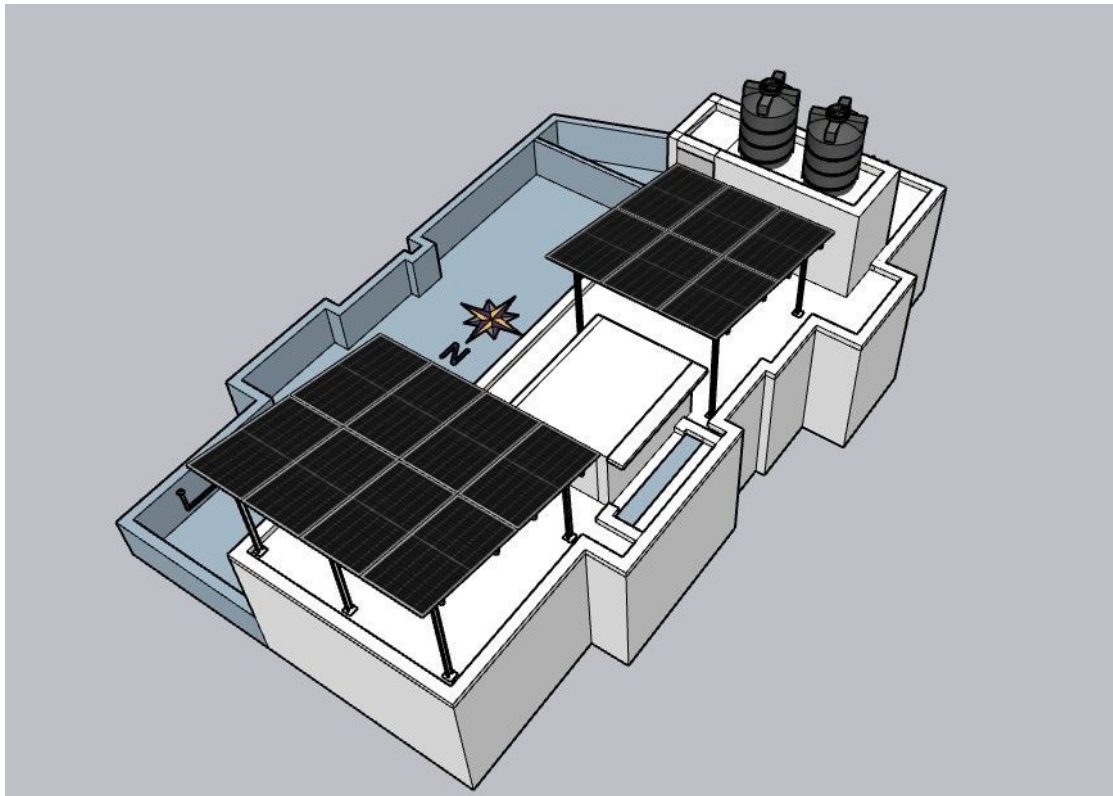

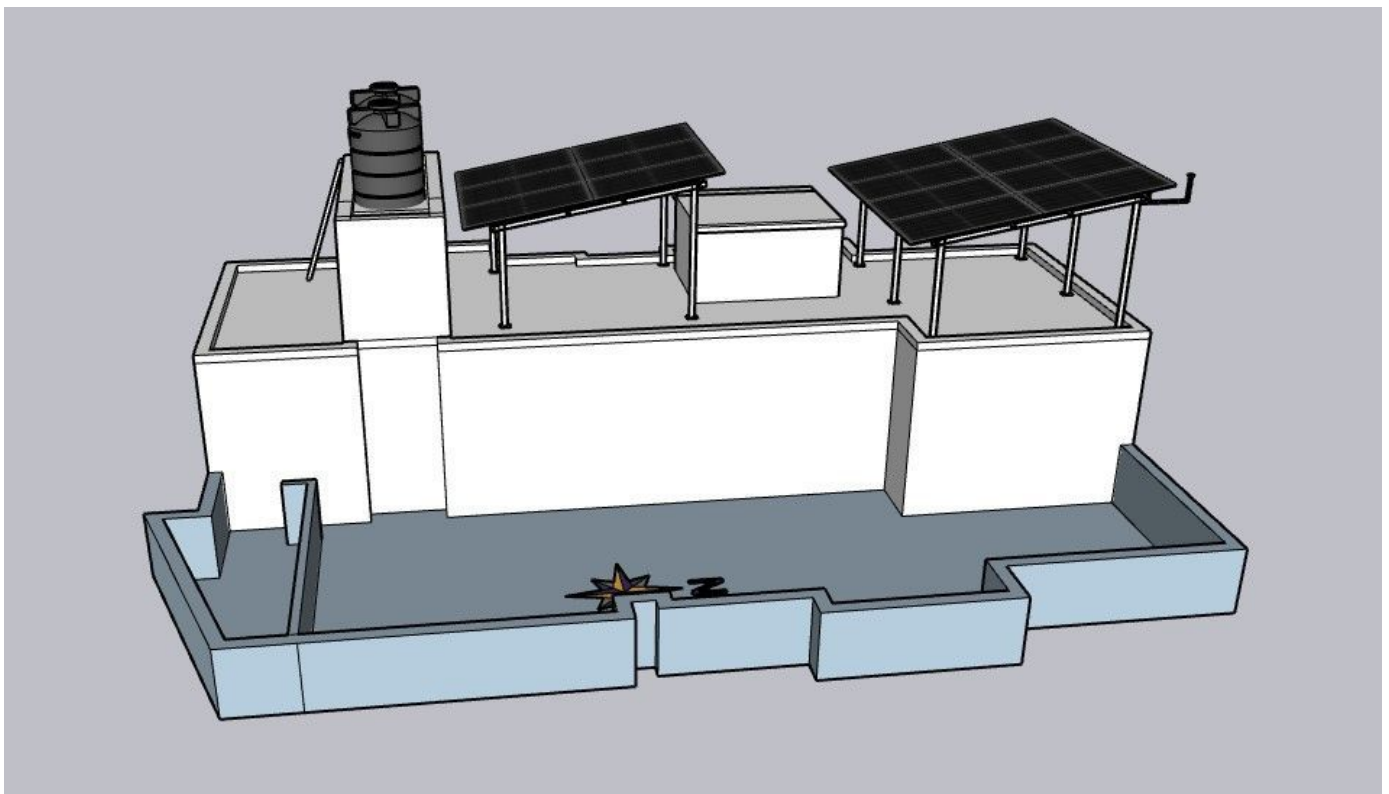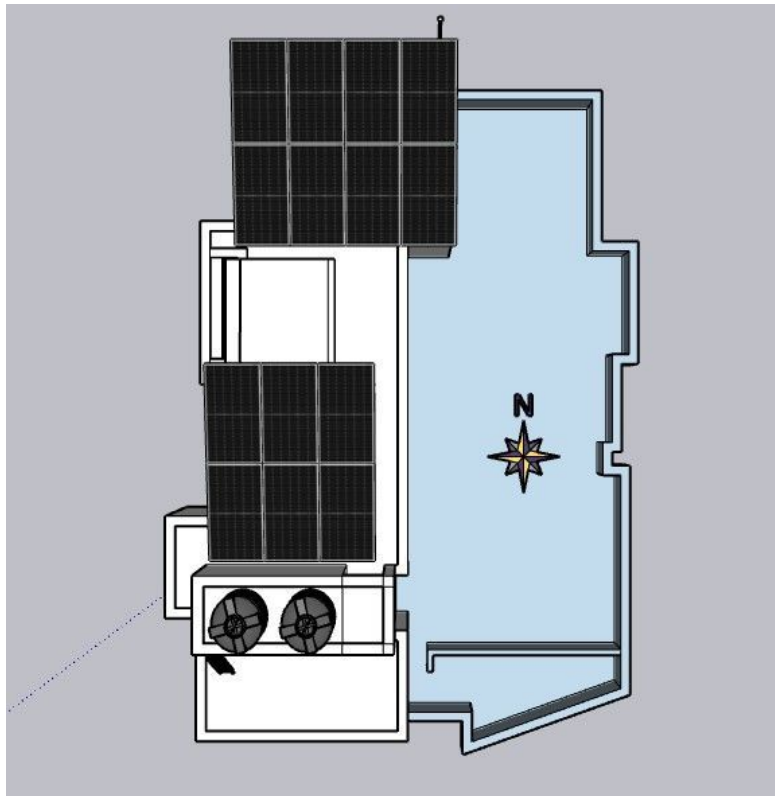

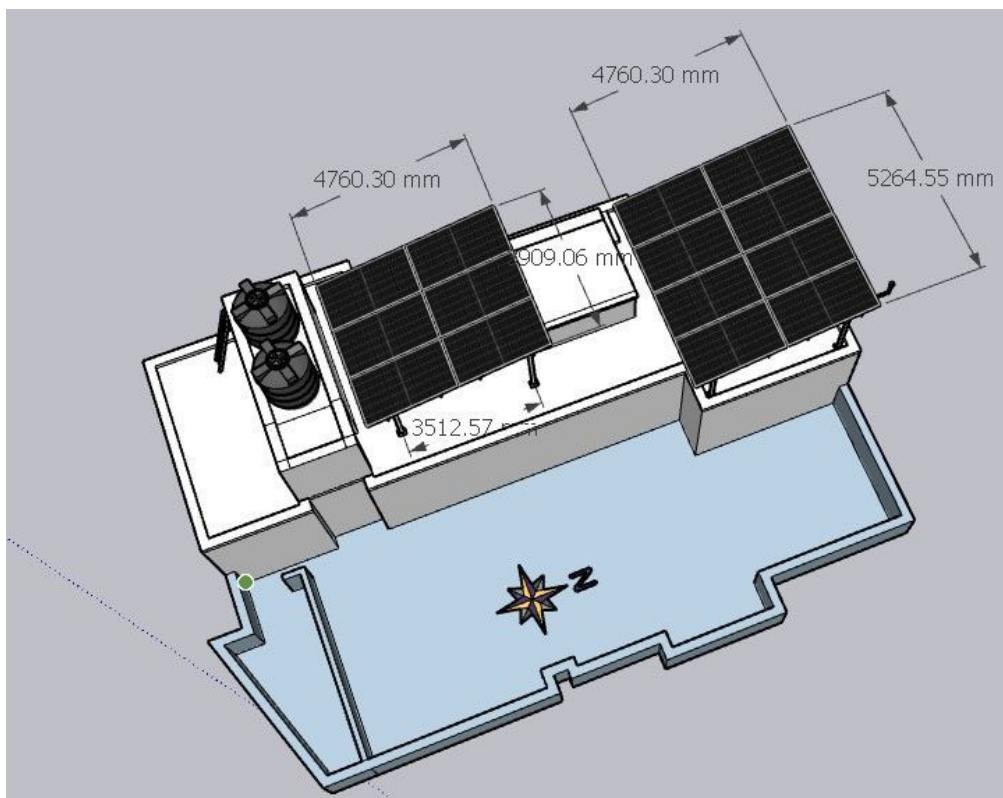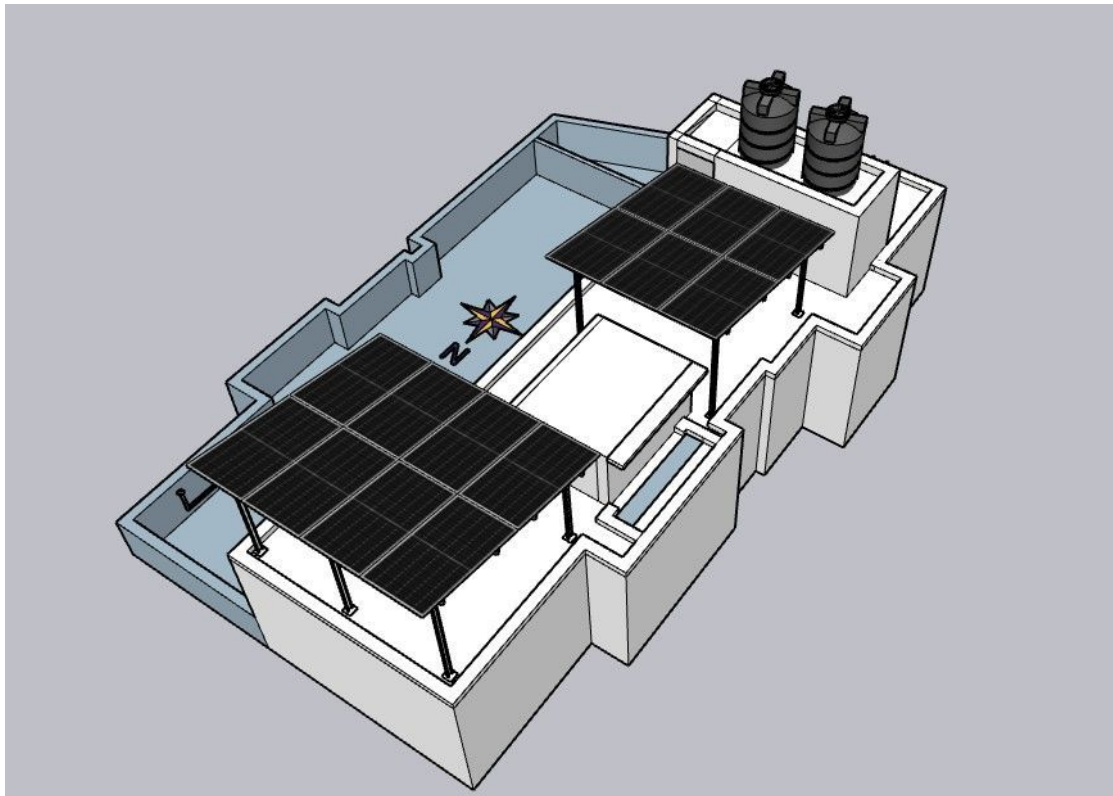

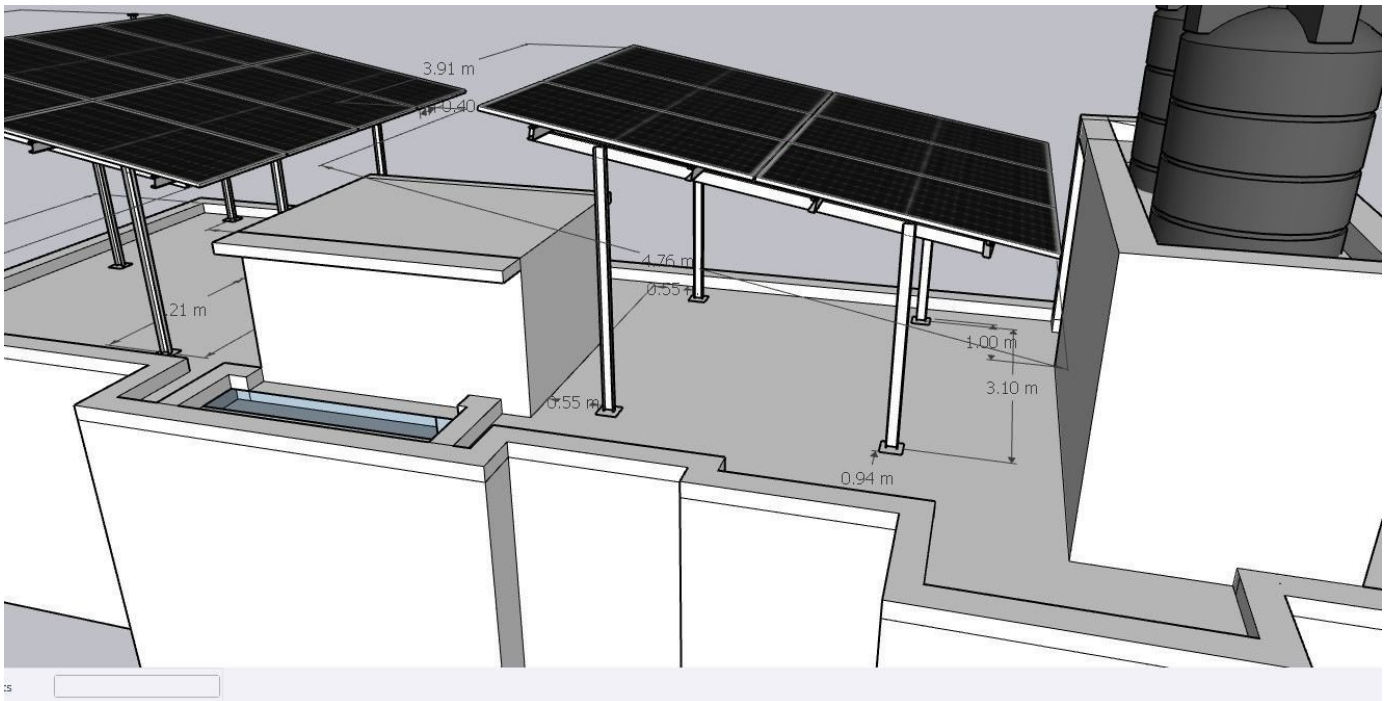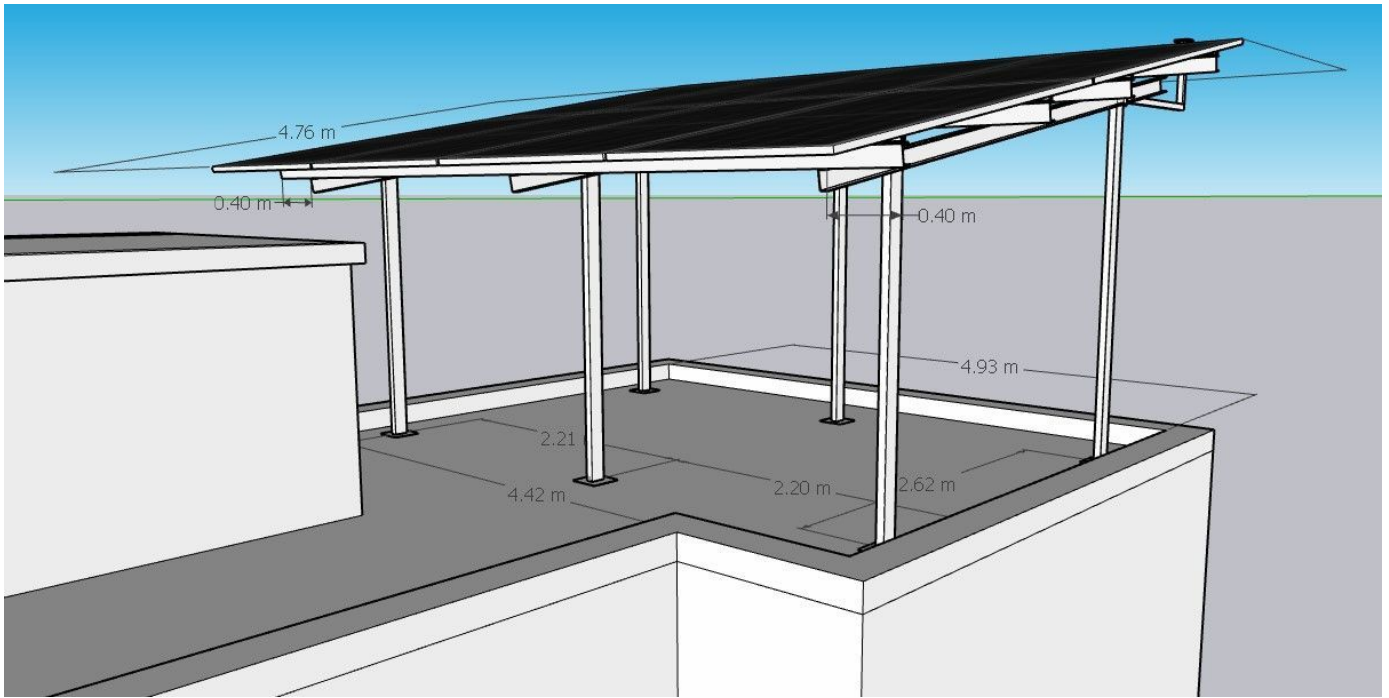

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	Still the site is in under construction ,main meter panel not yet installed.
3	UPS point near the inverter location is under customer scope.
4	As per customer suggestions only the pannnel layout,earthing location and cable routing has been finalised.

THANK YOU

Dear Dr. Anisha Hari,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
