

Technical Site Visit Report

Prepared for: BISINEER PROJECT - MAHATHI SENTHIL_Ecocity by SPA Group_9.8kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0105
Project ID	3CF859FC
Project Name	BISINEER PROJECT - MAHATHI SENTHIL_Ecocity by SPA Group_9.8kWp_Hybrid
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	John D
Site Address	NO. 6, 29/1-B, GROUND FLOOR KONANKUNTE INDUSTRIAL AREA AMRUTHNAGAR MAIN ROAD HARINAGAR CROSS, BANGALORE - 560062
GPS Coordinates	12.816386, 77.819732
Google Maps	https://www.google.com/maps?q=12.816386,77.819732
Visit Date	2026-05-04
Visited By	ABILASH N K
Revision	Rev 4

CLIENT INFORMATION

Client Name	BISINEER PROJECT - MAHATHI SENTHIL
Contact	8867910252

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	9.8
Sanction Load (kW)	14
Module Make & Capacity	Waaree Non DCR Topcon, 700 Wp
Module Length (mm)	2384

Module Width (mm)	1303
Number of Panels	14
Inverter Type	Hybrid (String)
Inverter Brand	Deye: 8KW - 48V - LV - Three Phase
Number of Inverters	1
Battery	Needed
Number of Batteries	4
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	In the second floor, the inverter and other accessories can be fixed on the wall, just below the headroom.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, discussed with the customer and finalised the location for earthing.	-
6	Where is the Internet Router located?	Building is under construction	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: Lift head room, a skylight, a water tank tower, etc. are present on the roof.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	HDGI elevated structure with a 2M front height.
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	No electrical DBs, earth pits or cable routing existed at the site at the time of the site survey.
13	What is the height of the building and how many floors does it have?	15 metres (G + 2 + head room)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	A temporary construction-purpose meter is available at the site.
2	Is the Meter cubicle photo matching with the previous answer?	N/A	-
3	Has the termination point in the Main meter panel been identified?	N/A	-
4	Is the Termination Point easily visible or sealed?	N/A	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Informed the customer that they would be


#	Question	Answer	Notes
			<i>providing a solar meter box in the LT panel that they would be fabricating.</i>
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>The earthing is expected to be dug around the current LT panel placement.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	Without Grouting	<i>In order to provide additional stability against wind, the customer asked for a brace support for the HDGI structure.</i>
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 3000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 1000	<i>The space available near the LT panel is considered for digging the earth pits as of now.</i>
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-

PHOTO DOCUMENTATION


Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit


Site Layout - Top View

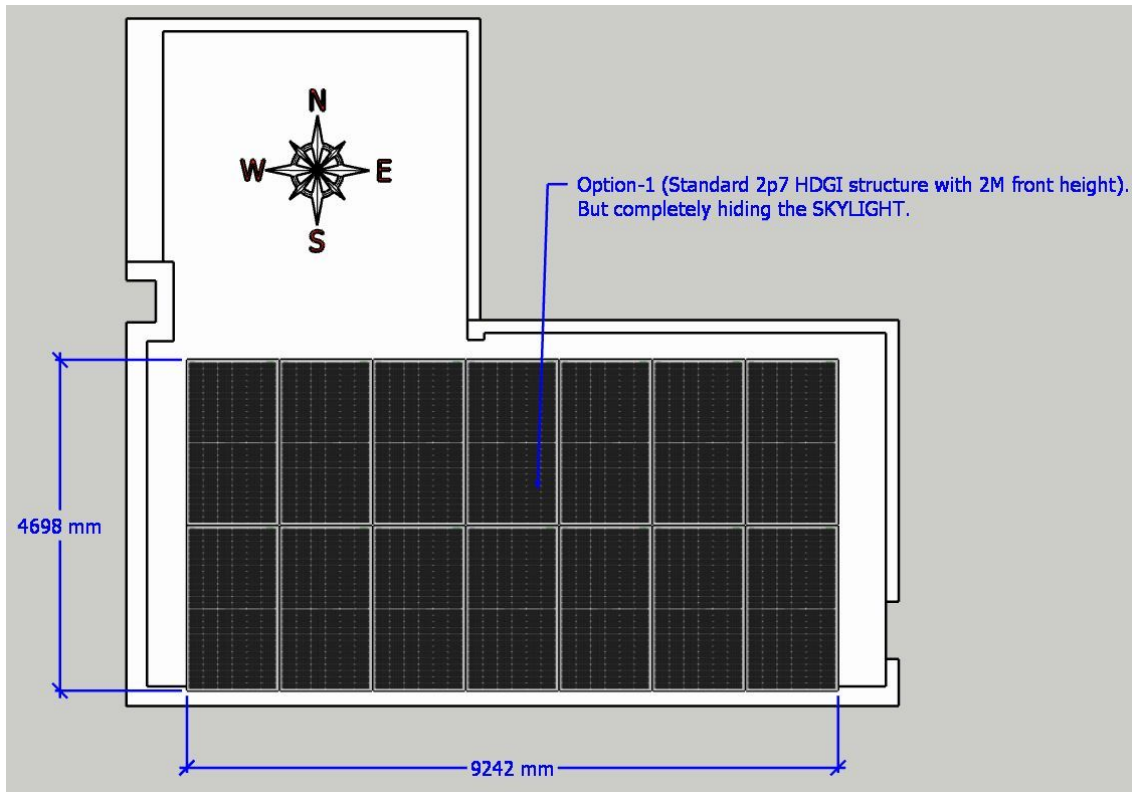


Option 1_Top view

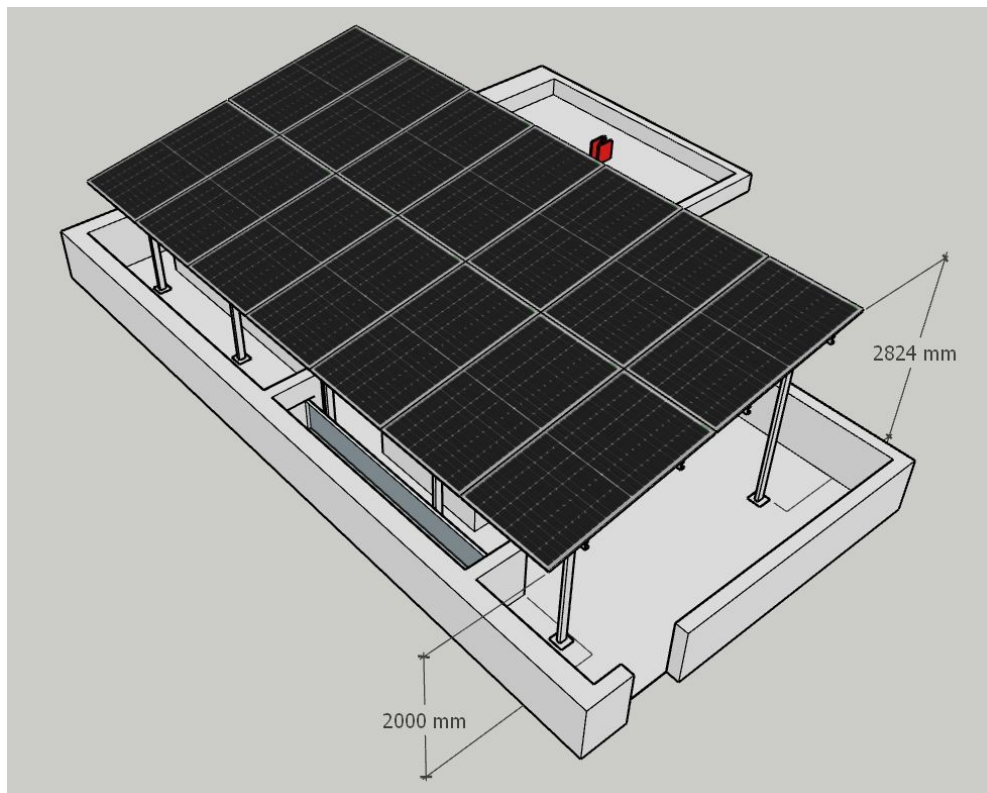


Option 1_Iso view 1

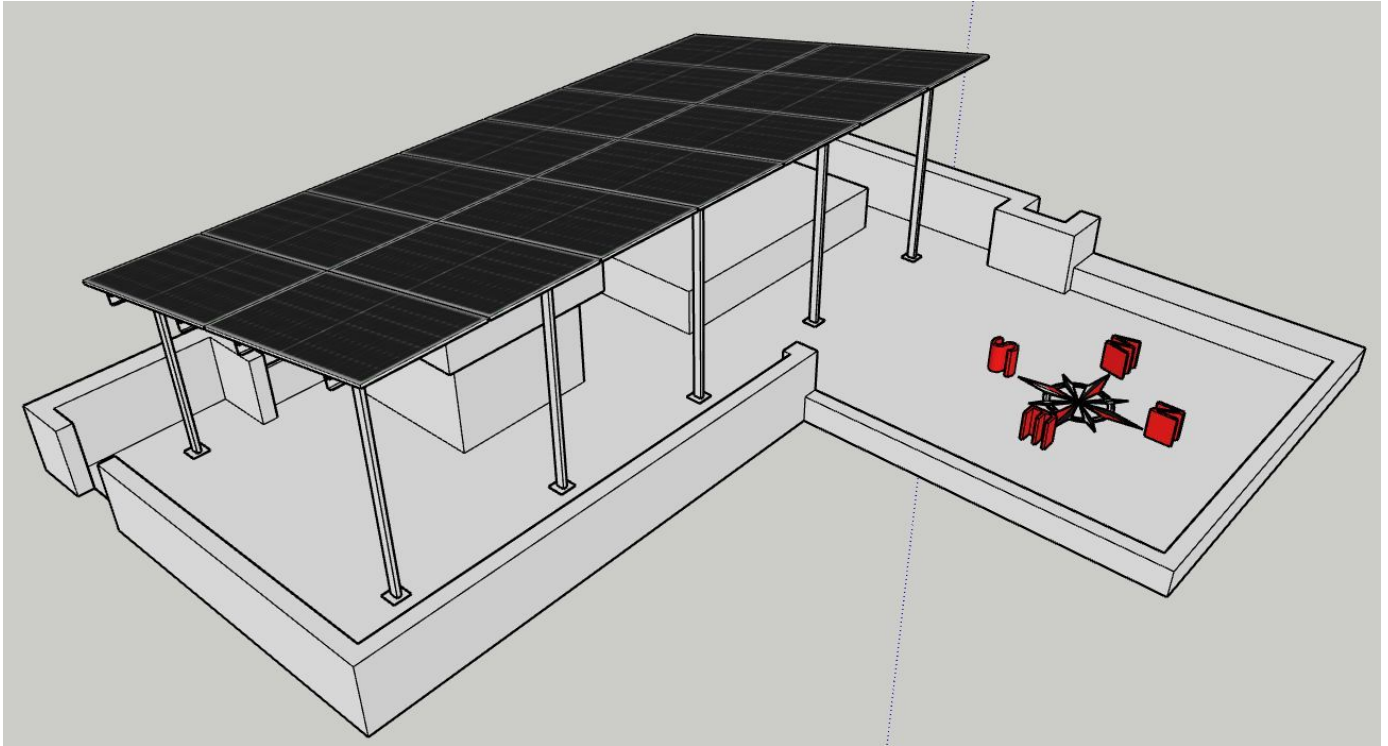


Option 1_Iso view 2

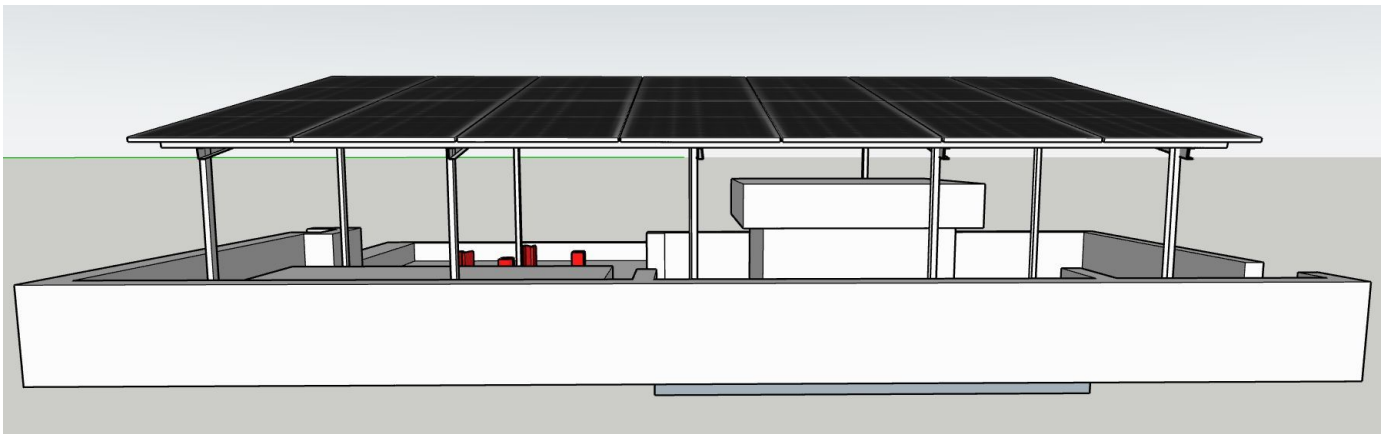


Option 1_front view

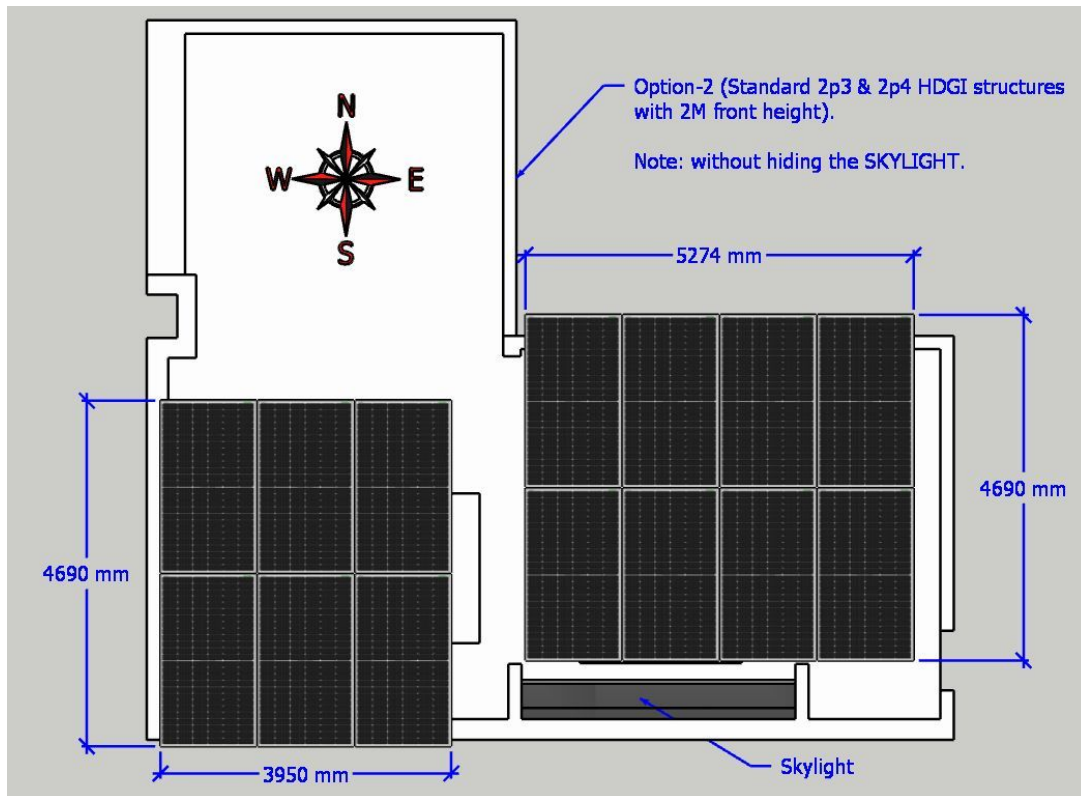


Option 2_Top view

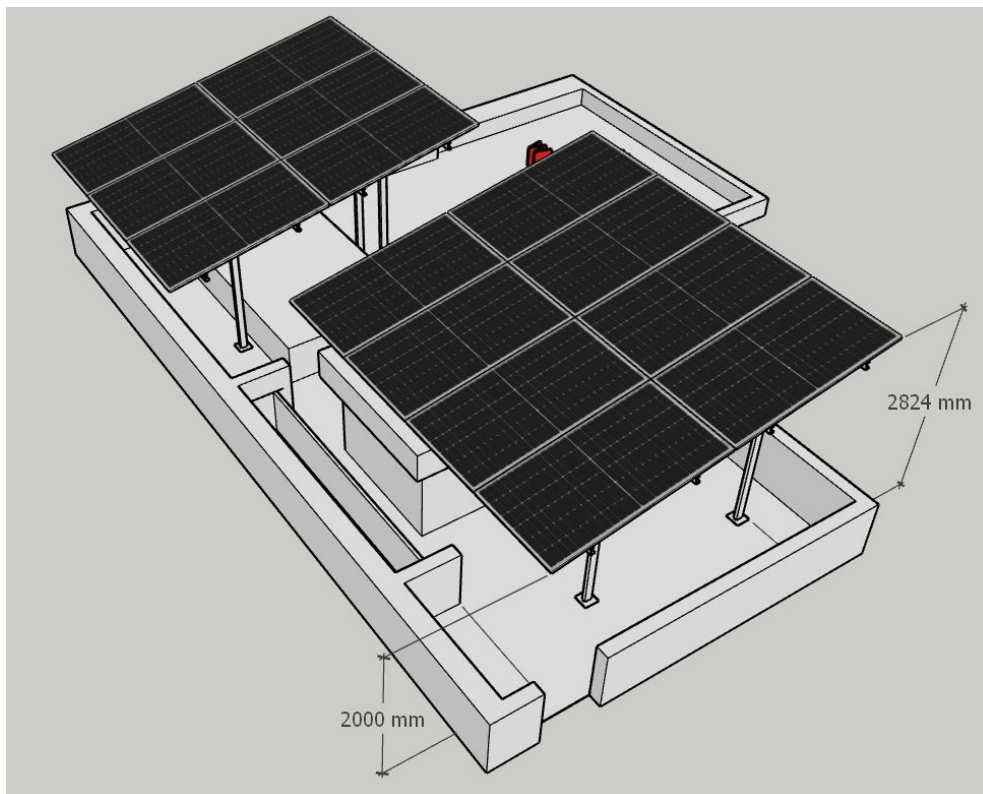

Option 2_Iso view1

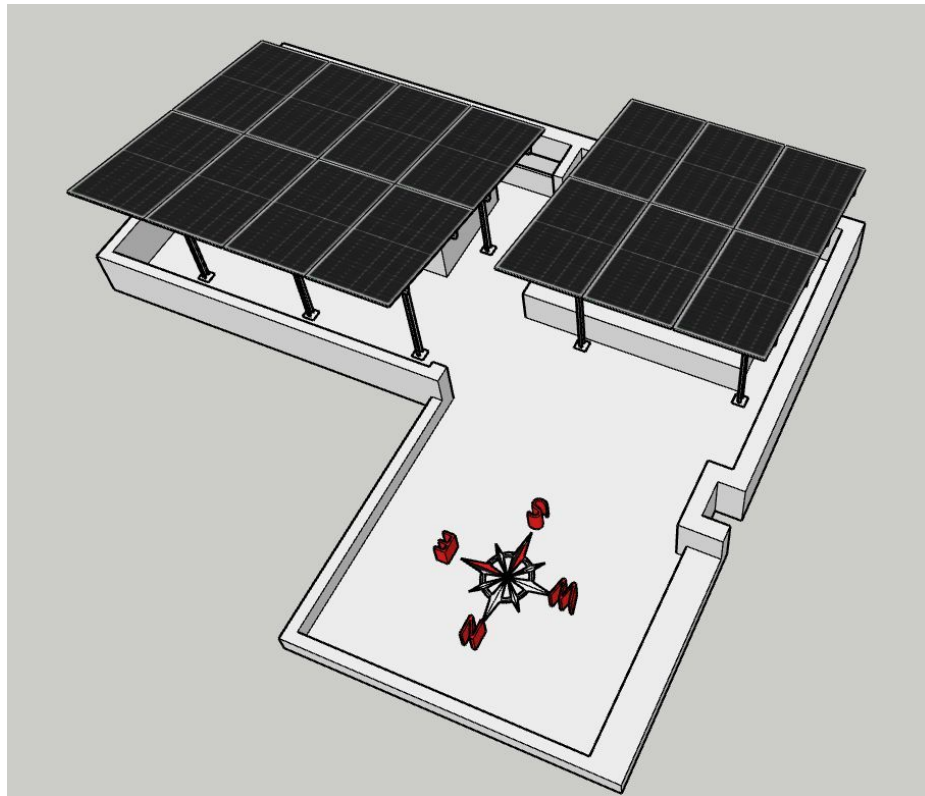

Option 2_Iso view 2

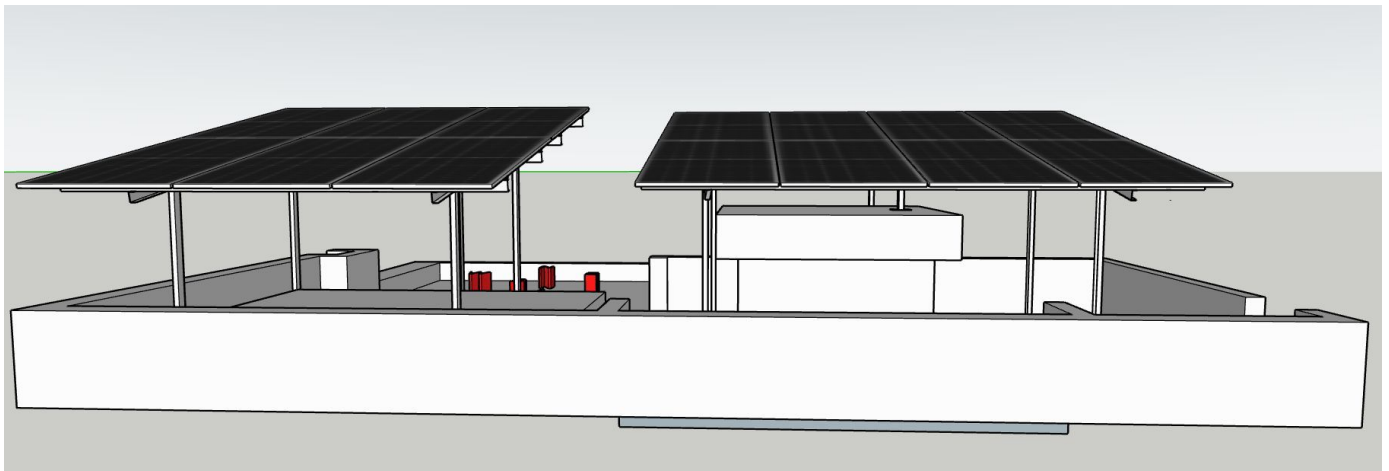

Option 2_Front view

Building Exterior



Proposed PV Area



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



staircase available in the 2nd floor to reach the roof top.



Materials storage area at the roof terrace.

Staircase Details



Inner staircase width: 800 mm



Upper terrace staircase width: 1000 mm

Cable Routing



The AC earthing cable, DC earthing cable and the LA earthing cable are running together horizontally over the parapet side wall till the electrical duct available at the west side of the terrace.



The DC cable (Red line) is coming downwards from the roof top, but the AC earthing cable (Pale green line) is moving upwards.



All the cables reaching the electrical duct are running vertically inside the duct on clamps till the ground level.



The earthing cables reaching the ground floor at the west side of the building via the duct has to cross the gap (1 feet under the soil) and then run over the wall, heading south-west corner.



The cables then heads east and run over the wall till reaching the next corner.



The cables continue to run till reaching the South-East corner of the building



After crossing the South-East corner the cables then move towards the North side wall.




The cables has to cross the wall to find the earth pits made on the ground.



The earthing cables can be terminated at the respective earth pits dug on the ground near the LT panel location.

Meter Box

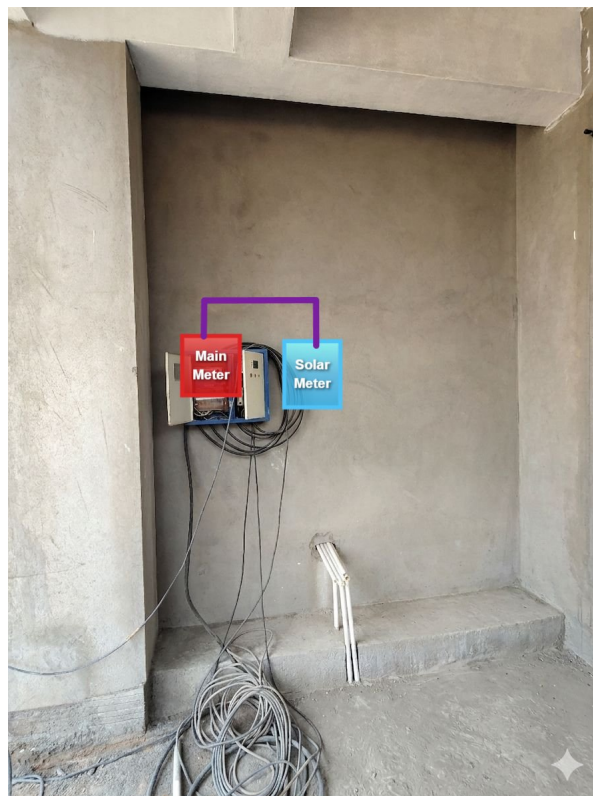

Proposed location for LT panel with Main meter and Solar meter



Existing temporary meter box d at the proposed LT meter location

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 9.8 kWp, Hybrid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	Providing UPS point near the Inverter and battery location.
3	Ensuring the Inverter-Battery room has adequate ventilation throughout the day.
4	Fabrication of a canopy/shield to protect the Inverter, AC and DC-DBs installed at the premises if necessary, in case of sideways drizzle.
5	Removing the floor tile for the convenient routing of the earthing cables (in conduit) crossing the west side tiled area- during the installation.

THANK YOU

Dear BISINEER PROJECT - MAHATHI SENTHIL,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
