

# Technical Site Visit Report

Prepared for: Aravinth Kumar\_Aashritha Honey Dell Layout\_3.1kWp\_String

## PROJECT INFORMATION

|                 |                                                                                                                                                    |
|-----------------|----------------------------------------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0205                                                                                                                                      |
| Project ID      | 0EAD4817                                                                                                                                           |
| Project Name    | Aravinth Kumar_Aashritha Honey Dell Layout_3.1kWp_String                                                                                           |
| Project Sector  | Residential                                                                                                                                        |
| Project Type    | With Subsidy                                                                                                                                       |
| Sales Lead      | HARIOM PATEL                                                                                                                                       |
| Site Address    | Villa 32, Aashritha Honey Dell Layout, Opposite to Celebrity Nature Habitat, Silkfarm road, Bidaraguppe, Sarjapur Attibele Road, Bengaluru 562107. |
| GPS Coordinates | 12.818133, 77.793015                                                                                                                               |
| Google Maps     | <a href="https://www.google.com/maps?q=12.818133,77.793015">https://www.google.com/maps?q=12.818133,77.793015</a>                                  |
| Visit Date      | 2026-09-15                                                                                                                                         |
| Visited By      | ABILASH N K                                                                                                                                        |
| Revision        | Rev 0                                                                                                                                              |

## CLIENT INFORMATION

|             |                |
|-------------|----------------|
| Client Name | Aravinth Kumar |
| Contact     | +91 9632916467 |

## PROJECT DETAILS

|                           |                                    |
|---------------------------|------------------------------------|
| Solar Rooftop System Type | On-Grid                            |
| System Capacity (kWp)     | 3.10                               |
| Sanction Load (kW)        | 3                                  |
| Module Make & Capacity    | Premier 620Wp Topcon Bi-Facial DCR |
| Module Length (mm)        | 2382                               |

|                         |                                     |
|-------------------------|-------------------------------------|
| Module Width (mm)       | 1133                                |
| Number of Panels        | 5                                   |
| Inverter Type           | String                              |
| Inverter Brand          | Deye: 3KW - 48V - LV - Single Phase |
| Number of Inverters     | 1                                   |
| Mounting Structure Type | RCC Flat Roof                       |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                                                                | Notes |
|---|----------------------------------------------------------------------------|---------------------------------------------------------------------------------------|-------|
| 1 | Can the delivery van/truck reach the material unloading point?             | Yes                                                                                   | -     |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | No                                                                                    | -     |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | The inverter, DCDB and ACDB can be mounted on the wall in the ground-floor car porch. | -     |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | No                                                                                    | -     |
| 5 | Did you discuss the location of the earth pits with the customer?          | Yes, discussed with the customer and finalised the location for earthing.             | -     |
| 6 | Where is the Internet Router located?                                      | Ground floor.                                                                         | -     |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | 3 bars                                                                                | -     |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                                                                   | -     |

### Roof Details

| # | Question                                                                             | Answer        | Notes |
|---|--------------------------------------------------------------------------------------|---------------|-------|
| 1 | What type of roof is present at the site?                                            | RCC Flat Roof | -     |
| 2 | Are there any obstructions on the roof that could affect the solar installation?     | No            | -     |
| 3 | What is the angle of the panels? (in degrees)                                        | 10            | -     |
| 4 | In case of sloped roof, what is the slope angle of the roof? (in degrees)            | N/A           | -     |
| 5 | On how many roofs at the site are we installing solar?                               | 1             | -     |
| 6 | If it is a Tiled roof, what is underneath the tiles?                                 | N/A           | -     |
| 7 | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled? | N/A           | -     |

| #  | Question                                                                                                 | Answer             | Notes                                                                                                      |
|----|----------------------------------------------------------------------------------------------------------|--------------------|------------------------------------------------------------------------------------------------------------|
| 8  | What type of mounting structure is planned?                                                              | Elevated           | <i>Elevated HDGI - 2m Front Leg (2 Rows, Portrait) with Drilling &amp; Only Base Plate Cement Covering</i> |
| 9  | What is the orientation of the solar panels?                                                             | ["South"]          | -                                                                                                          |
| 10 | How can the roof be accessed?                                                                            | Staircase          | -                                                                                                          |
| 11 | Is the building currently under construction?                                                            | No                 | -                                                                                                          |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | N/A                | -                                                                                                          |
| 13 | What is the height of the building and how many floors does it have?                                     | 8 meters. (G + 1 ) | -                                                                                                          |
| 14 | Is the site photo matching with the building description?                                                | Yes                | -                                                                                                          |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                 | -                                                                                                          |

### Residential / Electrical

| #  | Question                                                                                                | Answer                                                           | Notes                                                                                                                                            |
|----|---------------------------------------------------------------------------------------------------------|------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------|
| 1  | What type of energy meter is currently installed?                                                       | Phase: Single, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999) | -                                                                                                                                                |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes                                                              | -                                                                                                                                                |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes                                                              | -                                                                                                                                                |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible                                                          | -                                                                                                                                                |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No                                                               | <i>The existing RCC tank tower close to the planned installation is suitable for mounting the lightning arrester (LA).</i>                       |
| 6  | Is space available for CT within Energy meter panel?                                                    | N/A                                                              | -                                                                                                                                                |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | N/A                                                              | -                                                                                                                                                |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A                                                              | -                                                                                                                                                |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | No                                                               | -                                                                                                                                                |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | No                                                               | -                                                                                                                                                |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | Yes                                                              | <i>Space for digging the earth pit is available in the car porch floor of the building. The tiles have to be removed as per the requirement.</i> |
| 12 | In case of elevated structures, is an LA extension provided at the far end?                             | No                                                               | -                                                                                                                                                |
| 13 | In case of elevated structures, is it with or without grouting?                                         | With Grouting                                                    | -                                                                                                                                                |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                       | No                                                               | -                                                                                                                                                |
| 15 | Are there any safety risks associated with accessing the roof for installation?                         | No                                                               | -                                                                                                                                                |
| 16 | Is space present in rooftop to store the panels?                                                        | Vertically leaning against the wall                              | -                                                                                                                                                |



| #  | Question                                                                                          | Answer                       | Notes |
|----|---------------------------------------------------------------------------------------------------|------------------------------|-------|
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin. | N/A                          | -     |
| 18 | Is ventilation available in the battery location?                                                 | N/A                          | -     |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                       | Wall mounted.                | -     |
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).                         | length: 2000,<br>width: 1000 | -     |
| 21 | Provide the dimension for earth pits location (L x W of available space).                         | length: 3000,<br>width: 3000 | -     |
| 22 | Is LAN cable under customer scope?                                                                | Yes                          | -     |
| 23 | Is there any shadow that affects the solar installation?                                          | No                           | -     |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location?                  | N/A                          | -     |



## PHOTO DOCUMENTATION



### Cable Routing Legend

| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|   | Proposed PV Module Array |
|  | Main Meter Location      |
|  | Solar Meter              |
|  | Battery                  |
|  | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |
|  | LA Pit                   |
|  | LA                       |

### Site Layout - Top View

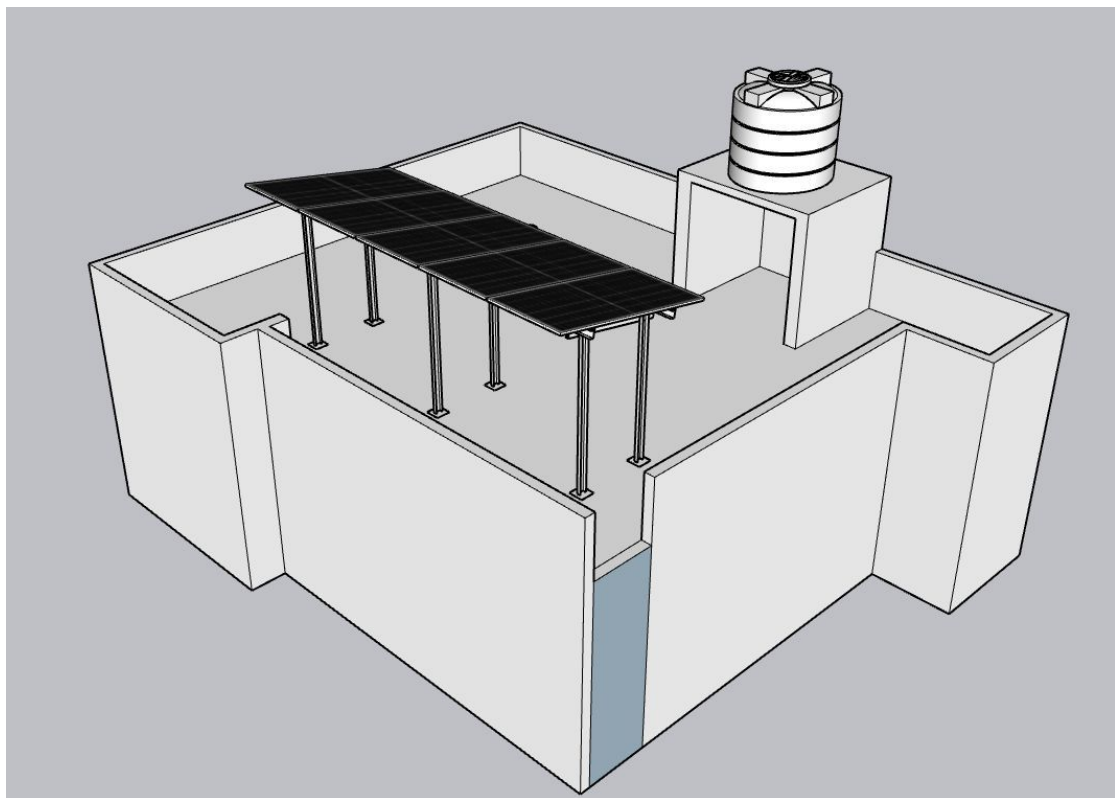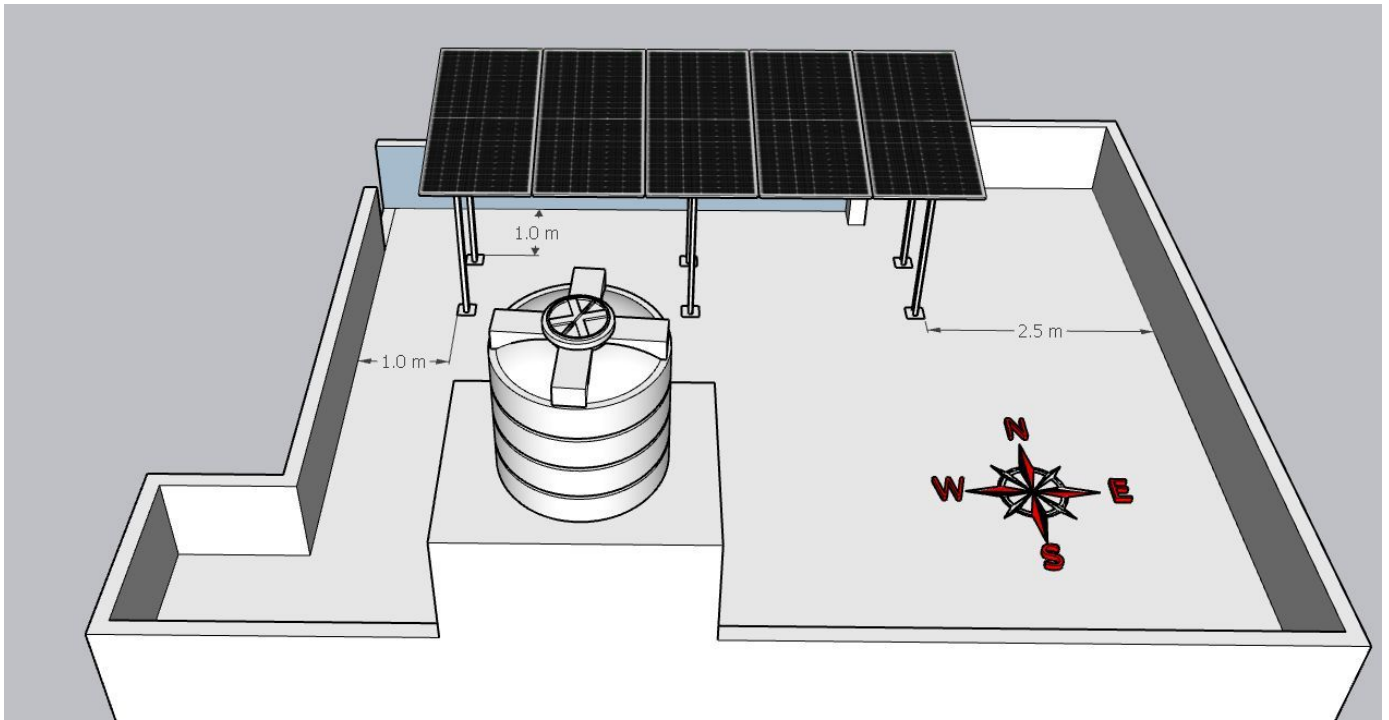

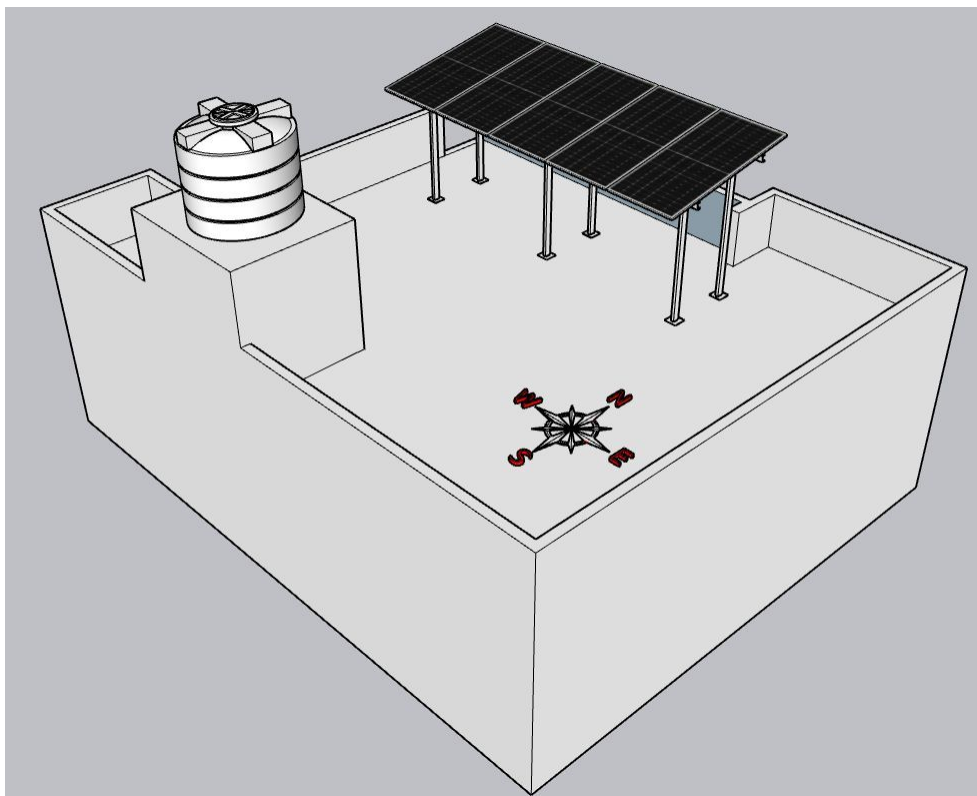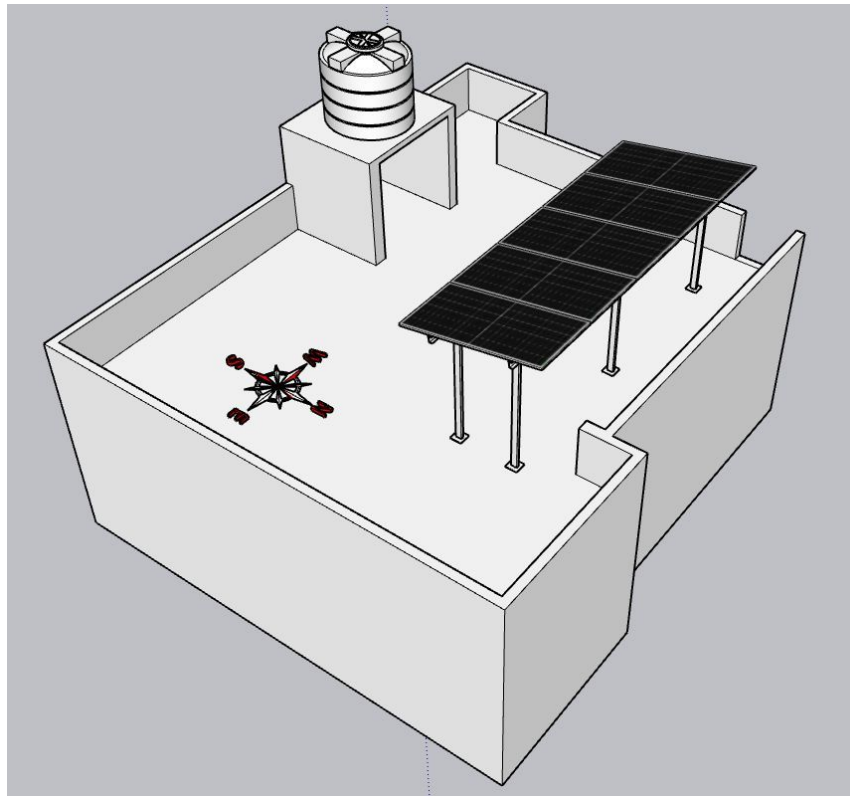

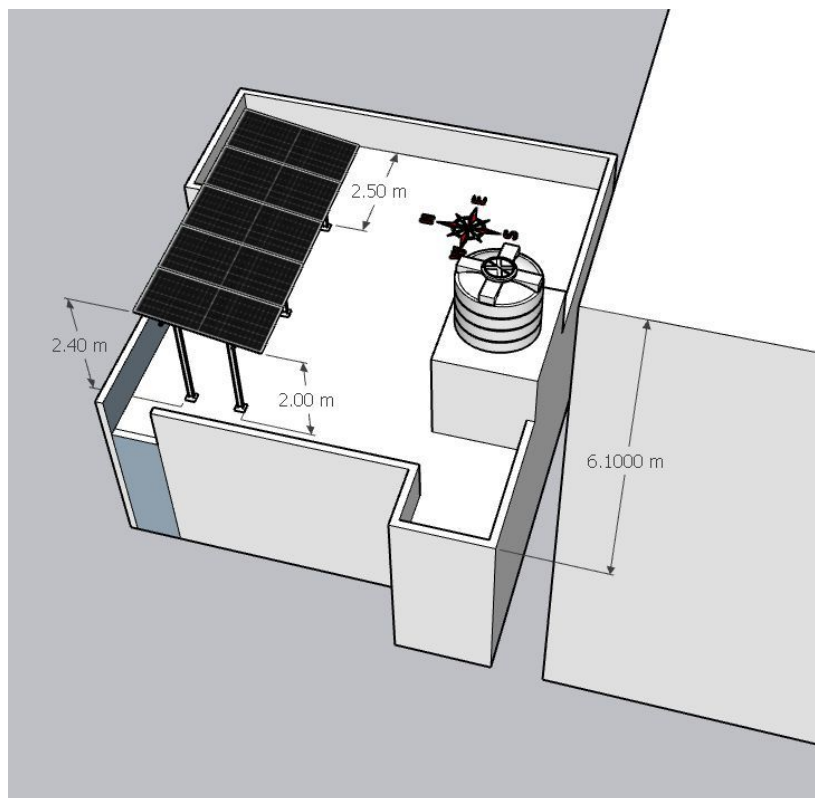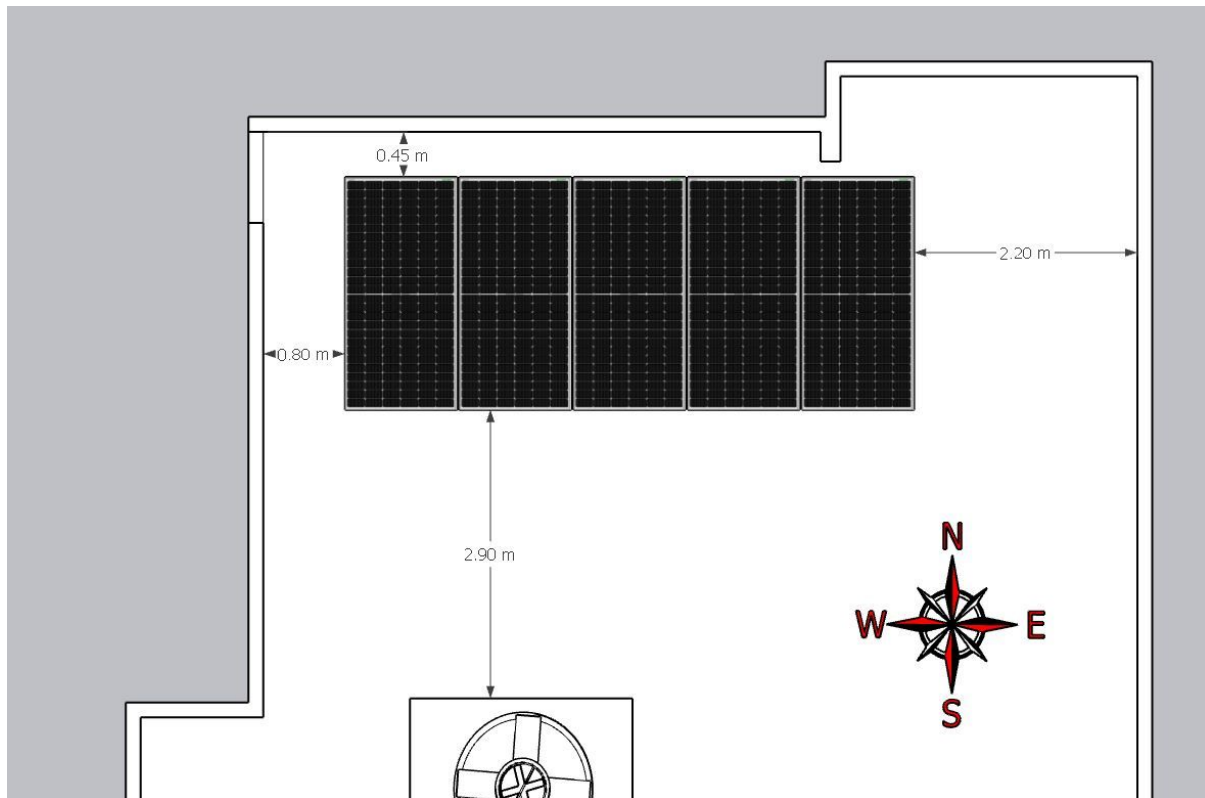

## Building Exterior



### Material Delivery Route



*Heavy materials such as PV modules can be shifted over the side wall of the building.*



*Light weight materials can be shifted to the terrace via the inner staircase.*



*The materials can follow the stairs until reaching the terrace.*




*The materials can follow the stairs until reaching the terrace.*



*The materials can follow the balcony stairs until reaching the terrace.*

## Staircase Details

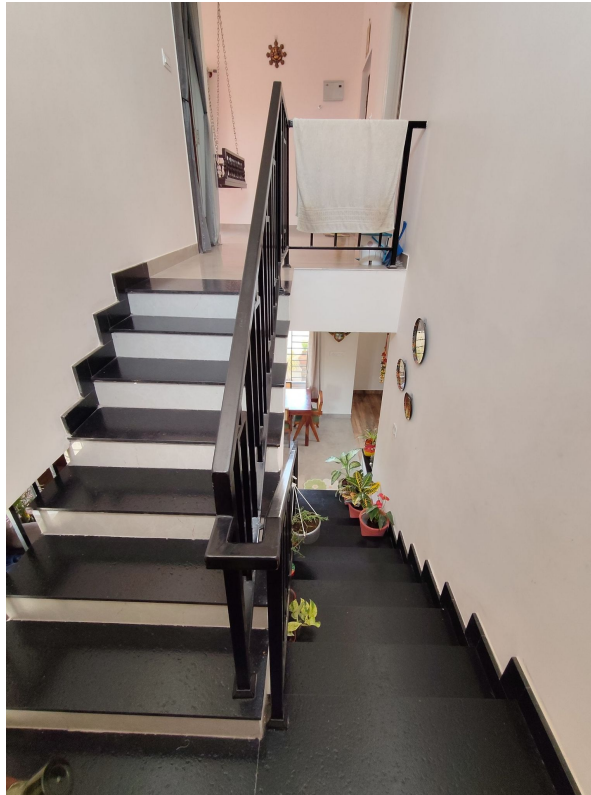

*Staircase width: 900 mm*

## Proposed PV Area




### Cable Routing










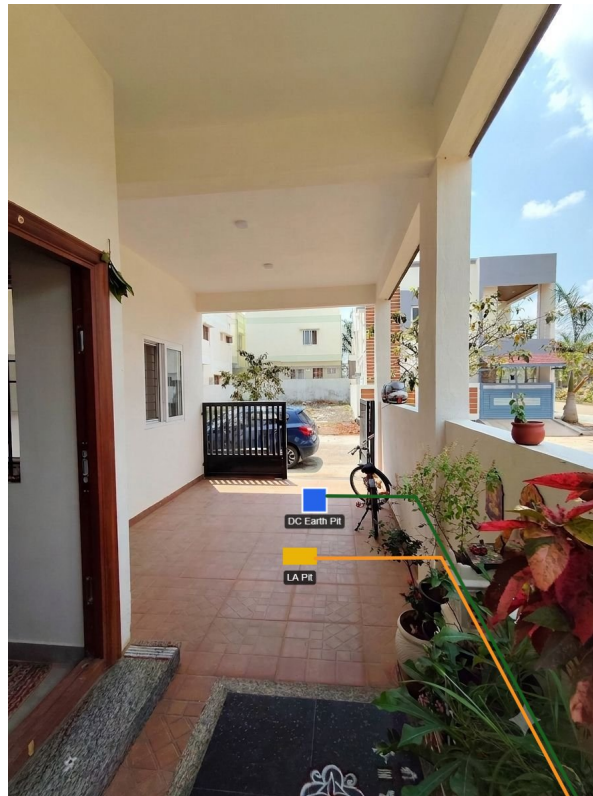

### Meter Box



## Shadow Analysis

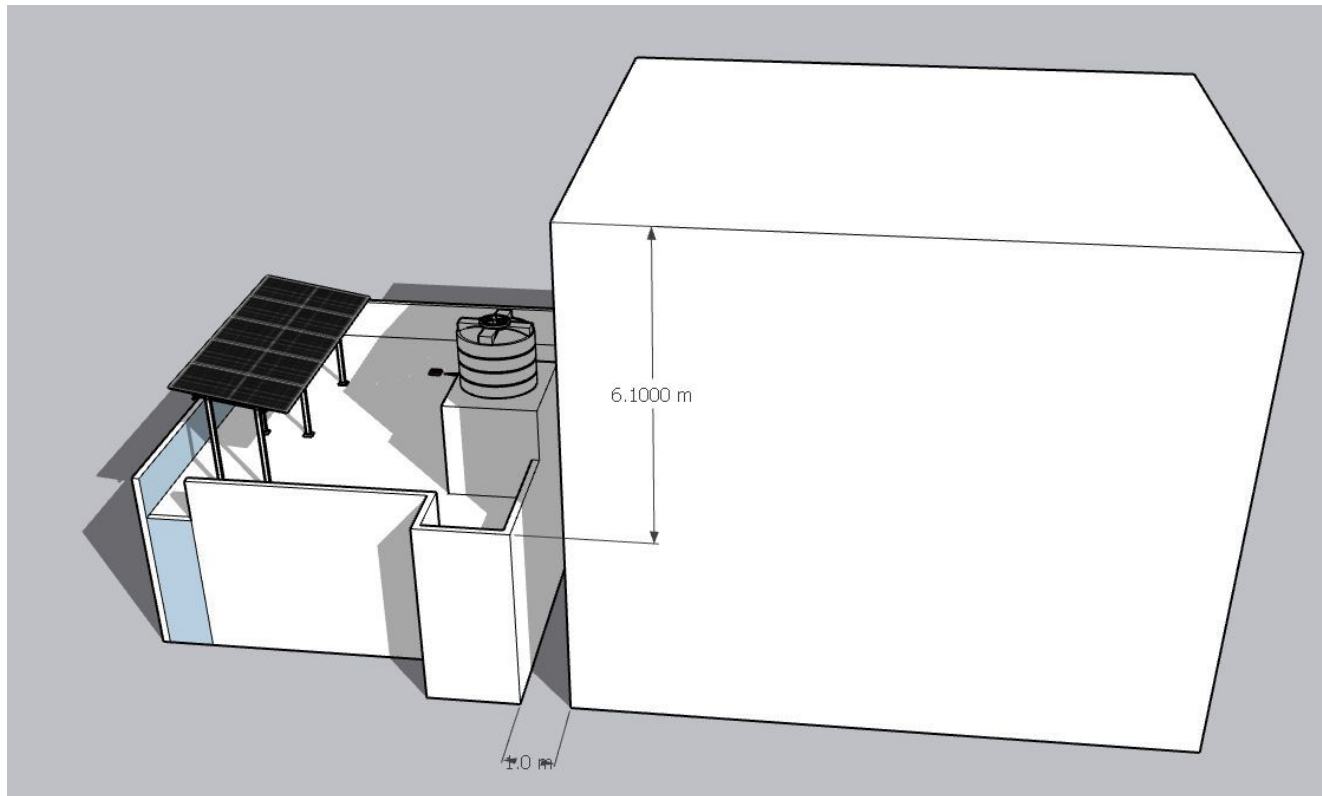

Shadow view (Nov - Jan at 3pm)

## OBSERVATIONS & RECOMMENDATIONS

### EcoSoch Scope

| # | Observation                                                                                   |
|---|-----------------------------------------------------------------------------------------------|
| 1 | The co-ordination and follow-up with BESCO regarding solar connectivity till commissioning.   |
| 2 | Installation and commissioning of 3.1 kWp On-Grid solar power plant at the proposed premises. |

### Customer Scope

| # | Observation                                                                                                                                                           |
|---|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1 | The co-ordination and follow-up with BESCO regarding solar connectivity till commissioning.                                                                           |
| 2 | The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution. |

## THANK YOU

Dear Aravinth Kumar,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
