

Technical Site Visit Report

Prepared for: MELVIN OSCAR DSOUZA_Dollars Colony Non Subsidy_10.98kWp_Hybrid - #406

PROJECT INFORMATION

Report Number	ESV-2026-0201
Project ID	1H9TACTB
Project Name	MELVIN OSCAR DSOUZA_Dollars Colony Non Subsidy_10.98kWp_Hybrid
Building Name	#406
Billing Name	MELVIN OSCAR DSOUZA
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju
Site Address	#406, 10th cross, Dollars Colony, RMV 2nd Stage, Bangalore 560094
GPS Coordinates	13.0409373, 77.5671811
Google Maps	https://www.google.com/maps?q=13.0409373,77.5671811
Visit Date	2026-09-05
Visited By	K Naveen
Revision	Rev 0

CLIENT INFORMATION

Client Name	MELVIN OSCAR DSOUZA
Contact	'+91 9945403645

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	10.98
Sanction Load (kW)	17

Module Make & Capacity	Premier TopCon Non- DCR Bifacial 610 Wp
Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	18
Inverter Type	Hybrid (String)
Inverter Brand	Deye 15 kW 3phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	3
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter,DCD B,ACDB,Battery will be installed near the car parking area.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the corridor which is near the main meter location area	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	2 bars	Customer Scope
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	<i>RCC Flat roof with laid of tiles</i>
2	Are there any obstructions on the roof that could affect the solar installation?	details: The Solar water heater and the existing solar panels are the obstructions that could affect the solar installaton.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	<i>HDGI Elevated</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	The Height of the building is G+2+headroom which is aproximately 12 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	N/A	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-

#	Question	Answer	Notes
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall Mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 360, width: 370	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1200, width: 2000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	Yes	<i>The existing tree shadow will cast on the panels but client will trim the branches</i>
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit

Material Delivery Route




This route (using lifting) will be followed to carry large items (like Panels).








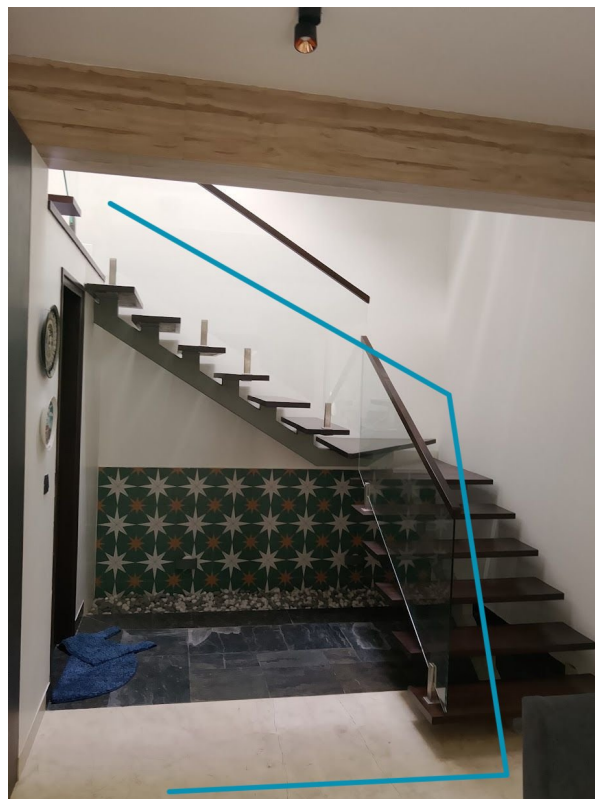

This route (using Staircase) will be followed to carry Small items.




Staircase Details

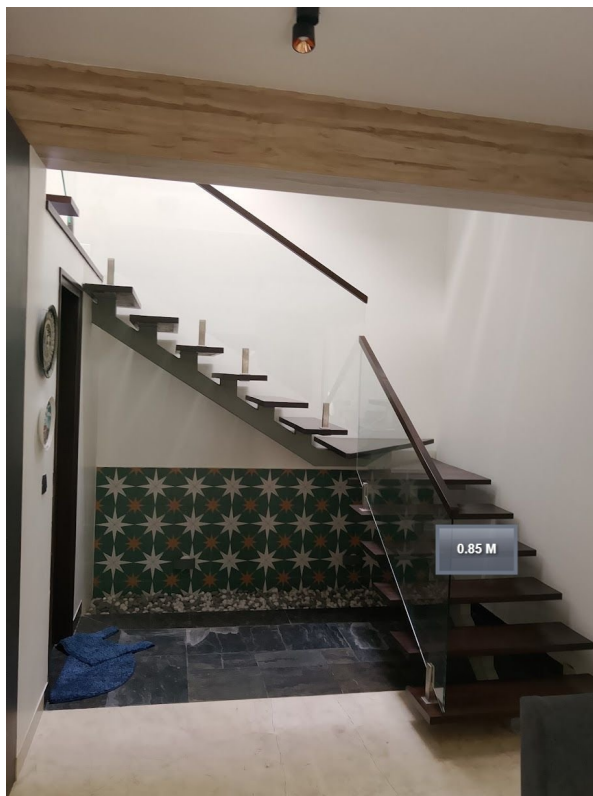


Meter Box



Material Storage

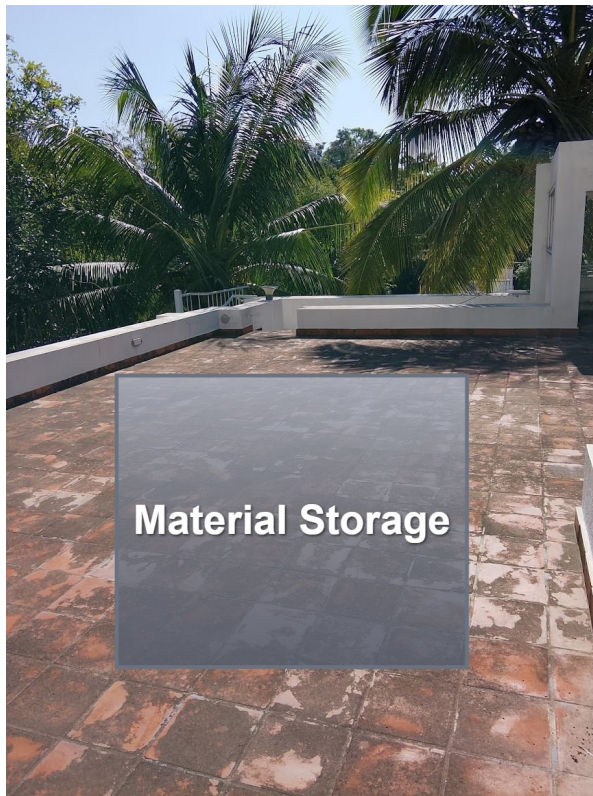

Proposed PV Area

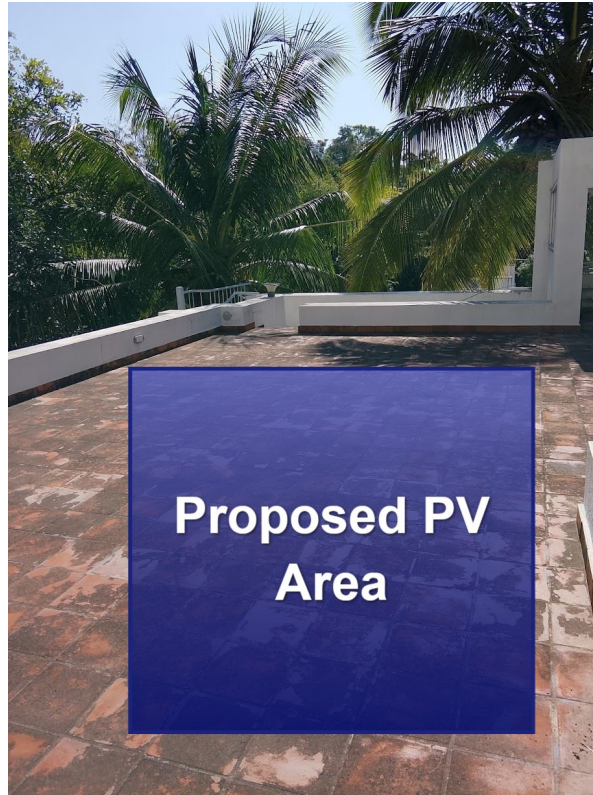



Cable Routing











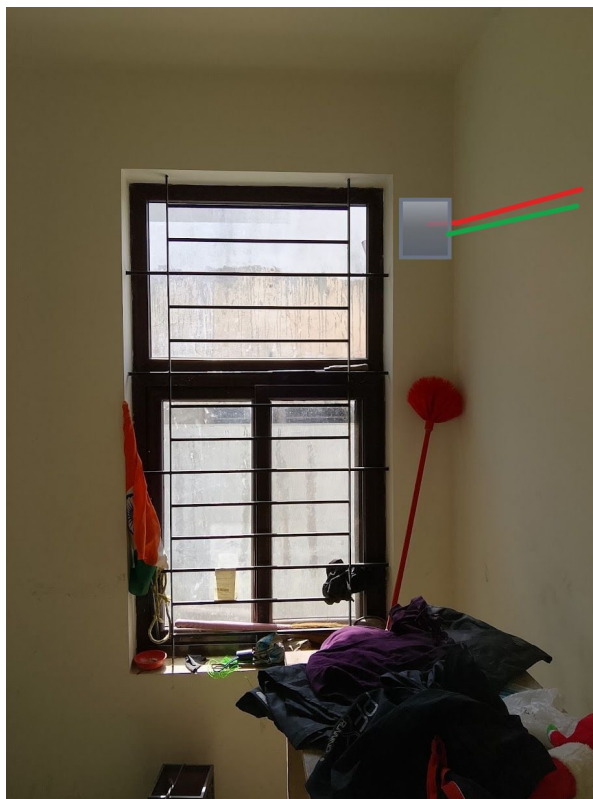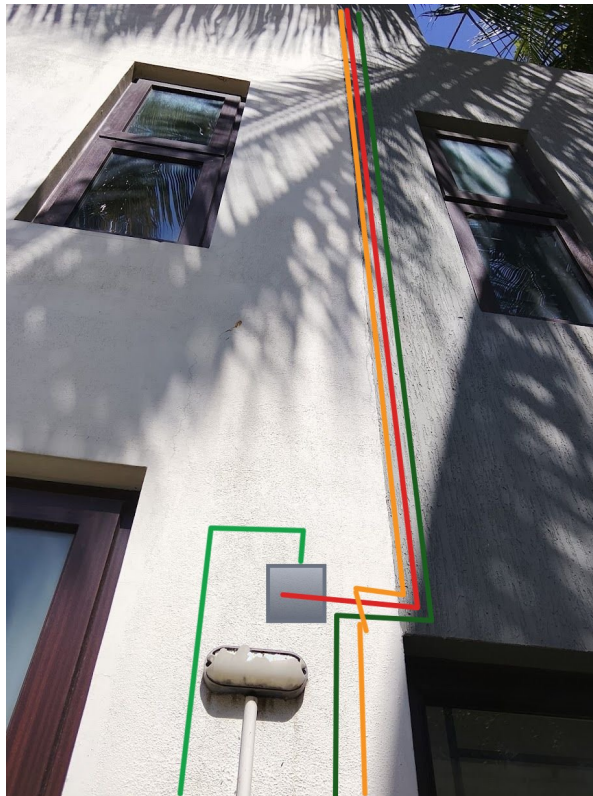

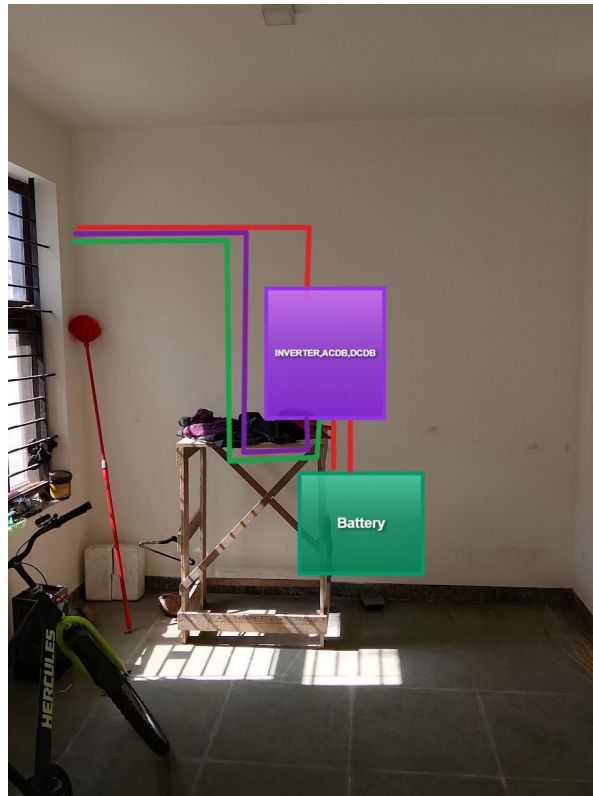



Equipment Location

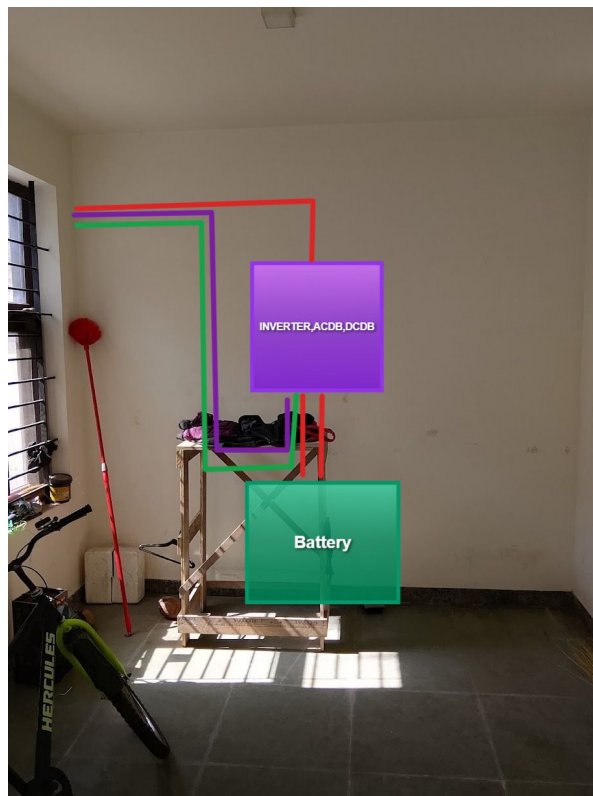



The out put Ac cable has to be terminated near the main power supply


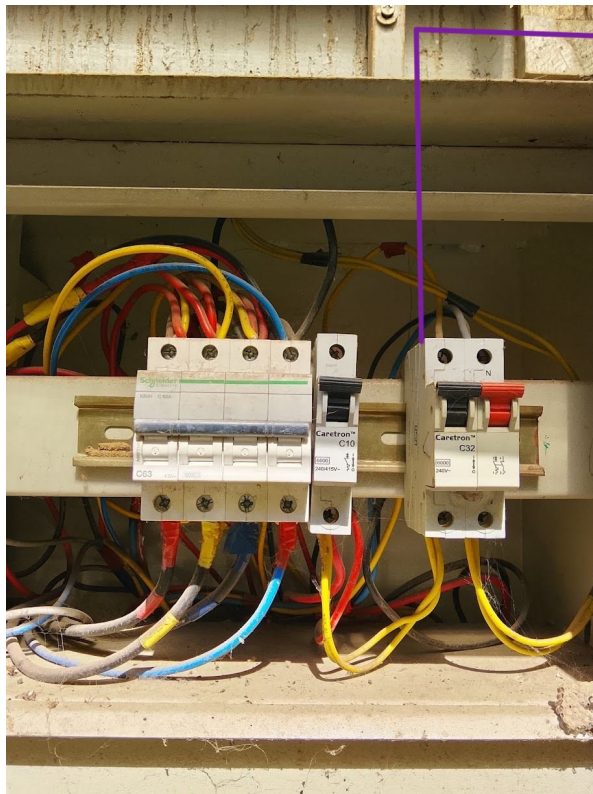



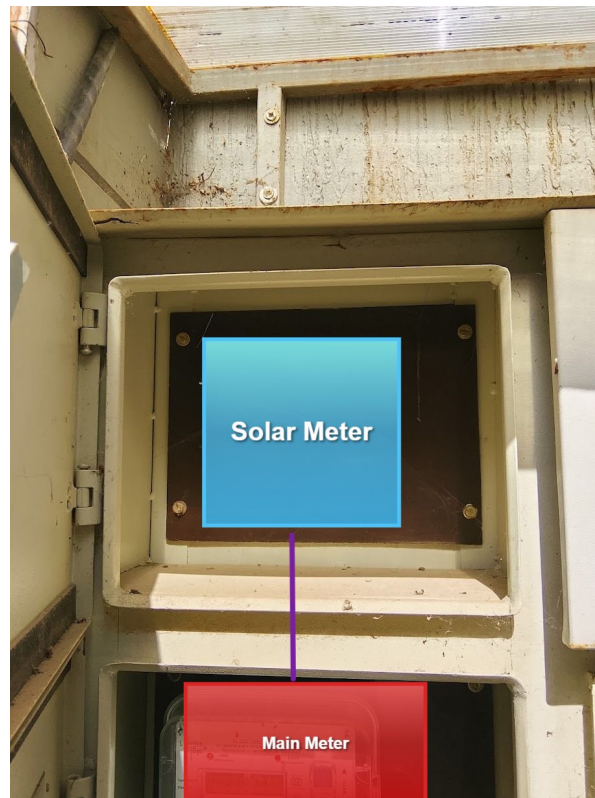



Earth Pit Location



Site Layout - Top View

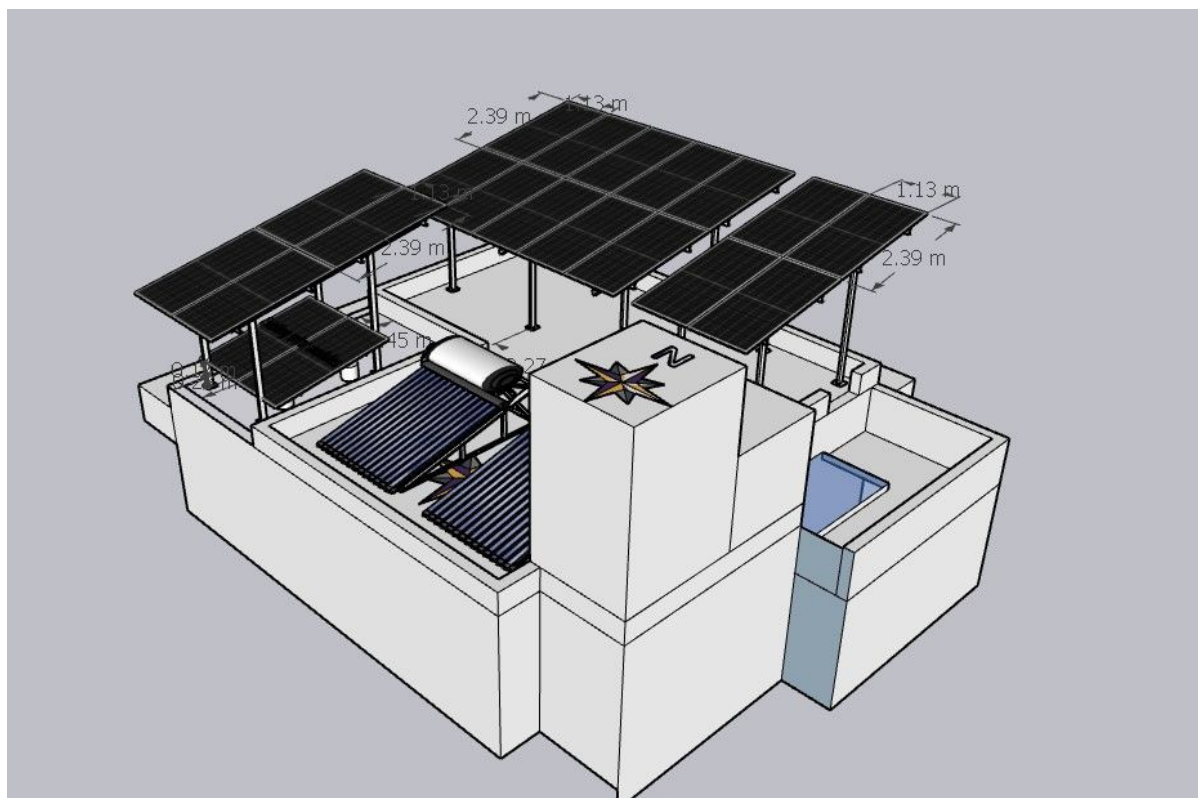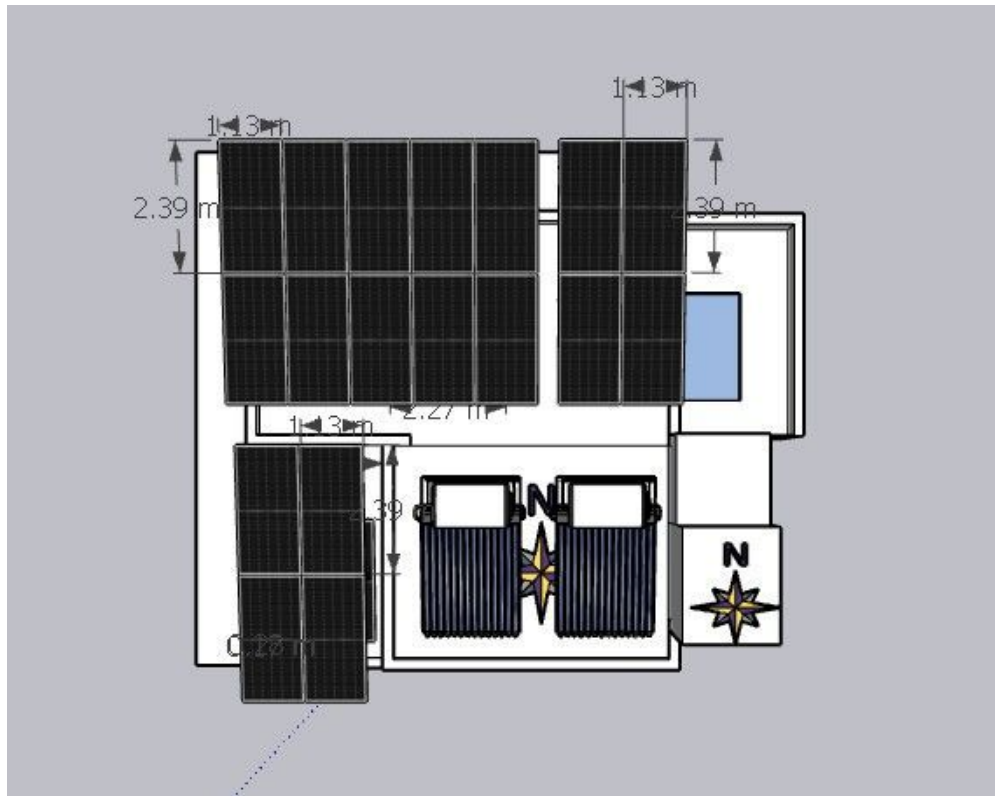

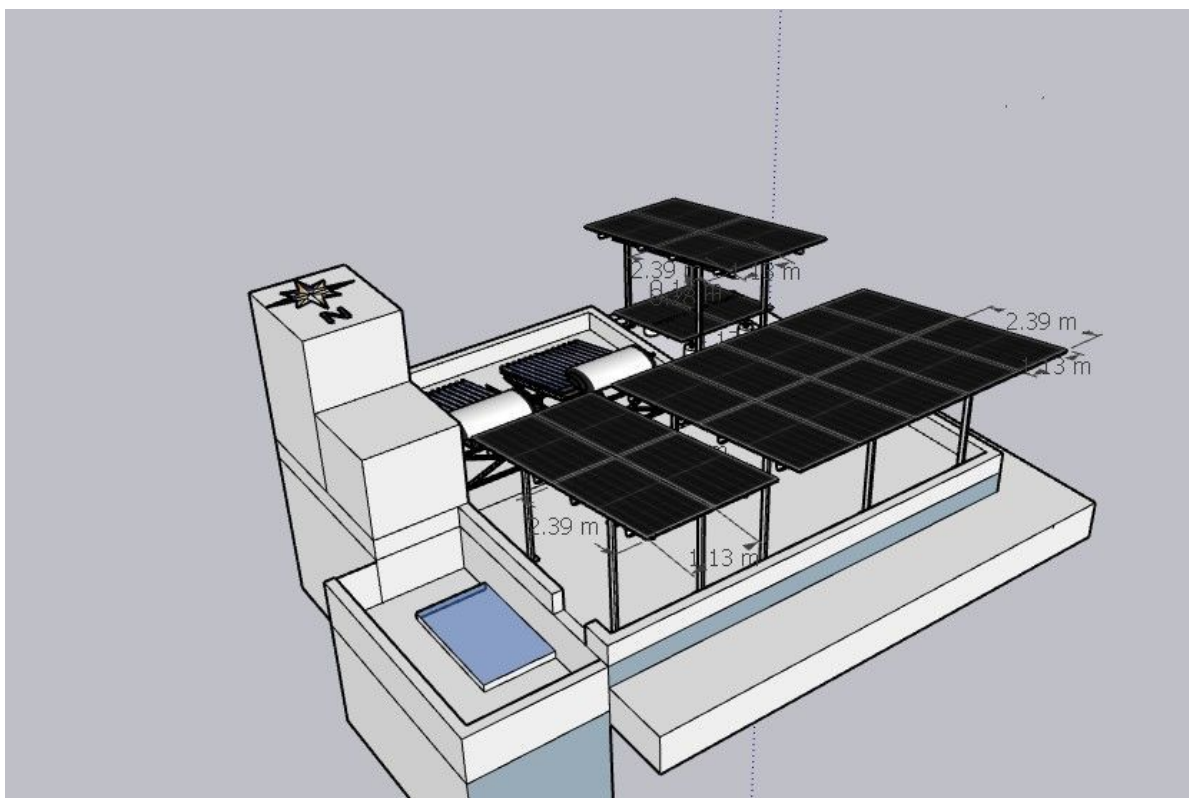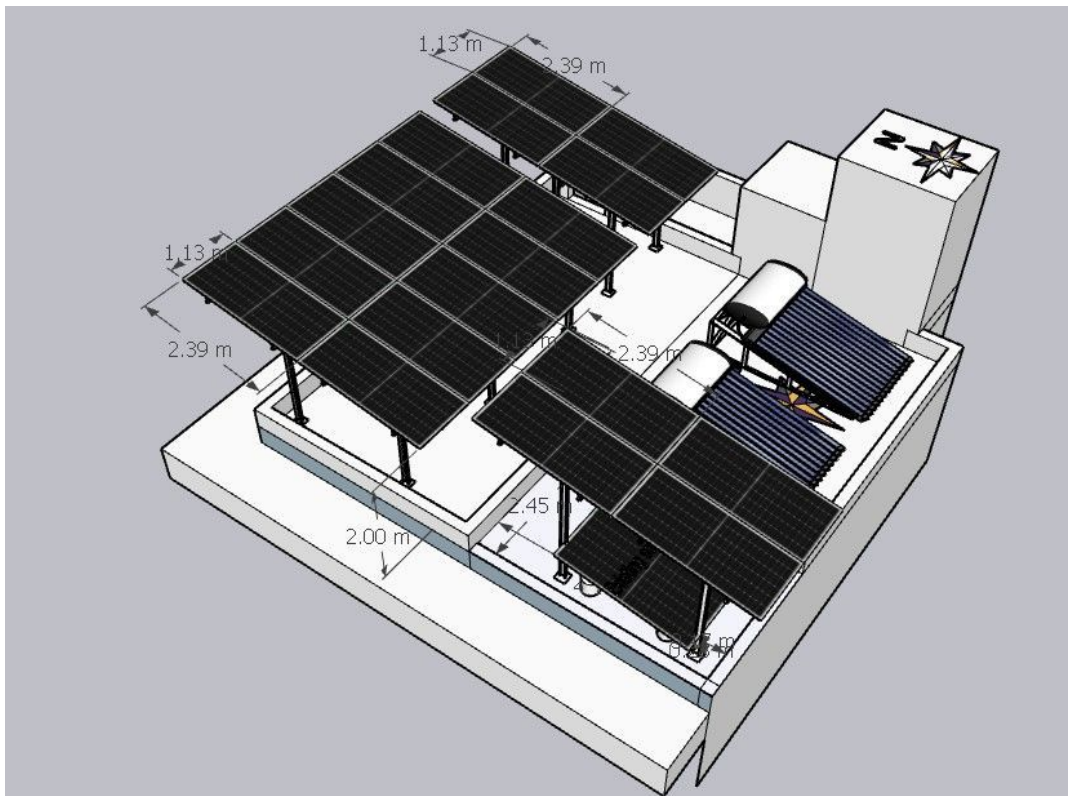

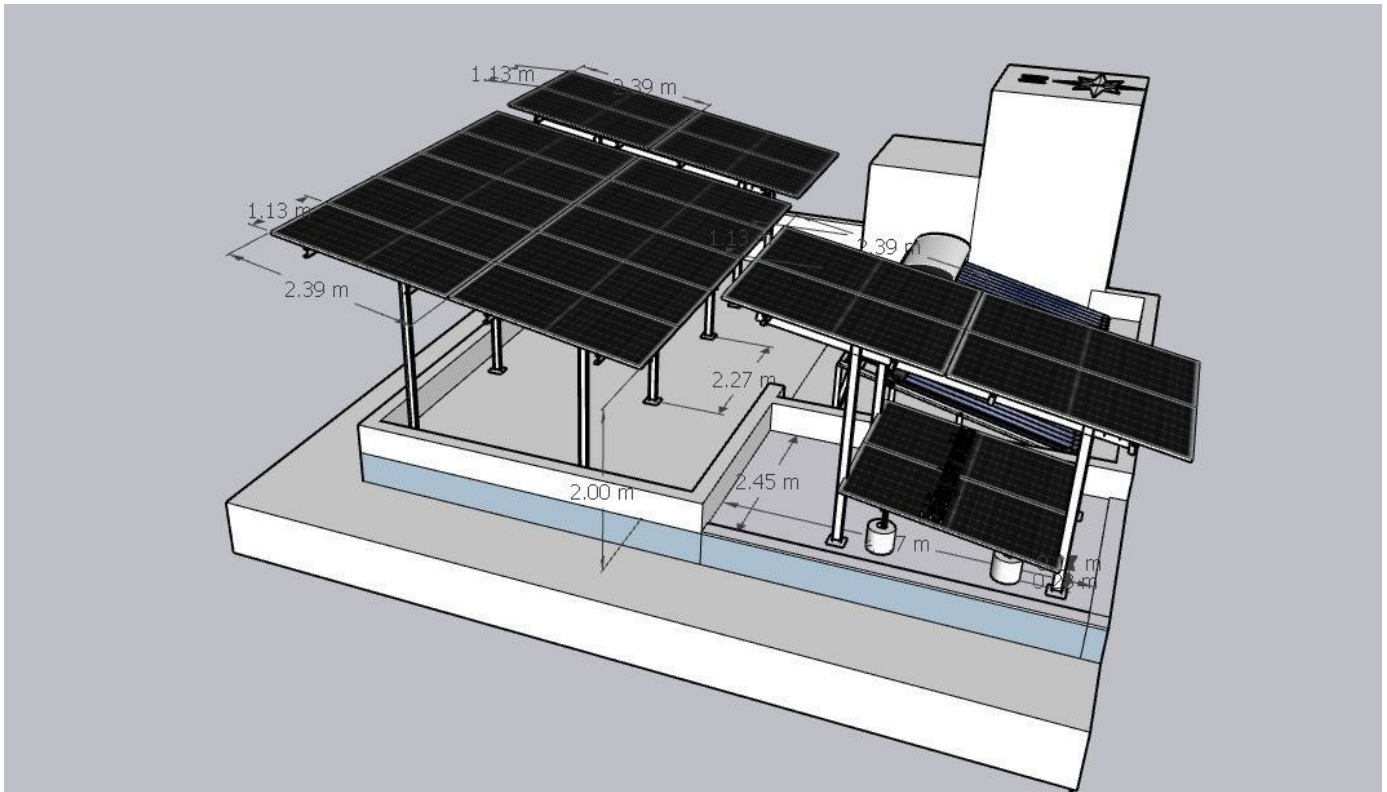

The existing solar Modules will be removed before proceeding the installtionis under customer scope

Shadow Analysis



Client has to trim the tree branches so that we can avoid the shadow

OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	UPS Point is under customer scope.
3	As per the customer concern only the panel Layout, earthing,cable routing has been considered.
4	For reducing the shadow to cut the tree branches is under customer scope.
5	Existing solar panels has been removed is under customer scope.

THANK YOU

Dear MELVIN OSCAR DSOUZA,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
