

## Technical Site Visit Report

Prepared for: Vivek M\_Skanda Spirit of One\_4.92kWp\_Microinverter (IQ Series)-Villa 37 - Villa 37

### PROJECT INFORMATION

|                 |                                                                                                                   |
|-----------------|-------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0179                                                                                                     |
| Project ID      | 0E1F2883                                                                                                          |
| Project Name    | Vivek M_Skanda Spirit of One_4.92kWp_Microinverter (IQ Series)-Villa 37                                           |
| Building Name   | Villa 37                                                                                                          |
| Project Sector  | Residential                                                                                                       |
| Project Type    | With Subsidy                                                                                                      |
| Sales Lead      | Gautam                                                                                                            |
| Site Address    | Villa 37, Skanda Spirit of One, Survey No 35,36, Hobli, Balagere, Varthur, Bengaluru, Karnataka 560087            |
| GPS Coordinates | 12.933135, 77.728271                                                                                              |
| Google Maps     | <a href="https://www.google.com/maps?q=12.933135,77.728271">https://www.google.com/maps?q=12.933135,77.728271</a> |
| Visit Date      | 2026-07-29                                                                                                        |
| Visited By      | ABILASH N K                                                                                                       |
| Revision        | Rev 2                                                                                                             |

### CLIENT INFORMATION

|             |            |
|-------------|------------|
| Client Name | Vivek M    |
| Contact     | 8105717868 |

### PROJECT DETAILS

|                           |                                   |
|---------------------------|-----------------------------------|
| Solar Rooftop System Type | On-Grid                           |
| System Capacity (kWp)     | 4.92                              |
| Sanction Load (kW)        | 5                                 |
| Module Make & Capacity    | Adani DCR Topcon bifacial, 615 Wp |

|                         |               |
|-------------------------|---------------|
| Module Length (mm)      | 2382          |
| Module Width (mm)       | 1133          |
| Number of Panels        | 8             |
| Inverter Type           | Micro         |
| Inverter Brand          | Enphase IQ8P  |
| Number of Inverters     | 8             |
| Mounting Structure Type | RCC Flat Roof |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                                                                                                                                                          | Notes |
|---|----------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------|
| 1 | Can the delivery van/truck reach the material unloading point?             | Yes                                                                                                                                                                             | -     |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | No                                                                                                                                                                              | -     |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | The Enphase accessories box, inbuilt with a solar meter provision can be installed near the existing main meter box located at the car porch on the front side of the building. | -     |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | No                                                                                                                                                                              | -     |
| 5 | Did you discuss the location of the earth pits with the customer?          | Yes, discussed with the customer and finalised the location for earthing.                                                                                                       | -     |
| 6 | Where is the Internet Router located?                                      | 2nd floor                                                                                                                                                                       | -     |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | 3 bars                                                                                                                                                                          | -     |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                                                                                                                                                             | -     |

### Roof Details

| # | Question                                                                         | Answer        | Notes |
|---|----------------------------------------------------------------------------------|---------------|-------|
| 1 | What type of roof is present at the site?                                        | RCC Flat Roof | -     |
| 2 | Are there any obstructions on the roof that could affect the solar installation? | No            | -     |
| 3 | What is the angle of the panels? (in degrees)                                    | 10            | -     |
| 4 | In case of sloped roof, what is the slope angle of the roof? (in degrees)        | N/A           | -     |

| #  | Question                                                                                                 | Answer                        | Notes                                                                                                                                              |
|----|----------------------------------------------------------------------------------------------------------|-------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------|
| 5  | On how many roofs at the site are we installing solar?                                                   | 1                             | -                                                                                                                                                  |
| 6  | If it is a Tiled roof, what is underneath the tiles?                                                     | N/A                           | -                                                                                                                                                  |
| 7  | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?                     | N/A                           | -                                                                                                                                                  |
| 8  | What type of mounting structure is planned?                                                              | Ballast                       | <i>Aluminium ballast with a 600 mm front height has to be considered for the structure.</i>                                                        |
| 9  | What is the orientation of the solar panels?                                                             | ["South"]                     | -                                                                                                                                                  |
| 10 | How can the roof be accessed?                                                                            | Staircase                     | <i>One can access the terrace floor via the inner staircase. But the roof proposed for installation can be accessed with the help of a ladder.</i> |
| 11 | Is the building currently under construction?                                                            | No                            | -                                                                                                                                                  |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | N/A                           | -                                                                                                                                                  |
| 13 | What is the height of the building and how many floors does it have?                                     | 12 Metres. (G + 2 + headroom) | -                                                                                                                                                  |
| 14 | Is the site photo matching with the building description?                                                | Yes                           | -                                                                                                                                                  |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                            | -                                                                                                                                                  |

## Residential / Electrical

| #  | Question                                                                                                | Answer        | Notes                                                                                                                                               |
|----|---------------------------------------------------------------------------------------------------------|---------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|
| 1  | What type of energy meter is currently installed?                                                       | No Meter      | -                                                                                                                                                   |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes           | <i>A metal three-phase meter cubicle is available at the site for the main meter. But the customer is awaiting the meter connection from BESCO.</i> |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes           | -                                                                                                                                                   |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible       | -                                                                                                                                                   |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No            | <i>A base support provision for the lightning arrester extension has to be provided on the rooftop.</i>                                             |
| 6  | Is space available for CT within Energy meter panel?                                                    | N/A           | -                                                                                                                                                   |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | Less than 50m | -                                                                                                                                                   |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A           | -                                                                                                                                                   |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | No            | -                                                                                                                                                   |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | No            | <i>An Enphase accessories box with a built-in solar meter fixing provision has to be provided.</i>                                                  |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | Yes           | <i>Space for digging the earth pit is available in front of the building at the</i>                                                                 |



| #  | Question                                                                                          | Answer                                                                                                      | Notes               |
|----|---------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------|---------------------|
|    |                                                                                                   |                                                                                                             | <i>garden area.</i> |
| 12 | In case of elevated structures, is an LA extension provided at the far end?                       | N/A                                                                                                         | -                   |
| 13 | In case of elevated structures, is it with or without grouting?                                   | N/A                                                                                                         | -                   |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                 | No                                                                                                          | -                   |
| 15 | Are there any safety risks associated with accessing the roof for installation?                   | No                                                                                                          | -                   |
| 16 | Is space present in rooftop to store the panels?                                                  | Vertically leaning against the wall                                                                         | -                   |
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin. | N/A                                                                                                         | -                   |
| 18 | Is ventilation available in the battery location?                                                 | N/A                                                                                                         | -                   |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                       | An Enphase accessories box with a built-in solar meter fixing provision has to be provided as wall mounted. | -                   |
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).                         | length: 2000, width: 2000                                                                                   | -                   |
| 21 | Provide the dimension for earth pits location (L x W of available space).                         | length: 3000, width: 1000                                                                                   | -                   |
| 22 | Is LAN cable under customer scope?                                                                | Yes                                                                                                         | -                   |
| 23 | Is there any shadow that affects the solar installation?                                          | No                                                                                                          | -                   |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location?                  | N/A                                                                                                         | -                   |



## PHOTO DOCUMENTATION

### Cable Routing Legend



| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|  | Proposed PV Module Array |
|  | Main Meter Location      |
|  | Solar Meter              |
|  | Battery                  |
|  | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |



## Site Layout - Top View

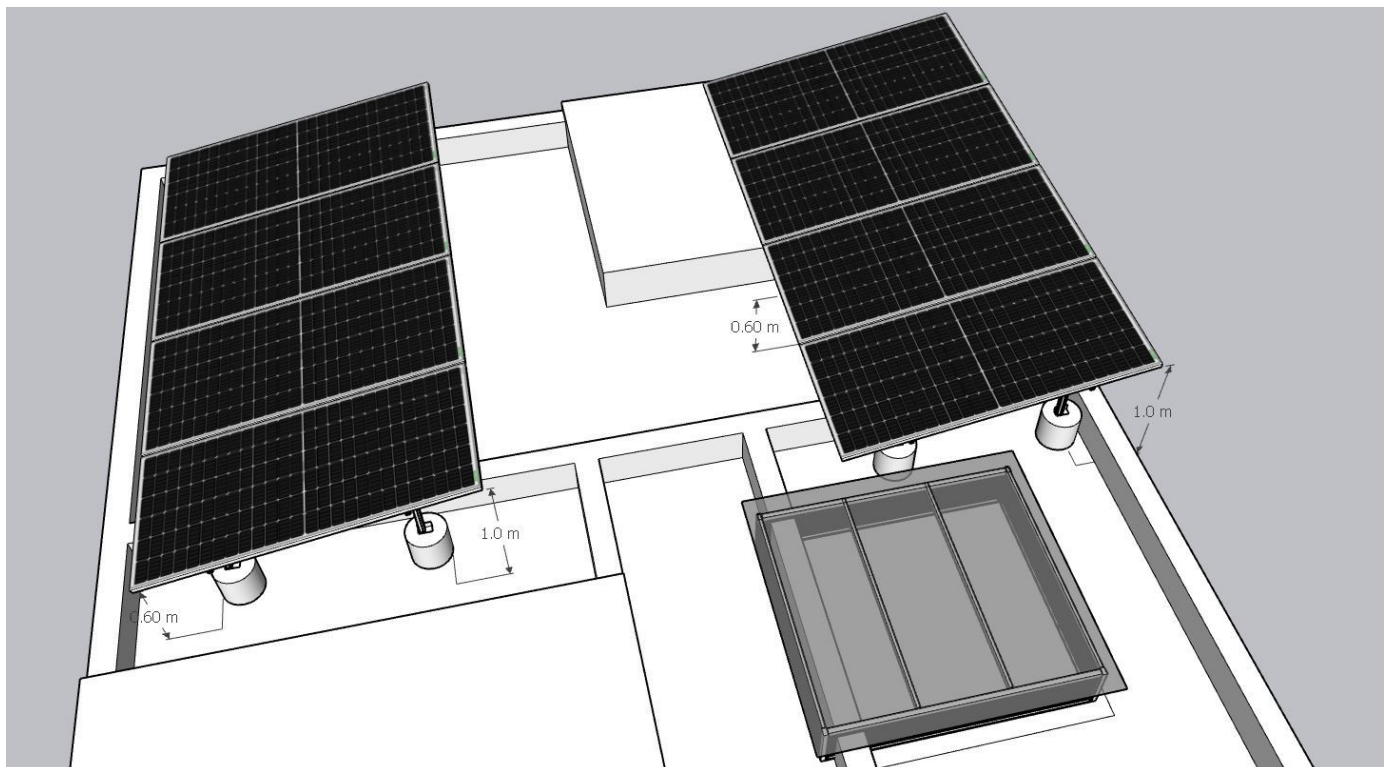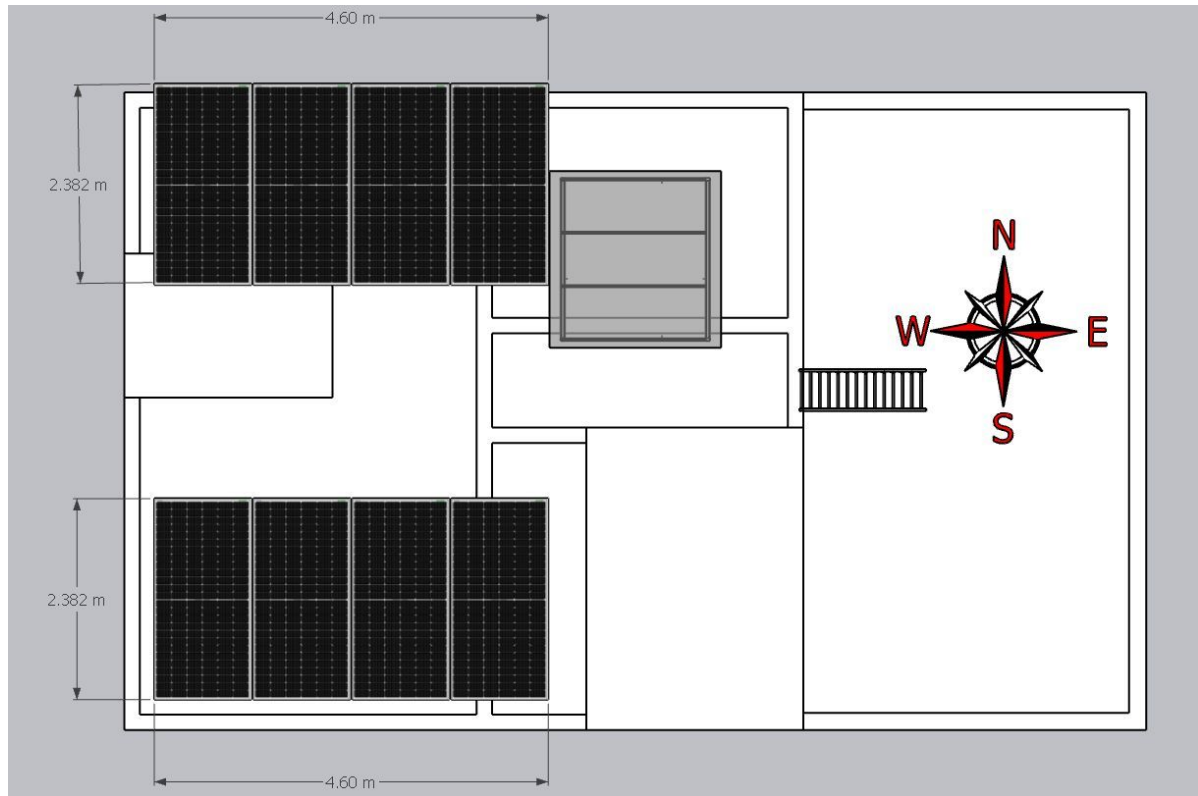

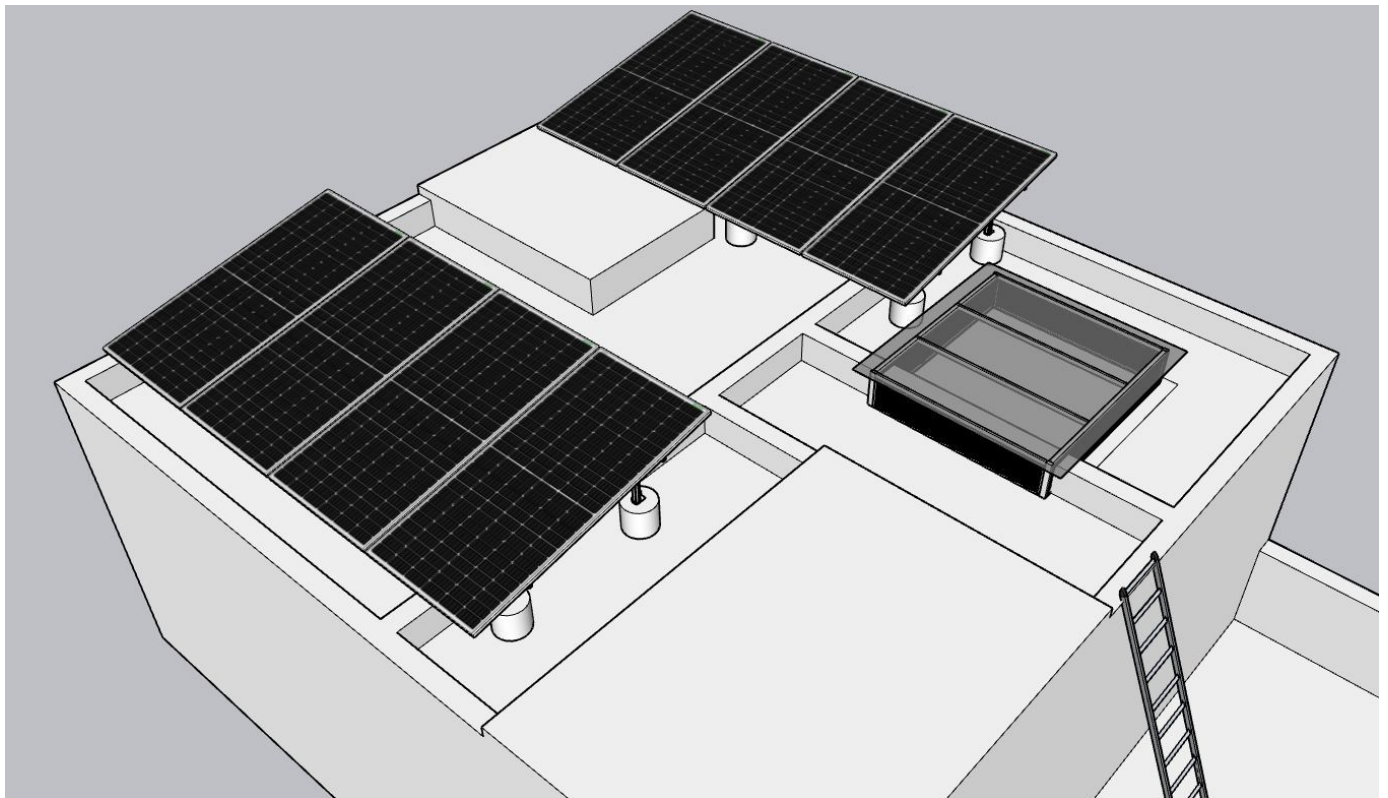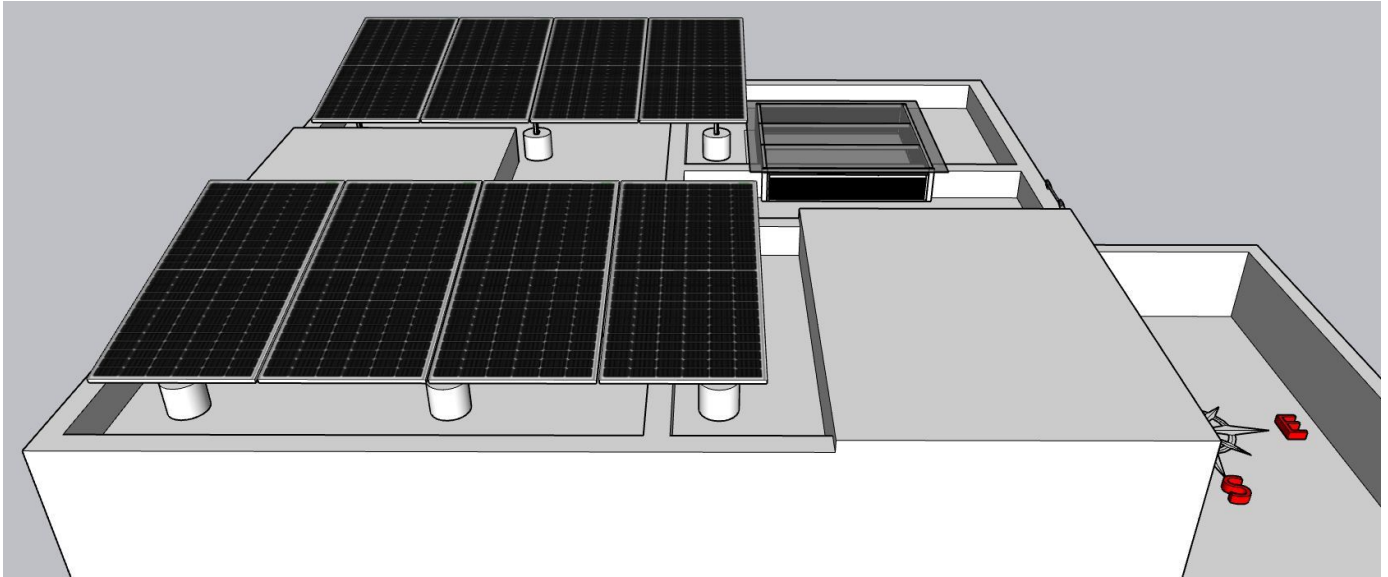



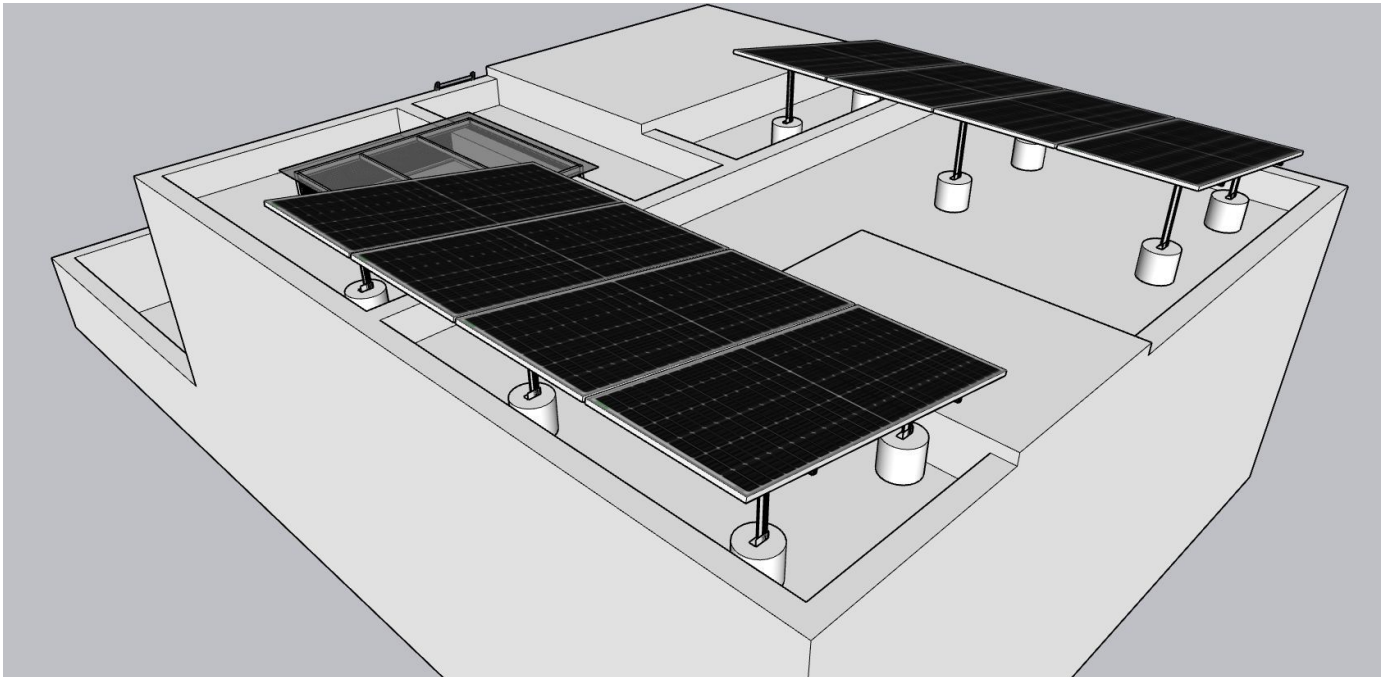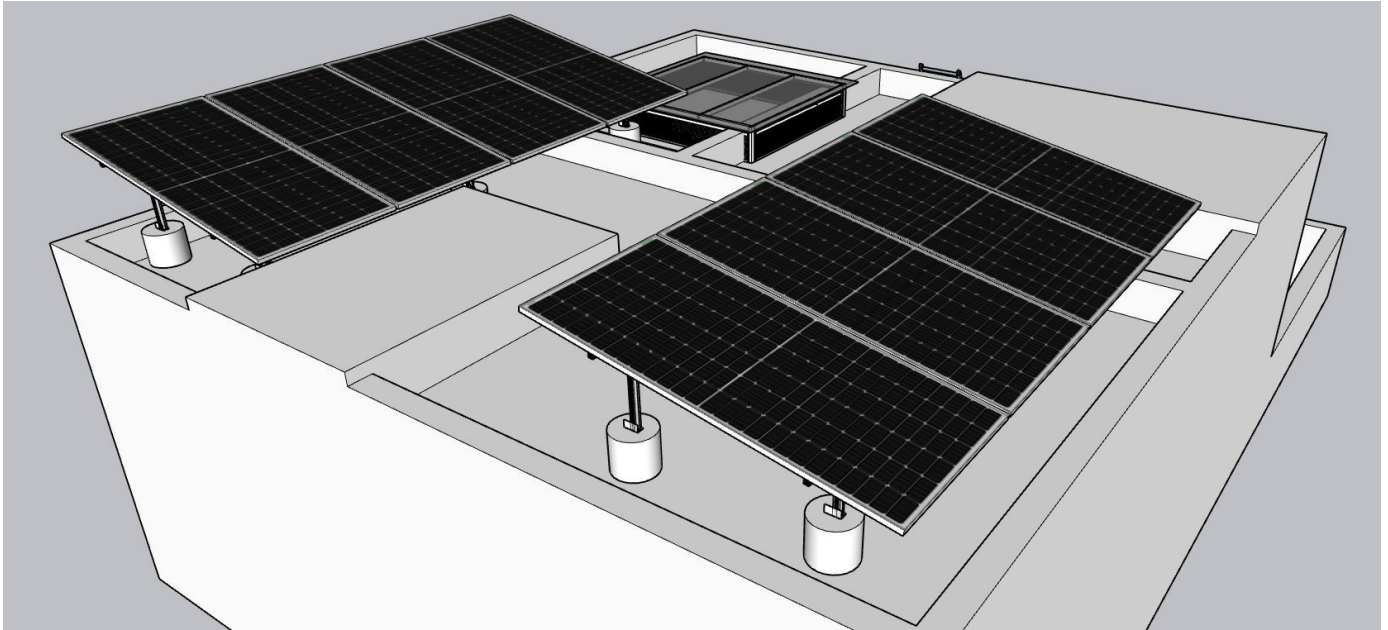

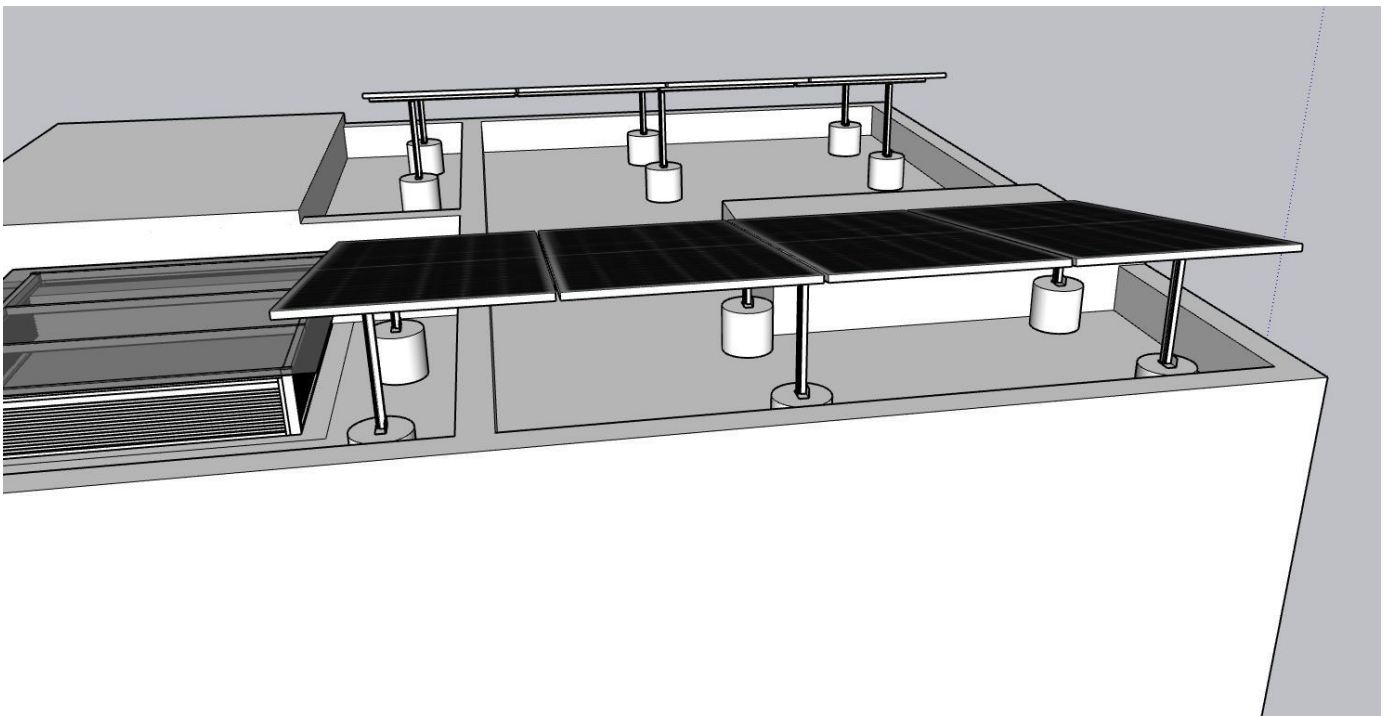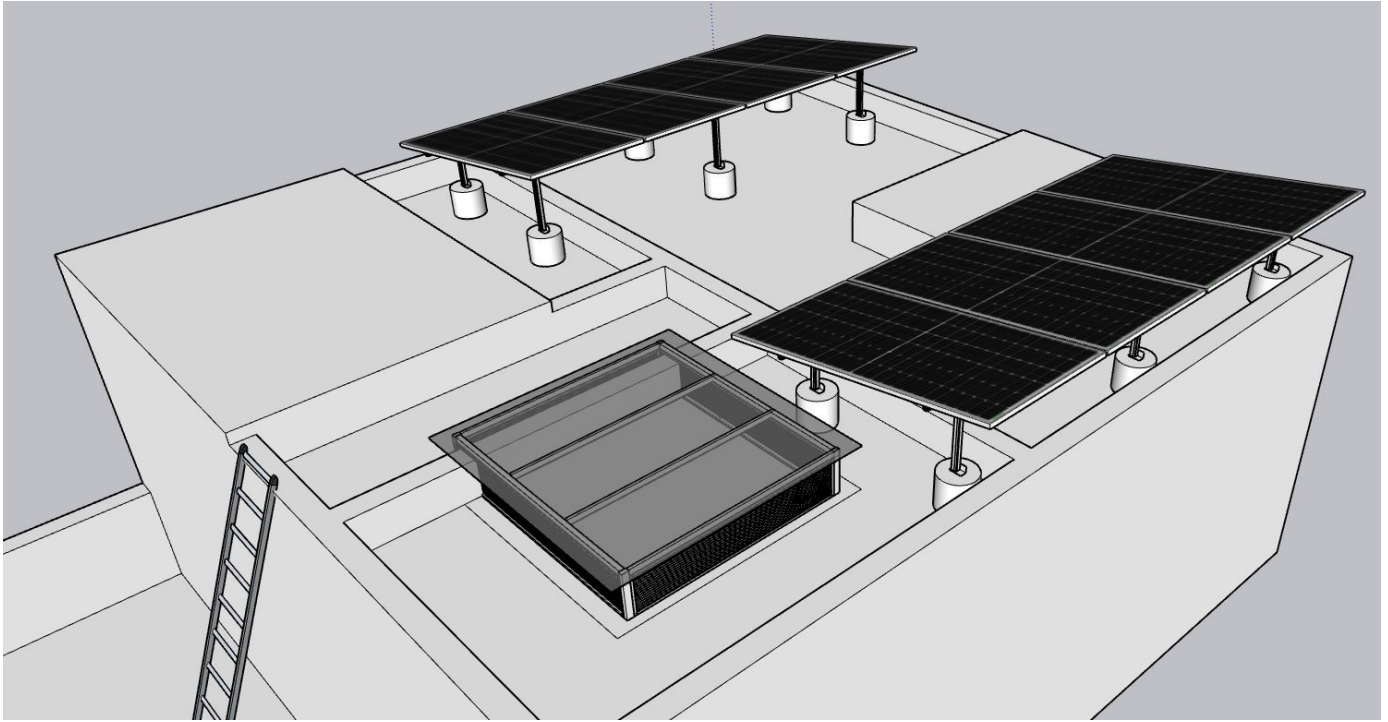

## Building Exterior





### Material Delivery Route



*The materials can be shifted to the terrace via two options available at the site. Heavy materials such as PV modules can be shifted over the side wall of the building.*



*Light weight materials can be shifted to the terrace via the inner staircase.*



*The materials can follow the stairs until reaching the 2nd floor terrace.*



*The materials are reaching the 2nd floor.*



*The materials are shifting outwards to the balcony area on the 2nd floor. The materials can be stacked here before shifting to the upper terrace.*




## Staircase Details




*Staircase width: 1000 mm*

## Proposed PV Area

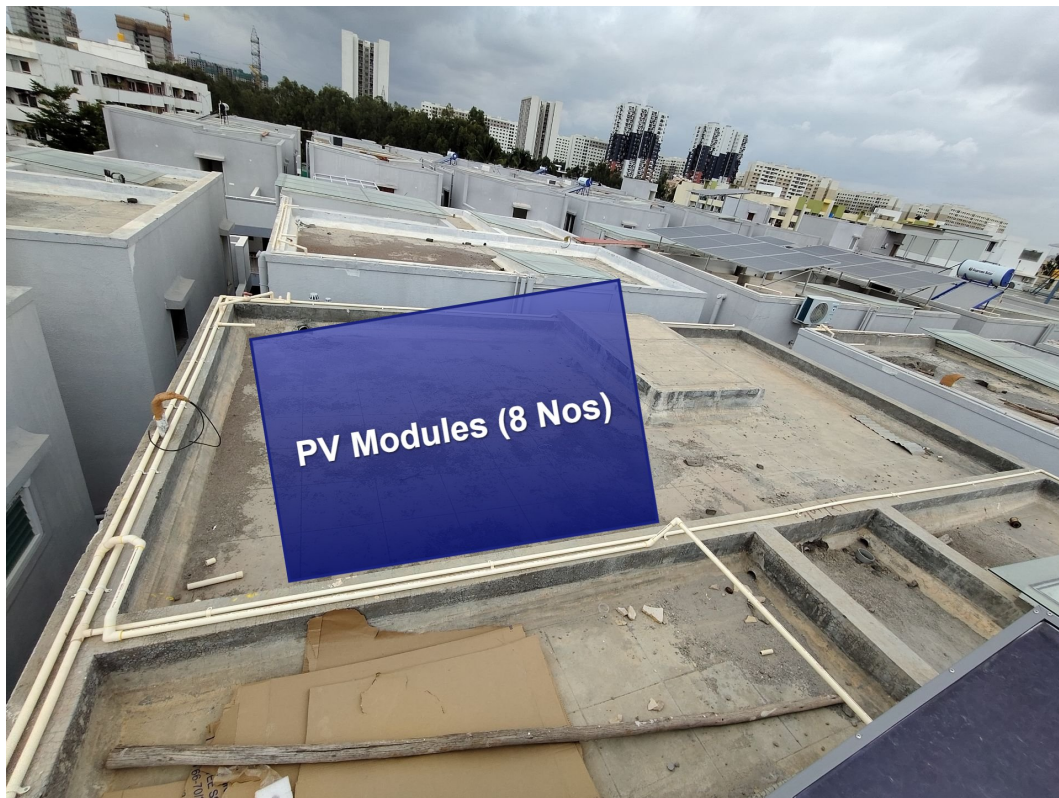


### Cable Routing

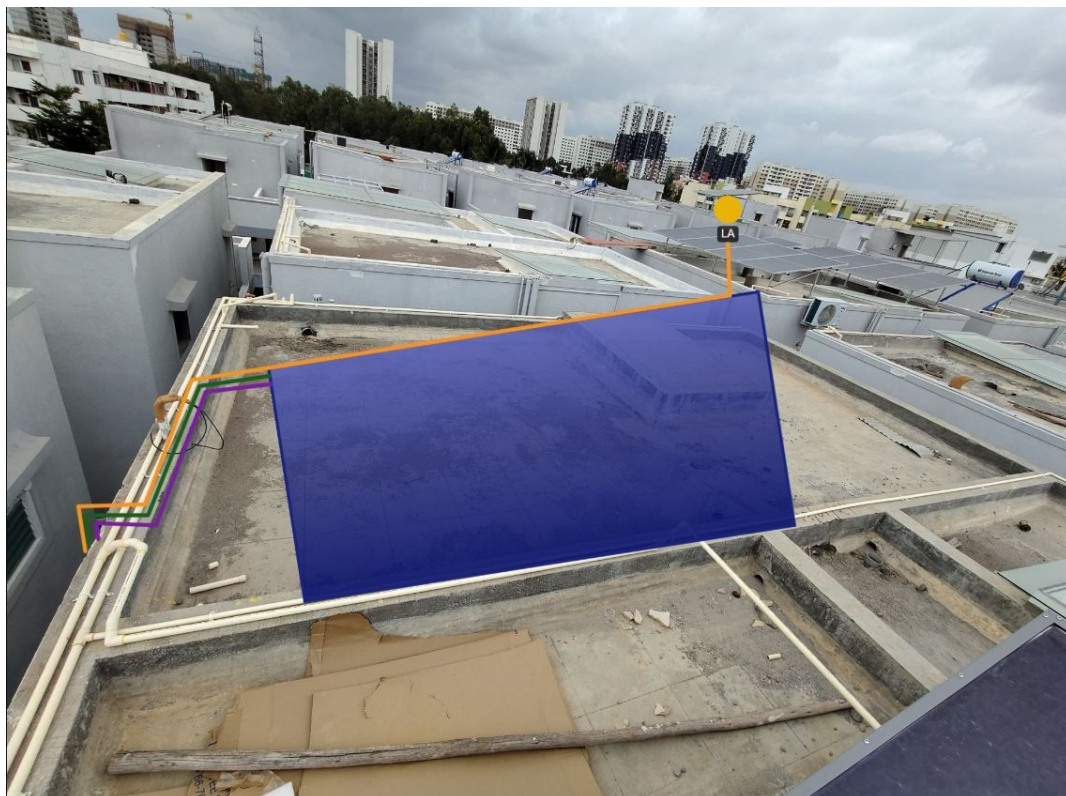








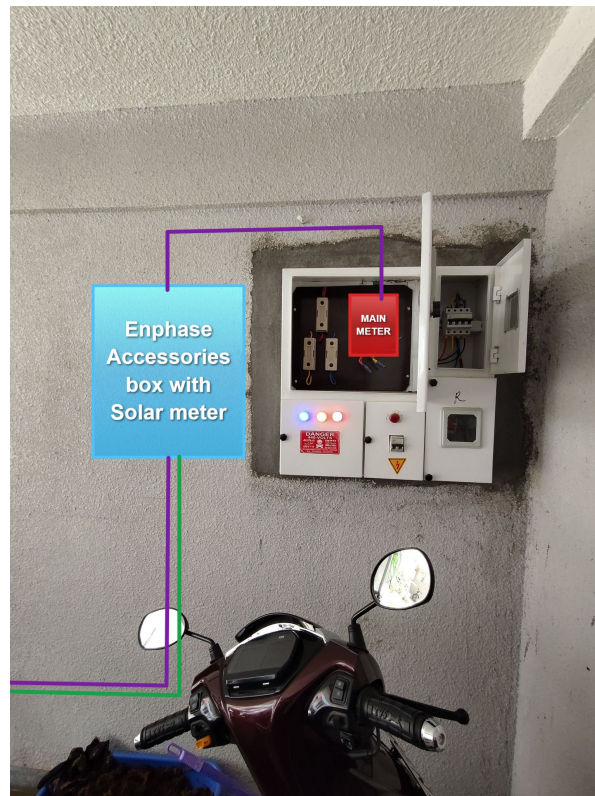

## Meter Box

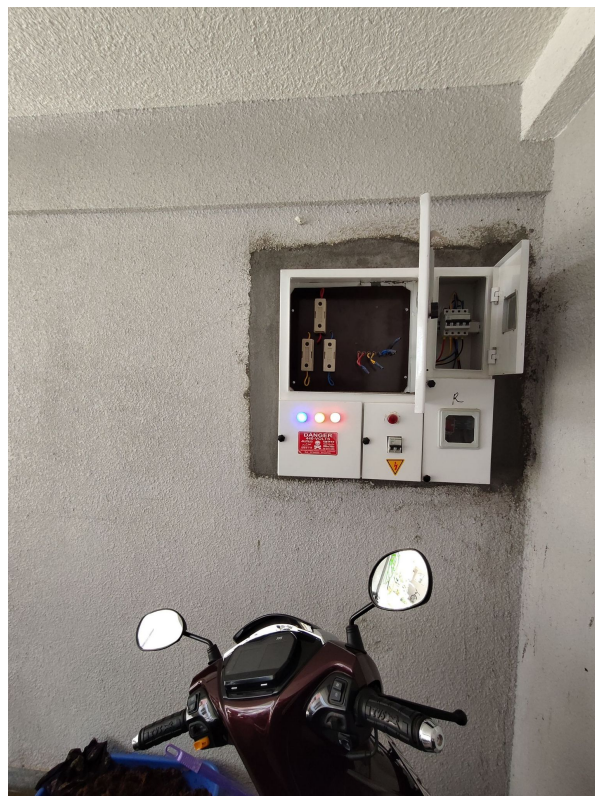

*Awaiting the BESCO meter connection*

## OBSERVATIONS & RECOMMENDATIONS

### EcoSoch Scope

| # | Observation                                                                                   |
|---|-----------------------------------------------------------------------------------------------|
| 1 | Installation and commissioning of 4.92kWp On-grid solar power plant at the proposed premises. |
| 2 | The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.  |
| 3 | Providing a base support provision for lightning arrester extension at the rooftop.           |

### Customer Scope

| # | Observation                                                                                                                                                           |
|---|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1 | Providing an active Wi-Fi or LAN cable connection up to the inverter location.                                                                                        |
| 2 | The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution. |

## THANK YOU

Dear Vivek M,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
