

Technical Site Visit Report

Prepared for: Dhanush_Non_Subsidy_Vidyaranyapura_9.6kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0045
Project ID	93F48284
Project Name	Dhanush_Non_Subsidy_Vidyaranyapura_9.6kWp_Hybrid
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Mahantayya
Site Address	Dhanush Vidyaranyapura GST.No: 29BYMPG6362C1ZA 920/1, "D" Block, 10th Main Road 16th Cross, Sahakara Nagar, Bangalore-560092
GPS Coordinates	13.061178, 77.585934
Google Maps	https://www.google.com/maps?q=13.061178,77.585934
Visit Date	2026-03-18
Visited By	Abilash N K
Revision	Rev 3

CLIENT INFORMATION

Client Name	Dhanush
Contact	7411 440 099

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	9.6
Sanction Load (kW)	10
Module Make & Capacity	AXITEC Bi-facial Non-DCR, 600 Wp
Module Length (mm)	2278

Module Width (mm)	1134
Number of Panels	16
Inverter Type	Hybrid (String)
Inverter Brand	Deye 10kW 3phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	SE-F5 Plus
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	7	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	7	-
5	On how many roofs at the site are we installing solar?	2	In the proposed building, we have two roofs available for installation. 1) Corrugated sheet roof (at the SOUTH SIDE of the terrace) with 12 panels. 2) Corrugated sheet roof (at the NORTH SIDE of the terrace) with 4 panels.
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Mini-rails	-
9	What is the orientation of the solar panels?	["South"]	1) Corrugated sheet roof (at the SOUTH SIDE): PV modules are facing SOUTH. 2) Corrugated sheet roof (at the NORTH SIDE): PV modules are facing NORTH.
10	How can the roof be accessed?	Staircase	-

#	Question	Answer	Notes
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	A PVC conduit (with a 1-inch dia.) will be provided by the customer from the top to the bottom of the building till the LT panel location for pulling the solar DC cable
13	What is the height of the building and how many floors does it have?	15 meters. (G + 3 + Headroom)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	A room is available on the ground floor to house the ACDB, DCDB, INVERTER & BATTERIES.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes. It's on the ground floor, near the main meter location.	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	The building is under construction. The LT panel not yet installed.
2	Is the Meter cubicle photo matching with the previous answer?	N/A	-
3	Has the termination point in the Main meter panel been identified?	N/A	-
4	Is the Termination Point easily visible or sealed?	N/A	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-



#	Question	Answer	Notes
9	In Main meter panel, is empty space available for solar meter?	N/A	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	No	-
13	In case of elevated structures, is it with or without grouting?	N/A	Customer scope.
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 600, width: 600	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 1000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit

Site Layout - Top View

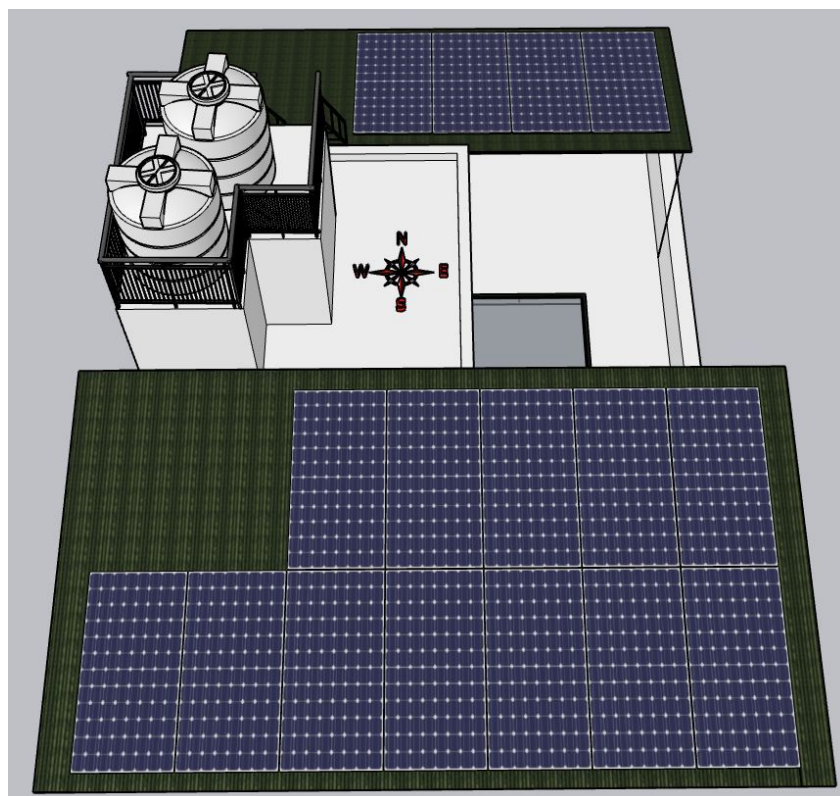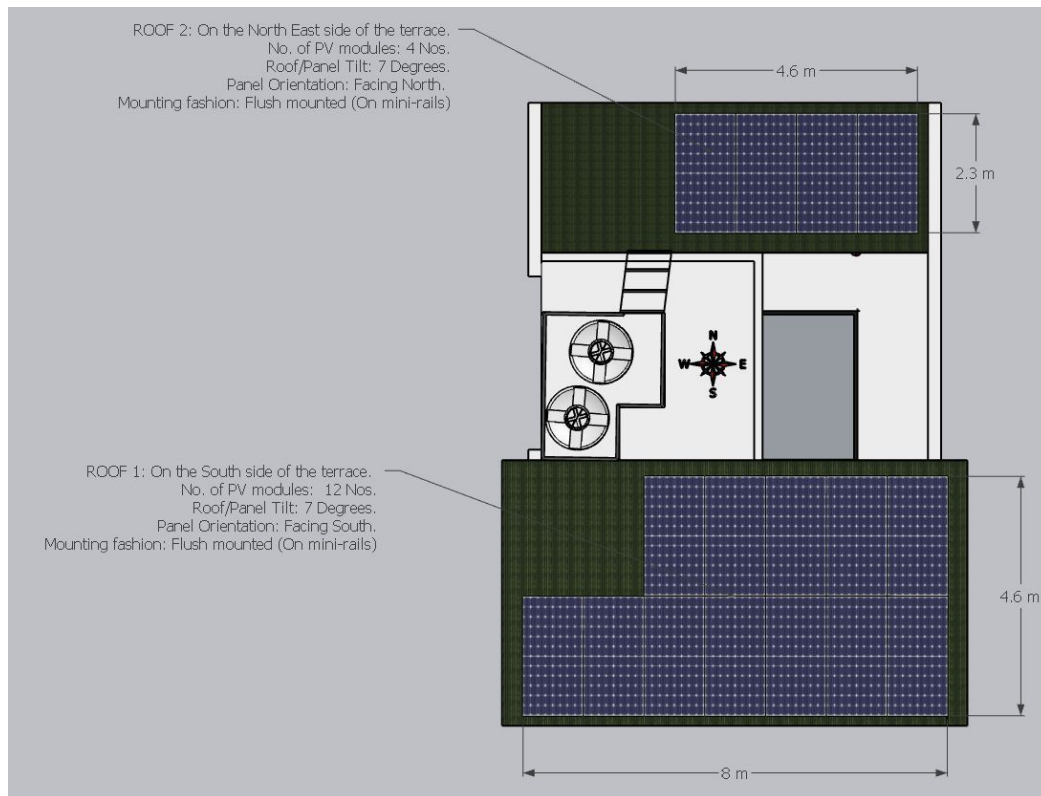

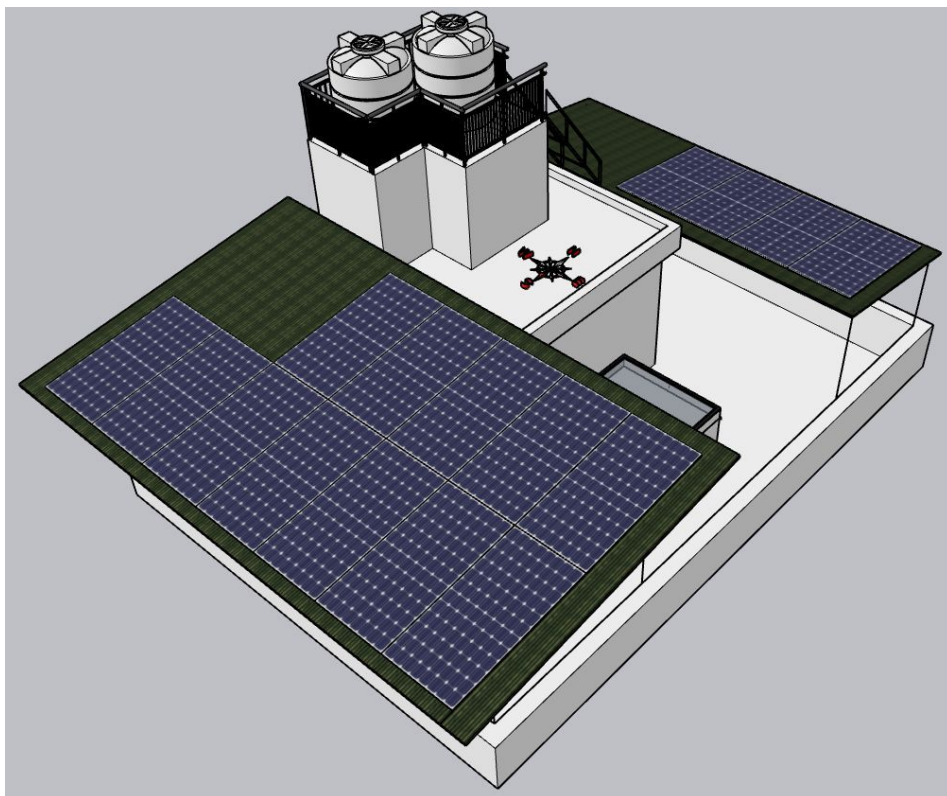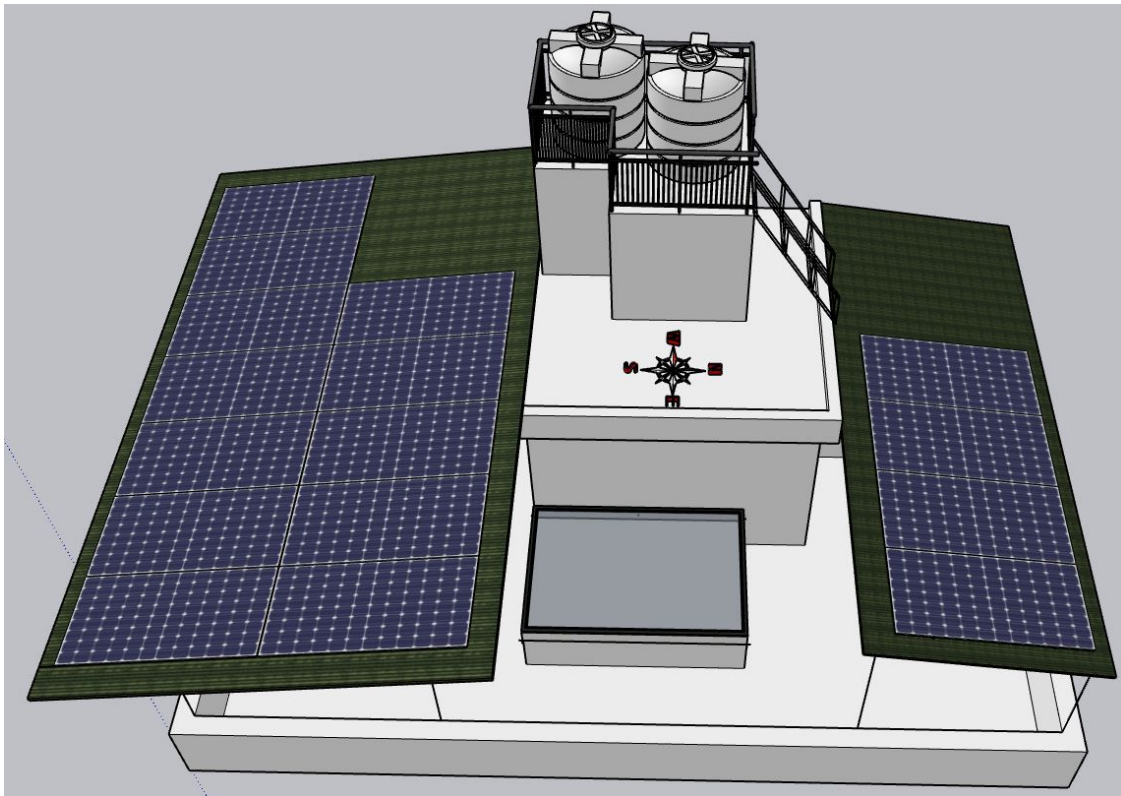

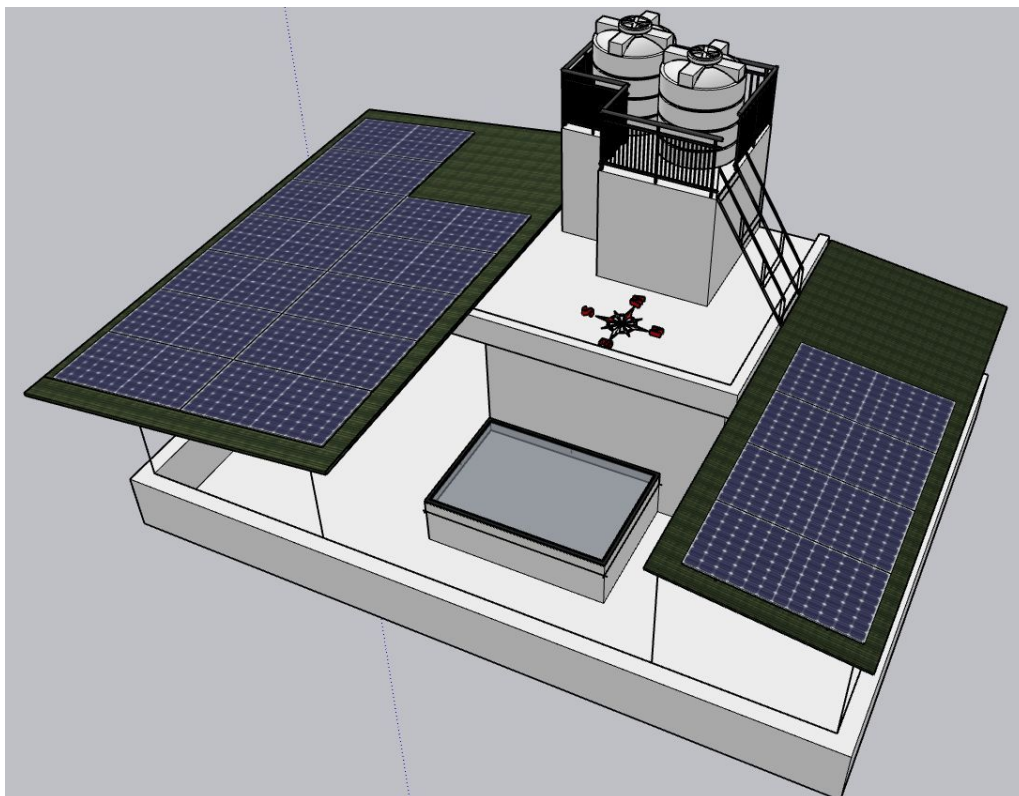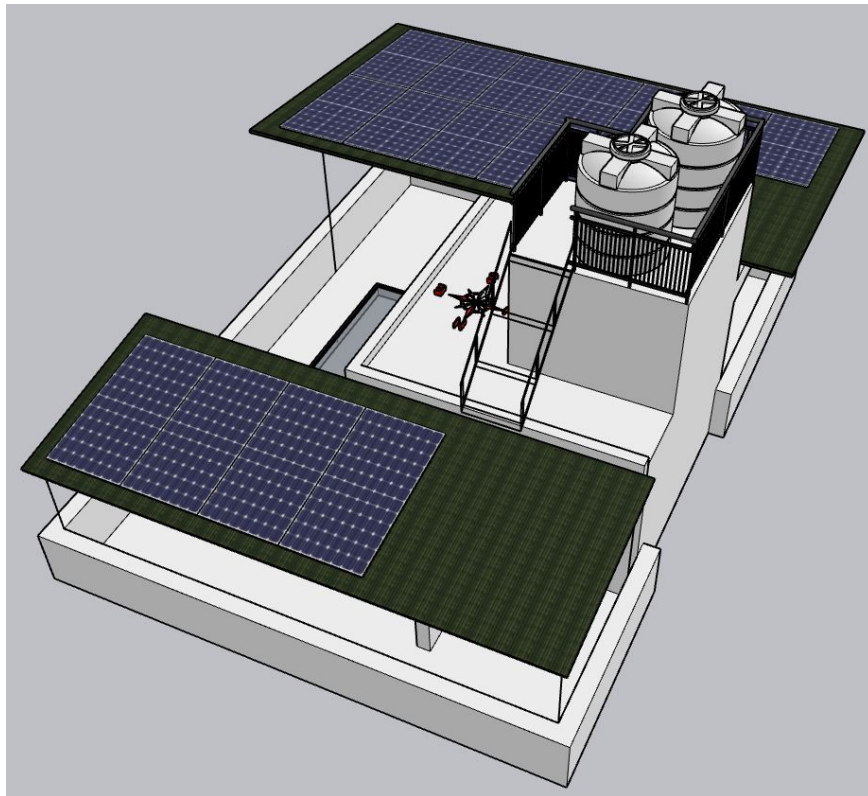

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



The materials can follow the stairs until reaching the terrace.



The materials are reaching the terrace floor of the 3rd floor.



Materials after reaching the 3rd floor can be shifted to the upper terrace roof via the ladder.

Staircase Details



Staircase (at the ground) width: 1000 mm





Staircase (inside) width: 800 mm

Material Storage



Proposed PV Area

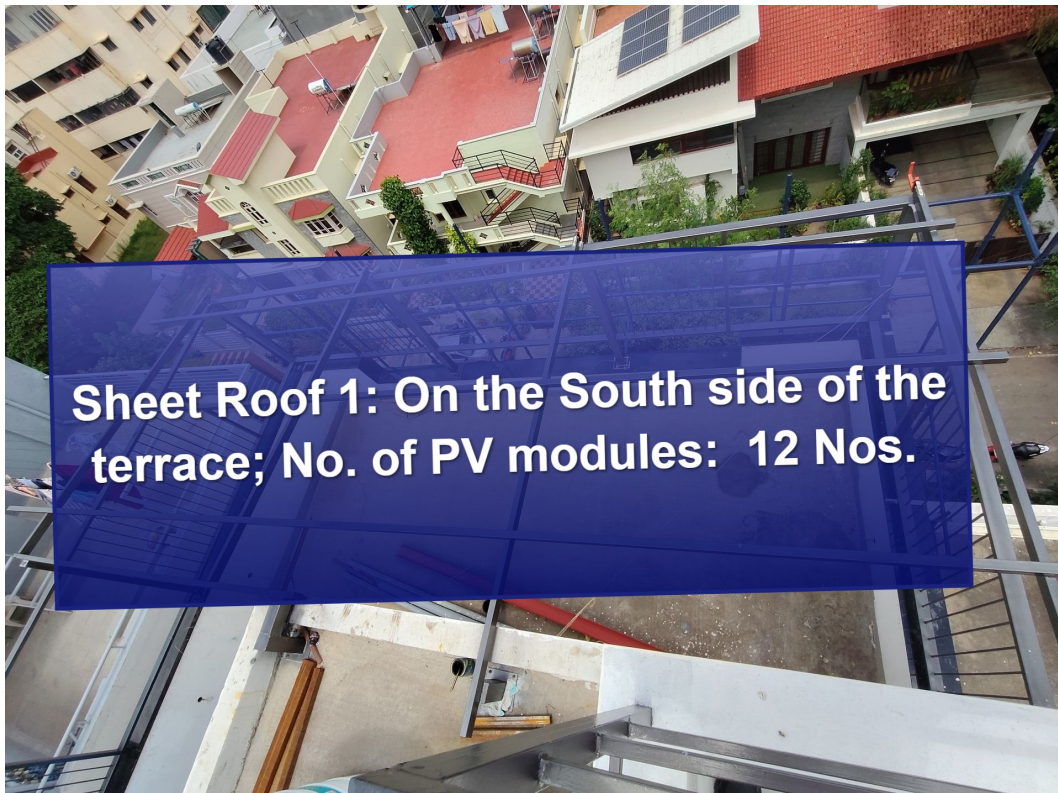

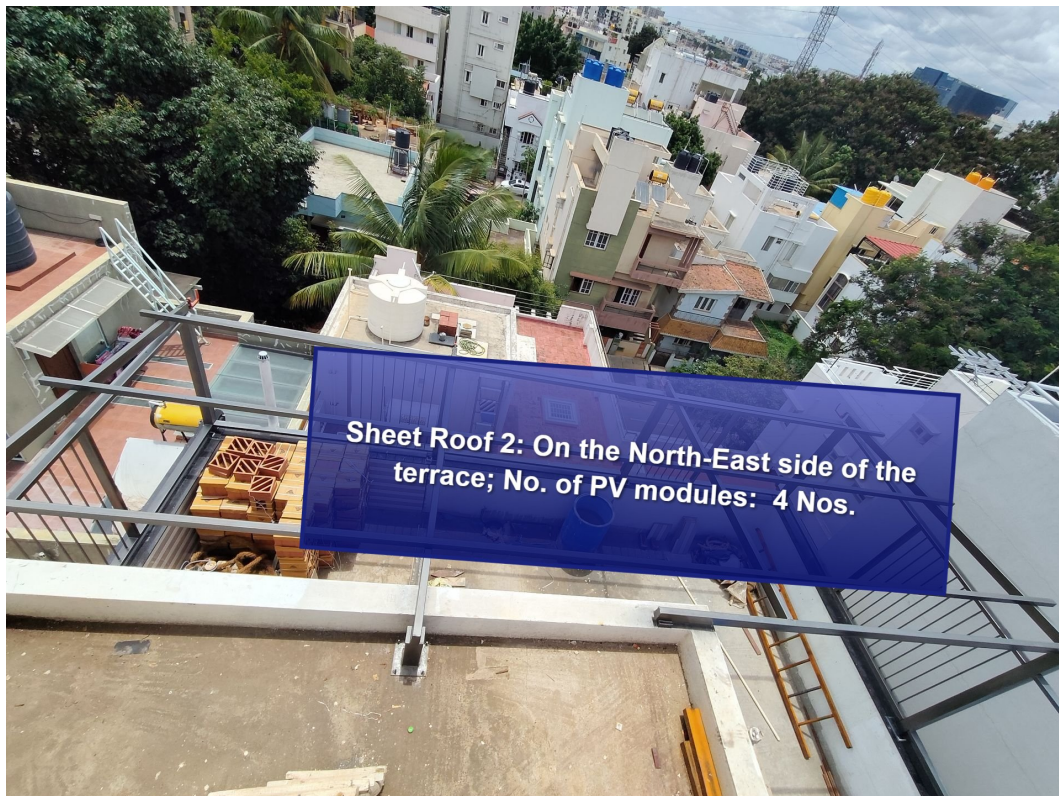

Cable Routing



The solar DC cable and the DC earthing cables can run over the short parapet wall connecting the North and South side base structures.



The DC cable after stringing between the two roofs can move towards the narrow open room where it can enter into a switch box provided.



A conduit runs from this switch box will lead the DC cable to reach the LT panel in the ground floor.



The DC earthing cable and the LA earthing cable can run together towards the left side (West) of the building near the plumbing pipe clamps.




Further, both the earthing cables can run along with the plumbing pipes till reaching the ground floor.




The earthing cables reaching the ground floor.



The earthing cables reaching the ground can be pulled via the existing conduit provided by the customer till reaching the earth pit.

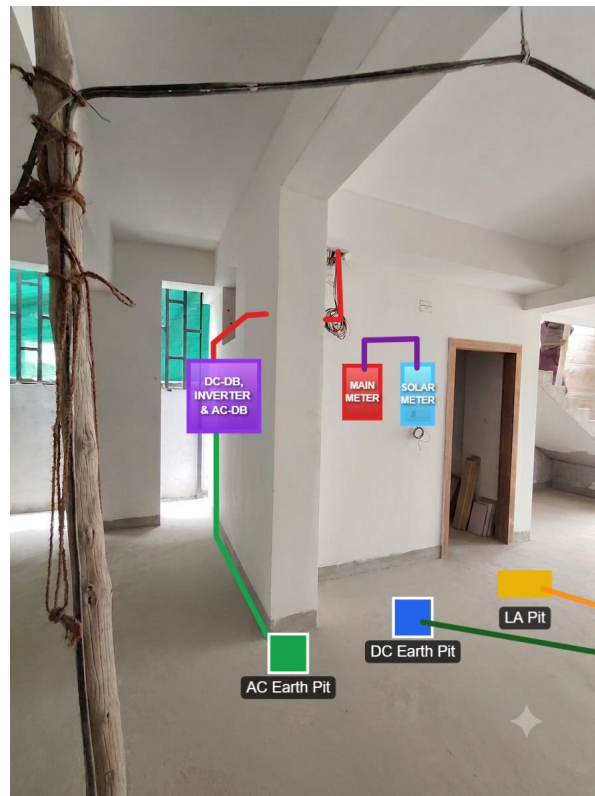

The solar DC cable coming from the terrace level appears near the main LT panel (Just below the ceiling, but above the panel board). Three earth pits already dug by the customer under the cemented floor.

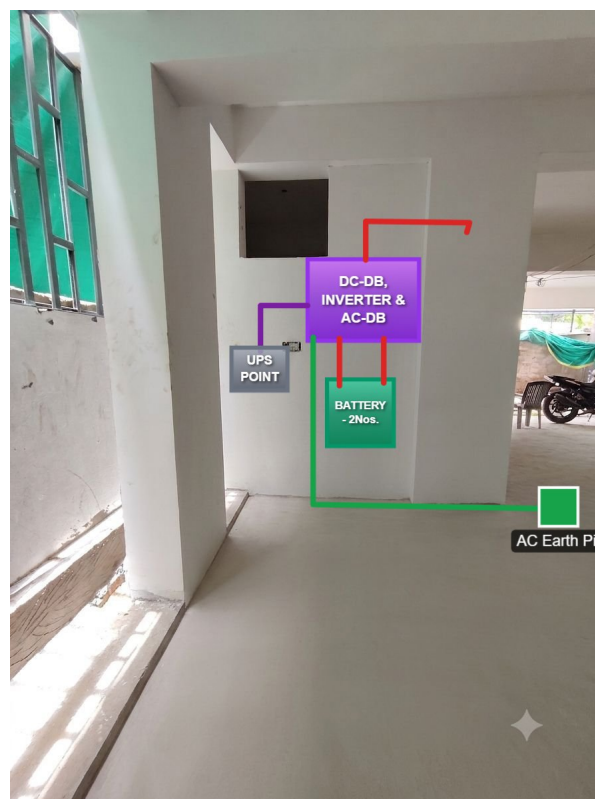


The UPS point will be provided by the customer at the inverter location.

Meter Box




The LT panel is under fabrication.

Shadow Analysis

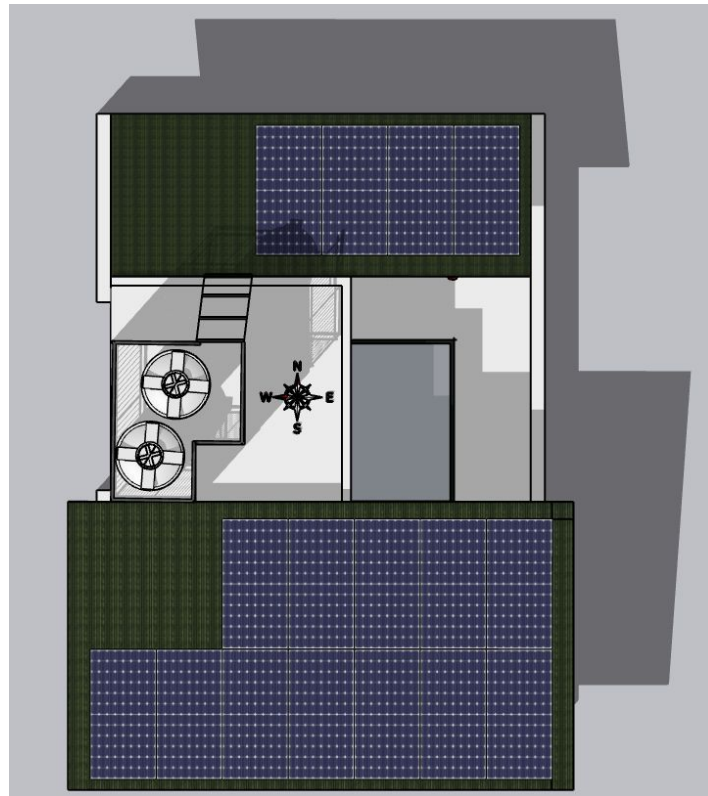

Shadow_November 2pm

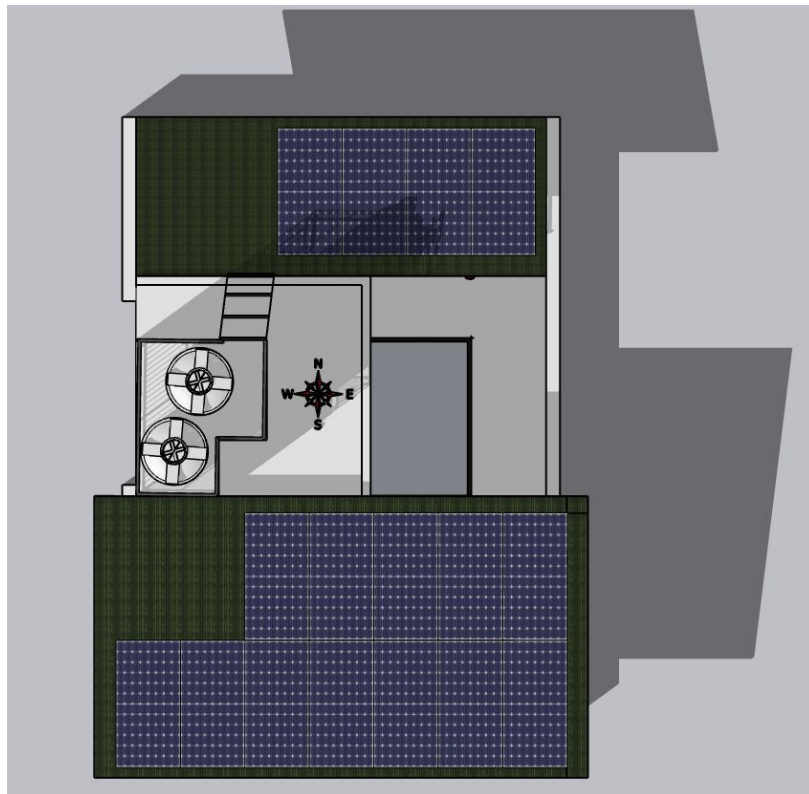

Shadow_November 3pm

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 9.6 kWp, HYBRID solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Fabrication of the sheet roof structure for 16 panels at the terrace level.
2	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
3	Providing UPS point near the Inverter and battery location.
4	Ensuring the Inverter-Battery room has adequate ventilation throughout the day.
5	Fabrication of adequate walk-way provision for PV module maintenance if necessary.
6	Installing two numbers of 1-inch electrical PVC conduits to span the ground floor's tiled area (from the plumbing shaft location to the earthing pit location)
7	Providing assistance to the ECOSoch installation team during the installation to ensure that the existing conduits are free to draw the cables.

THANK YOU

Dear Dhanush,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
