

## Technical Site Visit Report

Prepared for: Deepesh - Kanavu Koodu

### PROJECT INFORMATION

|                 |                                                                                                                                                           |
|-----------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0157                                                                                                                                             |
| Project Name    | Deepesh                                                                                                                                                   |
| Building Name   | Kanavu Koodu                                                                                                                                              |
| Billing Name    | Deepesh                                                                                                                                                   |
| Project Sector  | Residential                                                                                                                                               |
| Project Type    | With Subsidy                                                                                                                                              |
| Sales Lead      | Hariom                                                                                                                                                    |
| Site Address    | Deepesh Sudhakaran<br>Plot #194, Ashoka Aarna, 7th main,Hosakere alake, Gulakamale<br>Kanakapura Road, Bengaluru,<br>BENGALURU, KARNATAKA 560082<br>India |
| GPS Coordinates | 12.80402504779635, 77.52459519191764                                                                                                                      |
| Google Maps     | <a href="https://www.google.com/maps?q=12.804025047796355,77.52459519191764">https://www.google.com/maps?q=12.804025047796355,77.52459519191764</a>       |
| Visit Date      | 2026-06-25                                                                                                                                                |
| Visited By      | K Naveen                                                                                                                                                  |
| Revision        | Rev 2                                                                                                                                                     |

### CLIENT INFORMATION

|             |            |
|-------------|------------|
| Client Name | Deepesh    |
| Contact     | 9036044227 |

### PROJECT DETAILS

|                           |          |
|---------------------------|----------|
| Solar Rooftop System Type | Off-Grid |
| System Capacity (kWp)     | 4.9      |
| Sanction Load (kW)        | 6        |

|                                |                                  |
|--------------------------------|----------------------------------|
| Module Make & Capacity         | Waaree bifacial Non DCR - 700 Wp |
| Module Length (mm)             | 2382                             |
| Module Width (mm)              | 1303                             |
| Number of Panels               | 7                                |
| Inverter Type                  | Hybrid (String)                  |
| Inverter Brand                 | Deye 6 kW 1phase String          |
| Number of Inverters            | 1                                |
| Battery                        | Needed                           |
| Number of Batteries            | 1                                |
| Capacity of each Battery (kWh) | 5.12                             |
| Battery Model No.              | Deye SE-F5plus                   |
| Mounting Structure Type        | Elevated                         |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                                                       | Notes          |
|---|----------------------------------------------------------------------------|------------------------------------------------------------------------------|----------------|
| 1 | Can the delivery van/truck reach the material unloading point?             | Yes                                                                          | -              |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | No                                                                           | -              |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | The Inverter, DC DB, ACDB, Battery will be installed near the inverter room. | -              |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | No                                                                           | -              |
| 5 | Did you discuss the location of the earth pits with the customer?          | The earth pits are located near the north side of the garden area            | -              |
| 6 | Where is the Internet Router located?                                      | Under construction                                                           | Customer Scope |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | Not Available / Under Construction                                           | -              |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                                                          | -              |

## Roof Details

| #  | Question                                                                                                 | Answer                                  | Notes                                          |
|----|----------------------------------------------------------------------------------------------------------|-----------------------------------------|------------------------------------------------|
| 1  | What type of roof is present at the site?                                                                | RCC Flat Roof                           | <i>RCC Flat roof with laid of tiles</i>        |
| 2  | Are there any obstructions on the roof that could affect the solar installation?                         | No                                      | -                                              |
| 3  | What is the angle of the panels? (in degrees)                                                            | 10                                      | -                                              |
| 4  | In case of sloped roof, what is the slope angle of the roof? (in degrees)                                | N/A                                     | -                                              |
| 5  | On how many roofs at the site are we installing solar?                                                   | 1                                       | -                                              |
| 6  | If it is a Tiled roof, what is underneath the tiles?                                                     | N/A                                     | -                                              |
| 7  | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?                     | N/A                                     | -                                              |
| 8  | What type of mounting structure is planned?                                                              | Elevated                                | <i>Elevated HDGI Structure with 2.50 meter</i> |
| 9  | What is the orientation of the solar panels?                                                             | ["South"]                               | -                                              |
| 10 | How can the roof be accessed?                                                                            | Staircase                               | -                                              |
| 11 | Is the building currently under construction?                                                            | Yes                                     | -                                              |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | Yes                                     | -                                              |
| 13 | What is the height of the building and how many floors does it have?                                     | G+2+Headroom is approximately 15 meters | -                                              |
| 14 | Is the site photo matching with the building description?                                                | Yes                                     | -                                              |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                                      | -                                              |

## Residential / Electrical

| #  | Question                                                                                                | Answer                            | Notes |
|----|---------------------------------------------------------------------------------------------------------|-----------------------------------|-------|
| 1  | What type of energy meter is currently installed?                                                       | Phase: Three Phase, Type: Digital | -     |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes                               | -     |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes                               | -     |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible                           | -     |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No                                | -     |
| 6  | Is space available for CT within Energy meter panel?                                                    | No                                | -     |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | N/A                               | -     |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A                               | -     |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | No                                | -     |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | N/A                               | -     |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | Yes                               | -     |

| #  | Question                                                                                          | Answer                    | Notes |
|----|---------------------------------------------------------------------------------------------------|---------------------------|-------|
| 12 | In case of elevated structures, is an LA extension provided at the far end?                       | Yes                       | -     |
| 13 | In case of elevated structures, is it with or without grouting?                                   | With Grouting             | -     |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                 | No                        | -     |
| 15 | Are there any safety risks associated with accessing the roof for installation?                   | No                        | -     |
| 16 | Is space present in rooftop to store the panels?                                                  | Horizontally sleeping     | -     |
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin. | N/A                       | -     |
| 18 | Is ventilation available in the battery location?                                                 | Yes                       | -     |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                       | Wall Mount                | -     |
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).                         | length: 1500, width: 2000 | -     |
| 21 | Provide the dimension for earth pits location (L x W of available space).                         | length: 2500, width: 2000 | -     |
| 22 | Is LAN cable under customer scope?                                                                | No                        | -     |
| 23 | Is there any shadow that affects the solar installation?                                          | No                        | -     |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location?                  | No                        | -     |

## PHOTO DOCUMENTATION

### Cable Routing Legend

| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|  | Proposed PV Module Array |
|  | Main Meter Location      |
|  | Solar Meter              |
|  | Battery                  |
|  | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |
|  | LA Pit                   |
|  | LA                       |

## Material Delivery Route



*This route (using lifting) will be followed to carry large items (like Panels).*












*This route (using Staircase) will be followed to carry Small items.*






## Staircase Details

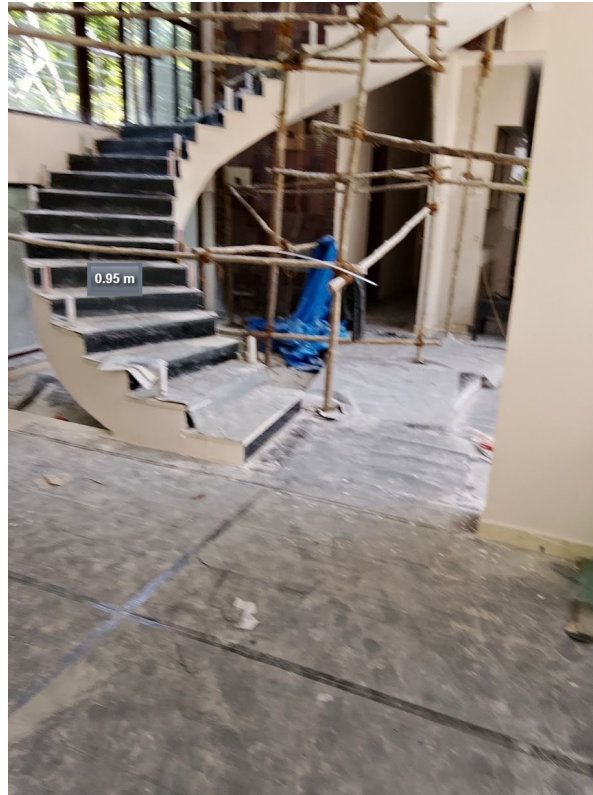

## Meter Box



## Material Storage

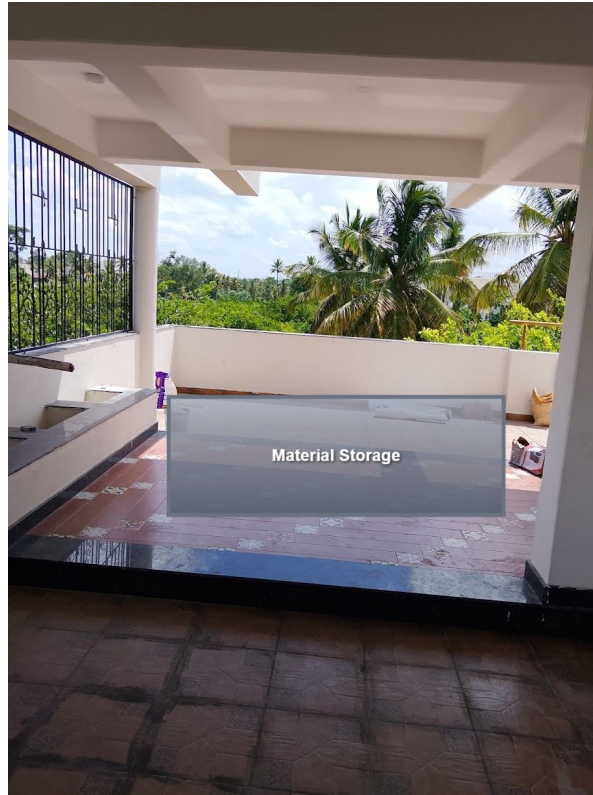

## Proposed PV Area





## Cable Routing



*The DC cable has to be run through the existing 1 inch conduit pipes*










## Equipment Location


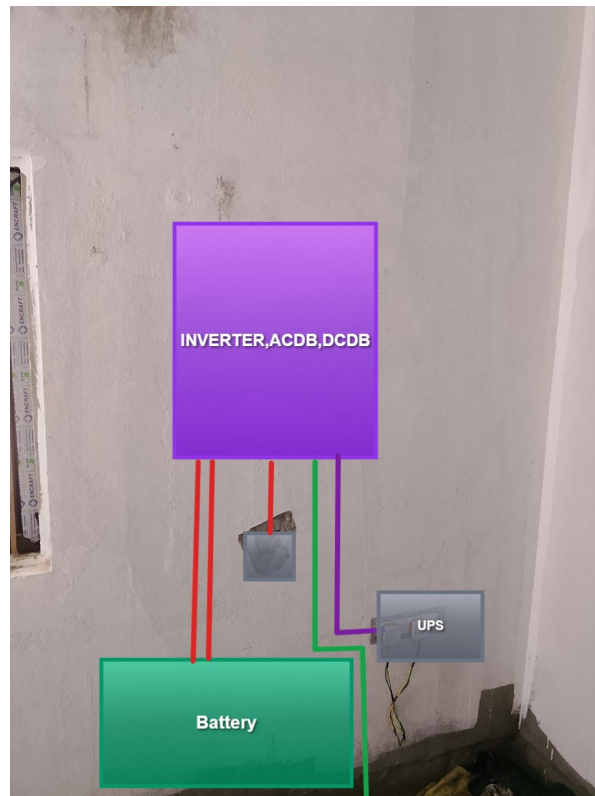



## Earth Pit Location





## Site Layout - Top View

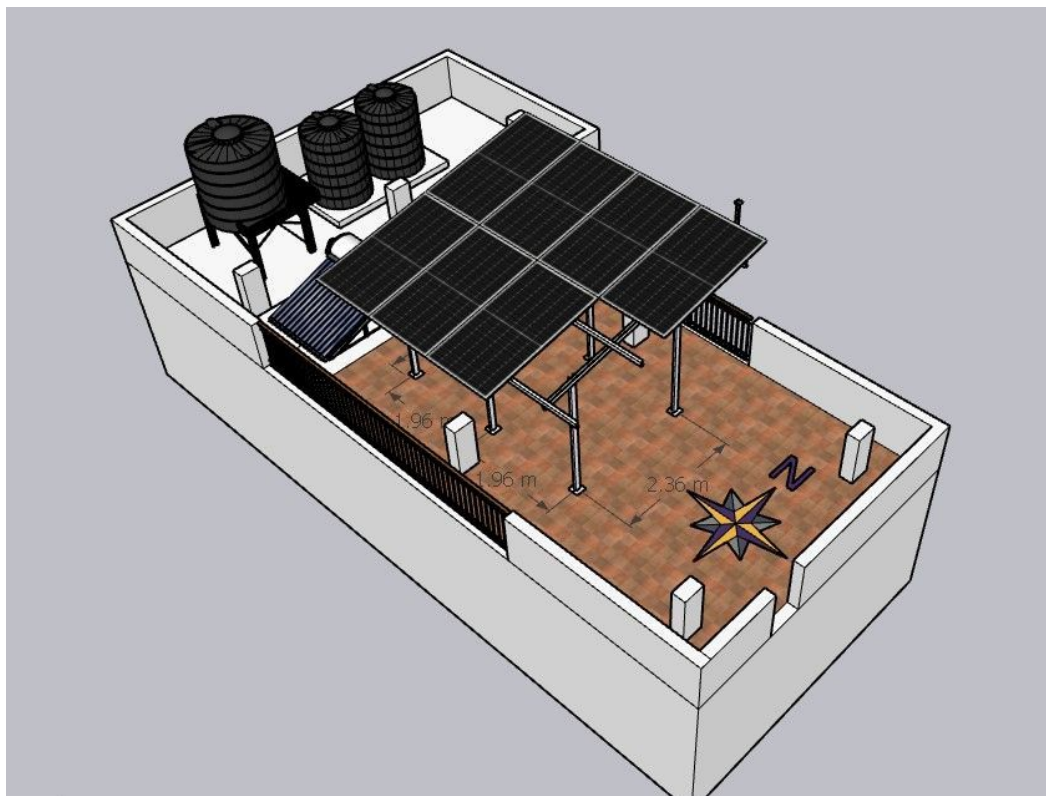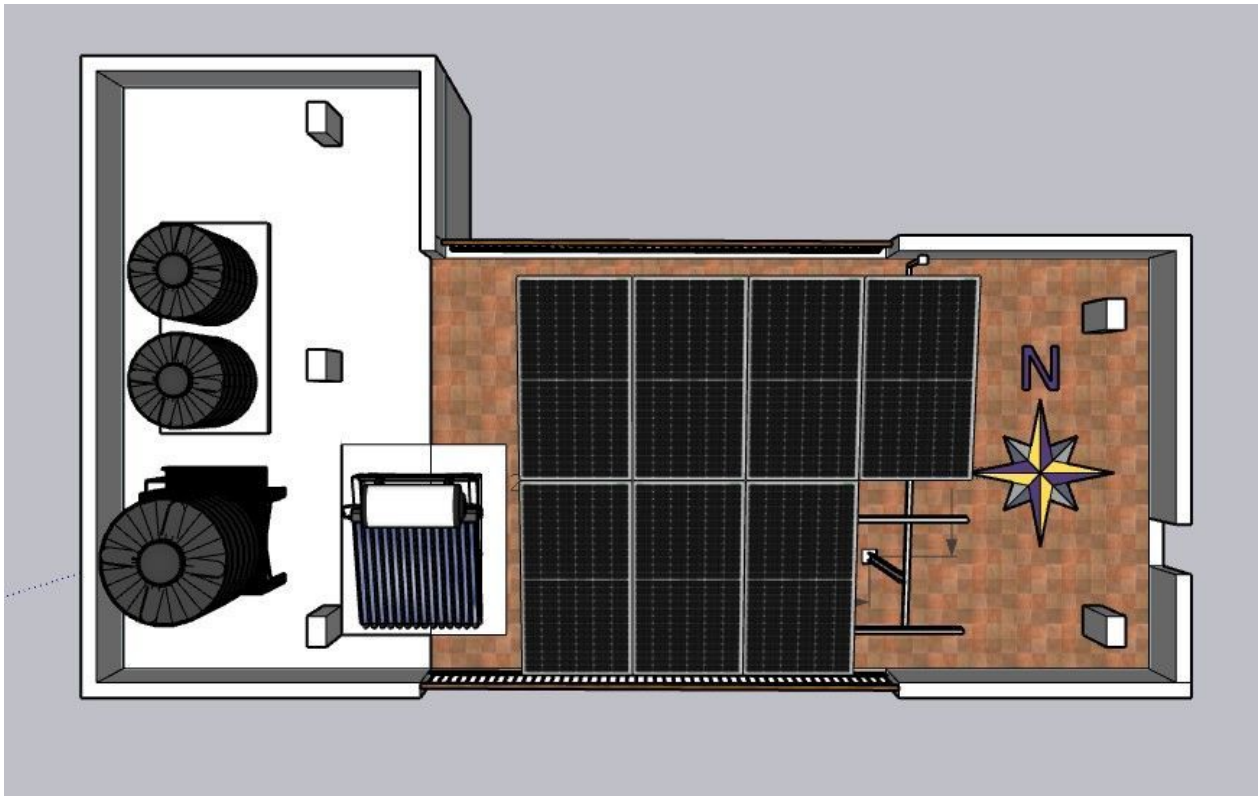

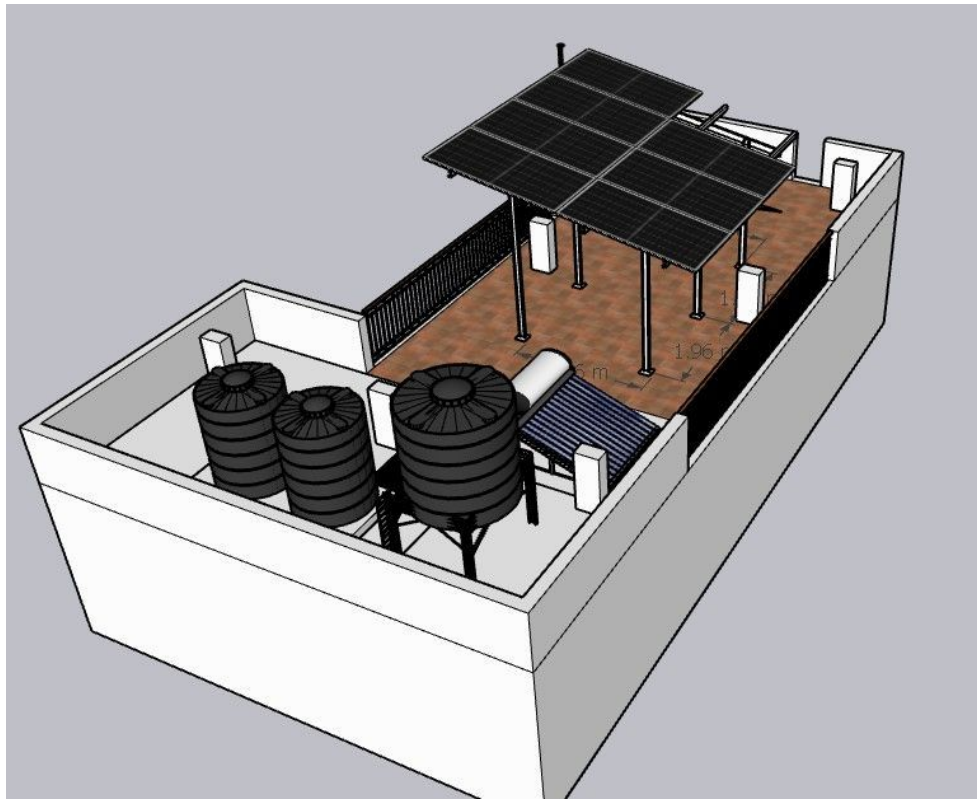

## Building Exterior





## OBSERVATIONS & RECOMMENDATIONS

### Customer Scope

| # | Observation                                                                                           |
|---|-------------------------------------------------------------------------------------------------------|
| 1 | Wi-Fi Up to the inverter location is under customer scope                                             |
| 2 | As per the customer suggestion only the above earthing,cable routing,panel layout has been considered |
| 3 | As per the client suggestions only the structure frot height 2.50m has been considered.               |

## THANK YOU

Dear Deepesh,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
