

Technical Site Visit Report

Prepared for: Jyotiranjana Mohapatra_Terrafem Lavender Meadows_9.8kWp_Hybrid - Plot 10, TERRAFEM - Lavender Meadows

PROJECT INFORMATION

Report Number	ESV-2026-0208
Project ID	D4CD6664
Project Name	Jyotiranjana Mohapatra_Terrafem Lavender Meadows_9.8kWp_Hybrid
Building Name	Plot 10, TERRAFEM - Lavender Meadows
Billing Name	Jyotiranjana Mohapatra_Terrafem Lavender Meadows_9.8kWp_Hybrid
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Hariom
Site Address	Plot 10, TERRAFEM - Lavender Meadows, Gunjur - Mugalur Rd, Bengaluru, Karnataka 562125.
GPS Coordinates	12.90013261999114, 77.80631041935322
Google Maps	https://www.google.com/maps?q=12.900132619991135,77.80631041935322
Visit Date	2026-09-19
Visited By	Sai
Revision	Rev 1

CLIENT INFORMATION

Client Name	Jyotiranjana Mohapatra
Contact	6363173828

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	9.8
Sanction Load (kW)	10

Module Make & Capacity	Waaree bifacial Non DCR 700 Wp
Module Length (mm)	2384
Module Width (mm)	1303
Number of Panels	14
Inverter Type	Hybrid (String)
Inverter Brand	Deye 10kW 3 phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Inverter, DCDB, ACDB, Battery is located near the ground floor.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Earth pits are located near the basement area.	-
6	Where is the Internet Router located?	Customer scope.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-

#	Question	Answer	Notes
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	HDGI structure with 2m front leg
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	Height of the building is 15m; it has G+2+headroom.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	Building is under construction.
2	Is the Meter cubicle photo matching with the previous answer?	No	Building is under construction.
3	Has the termination point in the Main meter panel been identified?	No	Building is under construction.
4	Is the Termination Point easily visible or sealed?	-	Building is under construction.
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Building is under construction.
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	No	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-

#	Question	Answer	Notes
15	Are there any safety risks associated with accessing the roof for installation?	No	Building is under construction.
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Inverters/ACDB/DCDB be installed on a wall mount.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 1000	Building is under construction.
21	Provide the dimension for earth pits location (L x W of available space).	length: 1000, width: 1000	Building is under construction.
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA


Building Exterior



Material Delivery Route



This route will carry the small items.

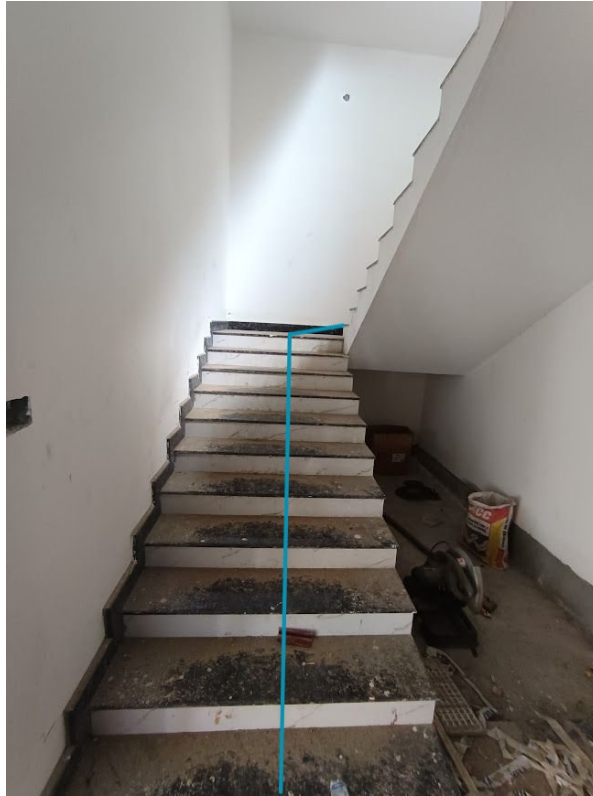

This route will carry the small items.



This route will carry the large items (like panels).

Staircase Details



Building is under construction.


Meter Box




Material Storage




Site Layout - Top View

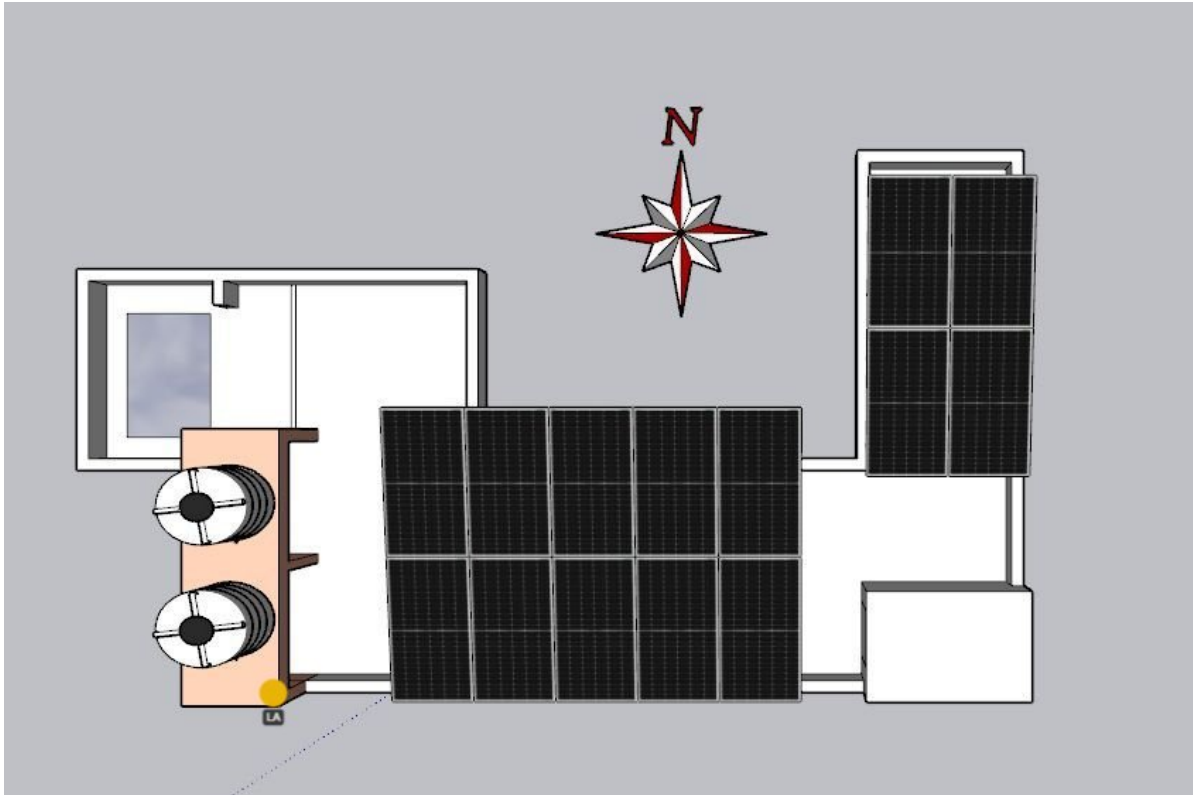


Top view

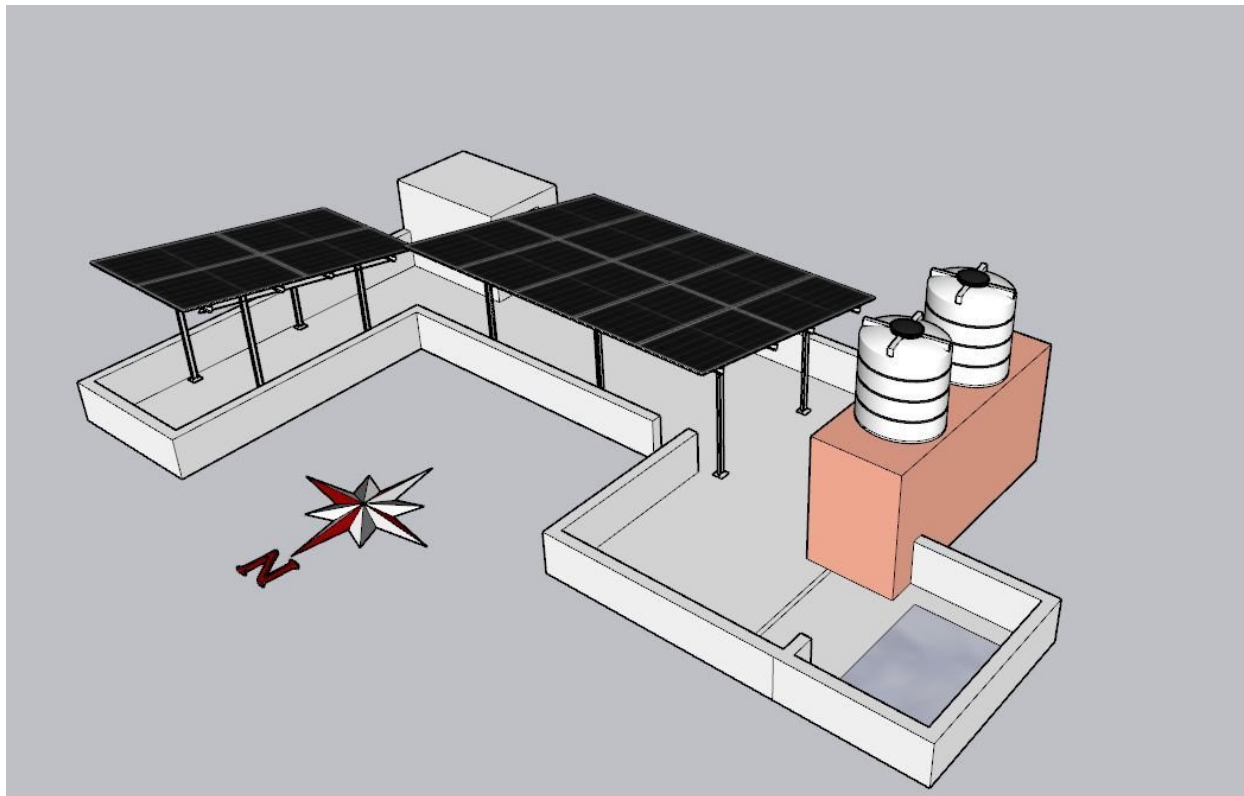


Side view (1)

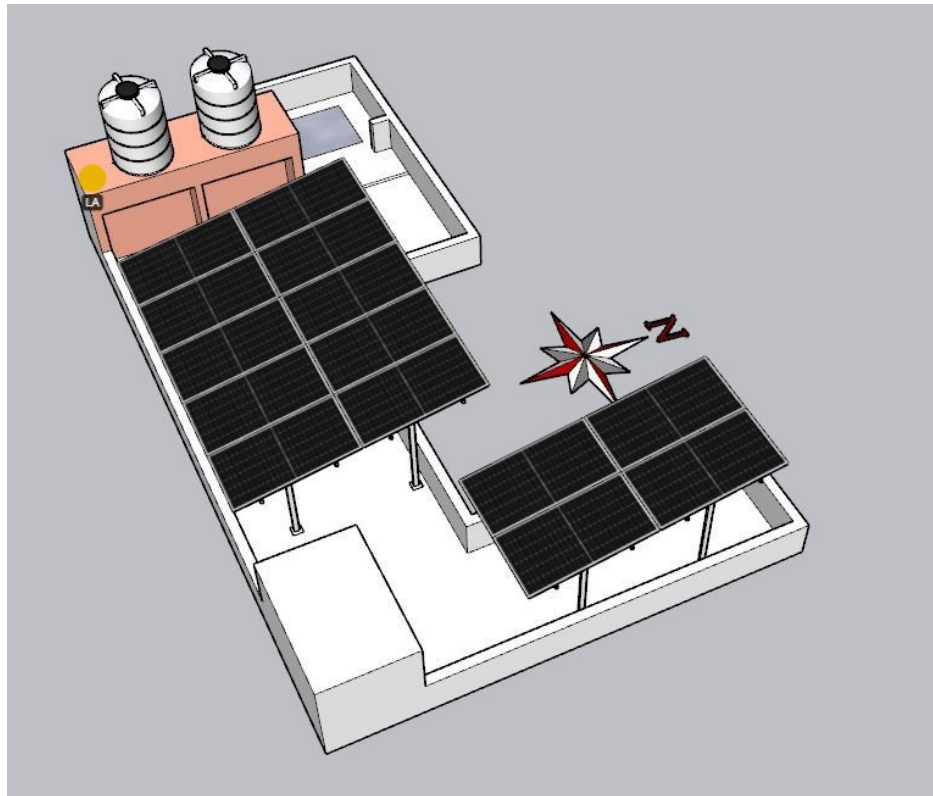


Side view (2)

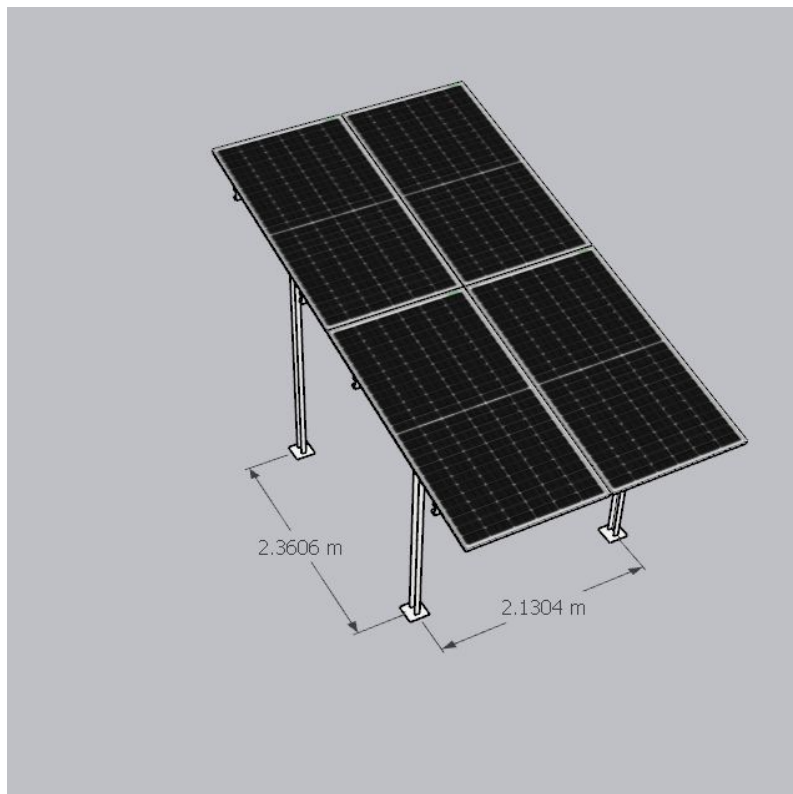


Structure details (1)

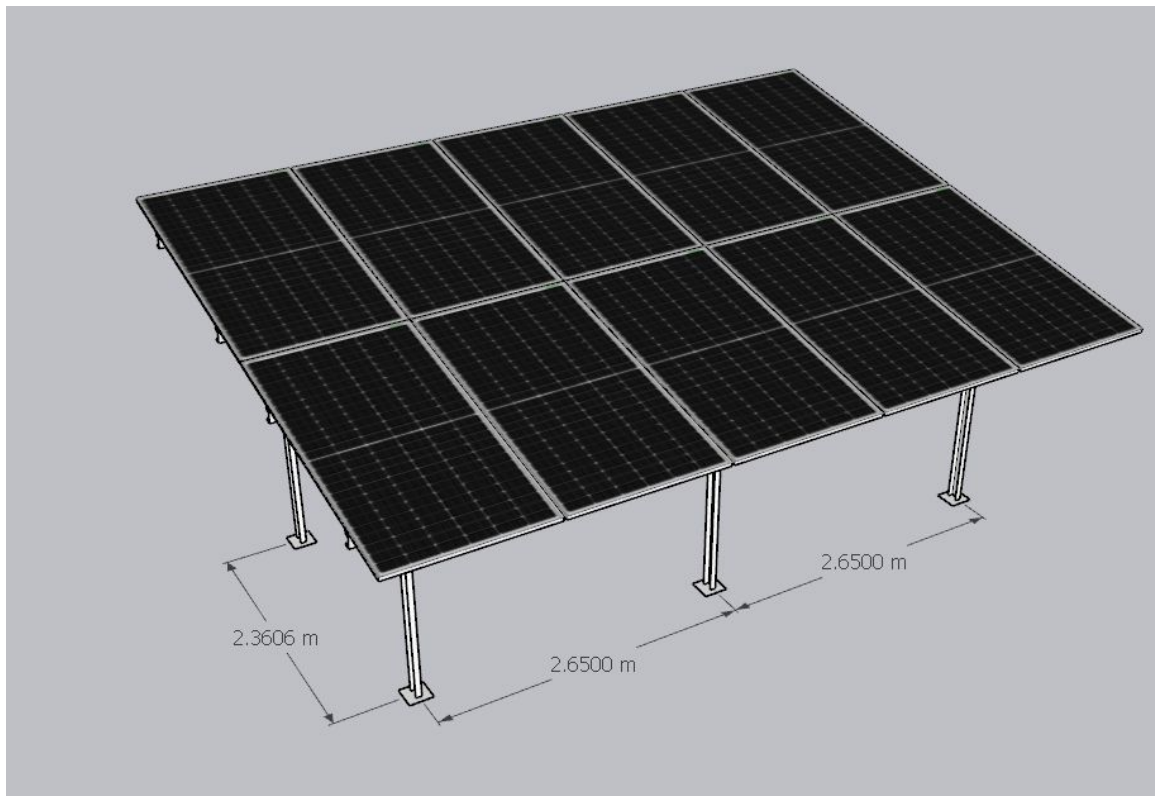

Structure details (2)

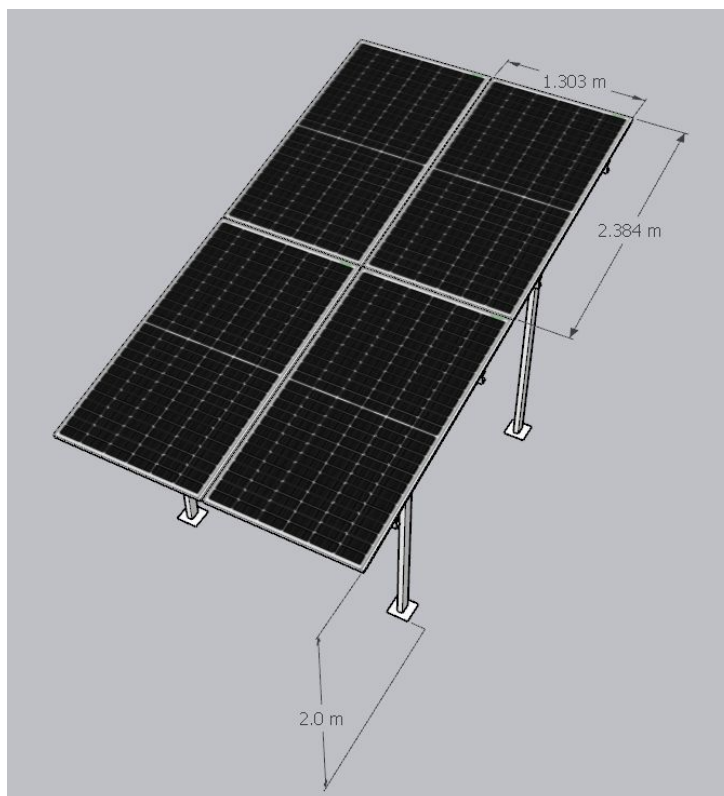

Panel dimensions (1)

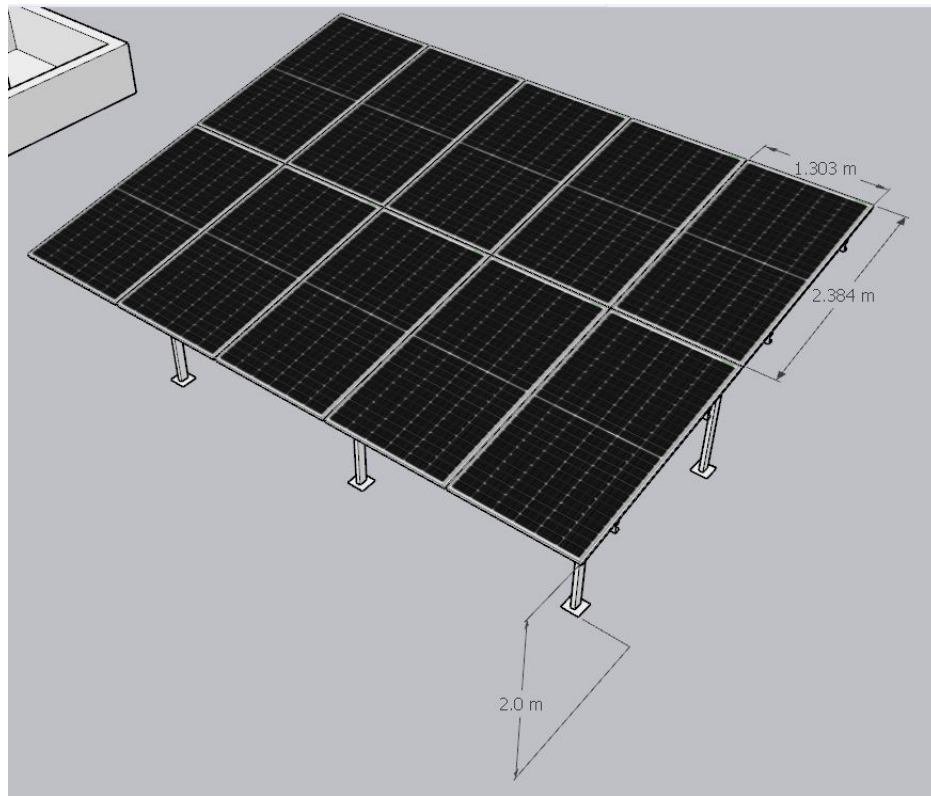

Panel dimensions (2)

Proposed PV Area






Cable Routing




One hole has to be made to run the DC cable.

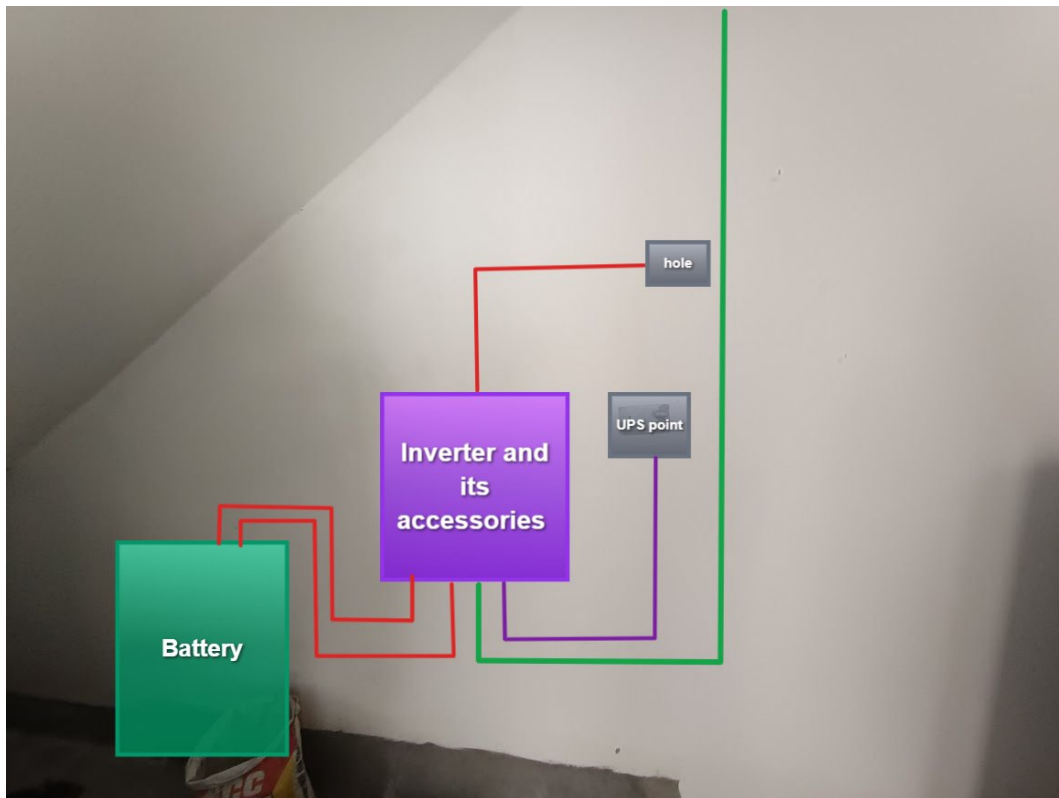

One hole has to be made to run the AC earthing cable.






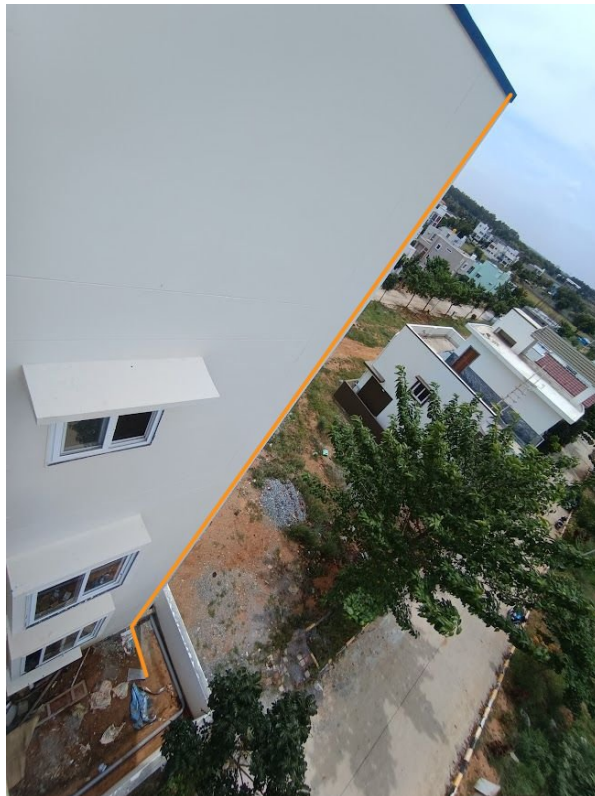



Equipment Location

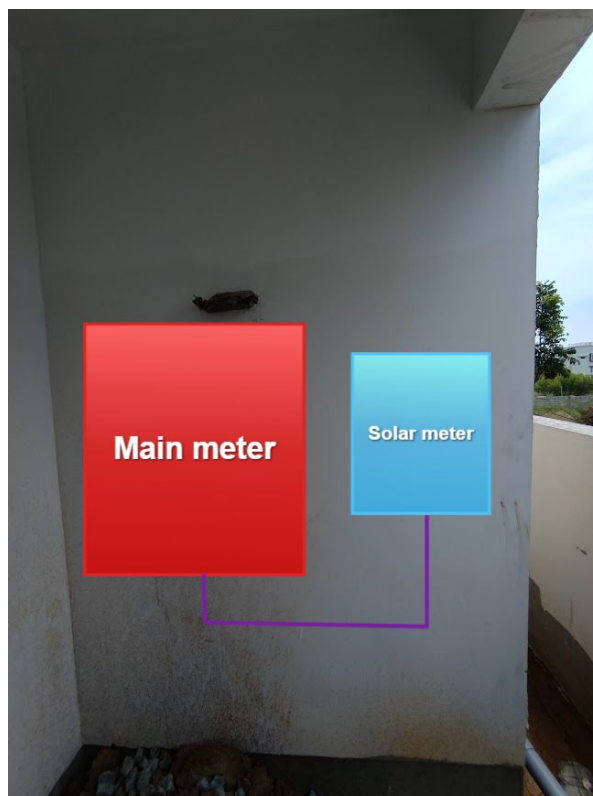

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As per the customer's suggestion, the routing, cable earthing, inverter location and also solar meter location have been considered.

Customer Scope

#	Observation
1	Wi-Fi upto solar meter is under customer scope.
2	UPS point is under customer scope.
3	Provision has to be provide to run the DC cable till the inverter location.

THANK YOU

Dear Jyotiranjana Mohapatra,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
