

Technical Site Visit Report

Prepared for: Ravinder S Arya_Devanahalli_Subsidy_18.6kWp_Hybrid - #Villa 24

PROJECT INFORMATION

Report Number	ESV-2026-0206
Project ID	USJ1BWWI
Project Name	Ravinder S Arya_Devanahalli_Subsidy_18.6kWp_Hybrid
Building Name	#Villa 24
Billing Name	Ravinder S Arya
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	Ravinder S Arya, Plot 24. Brindavan FarmsDevanahalli, Nandi Hills roadBengaluru 562110.
GPS Coordinates	13.2734354, 77.7162856
Google Maps	https://www.google.com/maps?q=13.2734354,77.7162856
Visit Date	2026-09-21
Visited By	K Naveen
Revision	Rev 1

CLIENT INFORMATION

Client Name	Ravinder S Arya
Contact	8828266353

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	18.6
Sanction Load (kW)	25

Module Make & Capacity	Premier DCR Bifacial 620
Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	30
Inverter Type	Hybrid (String)
Inverter Brand	Deye 20 kW 3phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F12 (12kW)
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	<i>During the site visit the material delivery route was not available to reach the site.</i>
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter,DCDB,ACDB,Battery will be installed inside the cctv room which is located in the first floor beside the staircase room.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the corridor which is located east side passage area.	-
6	Where is the Internet Router located?	Customer Scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstructions on the roof are the existing reinforcement that could affect the solar installation	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	HDGI Elevated Structure
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	But not visible on the terrace.
13	What is the height of the building and how many floors does it have?	The height of the building is G+1+Headroom is approximately 12 meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	Currenty the building is under construction.
2	Is the Meter cubicle photo matching with the previous answer?	No	-
3	Has the termination point in the Main meter panel been identified?	No	Under Construction
4	Is the Termination Point easily visible or sealed?	Visible	Under constructio
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Under construction

#	Question	Answer	Notes
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	Under construction
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1600, width: 1600	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1200, width: 1200	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).





Client they will cut the reinforcement to avoid the installtion distrunances.



This route (using Staircase) will be followed to carry Small items.






Staircase Details



Meter Box

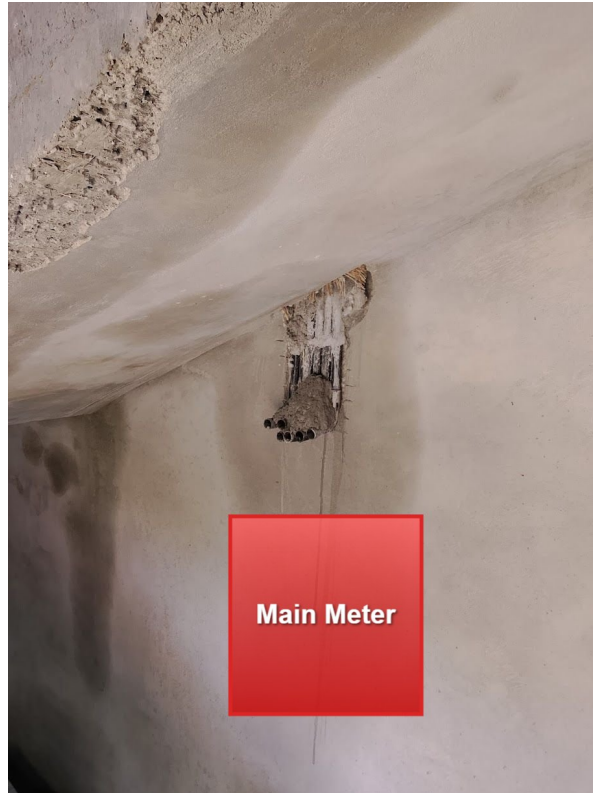

Main Meter is not yet installed ,building is under construction

Material Storage



Proposed PV Area



Cable Routing








Make a hole to run the DC Cable , AC earthing cable up to the earth pit locaion








Equipment Location

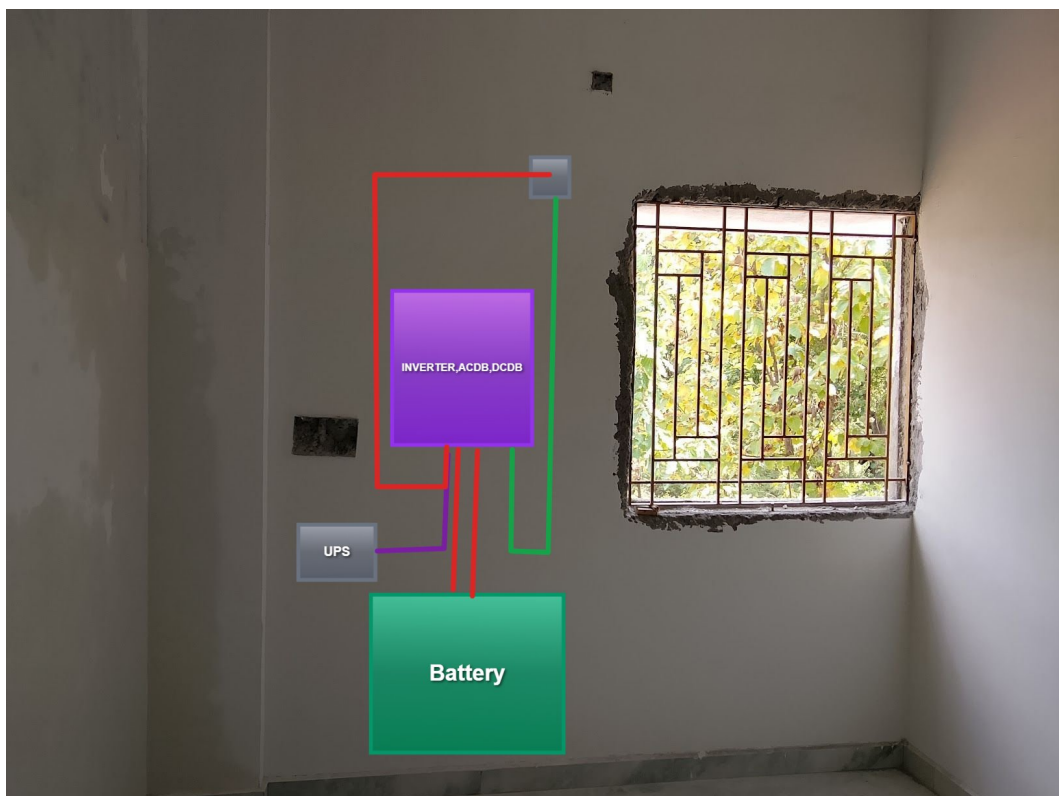




Earth Pit Location



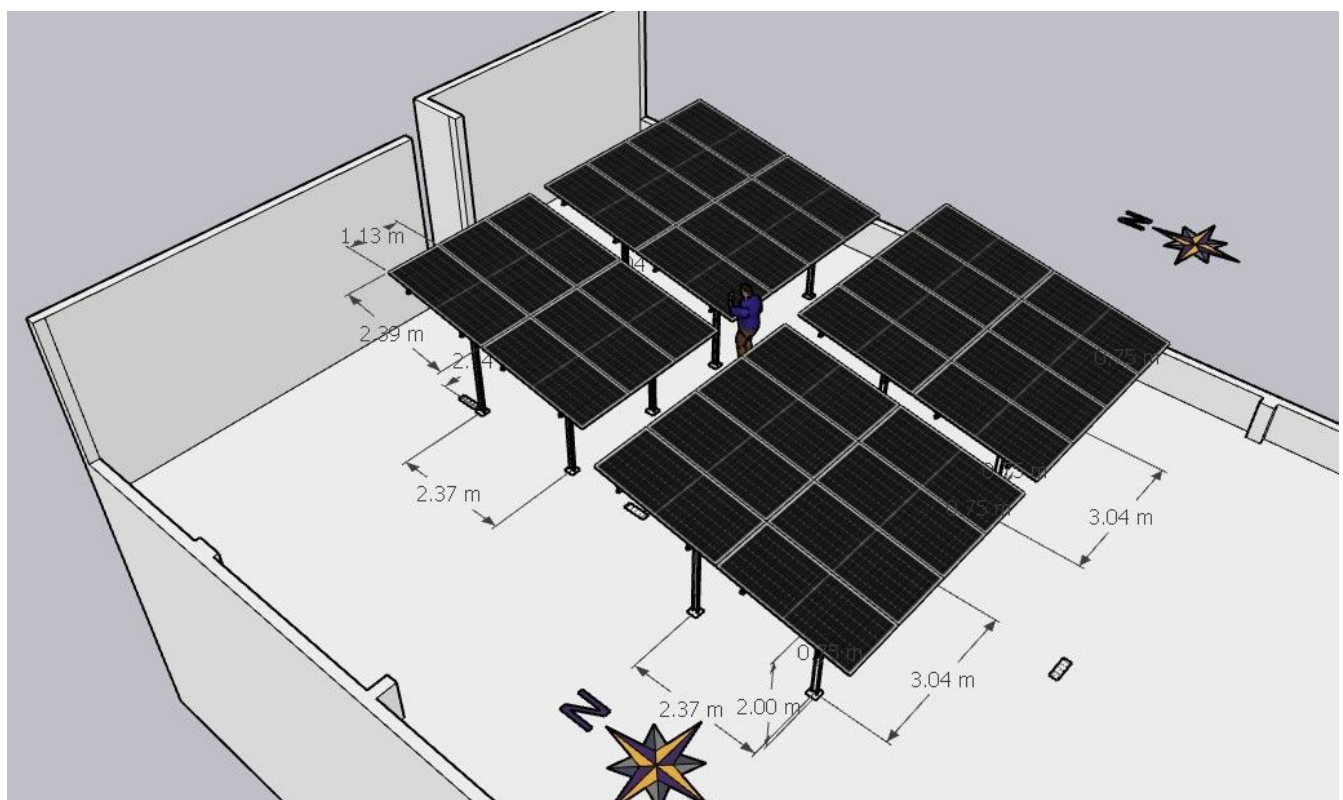

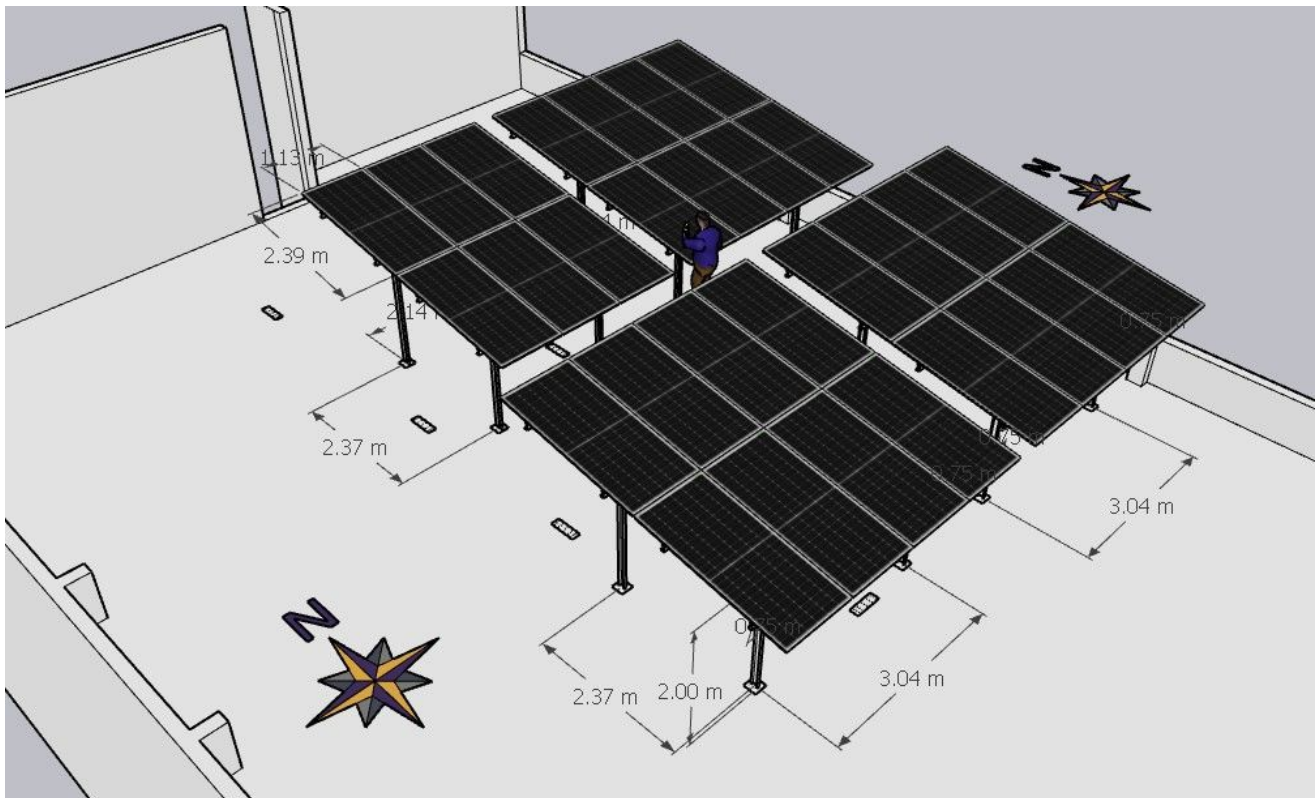

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	For installing the cables, conduit pipes, earthing pits is under our scope.

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	Ups point near the inverter location is under customer scope.
3	As per the site engineer and client suggestions only the panel layout,earthing,cable routing has been considered.
4	Main meter is not yet installed,the site is under construction.

THANK YOU

Dear Ravinder S Arya,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
