

Technical Site Visit Report

Prepared for: Gagan reddy_Odion Layout Woods of east_8.4kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0190
Project ID	18C22039
Project Name	Gagan reddy_Odion Layout Woods of east_8.4kWp_Hybrid
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	HARIOM PATEL
Site Address	Site 23&24, Phase 14, Odion Layout Woods of east, Chikkanayakanahalli, Sarjapur road, Bangalore - 560035.
GPS Coordinates	12.894561, 77.690876
Google Maps	https://www.google.com/maps?q=12.894561,77.690876
Visit Date	2026-08-18
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	Gagan reddy
Contact	+91 80504 15626

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	8.4
Sanction Load (kW)	10
Module Make & Capacity	Waaree Non DCR Topcon, 700 Wp
Module Length (mm)	2384

Module Width (mm)	1303
Number of Panels	12
Inverter Type	Hybrid (String)
Inverter Brand	Deye: 10KW - 48V - LV - Three Phase
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	A room is dedicatedly available on the 1st floor to house the ACDB, DCDB, INVERTER & BATTERIES.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, discussed with the customer and finalised the location for earthing.	-
6	Where is the Internet Router located?	Not yet installed. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	7	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	The MS structure will be fabricated at the premises by the customer. Alu. Mini Rails (for Elevated MS Structure) will be supplied by ECOSUCH.
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	The customer has provided the linking pipes at each floor to pull the cables from top to bottom in connection with the system installation.
13	What is the height of the building and how many floors does it have?	12 Metres. (G + 2 + Head room)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	-
2	Is the Meter cubicle photo matching with the previous answer?	No	LT panel not yet installed. Under construction.
3	Has the termination point in the Main meter panel been identified?	No	LT panel not yet installed. Under construction.
4	Is the Termination Point easily visible or sealed?	-	LT panel not yet installed. Under construction.
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	LT panel not yet installed.



#	Question	Answer	Notes
			<i>Under construction.</i>
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	<i>LT panel not yet installed. Under construction.</i>
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>Yes, enough space is available at the entrance near the LT panel location on the ground floor.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	No	<i>The LA can be installed on the water tank tower.</i>
13	In case of elevated structures, is it with or without grouting?	With Grouting	<i>The MS structure will be fabricated at the premises by the customer.</i>
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	The MS structure will be fabricated at the premises by the customer.	-
18	Is ventilation available in the battery location?	No	<i>The provision for ventilation will be arranged by the customer. The room is under construction.</i>
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1500, width: 1500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 5000, width: 2000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable

Site Layout - Top View

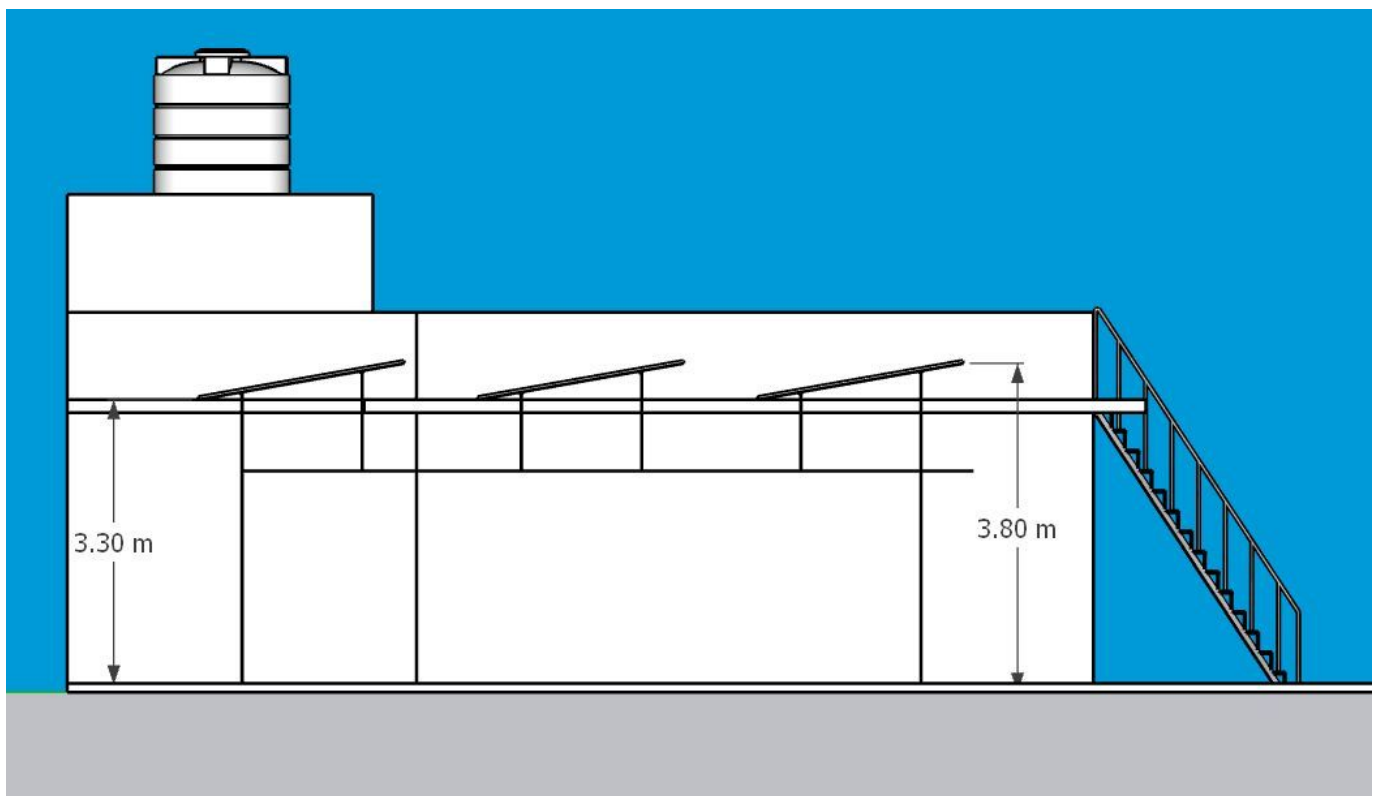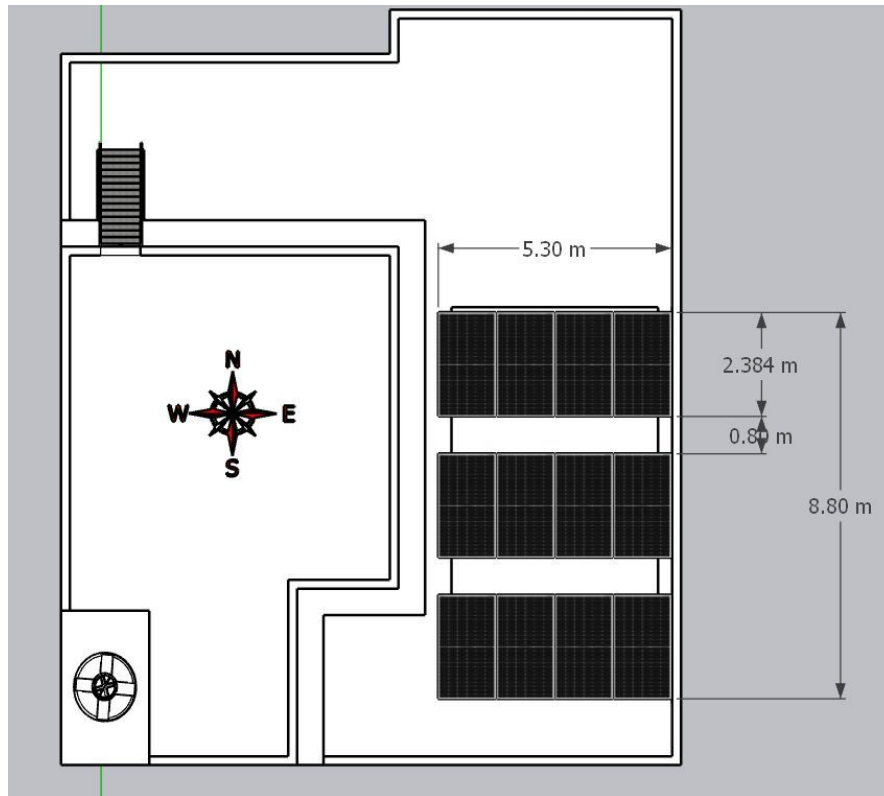

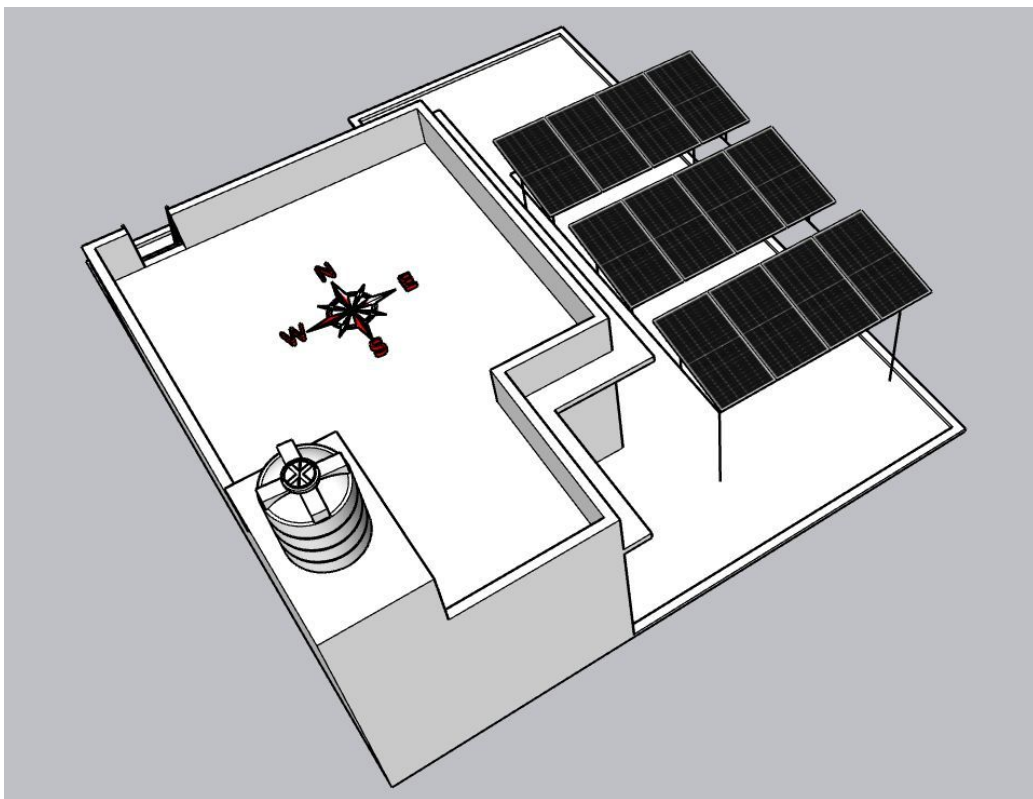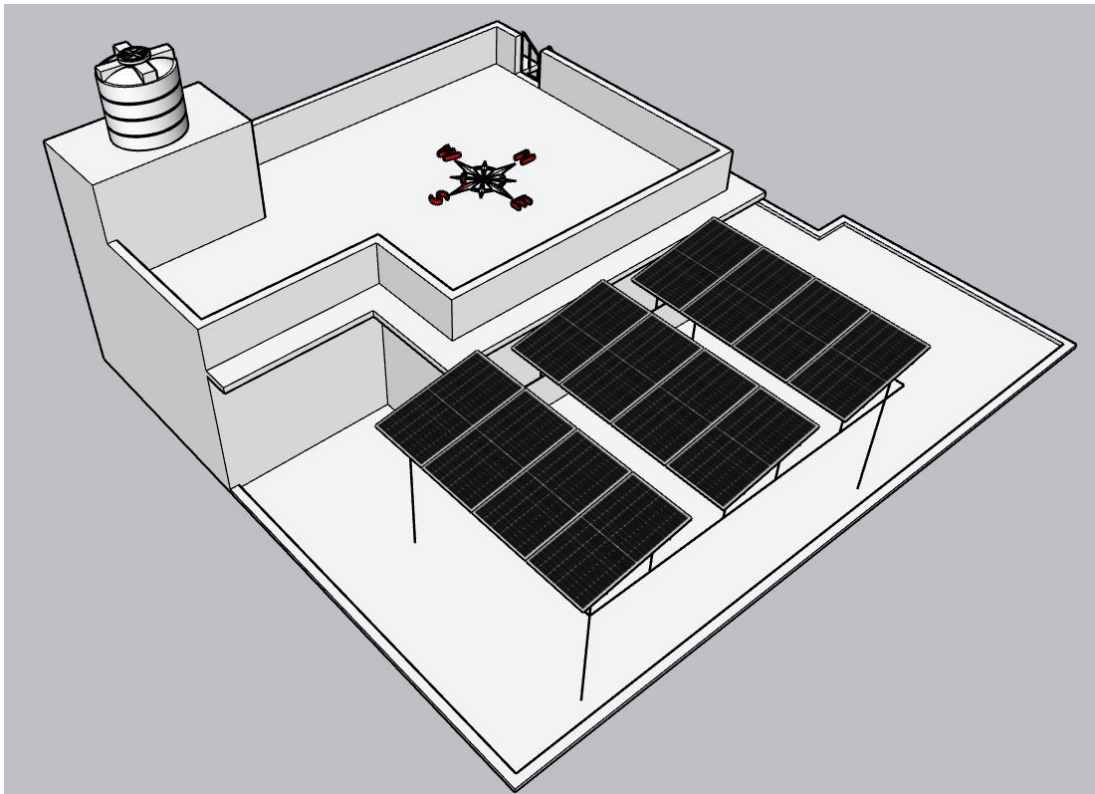

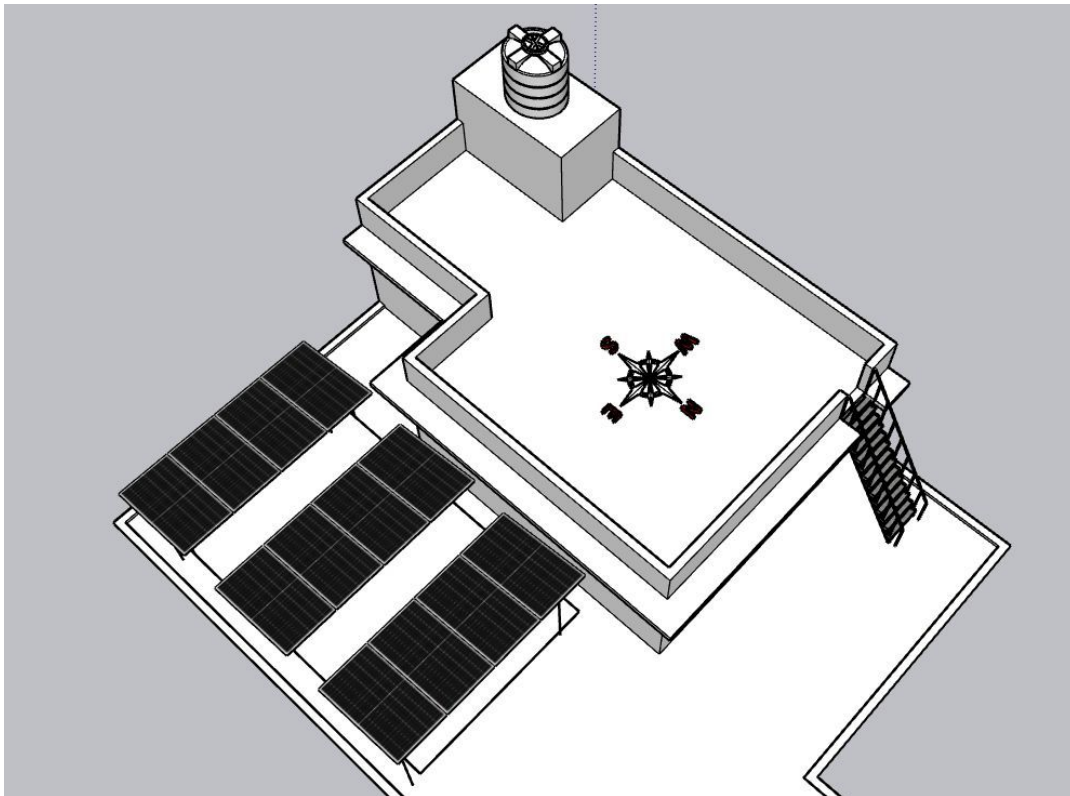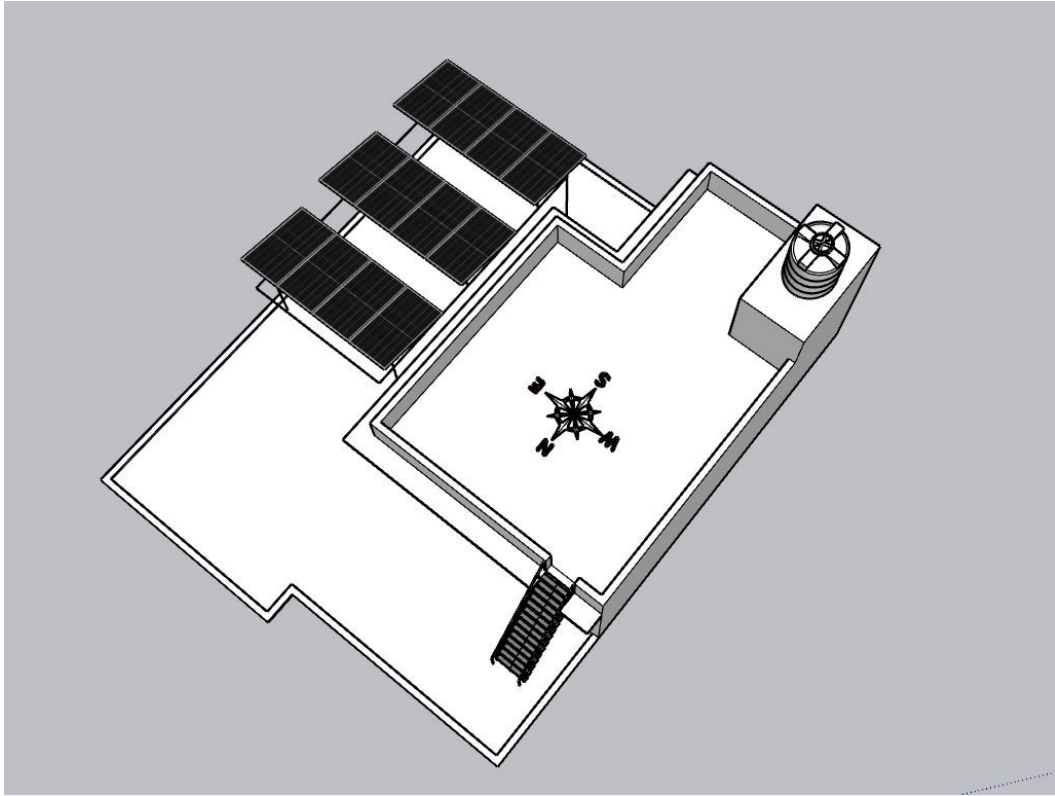

Building Exterior



Material Delivery Route



The materials can be shifted to the terrace via two options available at the site. Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



Materials moving towards the stairs.



The materials can follow the stairs until reaching the 2nd floor terrace.




The materials entering into the open terrace area can be stacked here before shifting to the upper terrace.

Staircase Details



Staircase width: 1000 mm

Proposed PV Area

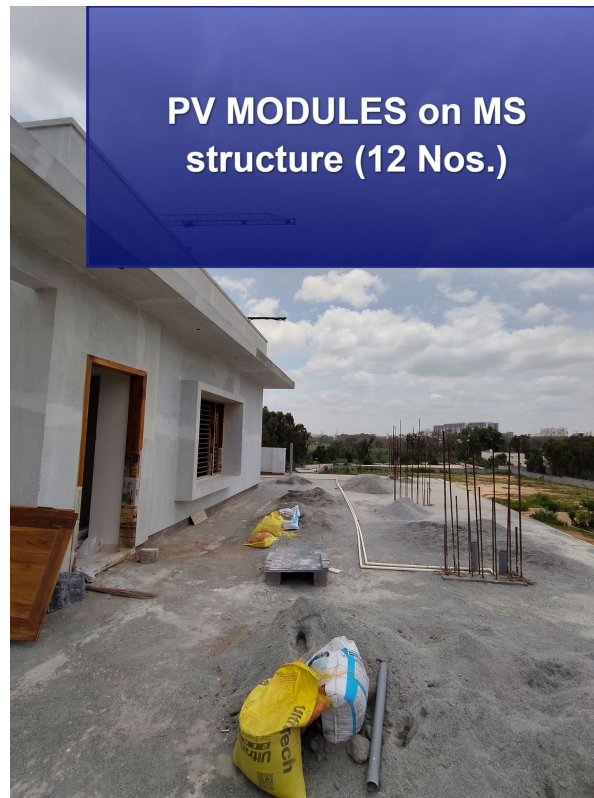

Cable Routing



LA can be mounted on the upper tank tower. The LA earthing cable has to be bring to the terrace along the solar structure columns.



The LA earthing cable, DC earthing cable & solar DC power cables can be pulled from top to bottom through a 40mm dia PVC pipe provided by the customer.



The cables are running via the pipe from terrace to the 2nd floor.



The cables continue running via the pipe from 2nd floor to the 1st floor.



The solar DC power cable will be re-directed to the inverter room via 25mm PVC conduit & the AC earthing cable from the inverter room will be bringing back to this point. All the 3 earthing cables together are allowed to run via the 40mm PVC pipe till reaching the ground floor.



A dedicated inverter room is available in the 1st floor for solar system setup.



All the 3 earthing cables after reaching the ground floor via the 40mm PVC pipe will be moved towards the respective earth pits dug at the front garden near the LT panel location.



All the 3 earthing cables can be terminated at the respective earth pits allocated.

Meter Box



LT panel not yet installed. Under construction.

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 8.4kWp On-grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the Enphase Accessories box location.
2	Supplying an MS-made structure in accordance with the ECOSOCH design.

THANK YOU

Dear Gagan reddy,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
