

## Technical Site Visit Report

Prepared for: Nayan Ambali\_Non\_Subsidy\_4.84kWp\_Hybrid - #509,4th E Cross

### PROJECT INFORMATION

|                 |                                                                                                                                                     |
|-----------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0102                                                                                                                                       |
| Project ID      | 3A25FA2C                                                                                                                                            |
| Project Name    | Nayan Ambali_Non_Subsidy_4.84kWp_Hybrid                                                                                                             |
| Building Name   | #509,4th E Cross                                                                                                                                    |
| Billing Name    | Nayan Ambali_Non_Subsidy_4.84kWp_Hybrid                                                                                                             |
| Project Sector  | Residential                                                                                                                                         |
| Project Type    | With Subsidy                                                                                                                                        |
| Sales Lead      | Mahantayya                                                                                                                                          |
| Site Address    | Nayan Ambali #509, 4th E Cross HRBR layout, II block Kalyan Nagar Bengaluru - 560043                                                                |
| GPS Coordinates | 13.02387641246595, 77.64151377032137                                                                                                                |
| Google Maps     | <a href="https://www.google.com/maps?q=13.023876412465947,77.64151377032137">https://www.google.com/maps?q=13.023876412465947,77.64151377032137</a> |
| Visit Date      | 2026-04-30                                                                                                                                          |
| Visited By      | Sai                                                                                                                                                 |
| Revision        | Rev 3                                                                                                                                               |

### CLIENT INFORMATION

|             |              |
|-------------|--------------|
| Client Name | Nayan Ambali |
| Contact     | 95919 96042  |

### PROJECT DETAILS

|                           |                             |
|---------------------------|-----------------------------|
| Solar Rooftop System Type | Hybrid                      |
| System Capacity (kWp)     | 4.84                        |
| Sanction Load (kW)        | 5                           |
| Module Make & Capacity    | Premier DCR bifacial 605 Wp |

|                                |                         |
|--------------------------------|-------------------------|
| Module Length (mm)             | 2382                    |
| Module Width (mm)              | 1134                    |
| Number of Panels               | 08                      |
| Inverter Type                  | Hybrid (String)         |
| Inverter Brand                 | Deye 5kW 1 phase Hybrid |
| Number of Inverters            | 01                      |
| Battery                        | Needed                  |
| Number of Batteries            | 01                      |
| Capacity of each Battery (kWh) | 5.12                    |
| Battery Model No.              | Deye SE-F5plus          |
| Mounting Structure Type        | RCC Flat Roof           |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                                                | Notes |
|---|----------------------------------------------------------------------------|-----------------------------------------------------------------------|-------|
| 1 | Can the delivery van/truck reach the material unloading point?             | Yes                                                                   | -     |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | No                                                                    | -     |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | Inverter, DCDB, ACDB, Battery is located near the ground floor.       | -     |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | No                                                                    | -     |
| 5 | Did you discuss the location of the earth pits with the customer?          | Earth pits are located near the ground floor (toward south direction) | -     |
| 6 | Where is the Internet Router located?                                      | customer scope                                                        | -     |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | N/A                                                                   | -     |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                                                   | -     |

### Roof Details

| # | Question                                                                         | Answer        | Notes |
|---|----------------------------------------------------------------------------------|---------------|-------|
| 1 | What type of roof is present at the site?                                        | RCC Flat Roof | -     |
| 2 | Are there any obstructions on the roof that could affect the solar installation? | No            | -     |

| #  | Question                                                                                                 | Answer                                             | Notes                    |
|----|----------------------------------------------------------------------------------------------------------|----------------------------------------------------|--------------------------|
| 3  | What is the angle of the panels? (in degrees)                                                            | 10                                                 | -                        |
| 4  | In case of sloped roof, what is the slope angle of the roof? (in degrees)                                | N/A                                                | -                        |
| 5  | On how many roofs at the site are we installing solar?                                                   | 01                                                 | -                        |
| 6  | If it is a Tiled roof, what is underneath the tiles?                                                     | N/A                                                | -                        |
| 7  | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?                     | N/A                                                | -                        |
| 8  | What type of mounting structure is planned?                                                              | Mini-rails                                         | MS fabrication structure |
| 9  | What is the orientation of the solar panels?                                                             | ["South"]                                          | -                        |
| 10 | How can the roof be accessed?                                                                            | Staircase                                          | -                        |
| 11 | Is the building currently under construction?                                                            | No                                                 | -                        |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | No                                                 | -                        |
| 13 | What is the height of the building and how many floors does it have?                                     | Height of the building is 12m, it has G+1+headroom | -                        |
| 14 | Is the site photo matching with the building description?                                                | Yes                                                | -                        |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                                                 | -                        |

## Residential / Electrical

| #  | Question                                                                                                | Answer                                                                | Notes                           |
|----|---------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------|---------------------------------|
| 1  | What type of energy meter is currently installed?                                                       | Phase: Three Phase, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999) | -                               |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes                                                                   | -                               |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes                                                                   | Building is under construction. |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible                                                               | Building is under construction. |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No                                                                    | -                               |
| 6  | Is space available for CT within Energy meter panel?                                                    | N/A                                                                   | -                               |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | N/A                                                                   | -                               |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A                                                                   | -                               |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | Yes                                                                   | -                               |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | N/A                                                                   | -                               |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | N/A                                                                   | -                               |
| 12 | In case of elevated structures, is an LA extension provided at the far end?                             | Yes                                                                   | -                               |
| 13 | In case of elevated structures, is it with or without grouting?                                         | N/A                                                                   | -                               |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                       | No                                                                    | -                               |

| #  | Question                                                                                          | Answer                                              | Notes |
|----|---------------------------------------------------------------------------------------------------|-----------------------------------------------------|-------|
| 15 | Are there any safety risks associated with accessing the roof for installation?                   | No                                                  | -     |
| 16 | Is space present in rooftop to store the panels?                                                  | Horizontally sleeping                               | -     |
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin. | N/A                                                 | -     |
| 18 | Is ventilation available in the battery location?                                                 | Yes                                                 | -     |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                       | Inverters/ACDB/D CDB be installed on a wall mounted | -     |
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).                         | length: 400, width: 400                             | -     |
| 21 | Provide the dimension for earth pits location (L x W of available space).                         | length: 500, width: 499                             | -     |
| 22 | Is LAN cable under customer scope?                                                                | No                                                  | -     |
| 23 | Is there any shadow that affects the solar installation?                                          | No                                                  | -     |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location?                  | No                                                  | -     |

## PHOTO DOCUMENTATION

### Cable Routing Legend

| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|  | Proposed PV Module Array |
|  | Main Meter Location      |
|  | Solar Meter              |
|  | Battery                  |
|  | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |
|  | LA Pit                   |
|  | LA                       |

## Building Exterior



## Material Delivery Route





*This route will carry the small items*



*This route will carry the large items (like panels)*




## Staircase Details




## Meter Box



## Material Storage

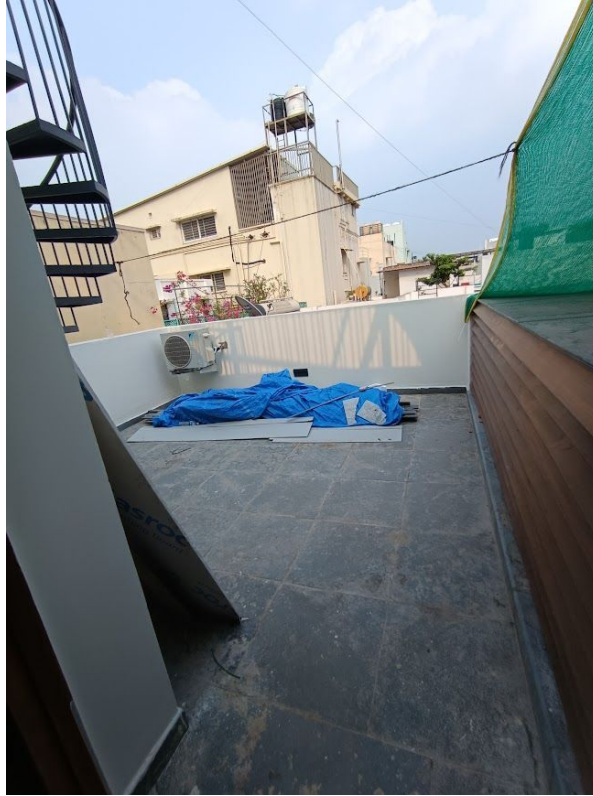


## Site Layout - Top View

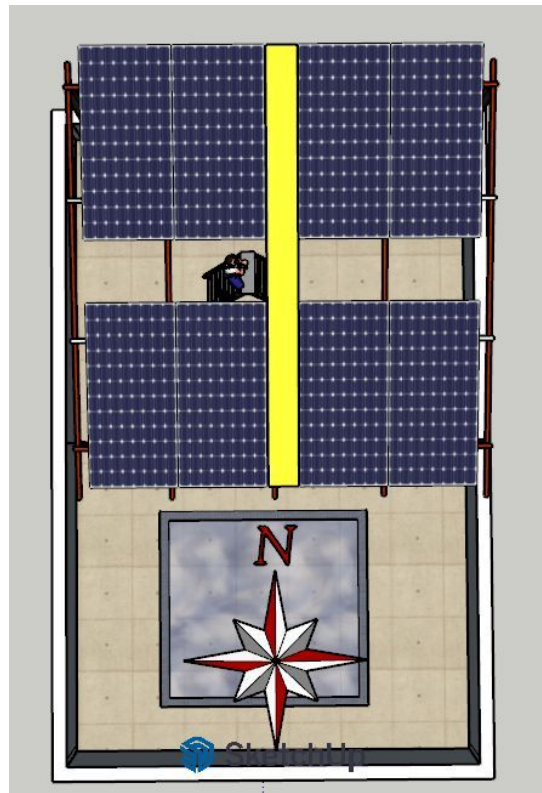


Top view




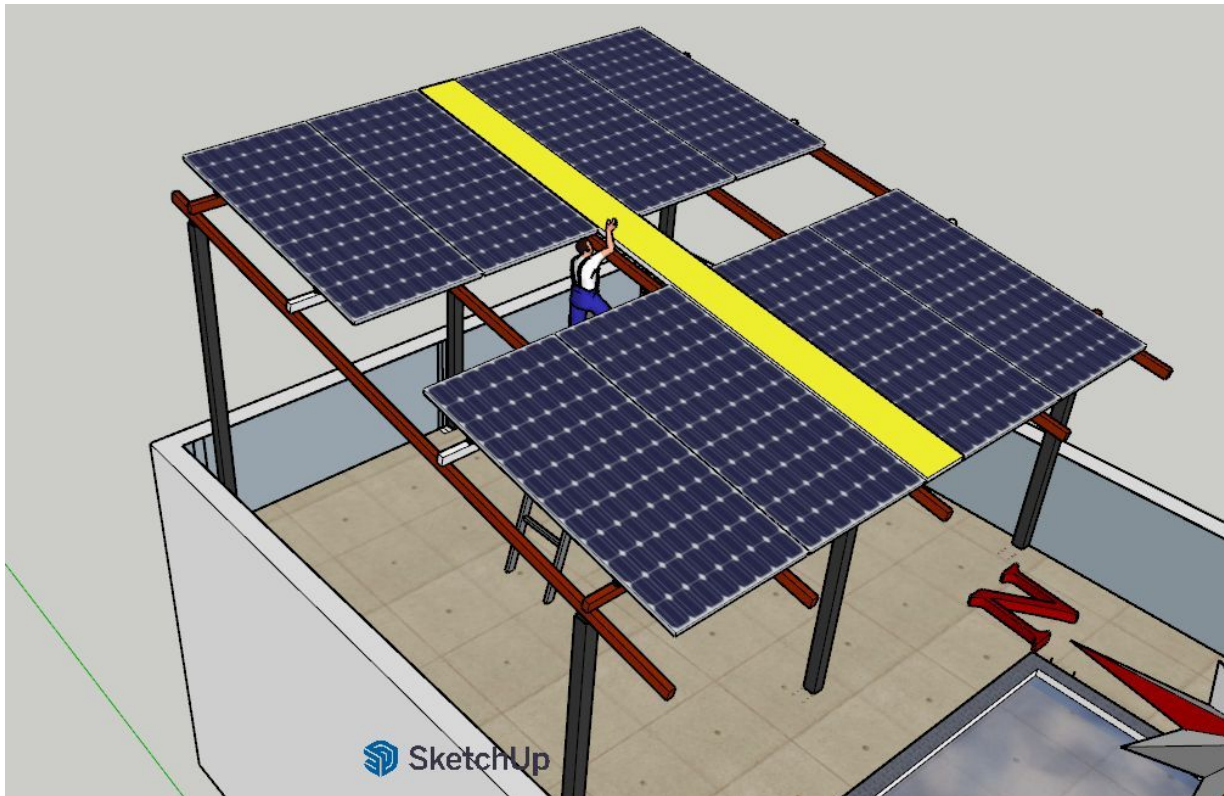


side view

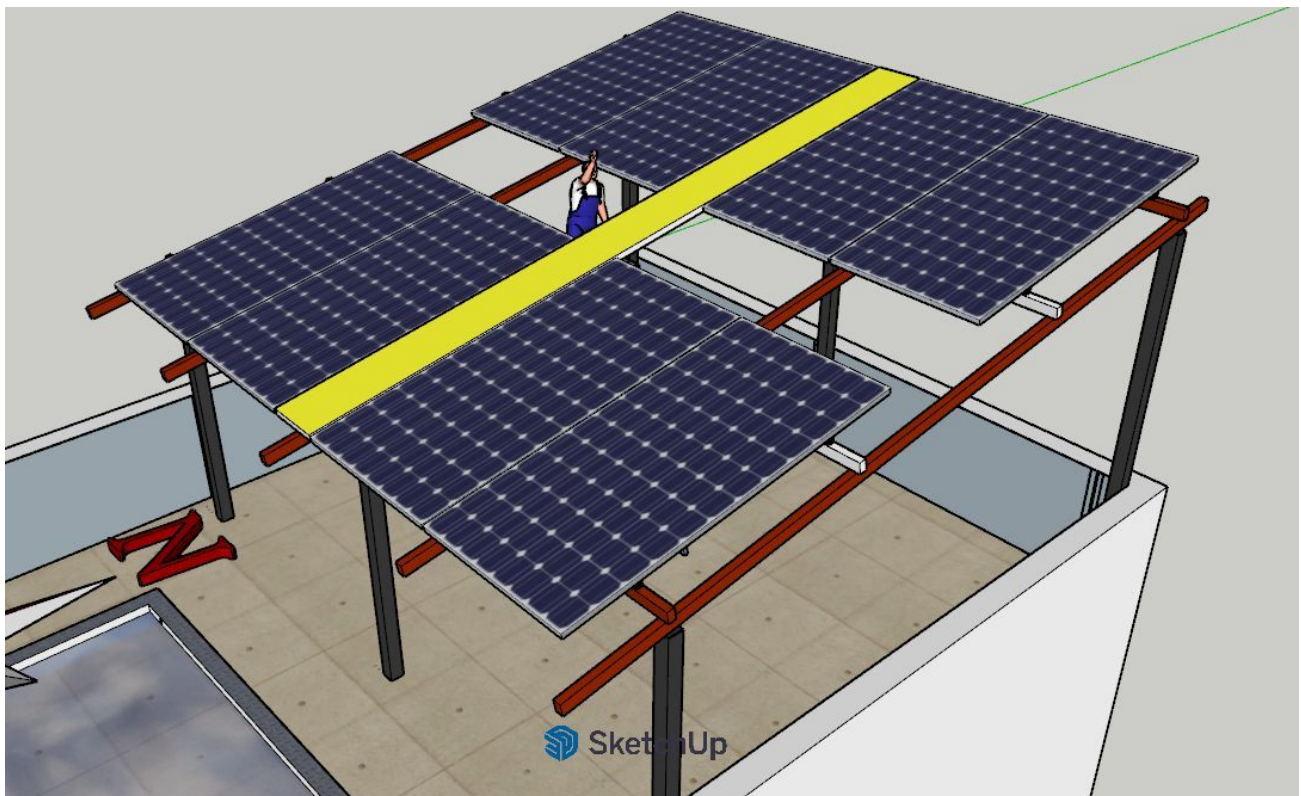


side view

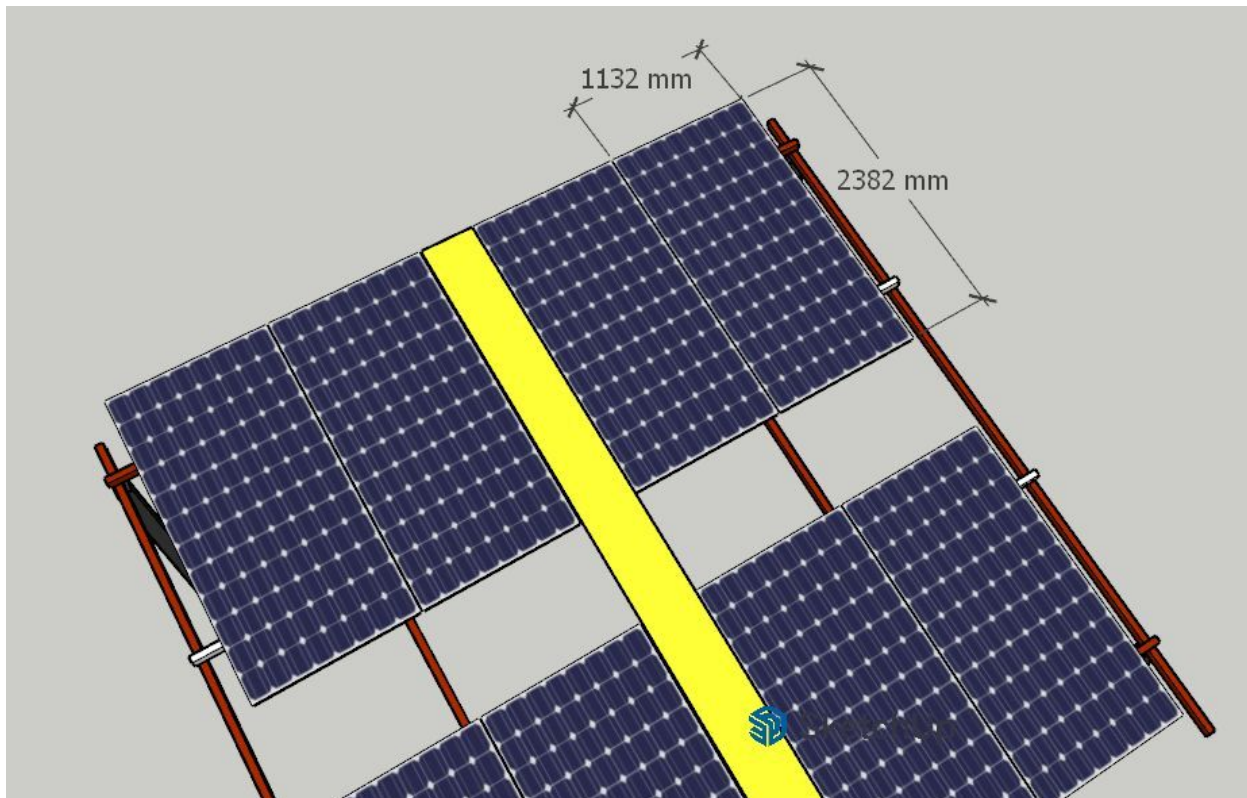

Panel dimension

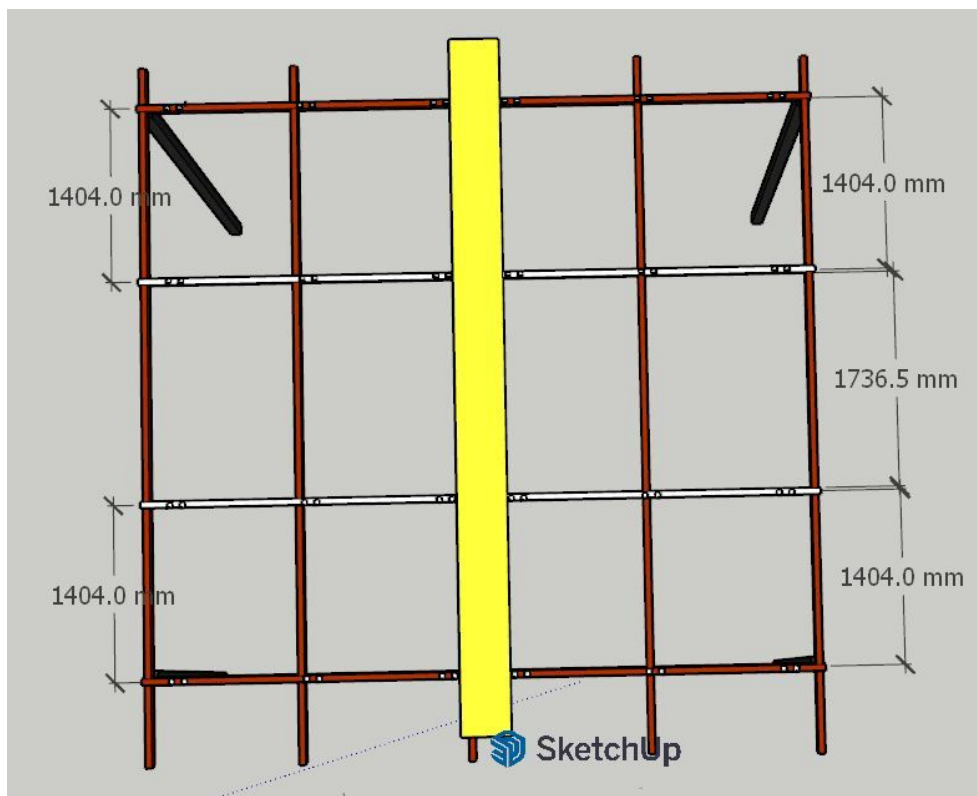

Structure details (1)

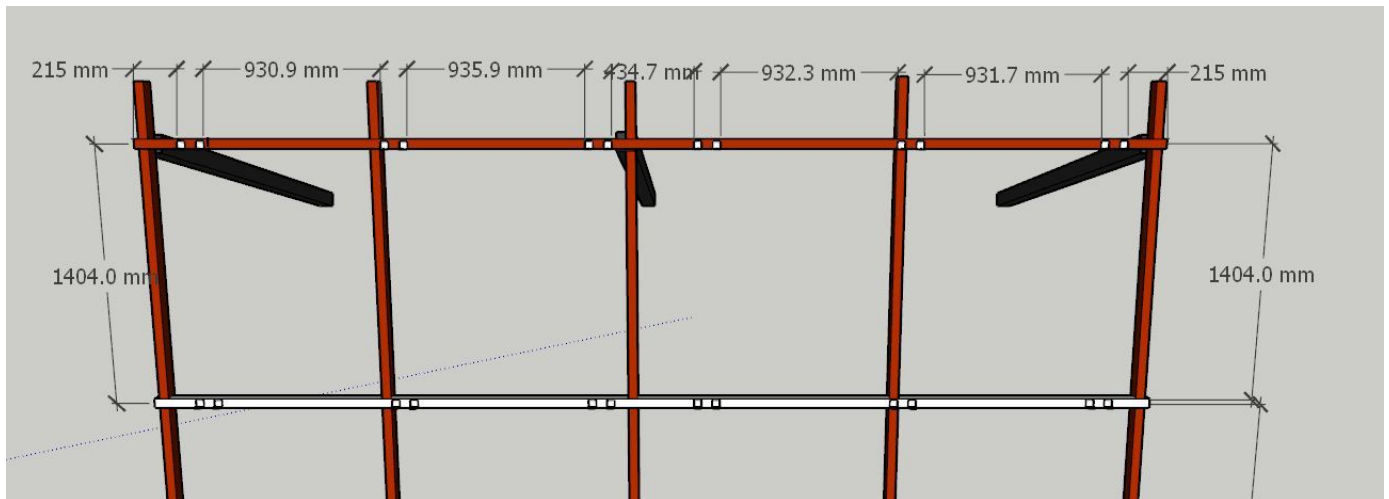


Structure details (2)




Structure details (3)




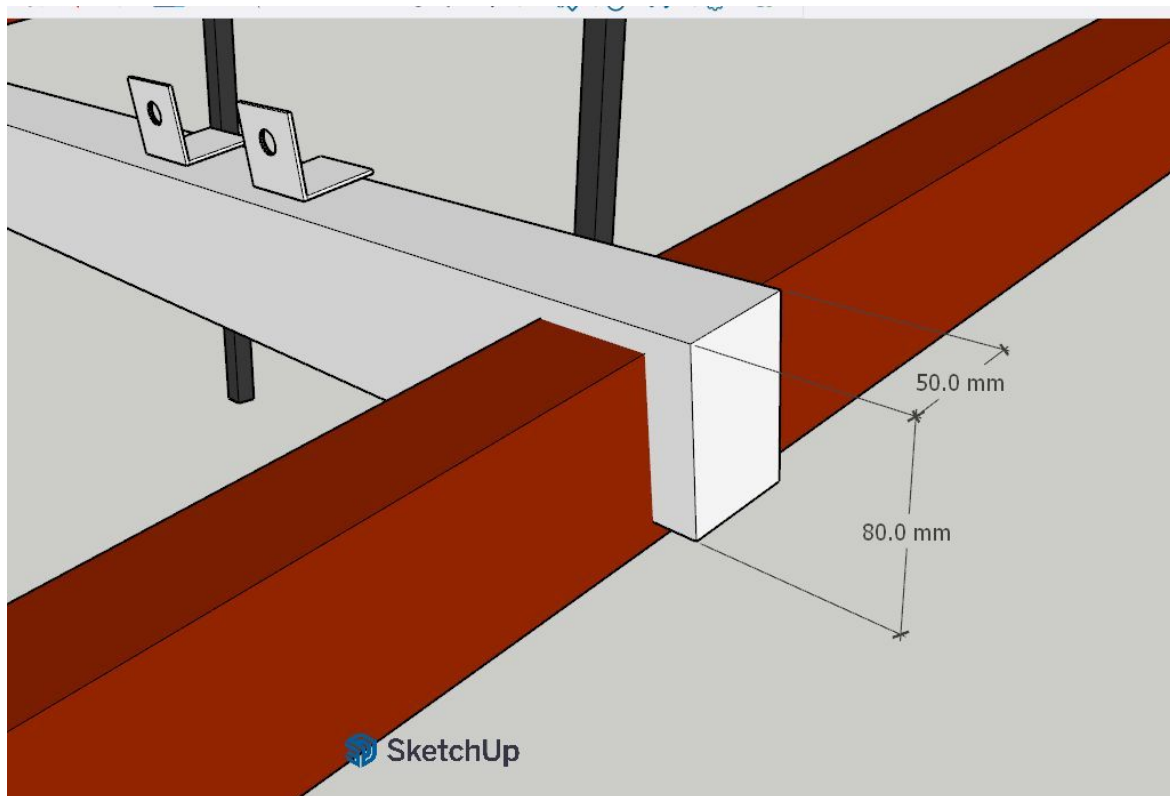

Structure details (4)

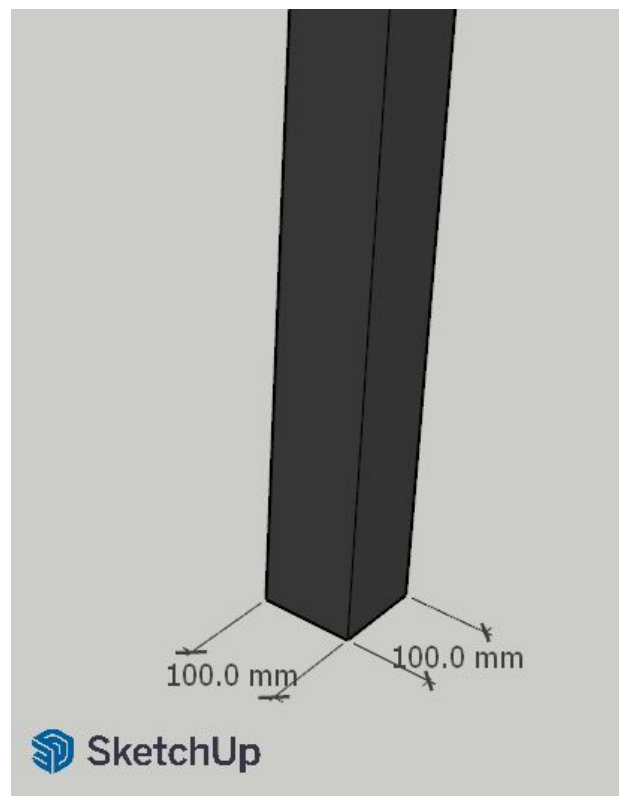

Structure details (5)

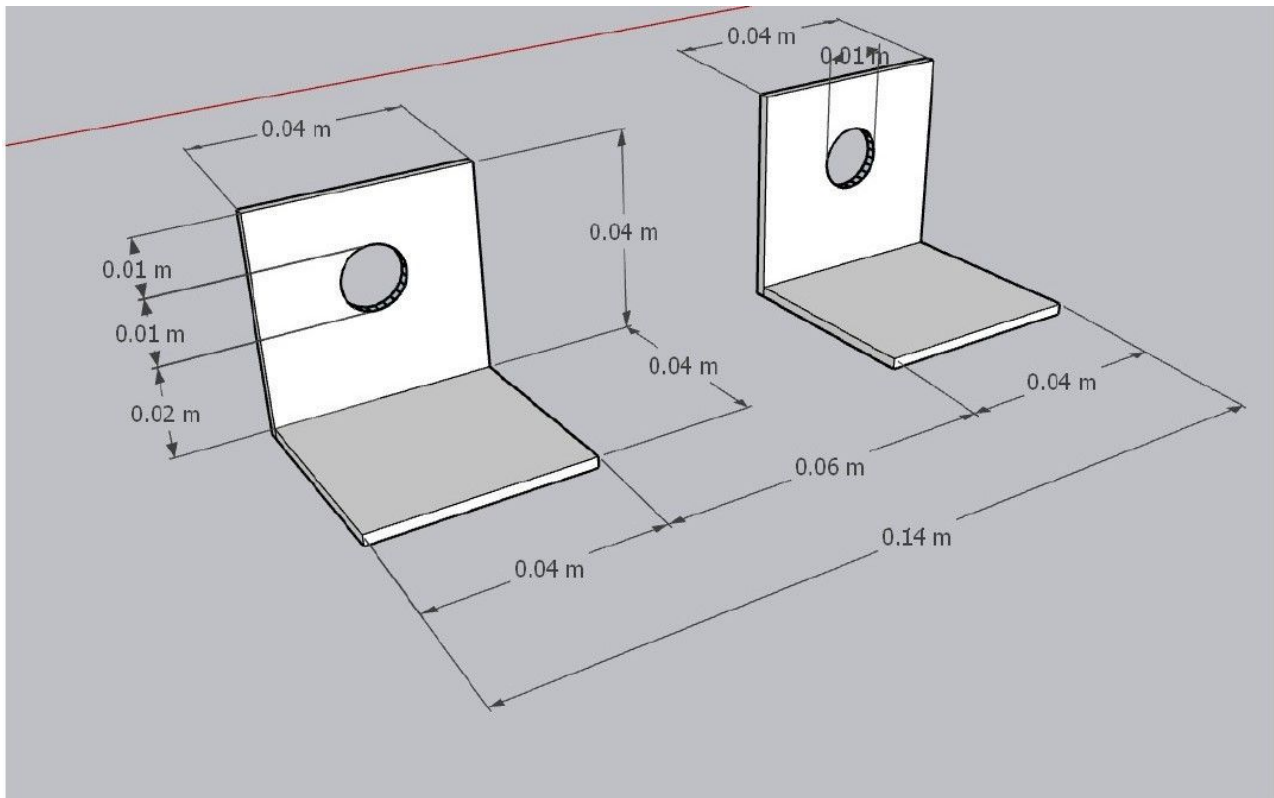

*L clamp dimension*


### Proposed PV Area






## Cable Routing




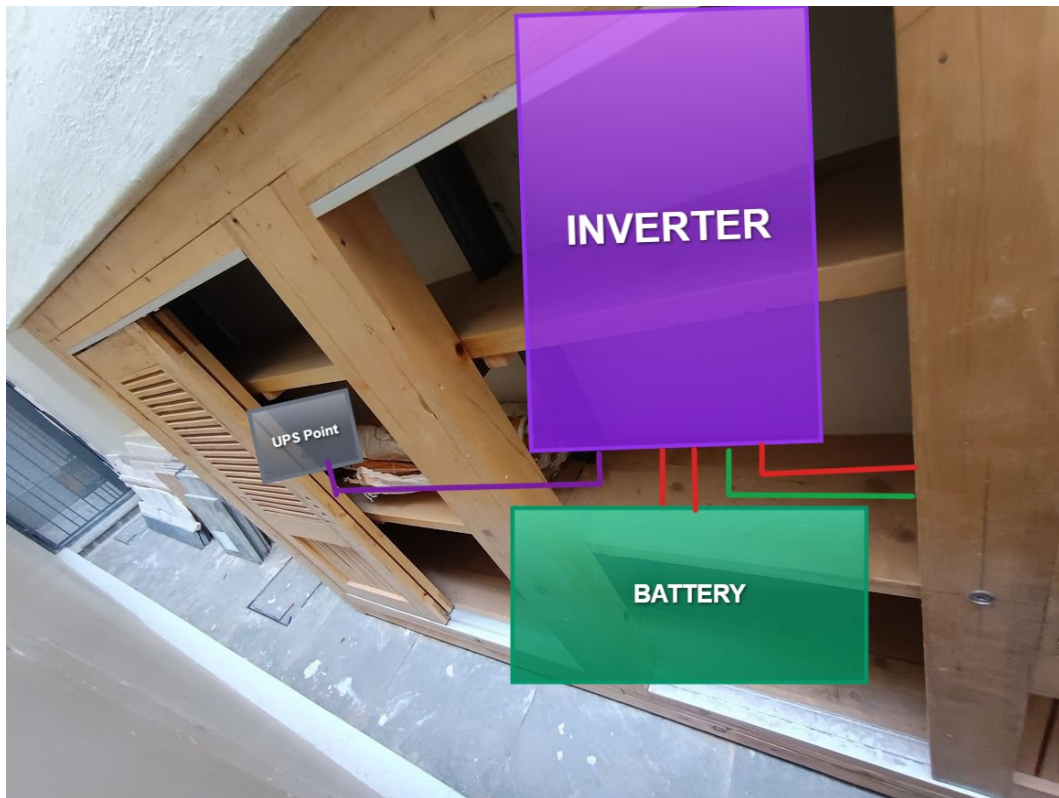



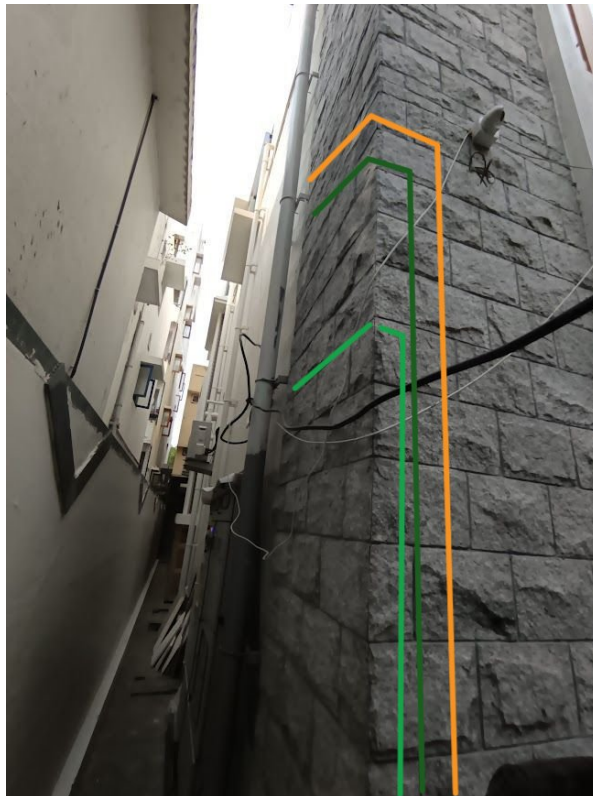

## Equipment Location

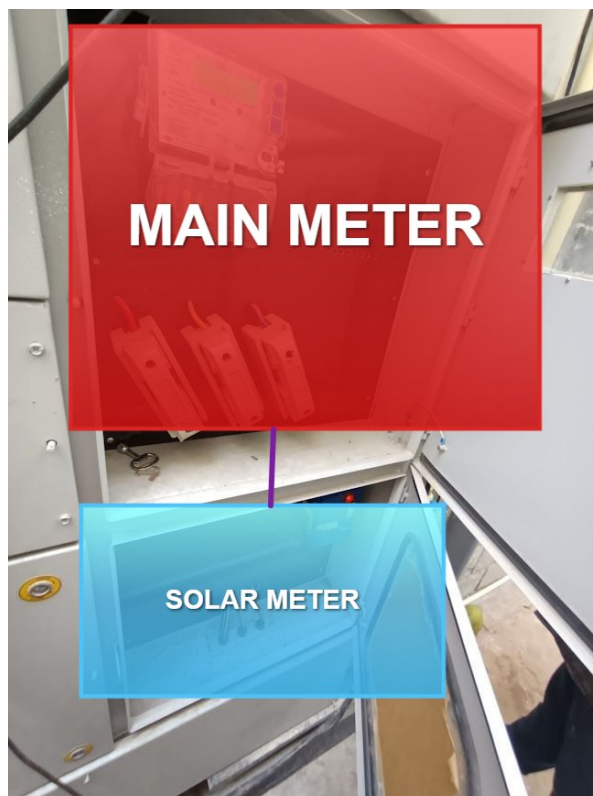

## Earth Pit Location



## OBSERVATIONS & RECOMMENDATIONS

### EcoSoch Scope

| # | Observation                                                                                                           |
|---|-----------------------------------------------------------------------------------------------------------------------|
| 1 | As per the customer suggestion, routing, cable earthing, inverter location and also solar meter have been considered. |

### Customer Scope

| # | Observation                                                                    |
|---|--------------------------------------------------------------------------------|
| 1 | Wi-Fi upto solar meter is under customer scope                                 |
| 2 | UPS point near the inverter location is under customer scope                   |
| 3 | MS fabrication is under customer scope                                         |
| 4 | At the time of installation wooden partition has to be removed by the customer |



## THANK YOU

Dear Nayan Ambali,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
