

Technical Site Visit Report

Prepared for: Amrendra kumar_Cascading Meadows Villa Non Subsidy_6.1kWp_Optimizer - House No - 55

PROJECT INFORMATION

Report Number	ESV-2026-0224
Project ID	LYWHZHVI
Project Name	Amrendra kumar_Cascading Meadows Villa Non Subsidy_6.1kWp_Optimizer
Building Name	House No - 55
Billing Name	Amrendra kumar_Cascading Meadows Villa Non Subsidy_6.1kWp_Optimizer
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju
Site Address	House No - 55, Cascading Meadows ph-2, Maragondanahalli Road, Anandpura, T C Palya, K R Puram, Bangalore - 560036
GPS Coordinates	13.0320902806438, 77.69667213040053
Google Maps	https://www.google.com/maps?q=13.032090280643798,77.69667213040053
Visit Date	2026-10-05
Visited By	Sai
Revision	Rev 0

CLIENT INFORMATION

Client Name	Amrendra kumar
Contact	9008483121

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	6.15
Sanction Load (kW)	17

Module Make & Capacity	Premier bifacial Non DCR 610 Wp
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	10
Inverter Type	SolarEdge
Inverter Brand	Solaredge 5kW 3 phase optimizer
Number of Inverters	1
Number of Optimizers	10
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Inverter, DCDB, ACDB is located below the terrace area.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Earth pits are located near the ground floor (utility area).	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: Syntex water tank and the heat pump could affect the solar installation.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-

#	Question	Answer	Notes
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	<i>MS fabrication is planned for this project.</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	<i>Existing conduit pipes available to run the AC cable till the main meter location.</i>
13	What is the height of the building and how many floors does it have?	Height of the building is 15m; it has G+2+Headroom.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>Existing DC, AC and LA pits are available in the utility area.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally	-

#	Question	Answer	Notes
		sleeping	
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Inverters/ACDB/DCDB be installed on a wall mount.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 550, width: 300	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 300, width: 300	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Building Exterior



Material Delivery Route



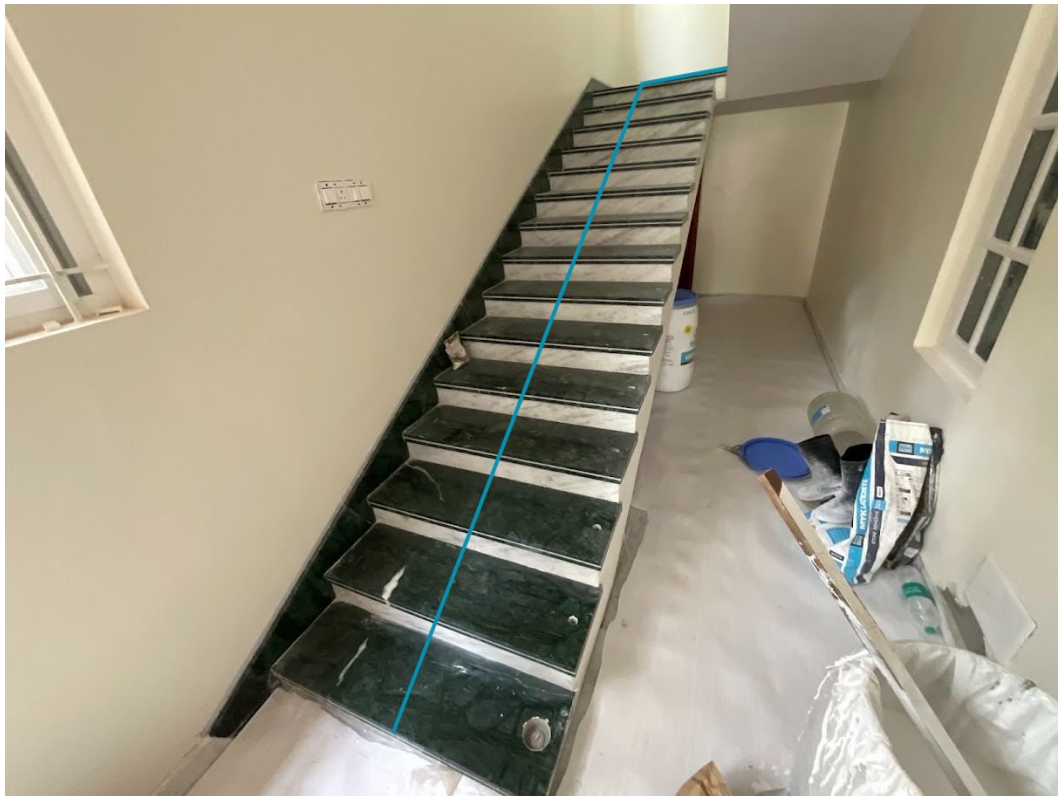

This route will carry the small items



This route will carry the large items (like panels)

Staircase Details




Meter Box




Material Storage




Site Layout - Top View

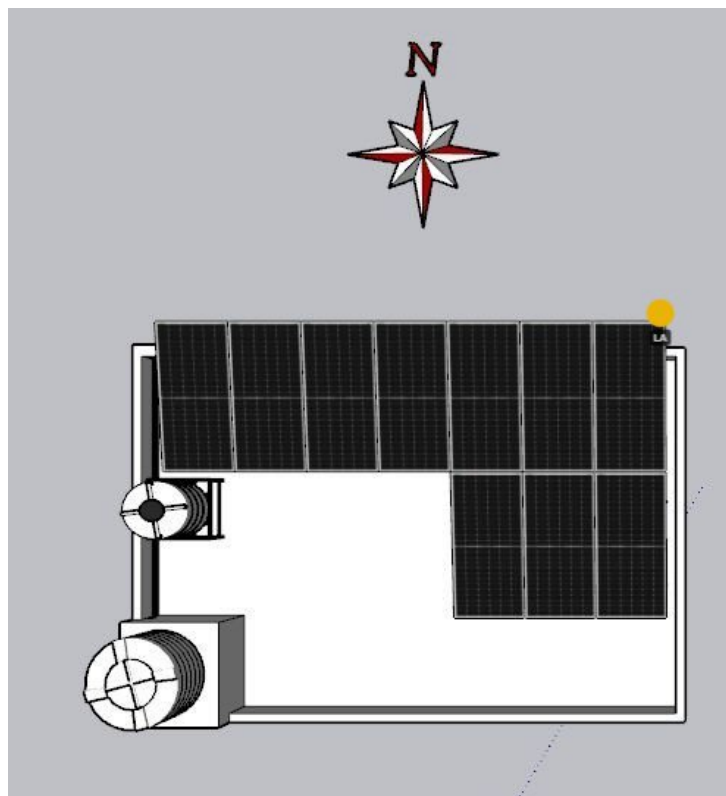


Top view

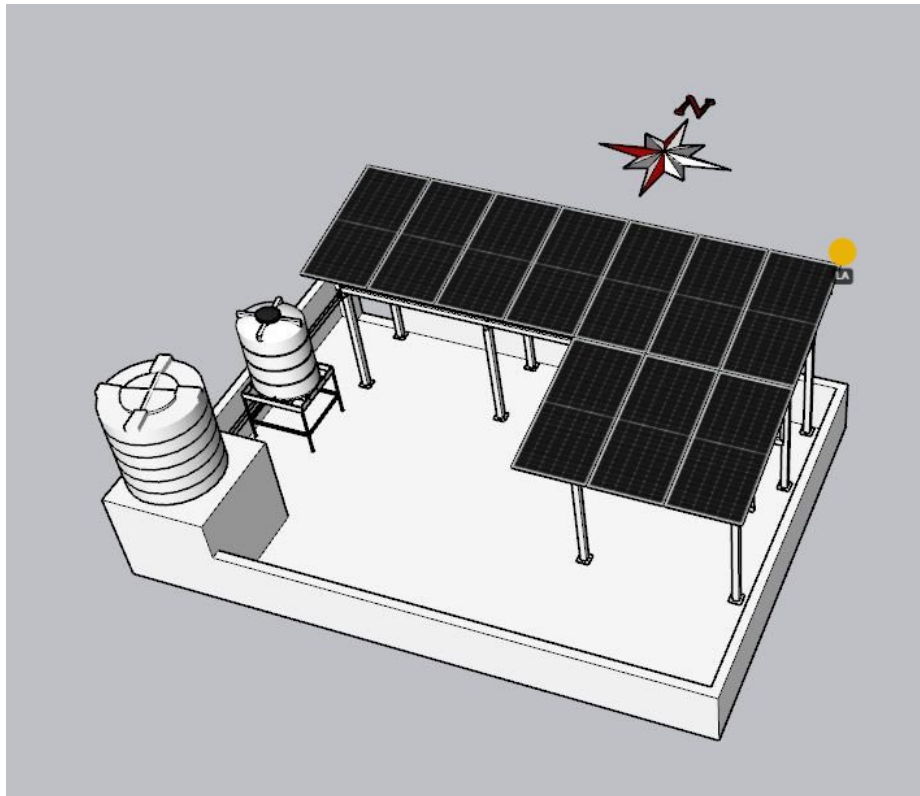


Side view (1)

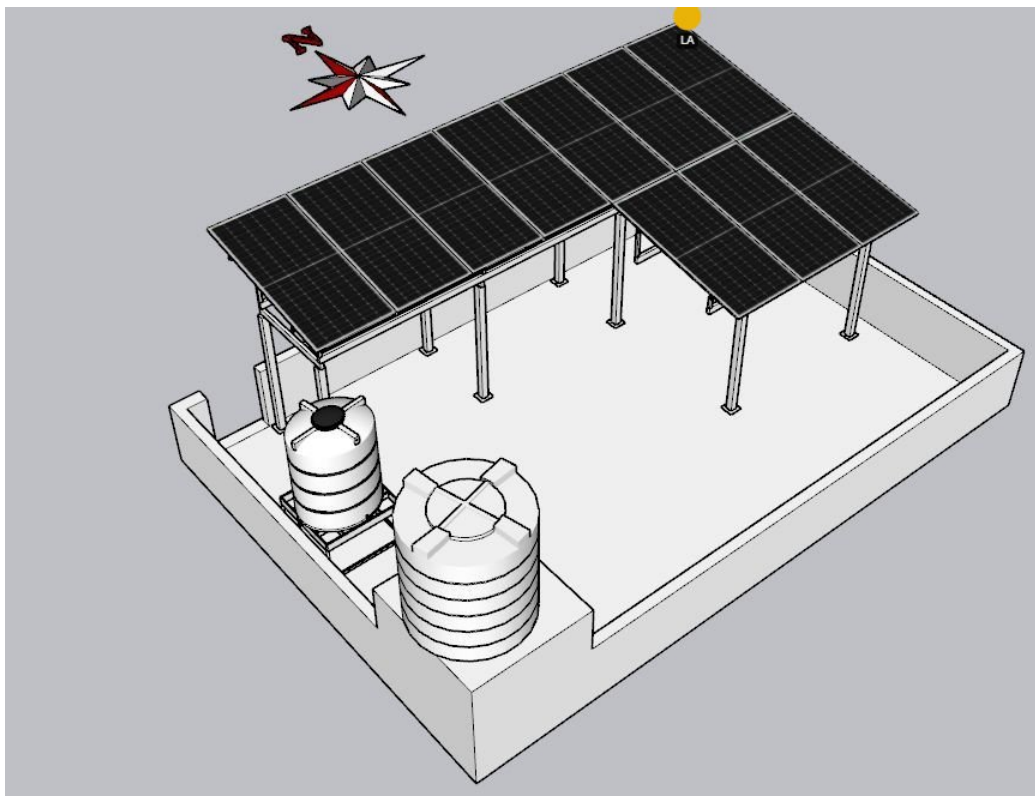


Side view (2)

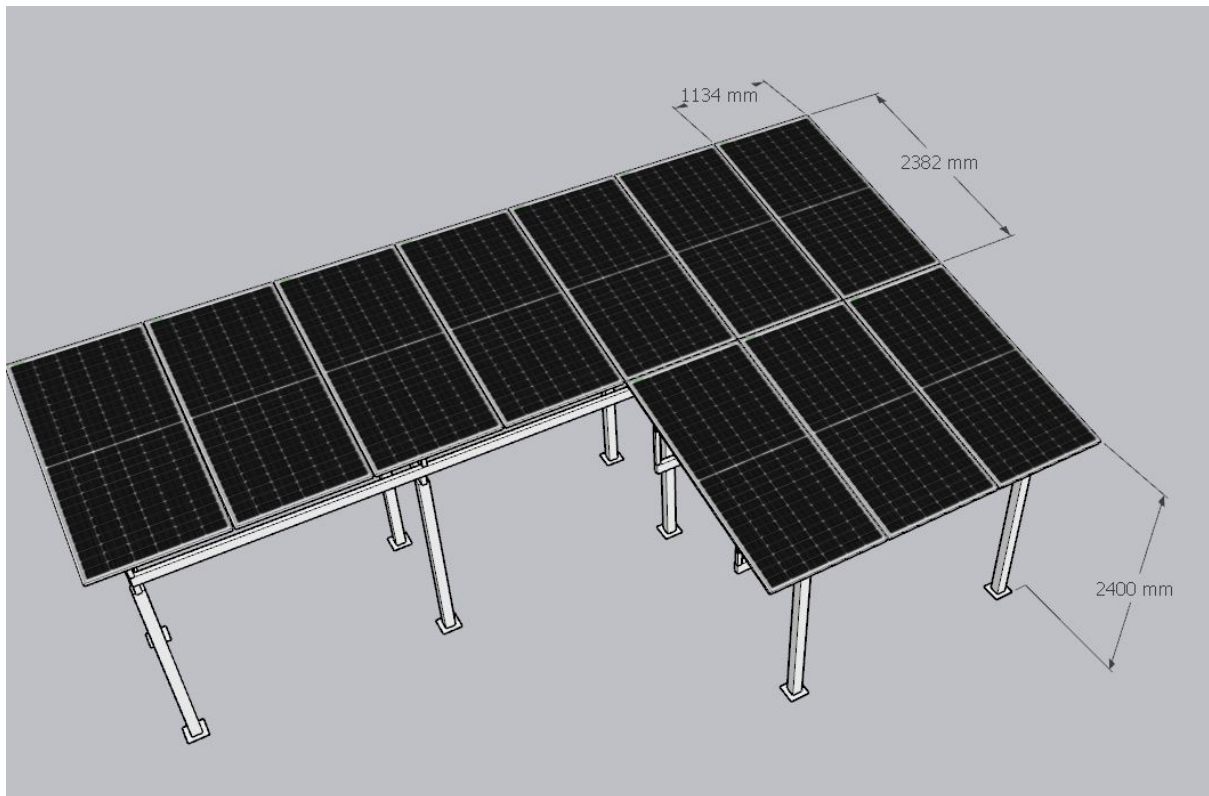


Panel dimensions

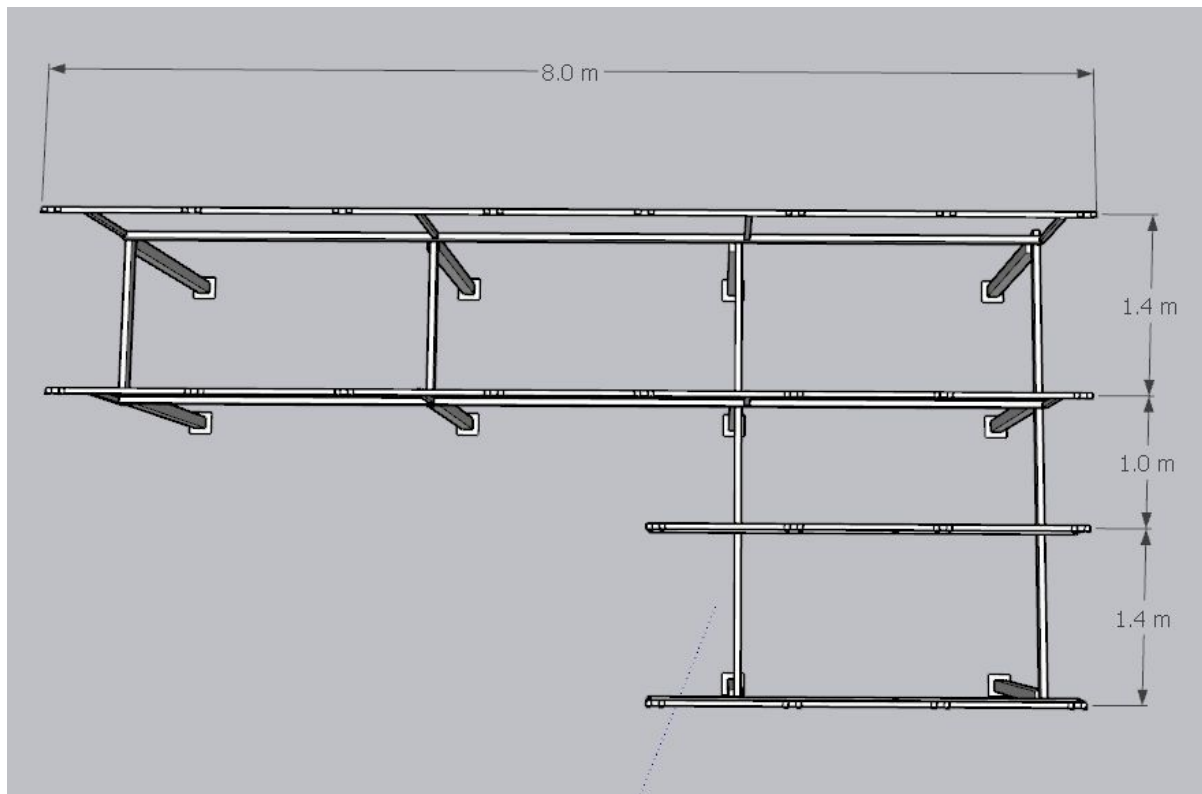


Structure details (1)

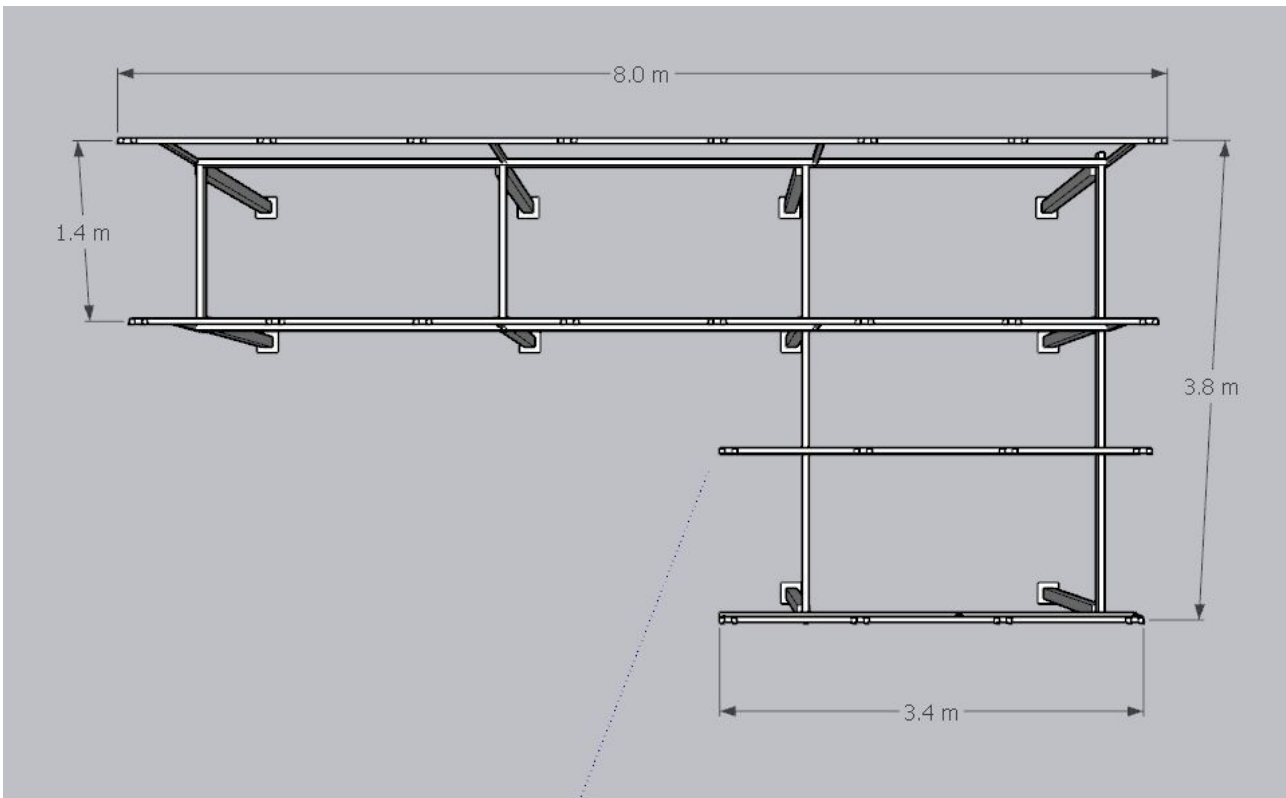


Structure details (2)

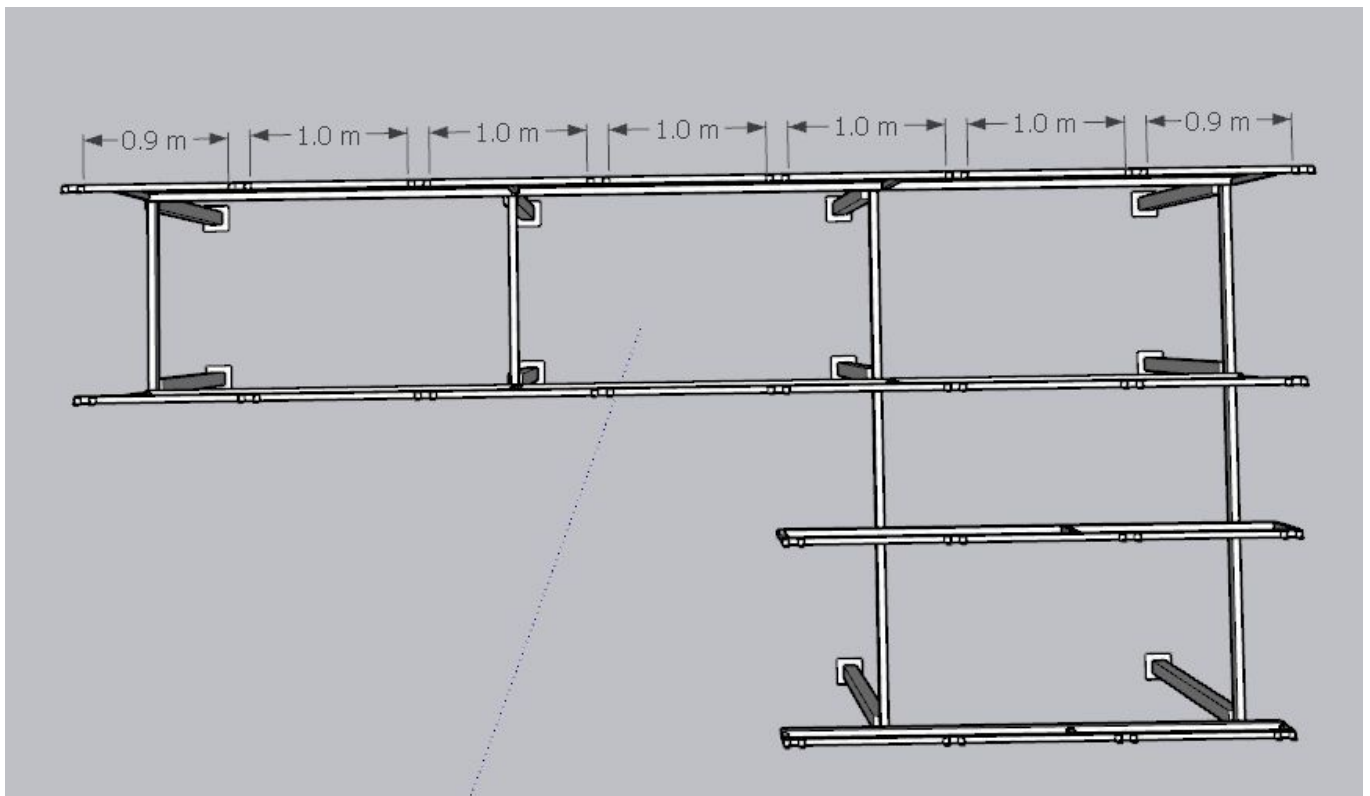


Structure details (3)

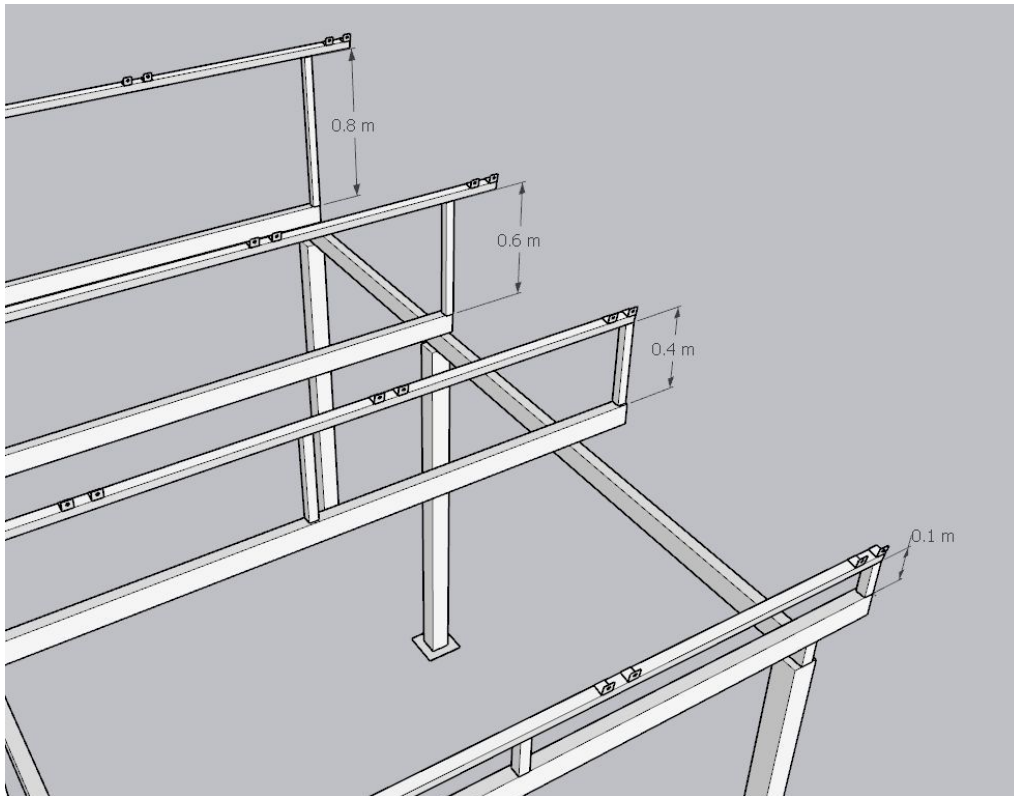


Structure details (4)

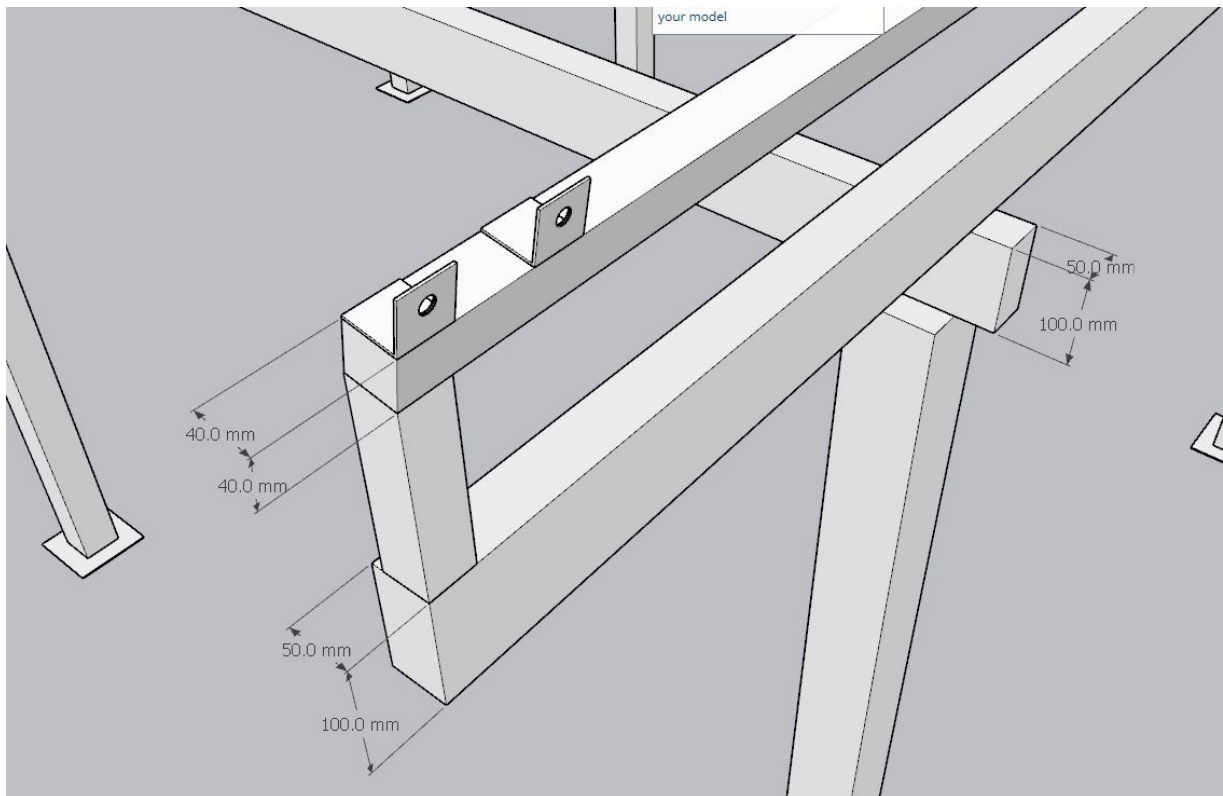


Structure details (5)

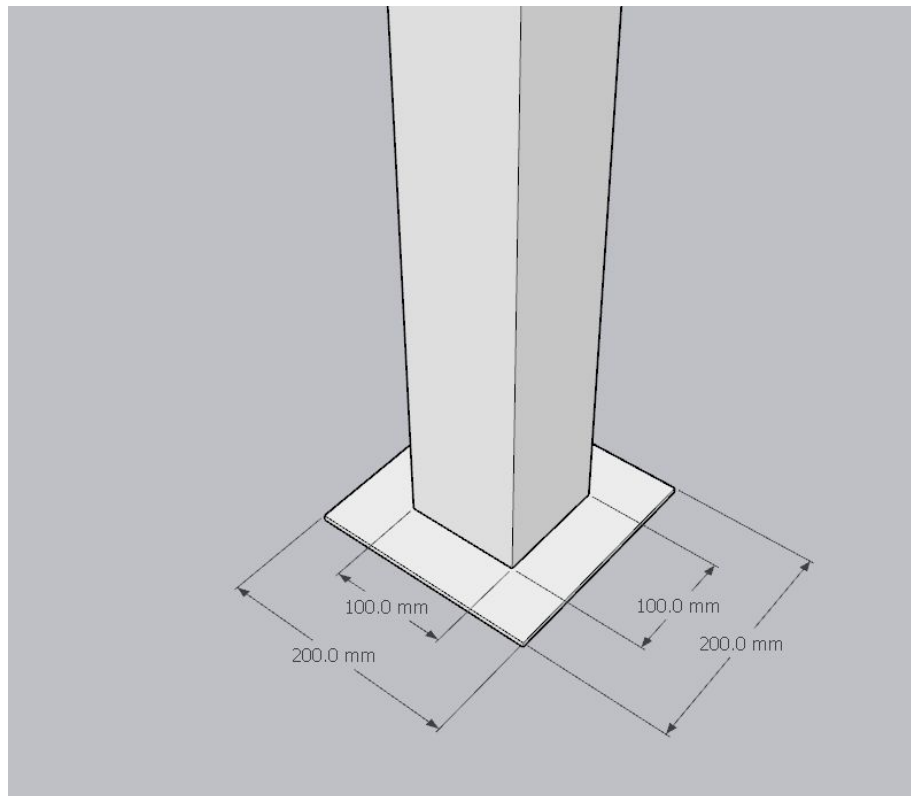


Structure details (6)

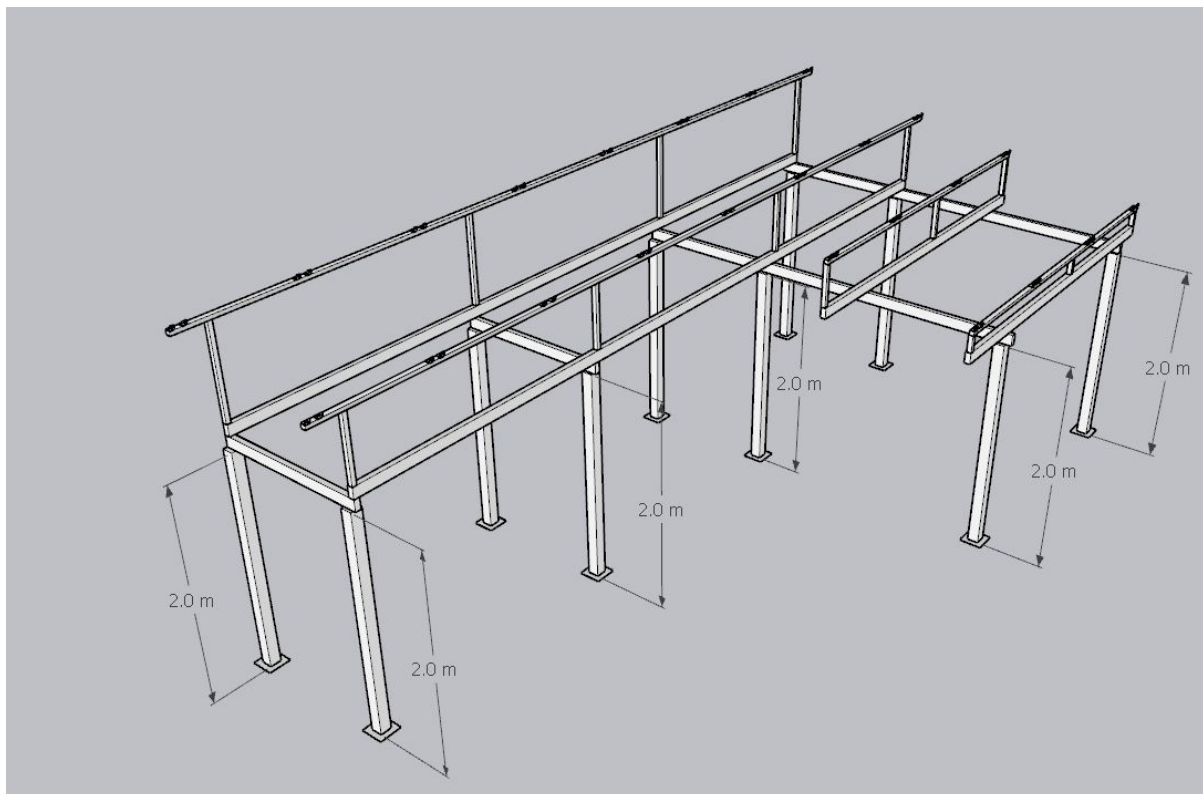


Structure details (7)

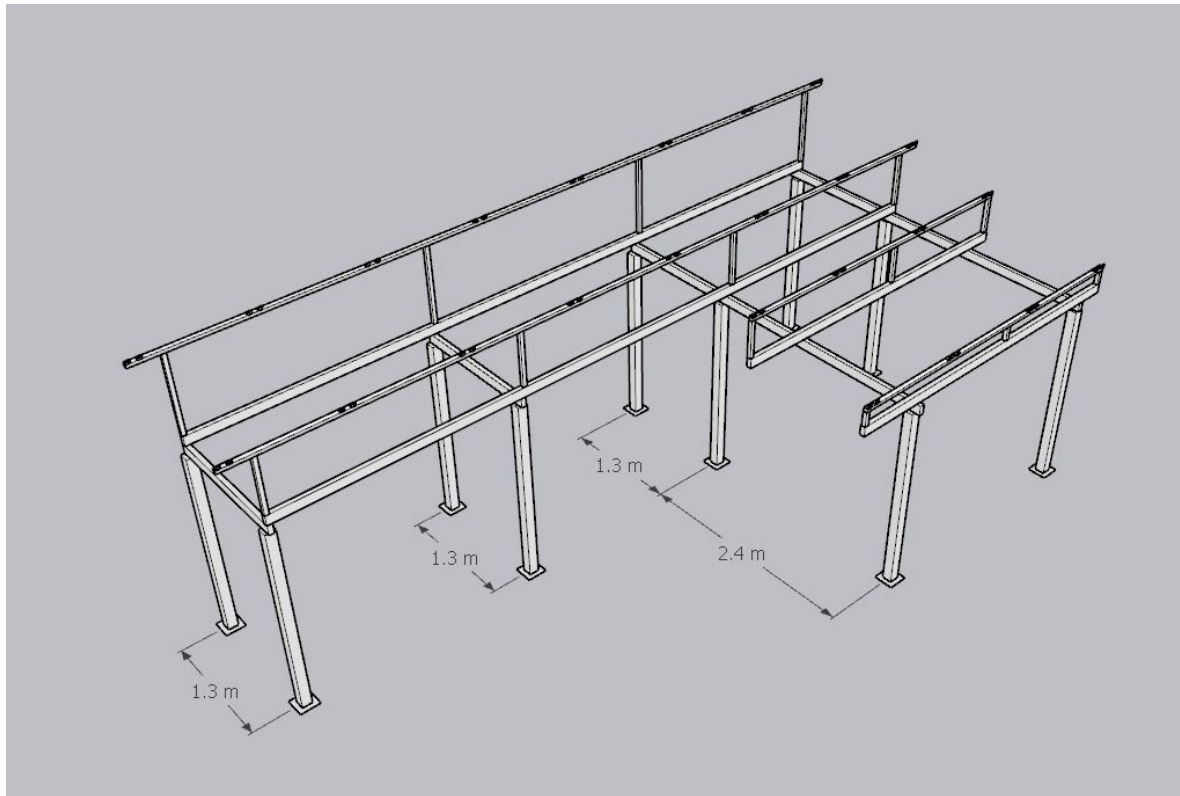


Structure details (8)

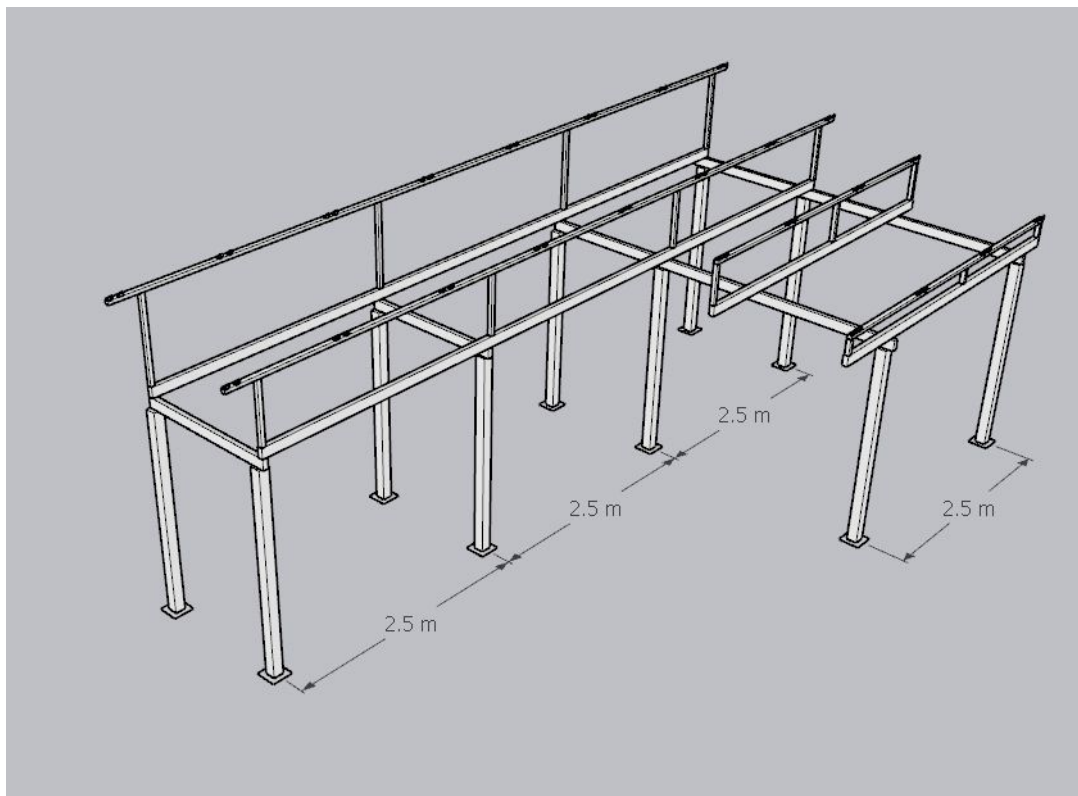

Structure details (9)

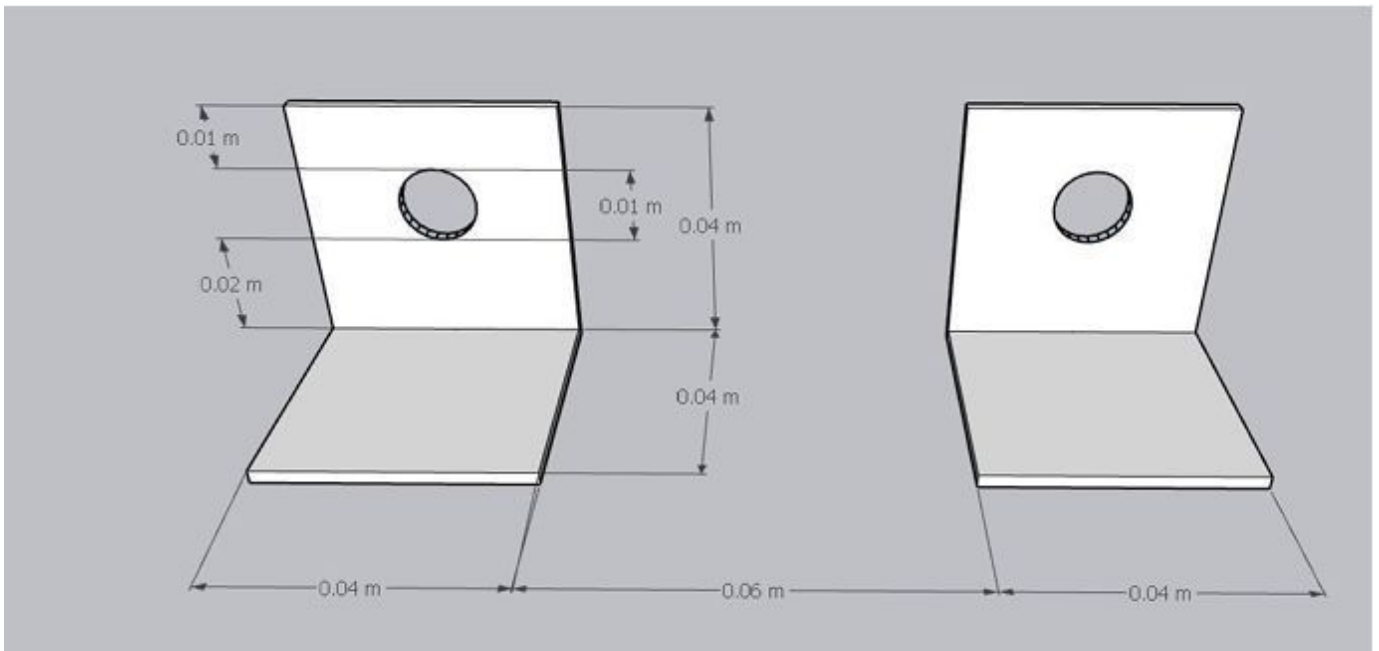

Structure details (10)

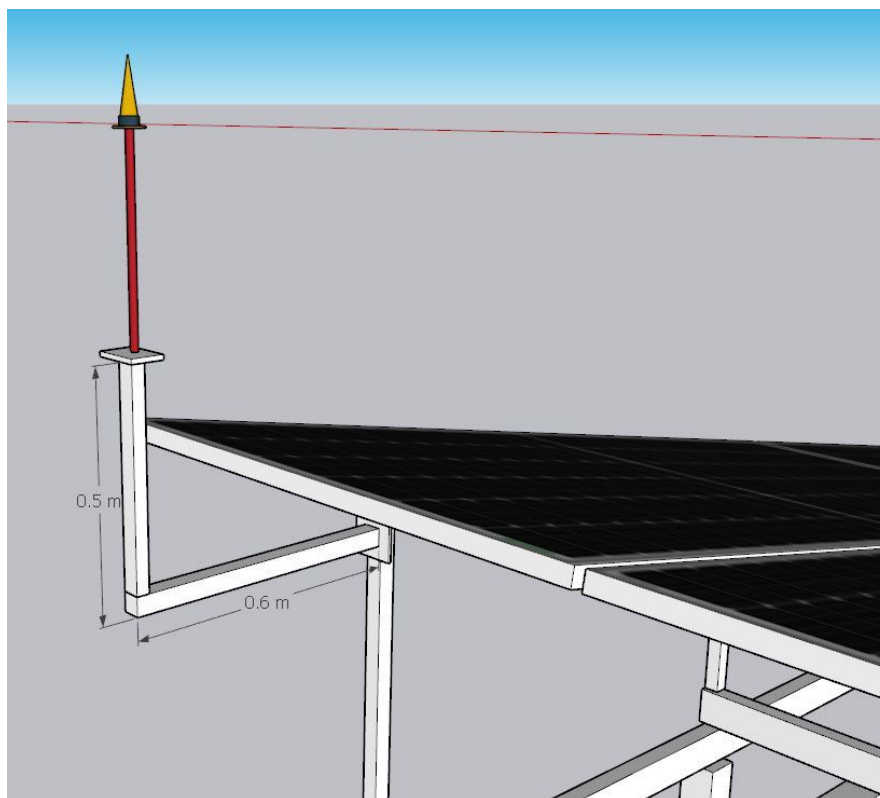

Structure details (11)


Proposed PV Area




Cable Routing



one hole has to be made to run the DC and AC earthing cable till the inverter location.

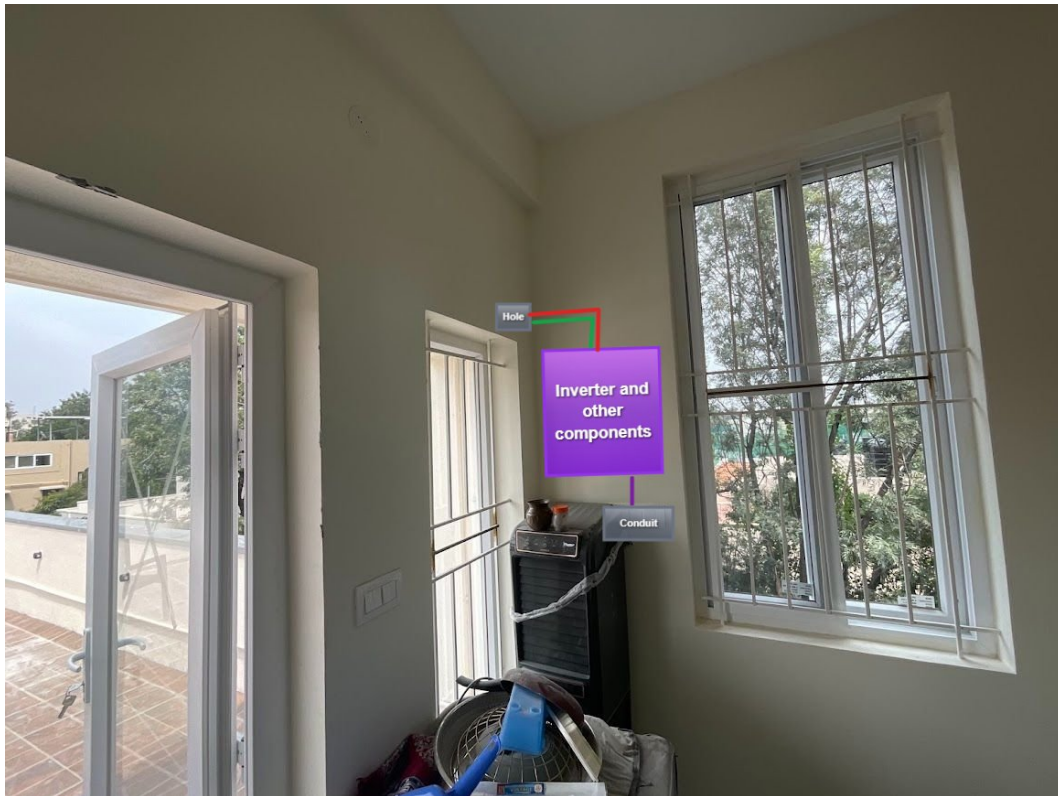

Existing conduit (switch board) is available to run the AC cable till the main meter location.

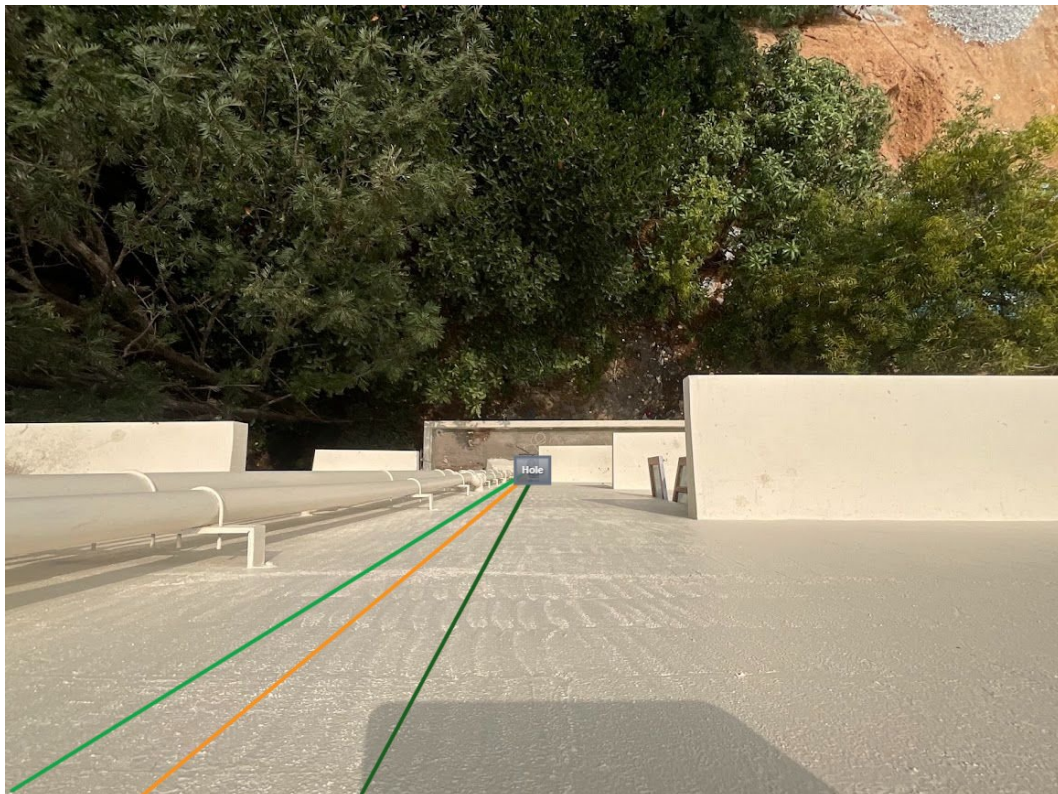

one hole has to be made to run the earthing cable till the earth pits location.

Equipment Location



Earth Pit Location



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As per the customer's suggestion, the routing, cable earthing, inverter location and also solar meter location have been considered.

Customer Scope

#	Observation
1	Wi-Fi upto solar meter is under customer scope.
2	MS fabrication is under customer scope.
3	cables has to pull till the meter location is under customer scope.

THANK YOU

Dear Amrendra kumar,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
