

Technical Site Visit Report

Prepared for: Guruprakash_Jp nagar_3.72kWp_Microinverter (IQ Series)

PROJECT INFORMATION

Report Number	ESV-2026-0129
Project ID	2C51AF60
Project Name	Guruprakash_Jp nagar_3.72kWp_Microinverter (IQ Series)
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	HARIOM PATEL
Site Address	#29, "Gurushree", 3rd Main, 3rd Cross, Gauravnagar, JPNagar 7th Phase, Bangalore 560078.
GPS Coordinates	12.885254, 77.581486
Google Maps	https://www.google.com/maps?q=12.885254,77.581486
Visit Date	2026-06-03
Visited By	ABILASH N K
Revision	Rev 3

CLIENT INFORMATION

Client Name	Guruprakash
Contact	+91 82960 77840

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	3.72
Sanction Load (kW)	4
Module Make & Capacity	Adani TOPCon DCR, 620 Wp
Module Length (mm)	2382

Module Width (mm)	1133
Number of Panels	6
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	6
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: Tree branches in front of the house. The installation team has to carefully lift the panels up.	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Enphase accessories box has to be installed at the roof level.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, Discussed with the customer and finalised the location for earthing.	-
6	Where is the Internet Router located?	At the terrace level, nearer to the Enphase accessories box.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	The LAN cable connection will be provided to the ENVOY location by the customer at the time of installation.
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-

#	Question	Answer	Notes
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	<i>The MS structure has been fabricated at the site. And is ready for installation.</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	7 Metres (G + 1)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999)	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	<i>LA can be installed above the overhead tank base structure available at the terrace roof.</i>
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	<i>There exists one cubicle for the pump starter where the solar meter can be accommodated.</i>
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>A narrow space (width = 500 mm) is available on the south side of the building for digging 2 nos. of earth pits. Where 3-inch concrete has to be removed to dig the earth pits.</i>



#	Question	Answer	Notes
12	In case of elevated structures, is an LA extension provided at the far end?	No	LA can be installed above the OHT base structure.
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	The Enphase accessories box can be wall mounted at the terrace level.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 500	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout - Top View

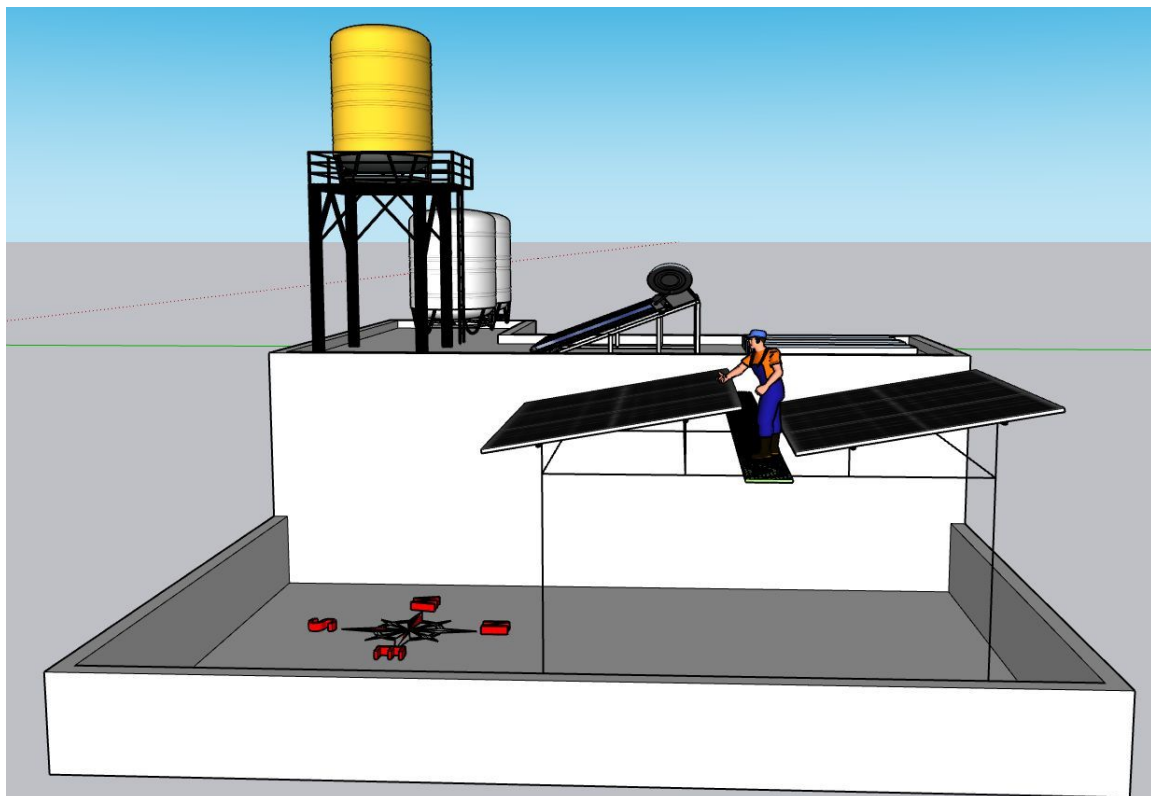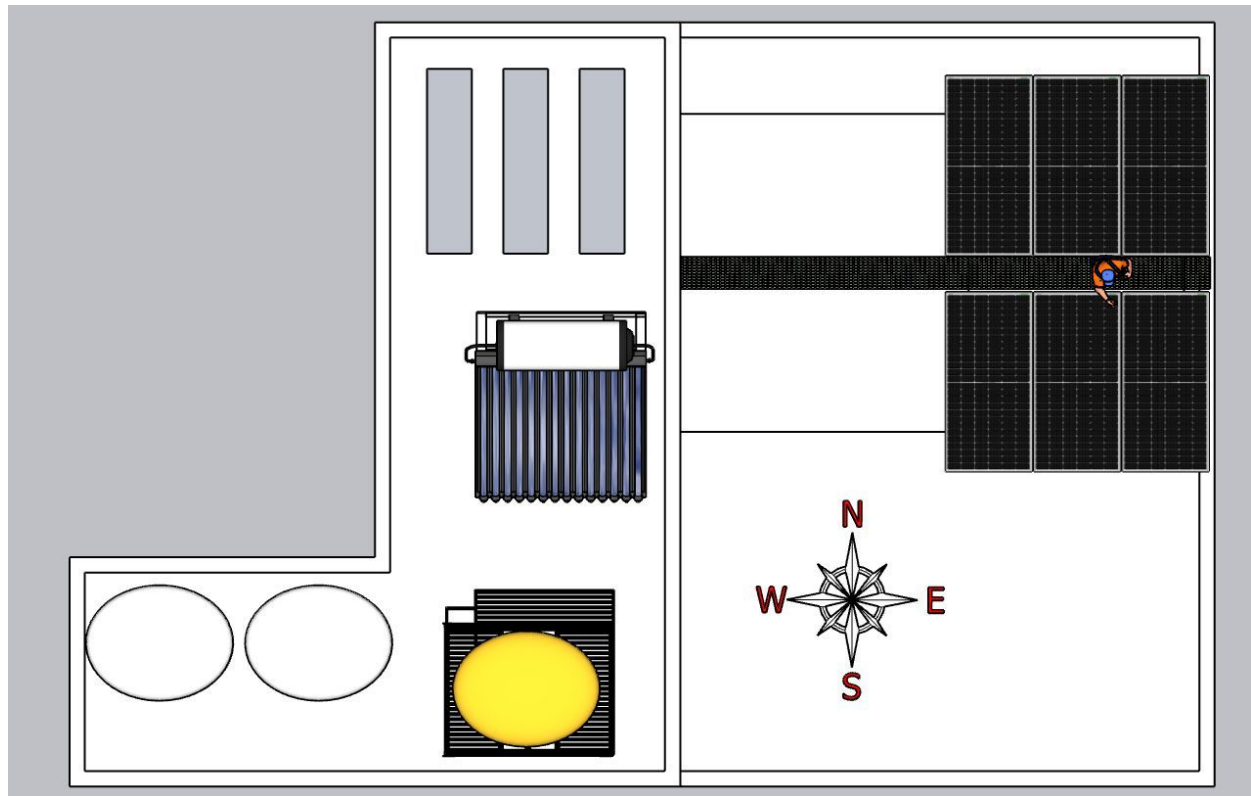

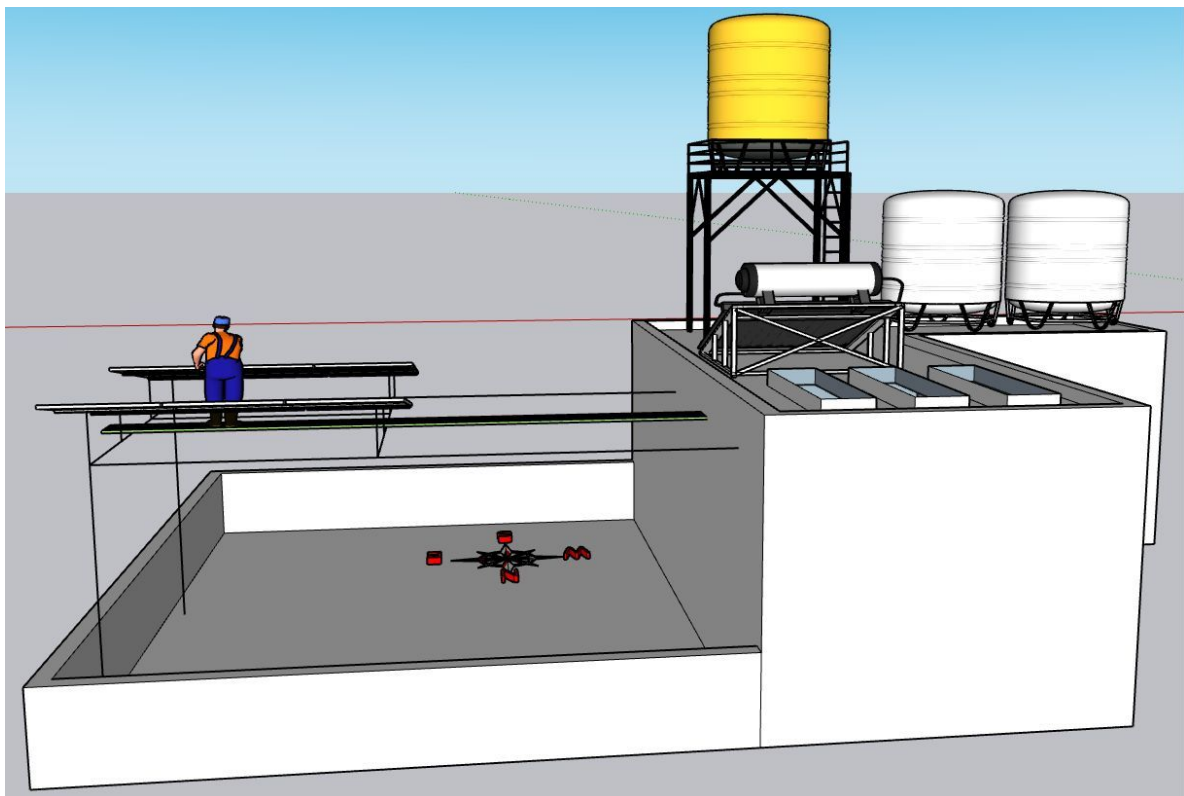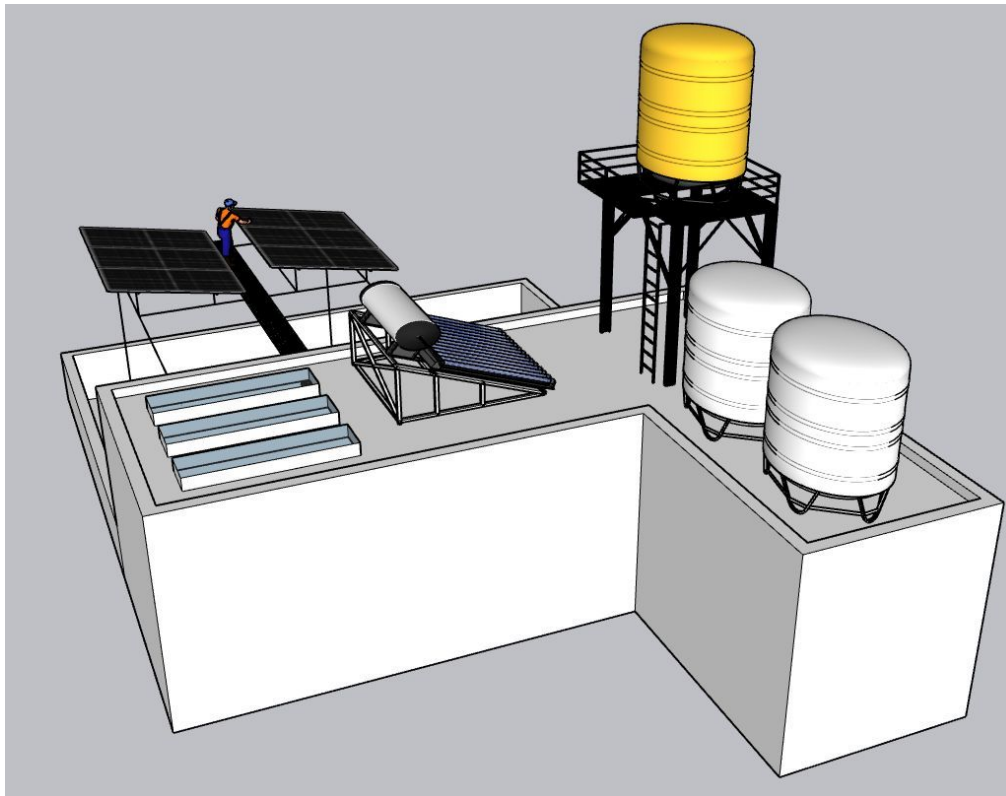


Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.

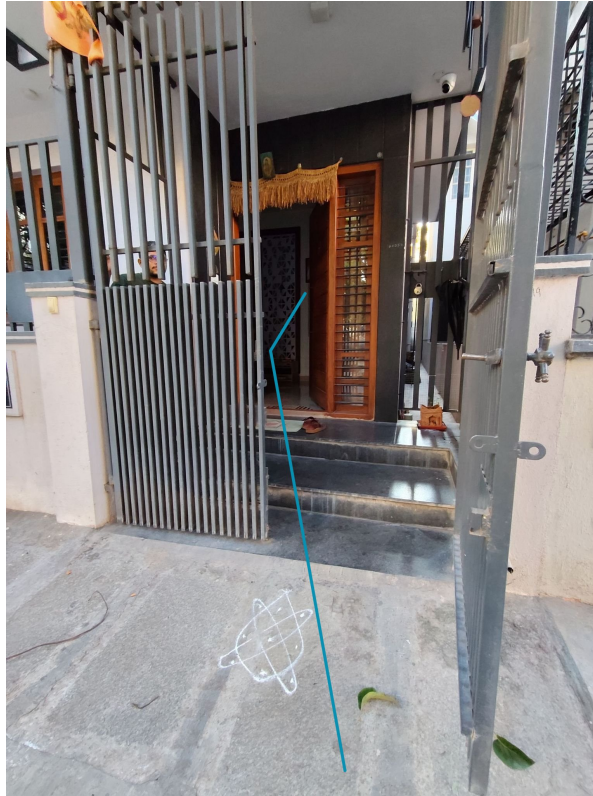

Light weight materials can be shifted to the terrace via the inner staircase.



Follow the staircase till the top floor.



The materials reaching the top floor door steps.



Materials reaching the terrace area.



Materials storage location.

Staircase Details




Staircase width: 850mm

Proposed PV Area



Cable Routing

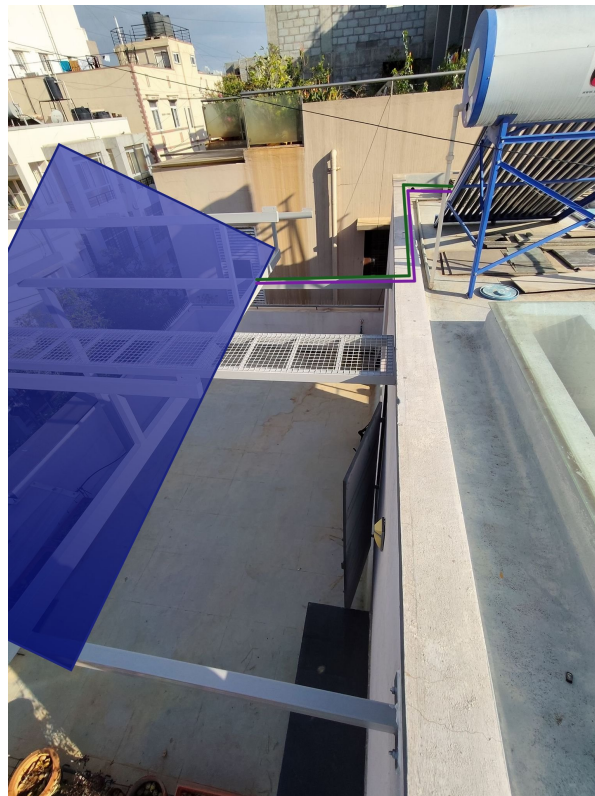

The solar AC output cable and the DC earthing cable can run parallel over the short parapet wall.



The LA earthing cable jumping down.



The LA earthing cable and the AC output cable can run parallel along with the existing plumbing pipe channel and then run horizontally over the wall just above the sun-shade until the earth pit location.



The output AC cable has to go back to the terrace (behind the water tank) towards the LA cable routing location.



The Envoy location is inside the Enphase accessories box.



In order to reach the solar meter box, the output AC cable has to run along with the LA cable



The DC earthing cable can be connected to the existing earthing cable available at the site. (Where, the earth pit is already dug by the customer)



The AC earthing and LA earthing pits can be dug at the space available at the south most end of the building.



The DC earthing cable has to run towards the existing earth pit at the N-W corner of the building.



The earthing cable can be connected to the copper conductor exposed above the door.



The earth pit already sealed and is not visible outside

Meter Box



This box will receive the AC output cable straight from the Enphase accessories box that is situated on the terrace level.



The AC cable from the solar meter to the main meter can be pulled through the existing conduit available (Concealed)



The final termination can be done here at the main meter cubicle.

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 3.72kWp, On-grid solar power plant at the proposed premises.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	The customer is responsible for arranging the ladder provision to get access to the proposed solar panel installation area prior to the project's execution.
3	Ensuring the existing concealed conduits good enough to pull the solar output cables.
4	Ensuring the reliability of the existing spare earth-pit provided for DC earthing.

THANK YOU

Dear Guruprakash,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
