

Technical Site Visit Report

Prepared for: Harikrishnan_Trinity woods_5.49kWp_Hybrid - #122

PROJECT INFORMATION

Report Number	ESV-2026-0200
Project ID	BB30B56F
Project Name	Harikrishnan_Trinity woods_5.49kWp_Hybrid
Building Name	#122
Billing Name	Harikrishnan
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Hariom
Site Address	122 West, Trinity Acres & Woods, 25/2, Ambalipura, Sarjapura Main Road, Bengaluru, Karnataka 560102.
GPS Coordinates	12.91648135188384, 77.66553097525173
Google Maps	https://www.google.com/maps?q=12.91648135188384,77.66553097525173
Visit Date	2026-09-04
Visited By	Abhilash R.S
Revision	Rev 1

CLIENT INFORMATION

Client Name	Harikrishnan
Contact	+91 99721 16333

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	5.49
Sanction Load (kW)	5

Module Make & Capacity	Premier DCR Bifacial 610
Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	9
Inverter Type	Hybrid (String)
Inverter Brand	Deye 5 kW 1phase String
Number of Inverters	1
Battery	Needed
Number of Batteries	1
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The building elevation are the obstruction that could hinder the material lifting.	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Beside the stair case the inverter, ACDB,DCDB will be installed	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	The location of the earth pits near the car parking area.	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstructions on the roof are plumbing lines, electrical wires ,dish anteenas that could affect the solar installtion.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	One roof but two different places
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	2P2, 1P5,HDGI Elevated Structure with 2m front clearance
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Not Applicable	-
13	What is the height of the building and how many floors does it have?	The building height is G+3+headroom is approximately 15 meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	Main meter is located near the panel room area which is near to next to the 5houses
2	Is the Meter cubicle photo matching with the previous answer?	No	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	No	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter	N/A	-

#	Question	Answer	Notes
	and IQ Gateway > 50m?		
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	N/A	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	-	-
21	Provide the dimension for earth pits location (L x W of available space).	-	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit



Material Delivery Route



This route (using Staircase) will be followed to carry Small items.

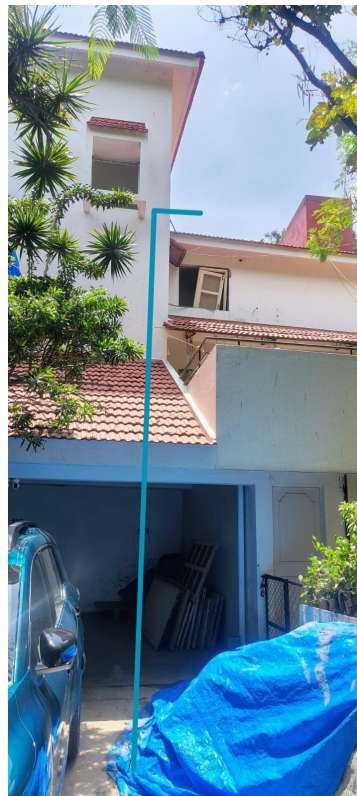







This route (using lifting) will be followed to carry large items (like Panels).






Staircase Details



Meter Box



Material Storage

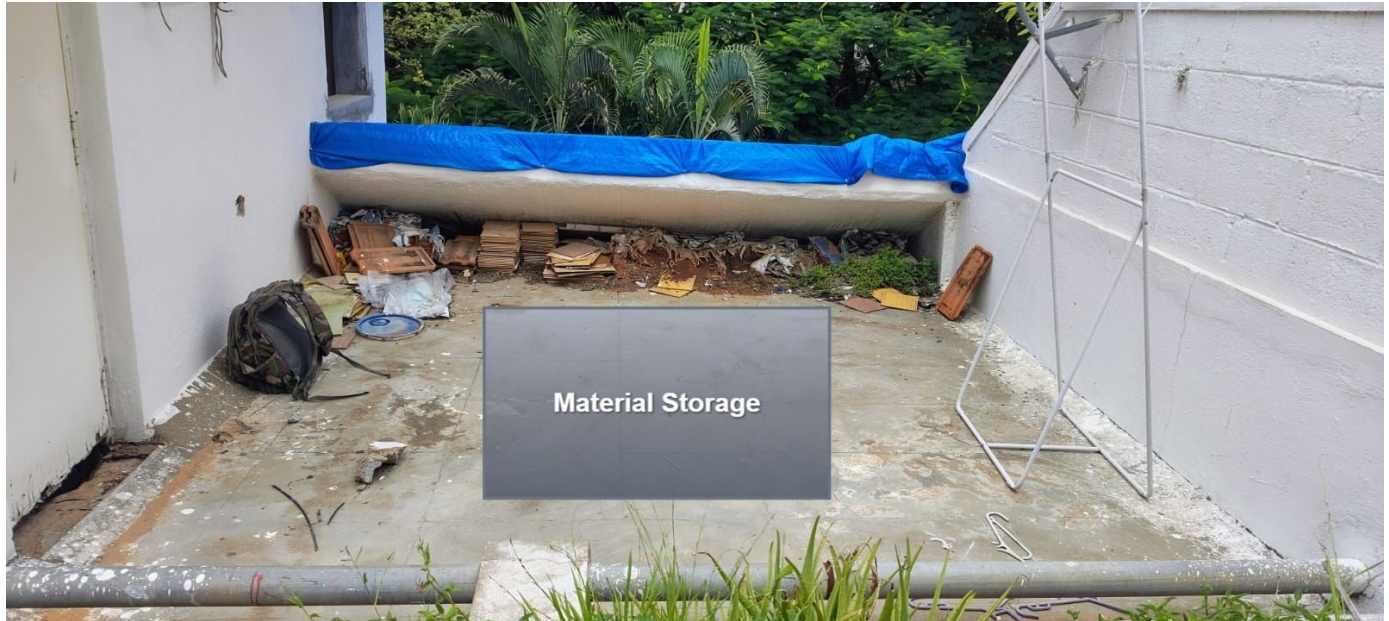


Proposed PV Area








Cable Routing



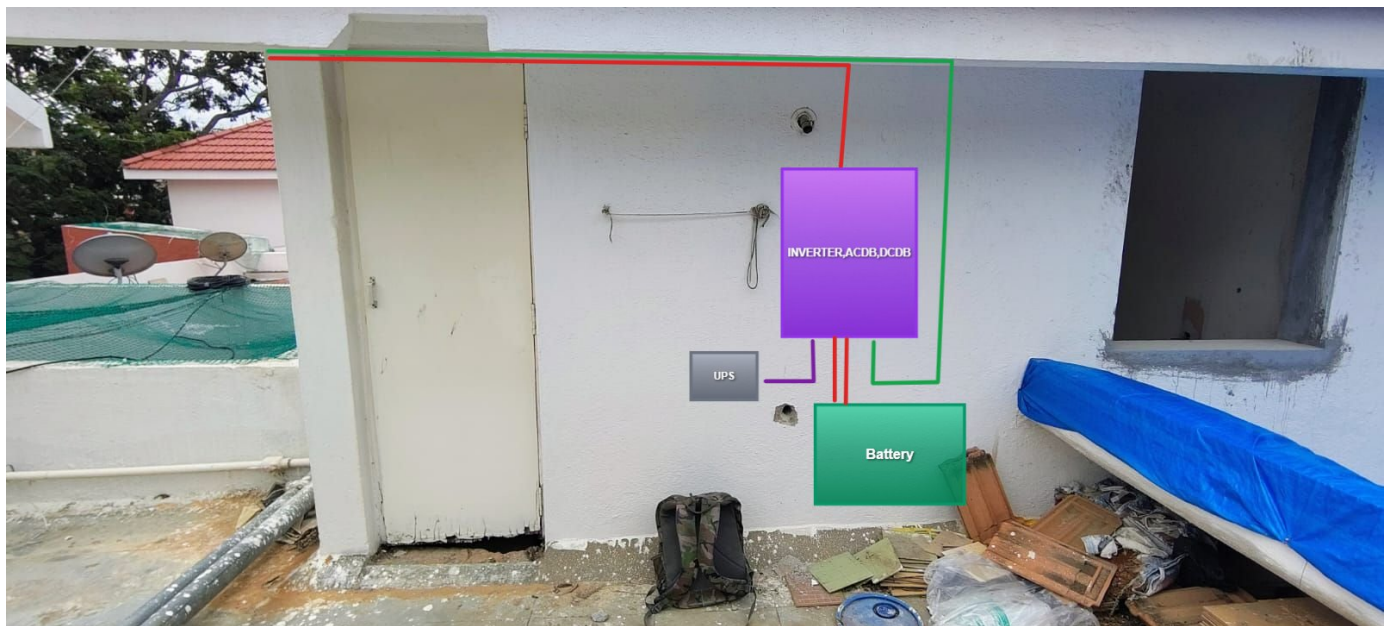

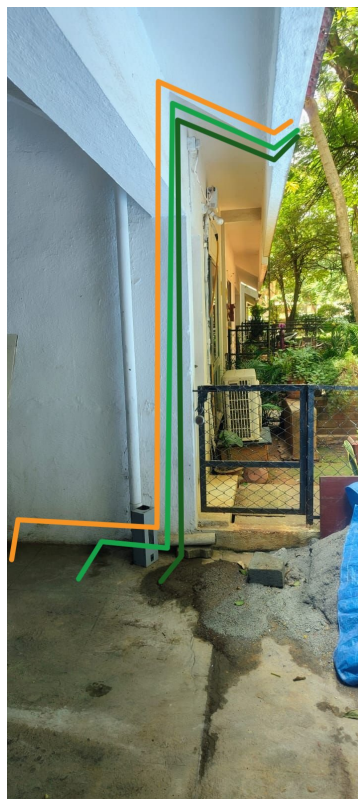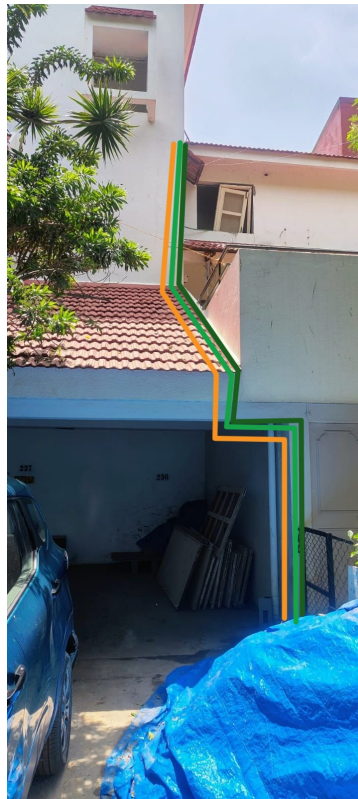

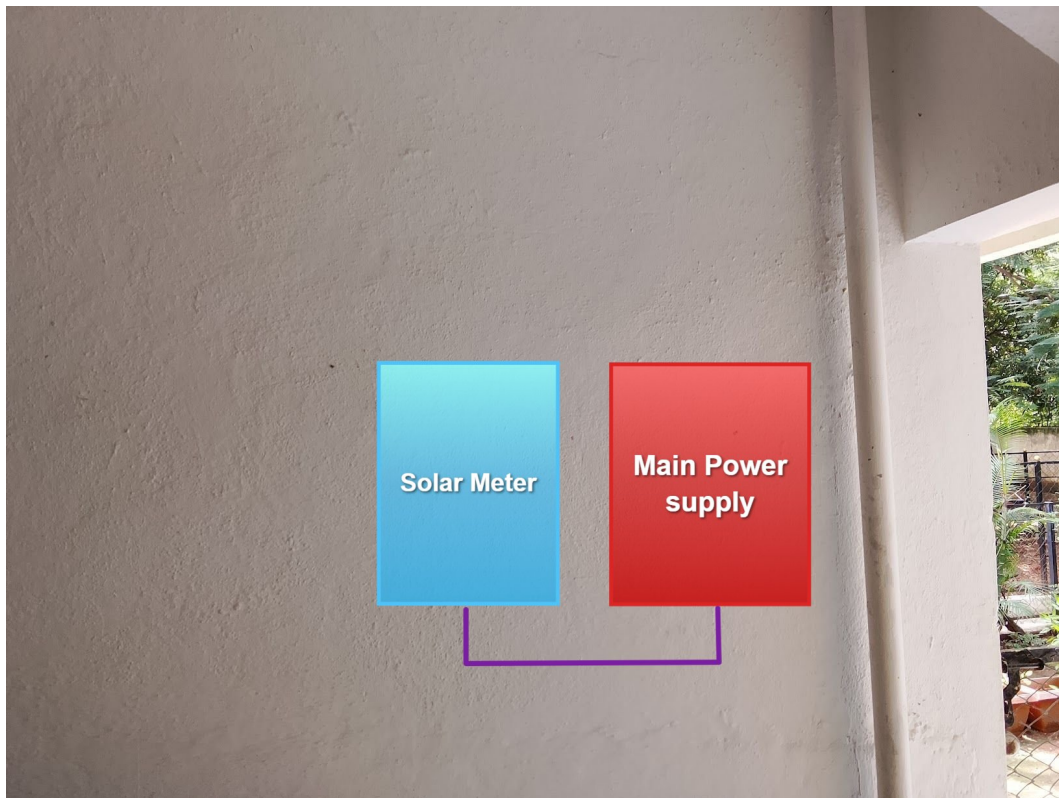

During the site visit, based on the electrician suggestions the main power supply they will arrange the car parking area.


Equipment Location







Earth Pit Location





Site Layout - Top View

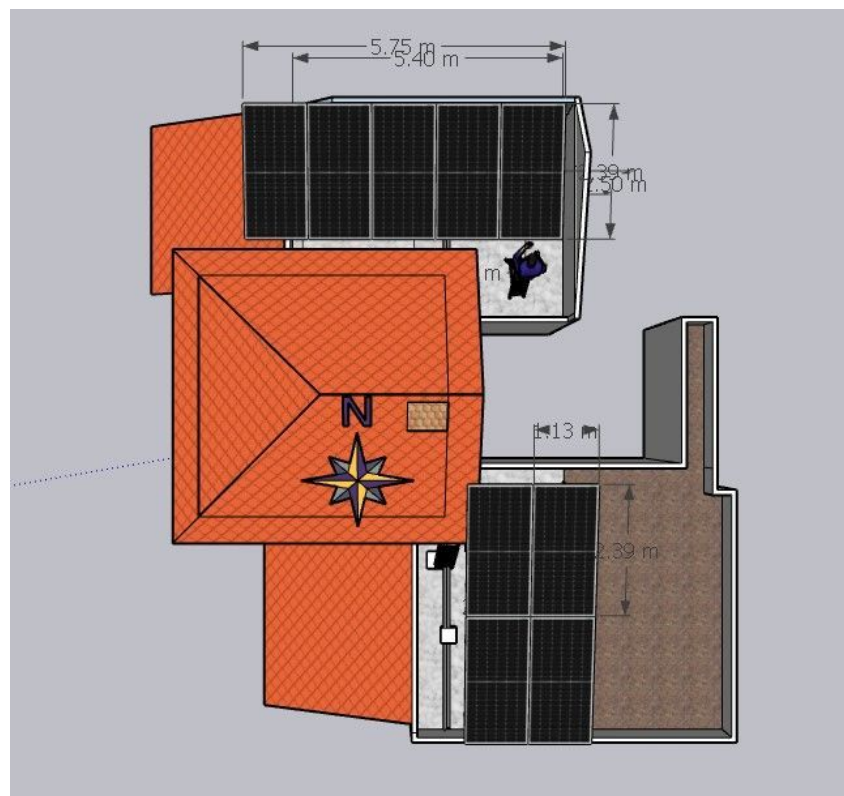

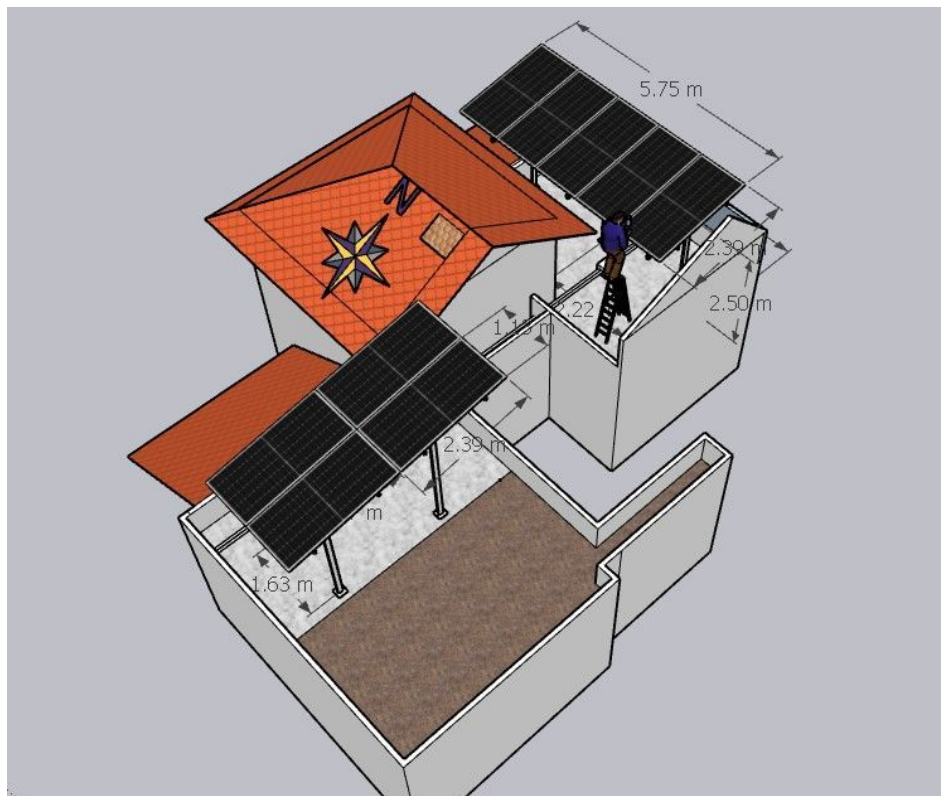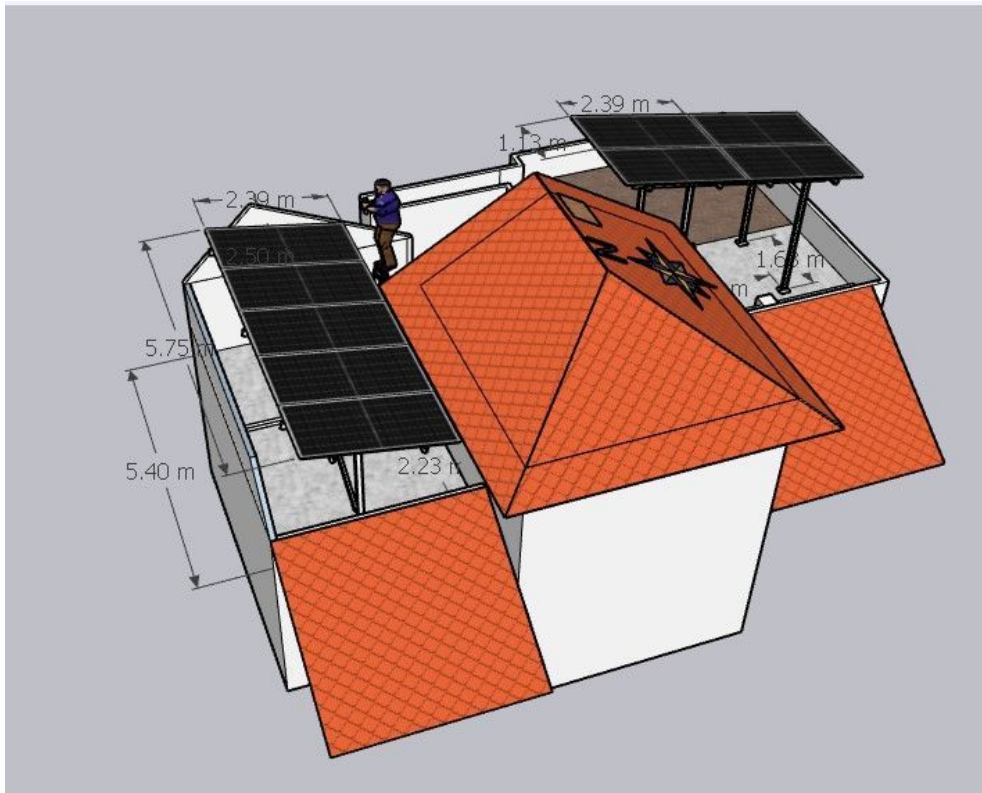

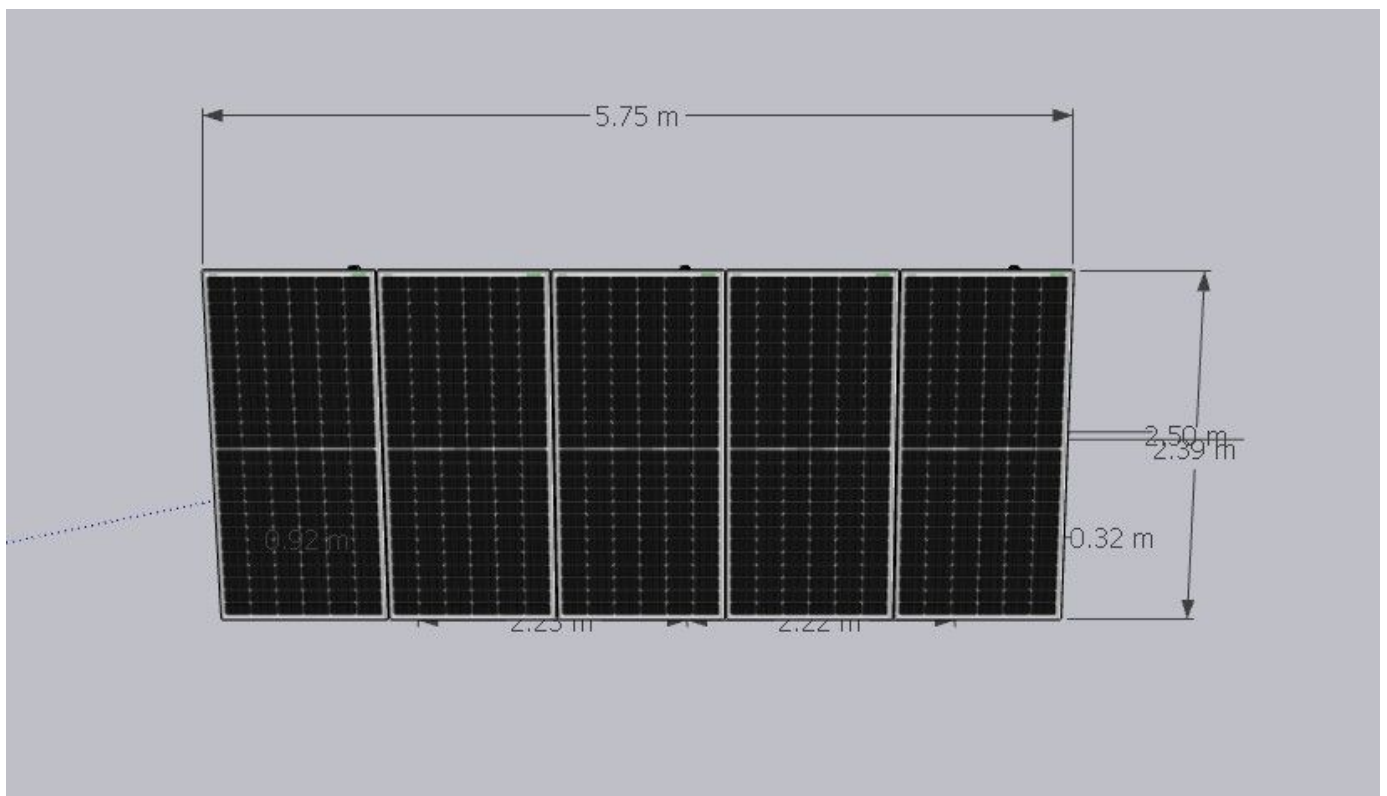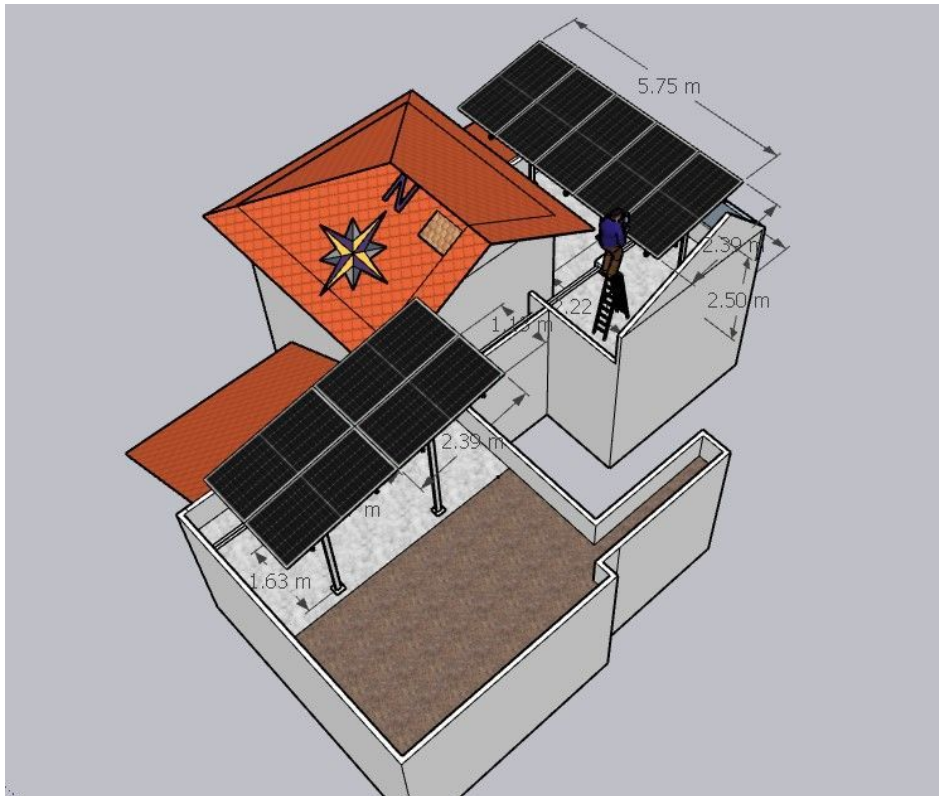

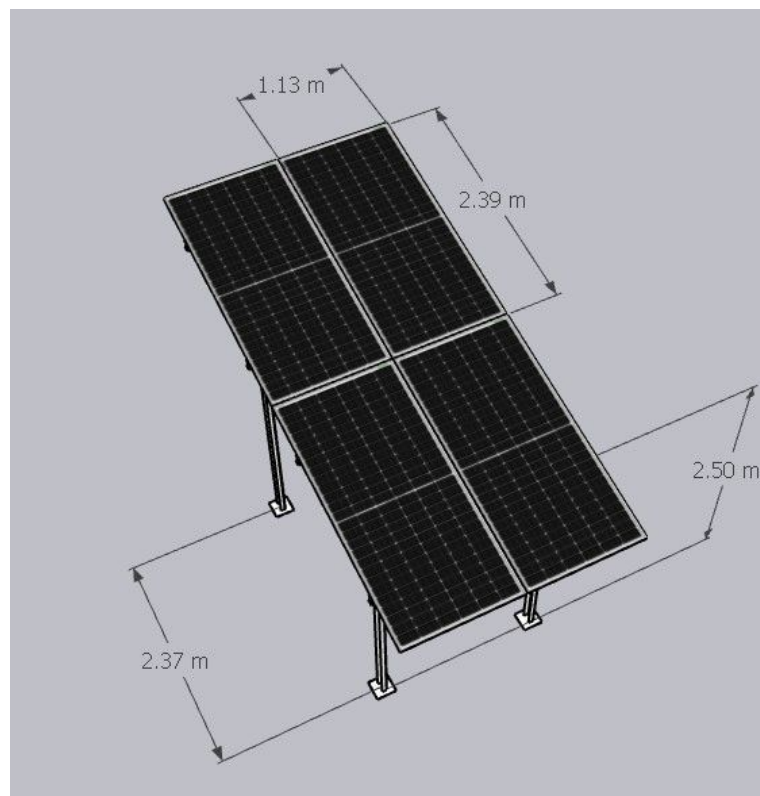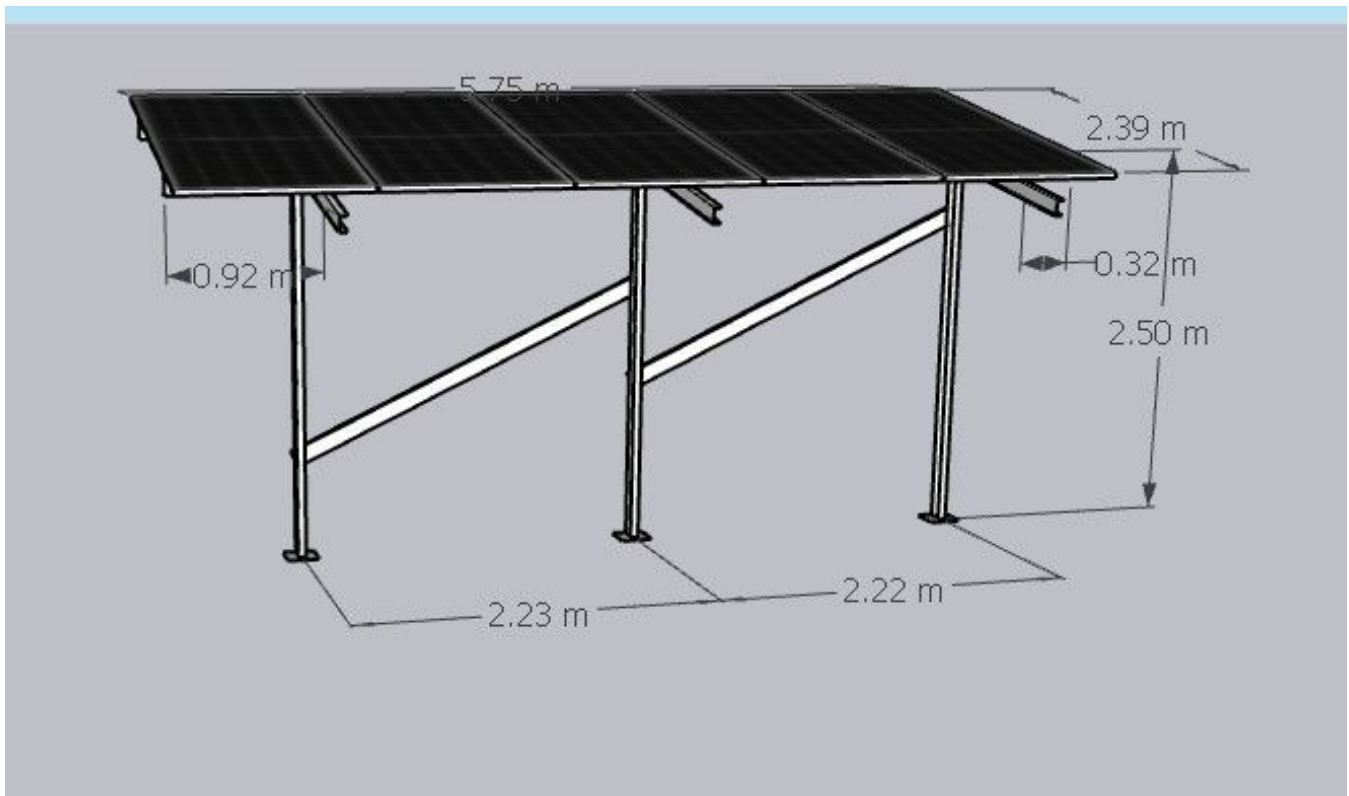

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	UPS point is under customer scope.
3	As per the customer scope only, the panel layout, earthing, cable routing, inverter location has been finalised
4	Ladder is under customer scope.
5	Based on the site conditions the both 1P5 and 2P2 structure front height is 2.50m
6	During the site visit, based on the electrician suggestions the main power supply they will arrange the car parking area is under customer scope.

THANK YOU

Dear Harikrishnan,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
