

Technical Site Visit Report

Report for: Nischal Dutta_Subsidy_Adarsh palm retreat_7.38kWp_Microinverter (IQ Series) - Villa 511, Lane 1N, Phase 3, Adarsh Palm Retreat Villas

PROJECT INFORMATION

Report Number	ESV-2026-0178
Project ID	B55AA886
Project Name	Nischal Dutta_Subsidy_Adarsh palm retreat_7.38kWp_Microinverter (IQ Series)
Building Name	Villa 511, Lane 1N, Phase 3, Adarsh Palm Retreat Villas
Billing Name	Nischal Dutta_Subsidy_Adarsh palm retreat_7.38kWp_Microinverter (IQ Series)
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	Nischal Dutta Villa 511, Lane 1N, Phase 3, Adarsh Palm Retreat Villas DevaraBeesanHalli, Outer Ring Road BENGALURU, KARNATAKA 560103
GPS Coordinates	12.91829680005437, 77.69228460121654
Google Maps	https://www.google.com/maps?q=12.918296800054373,77.69228460121654
Visit Date	2026-07-25
Visited By	Sai
Revision	Rev 1

CLIENT INFORMATION

Client Name	Nischal Dutta
Contact	9945512727

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	7.38
Sanction Load (kW)	10

Module Make & Capacity	Adani DCR bifacial 615 Wp
Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	12
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	12
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	No	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	Earth pits are located near the basement area.	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	9	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	0	-
6	If it is a Tiled roof, what is underneath the tiles?	-	The posts (legs) have been positioned beneath the tiled roof, where a concrete slab is present underneath the tiles.
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-

#	Question	Answer	Notes
8	What type of mounting structure is planned?	Elevated	MS Elevated structure.
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	Height of the building is 10m; it has G+1+Headroom	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	Building is under construction.
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	No	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	Building is under construction.
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	Yes	Building is under construction.
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-

#	Question	Answer	Notes
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 800, width: 498	<i>Building is under construction.</i>
21	Provide the dimension for earth pits location (L x W of available space).	length: 1000, width: 1000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Building Exterior



Material Delivery Route






This route carry the small items



This route carry the large items (like panels)


Meter Box

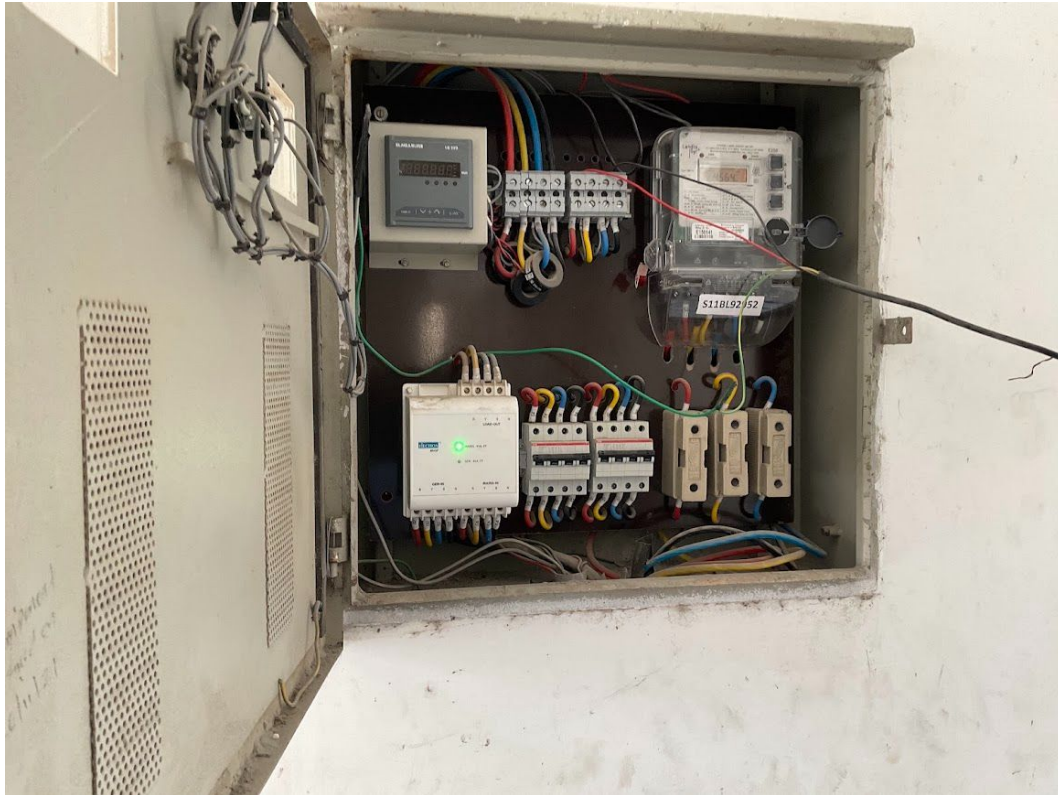


Staircase Details




Site Layout - Top View

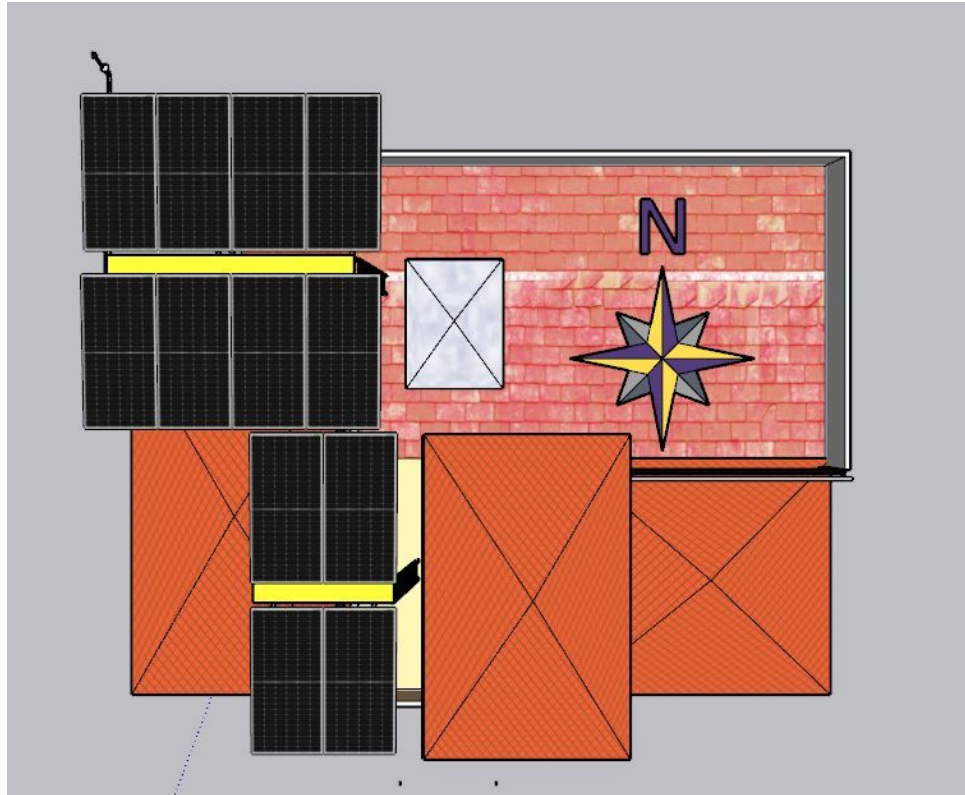


Top View

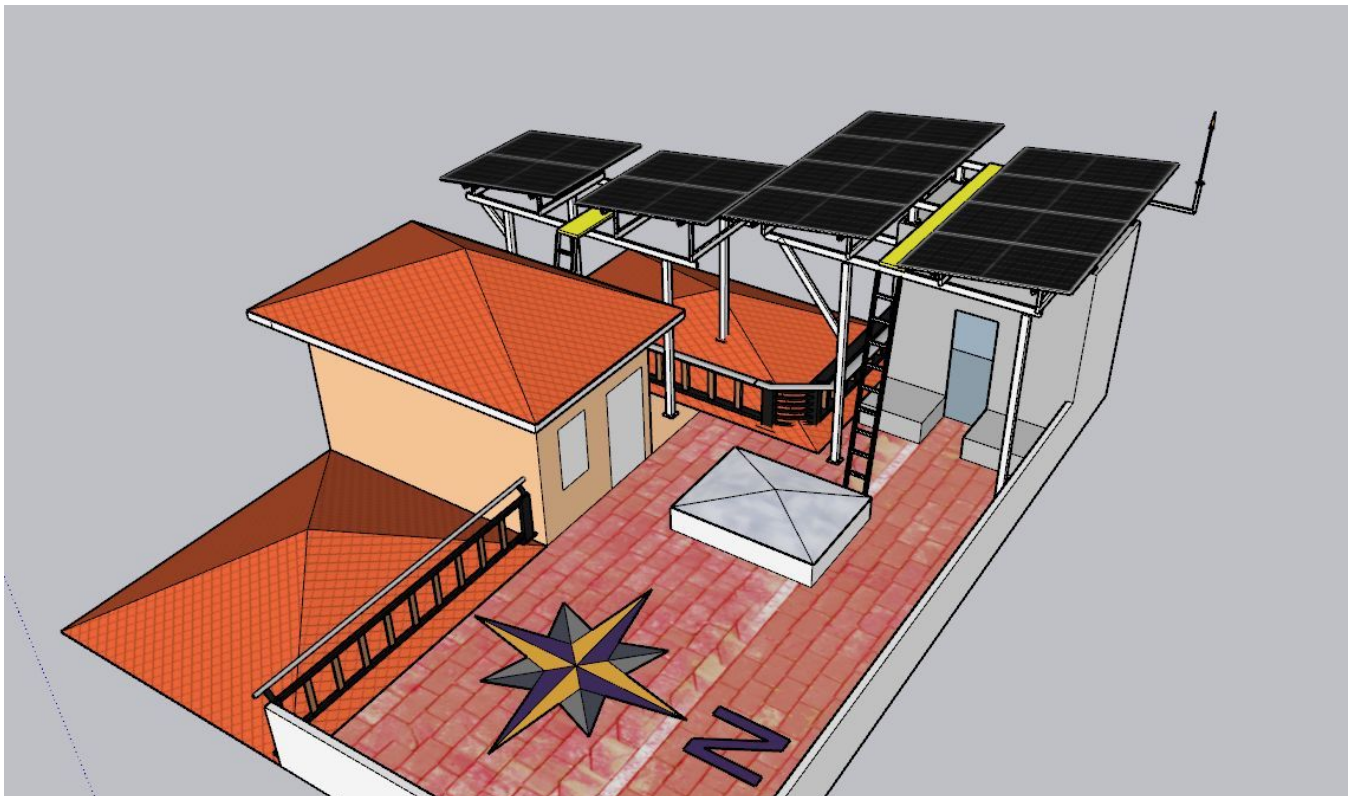


Side View (1)

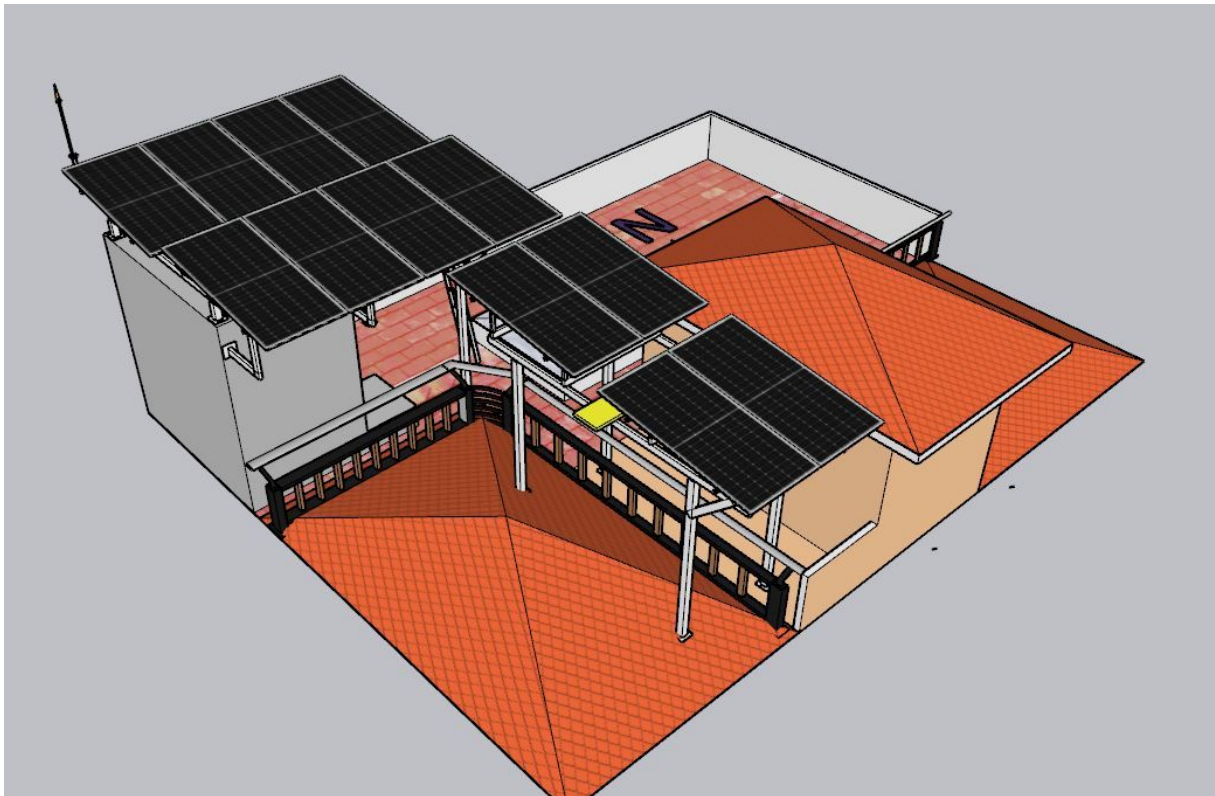


Side View (2)

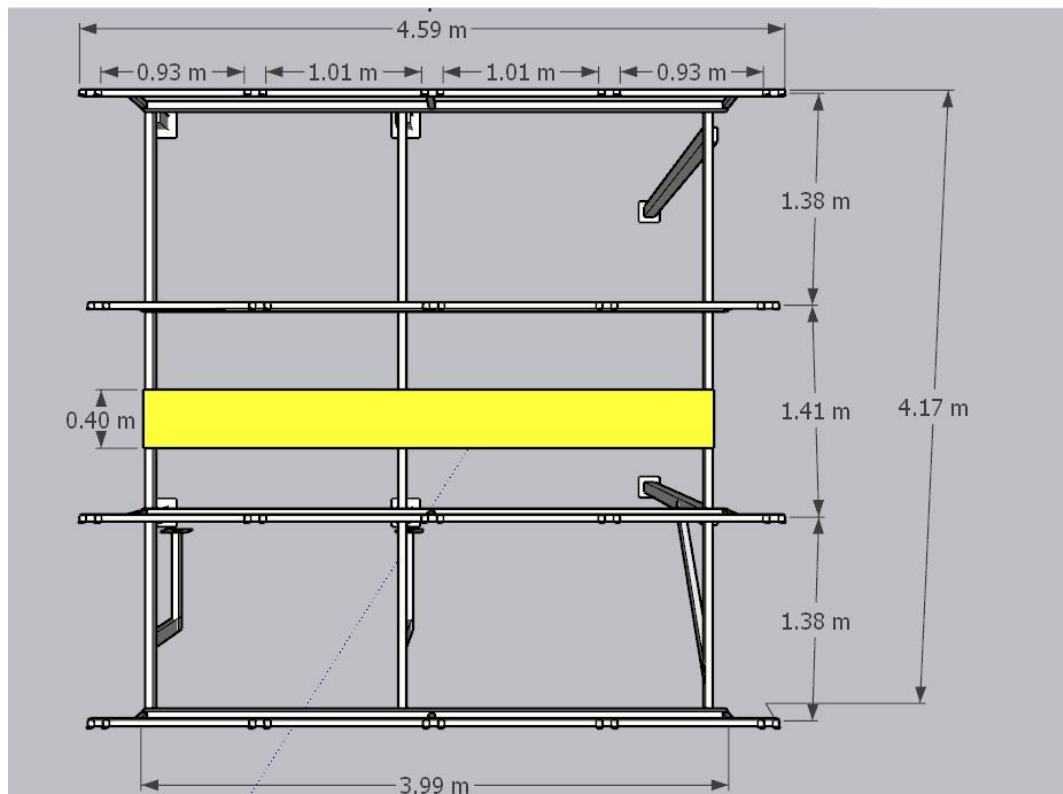


Structure details (1)

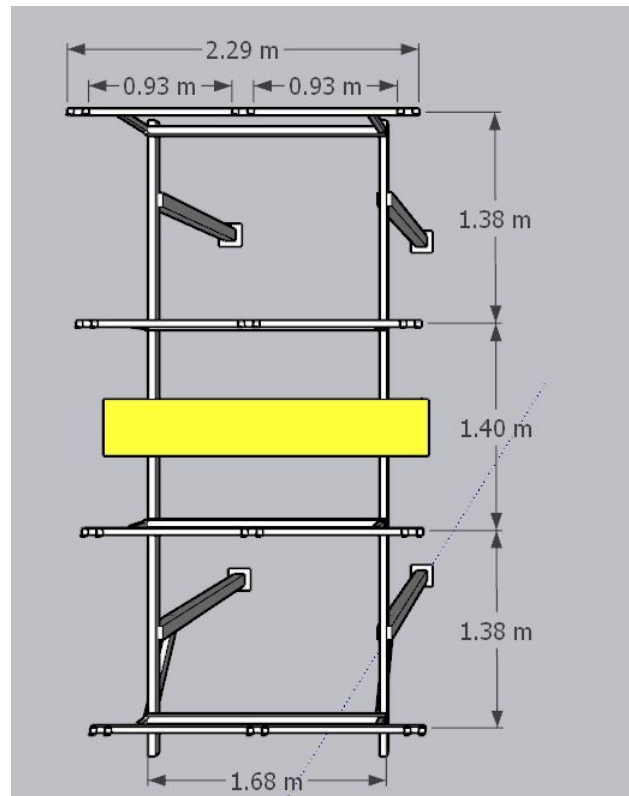


Structure details (2)

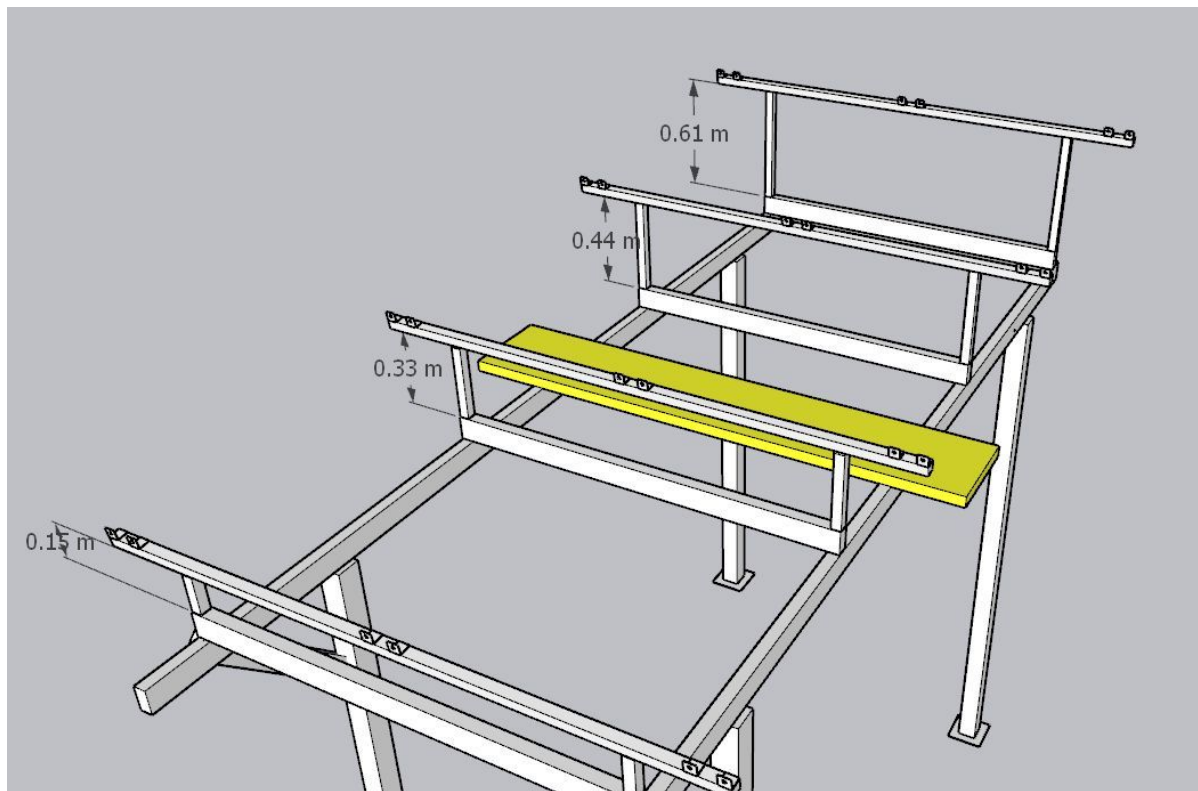


Structure details (3)

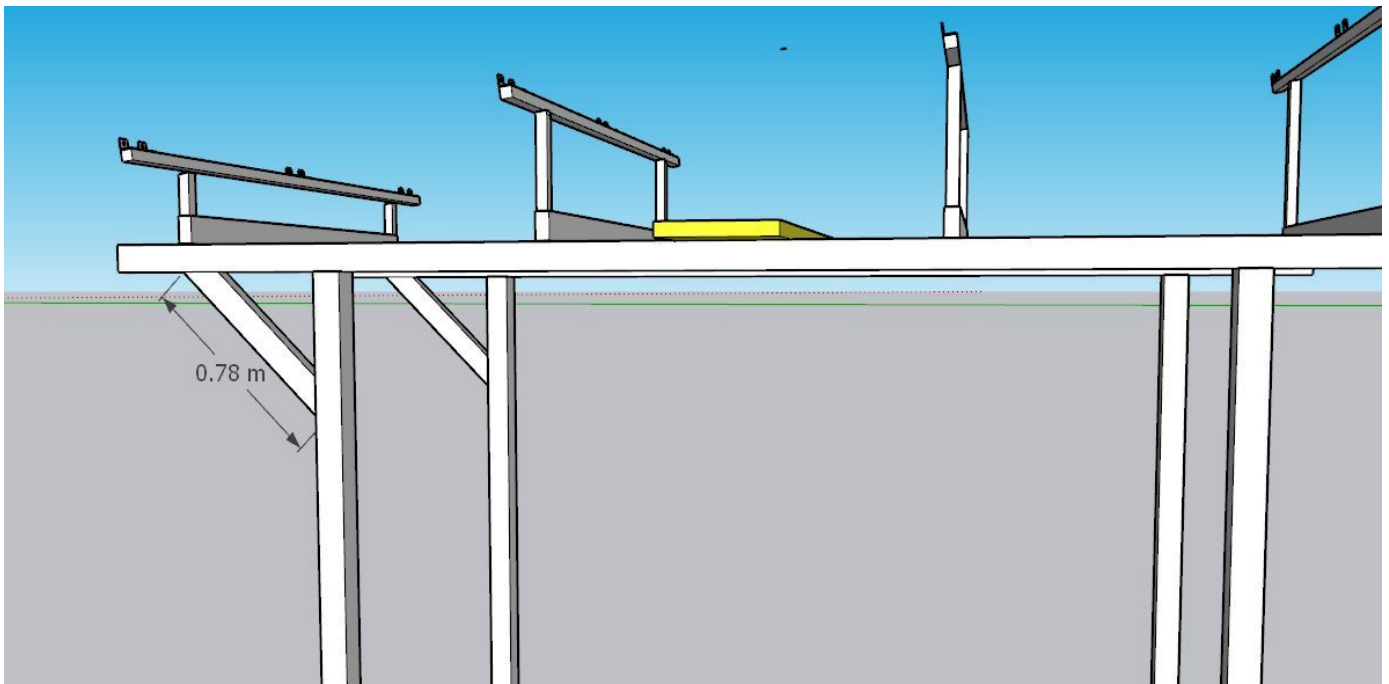


Structure details (4)

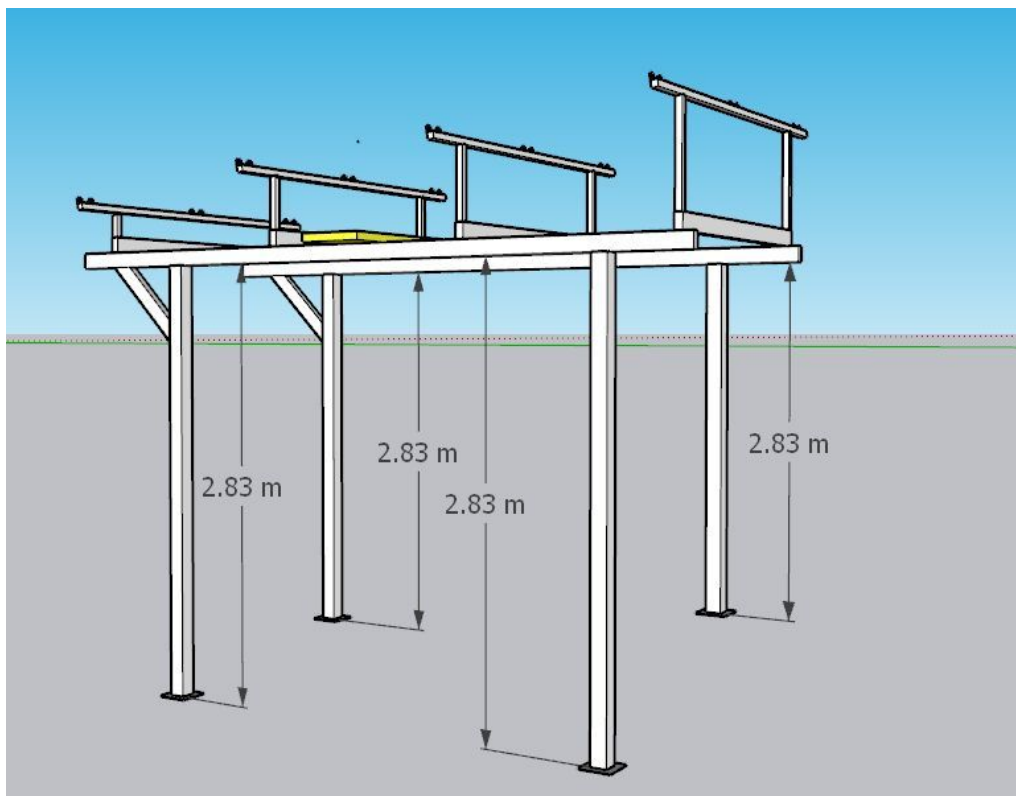


Structure details (5)

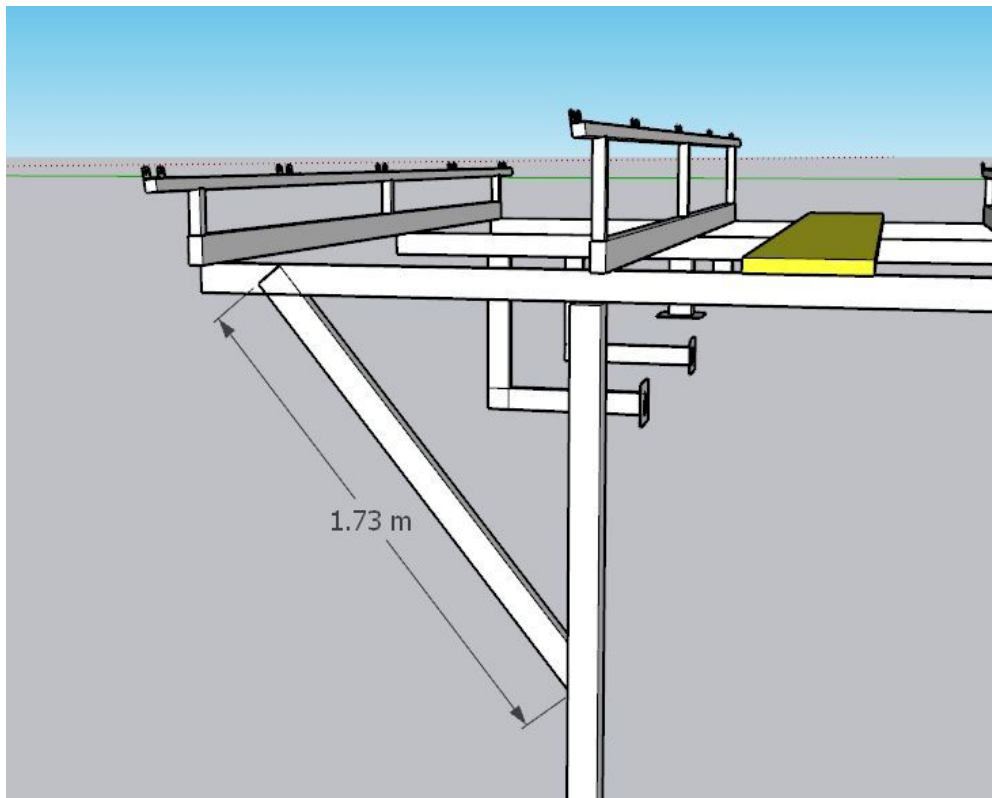


Structure details (6)

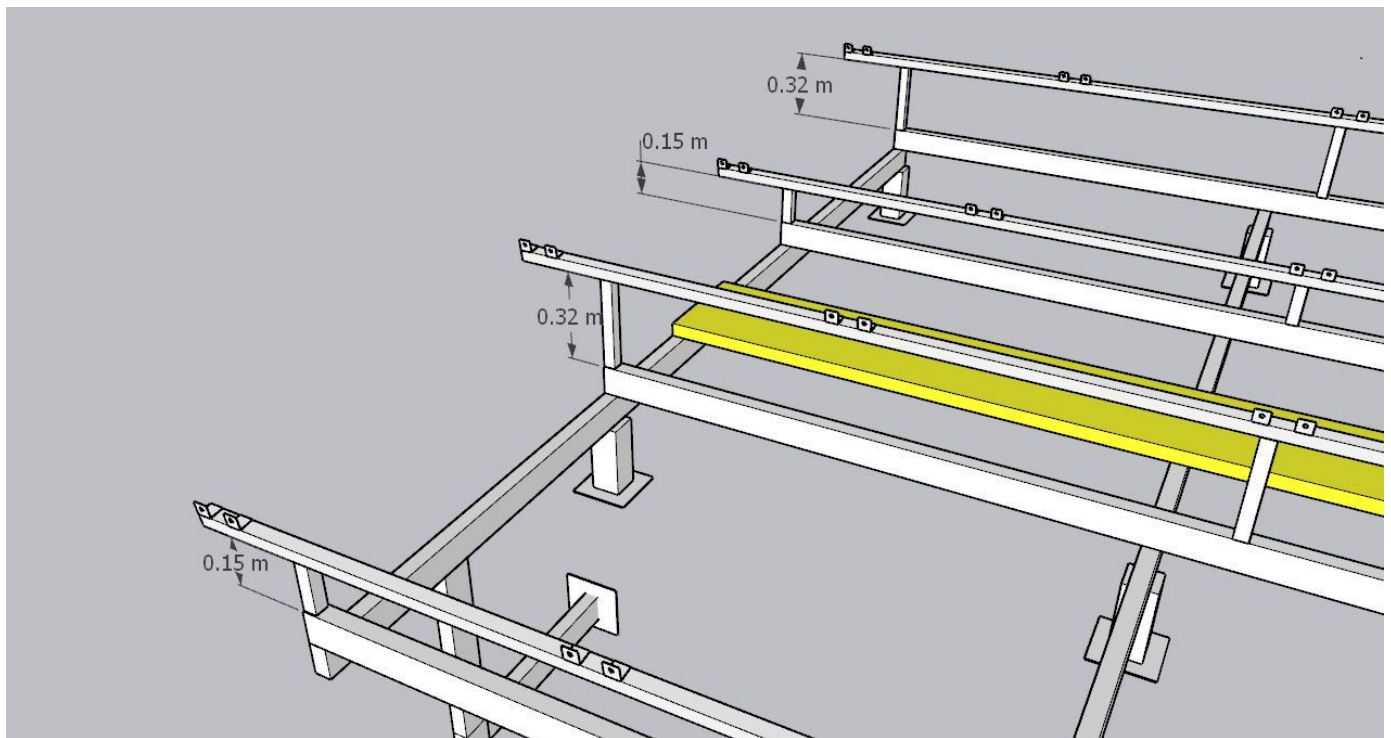


Structure details (7)

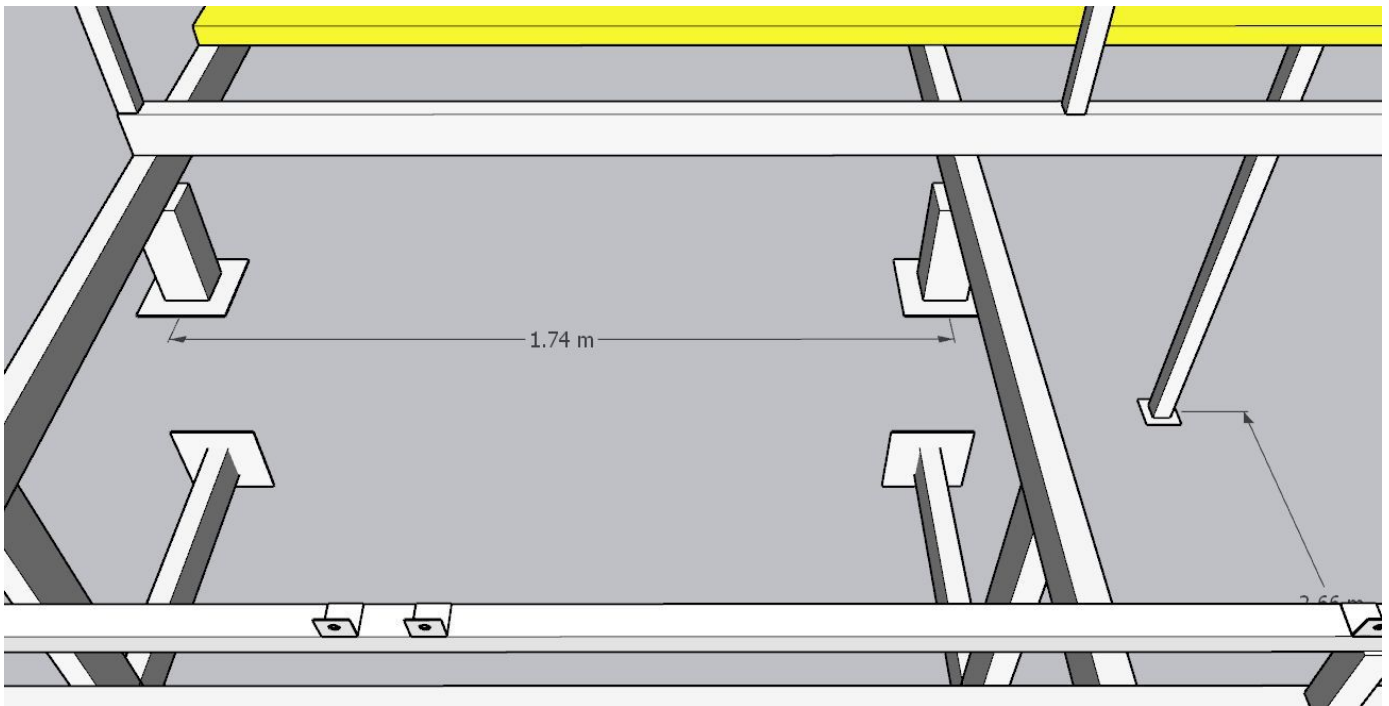


Structure details (8)

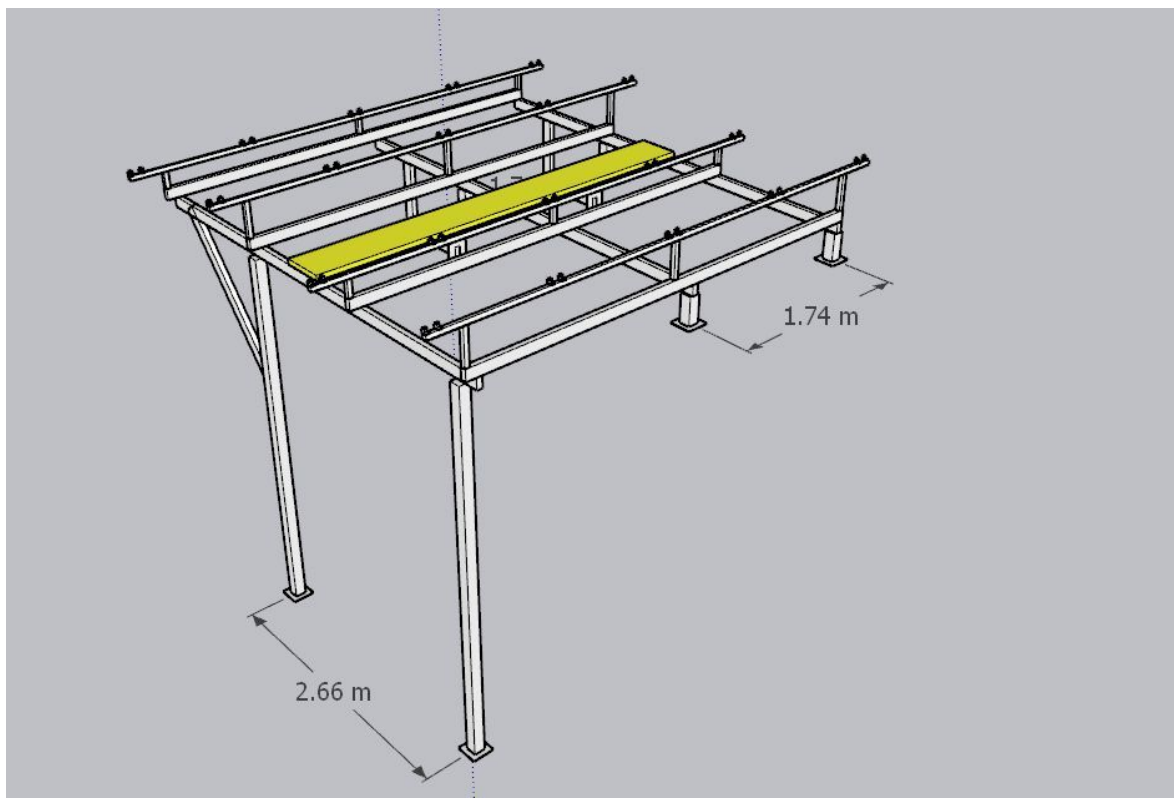


Structure details (9)

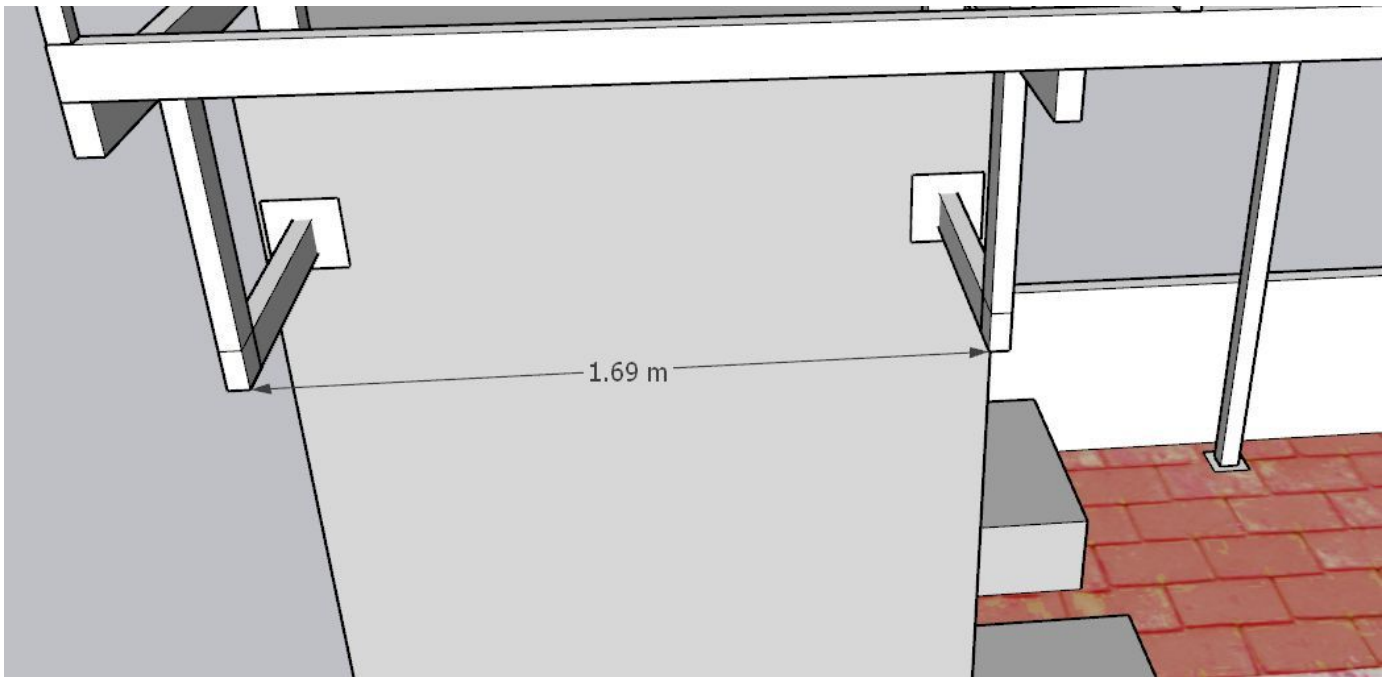


Structure details (10)

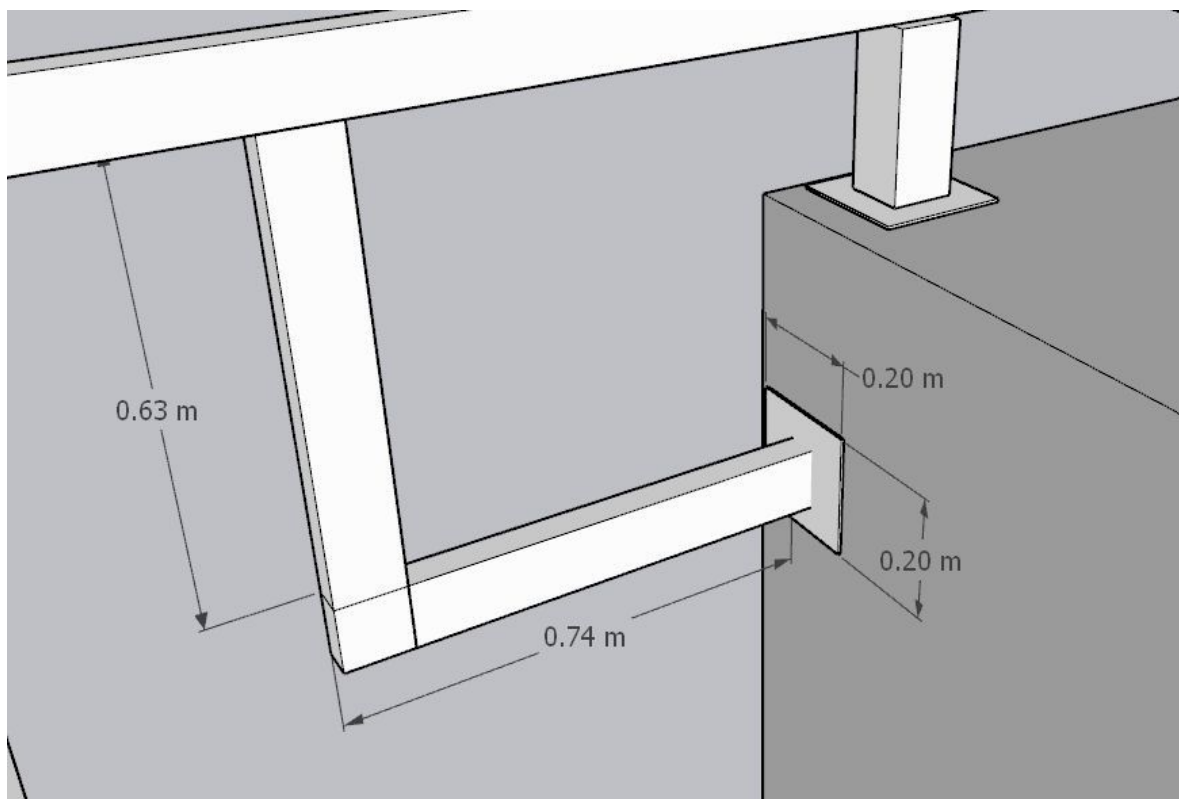


Structure details (11)

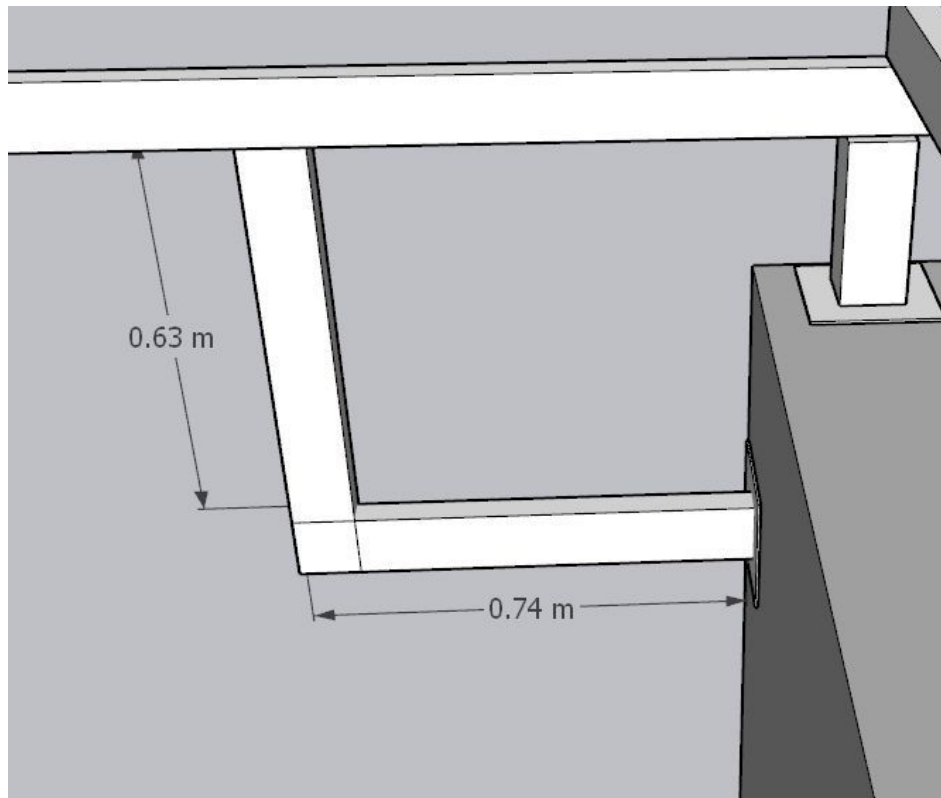


Structure details (12)

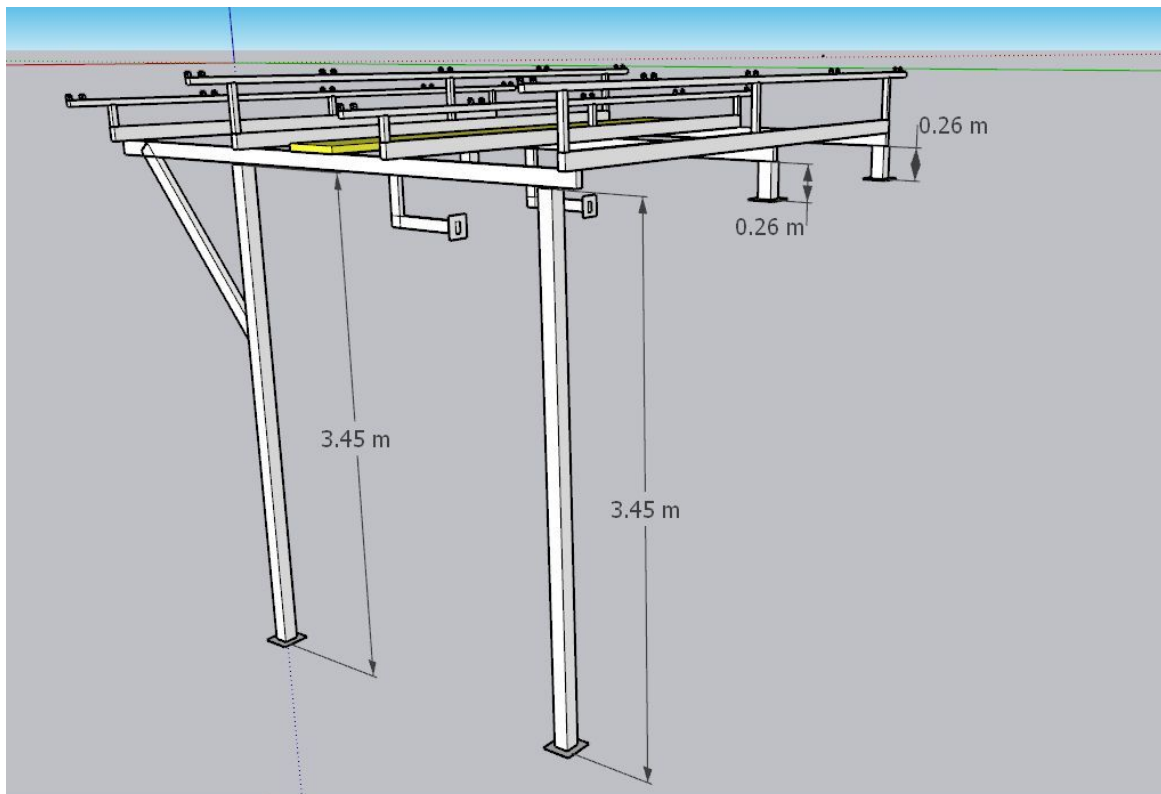


Structure details (13)

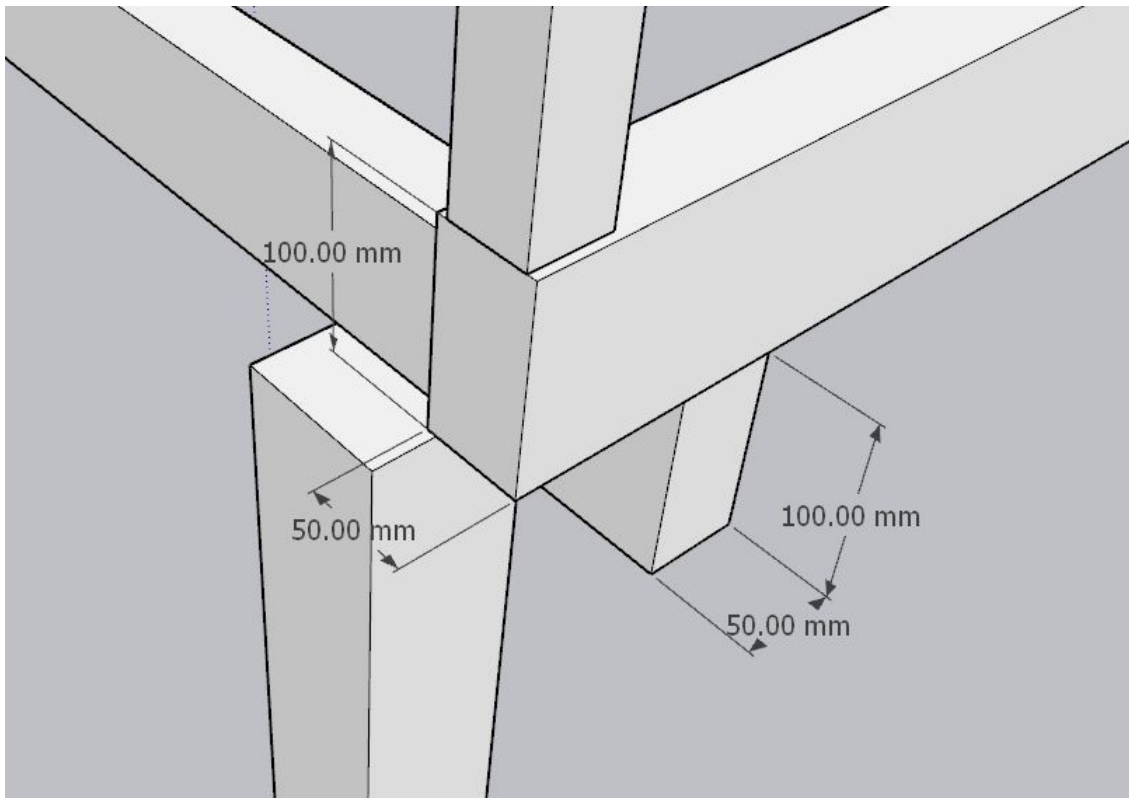


Structure details (14)

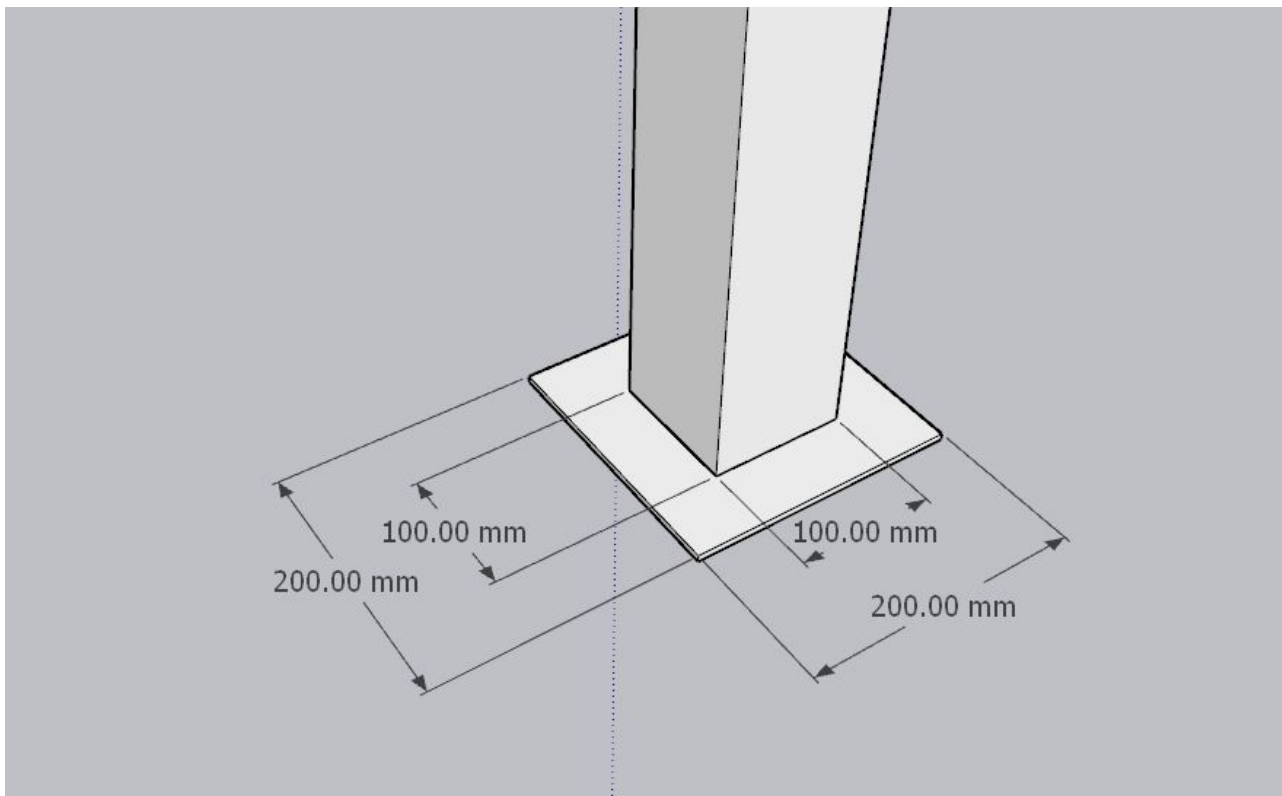


Structure details (15)

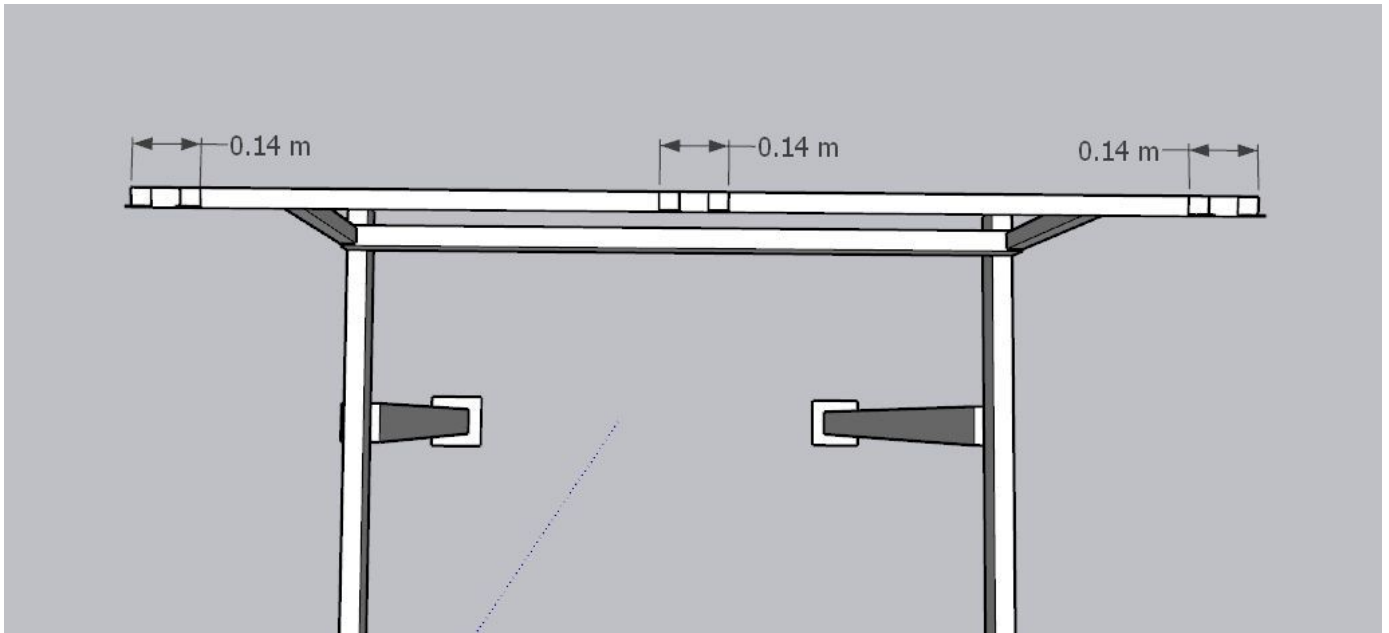


Structure details (16)

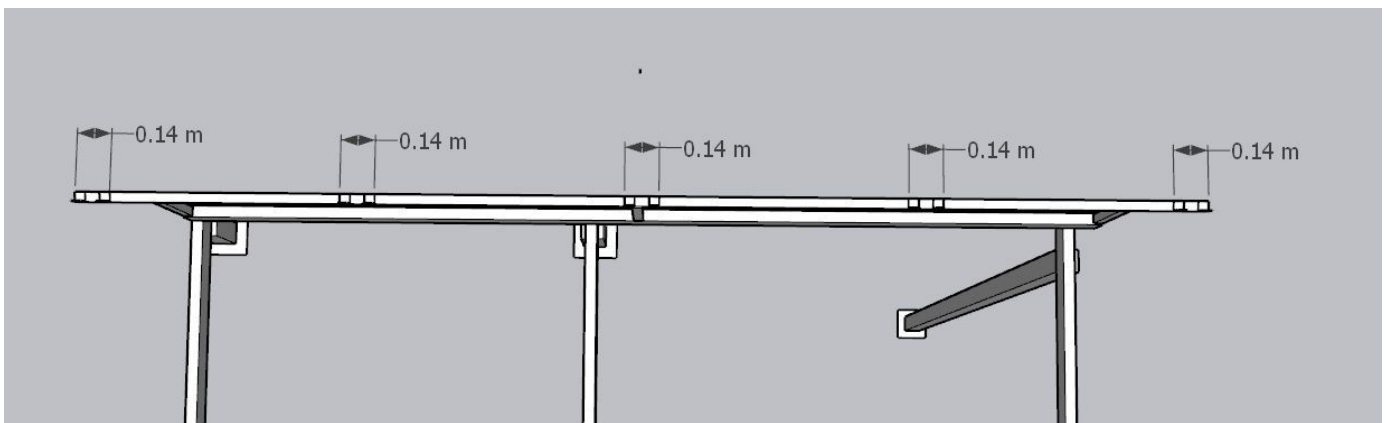

Structure details (17)

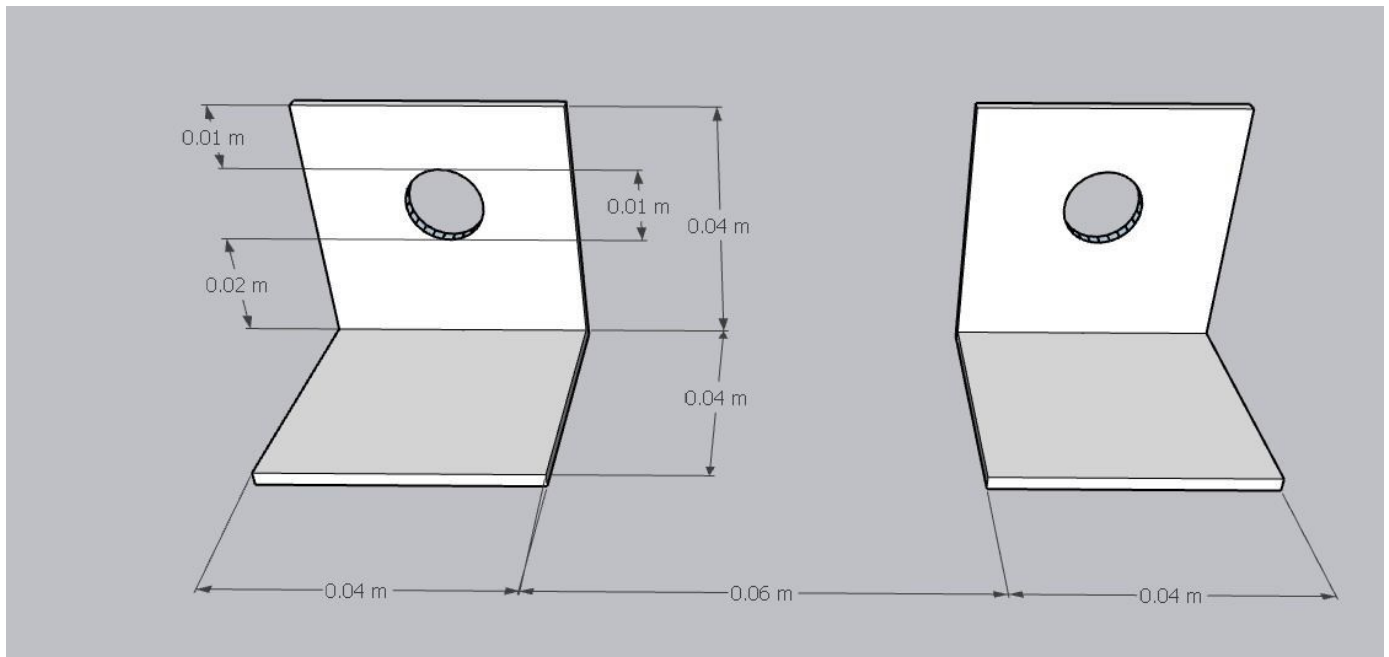

Structure details (18)

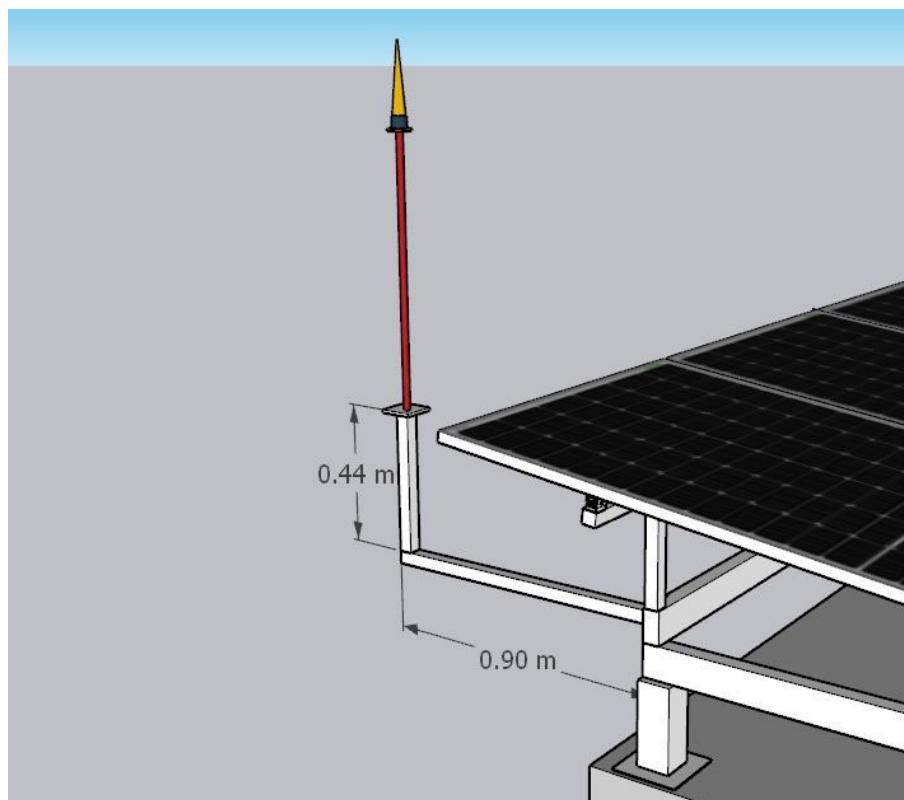


Structure details (19)

Material Storage



Proposed PV Area

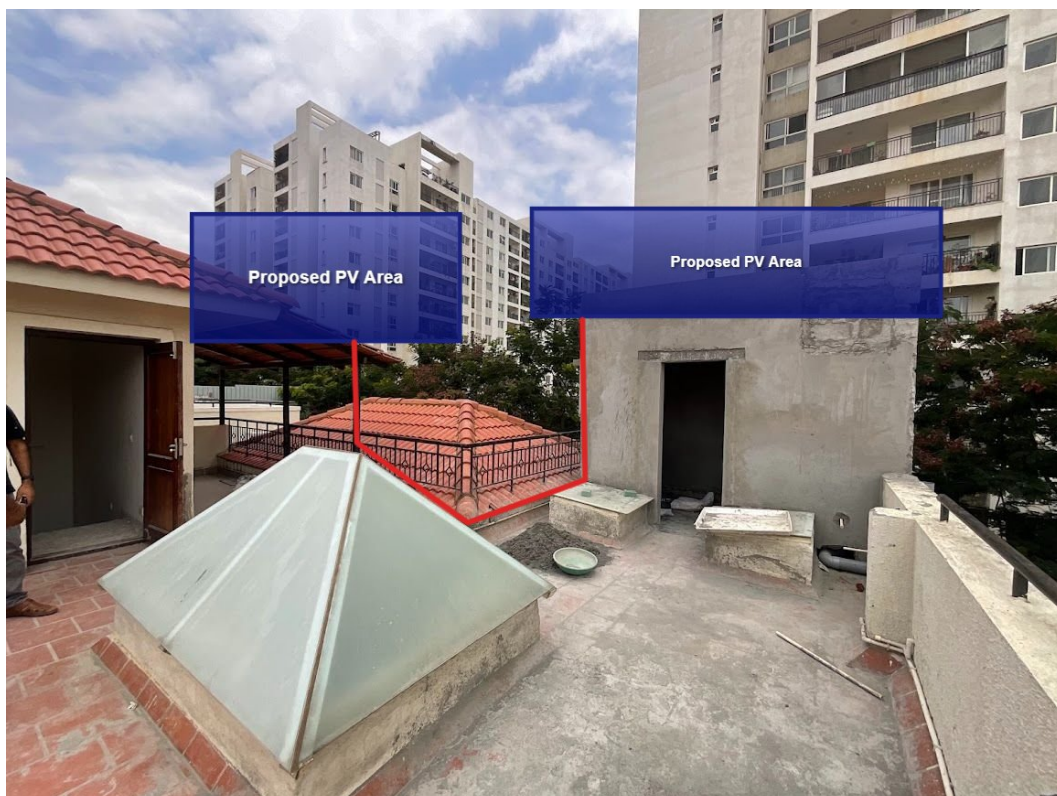


Cable Routing





Equipment Location

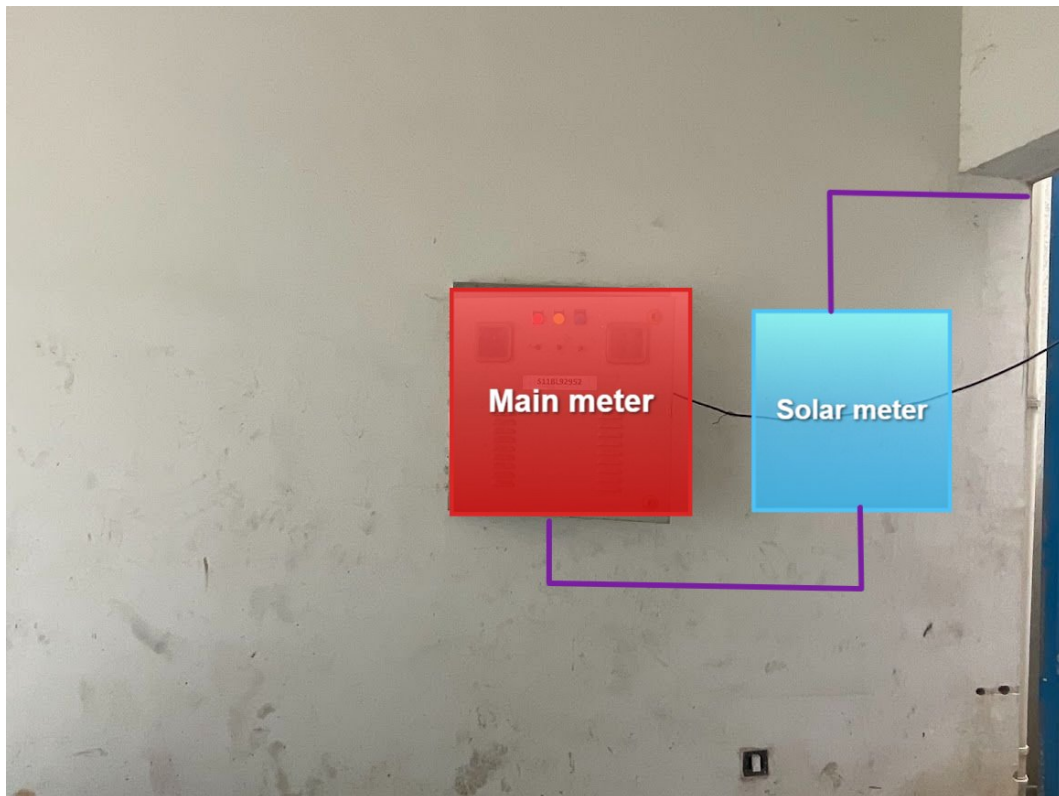

Earth Pit Location





OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As per the customer's suggestion, the routing, cable earthing and also solar meter location have been considered.
2	At the time of installation, the tiled roof adjacent to the headroom area must be removed. Additionally, the tiles on the west side of the roof must be removed to facilitate the installation of the posts (legs). Both activities are under the customer's scope of work.

Customer Scope

#	Observation
1	Wi-Fi is under the customer scope
2	MS fabrication is under customer scope

THANK YOU

Dear Nischal Dutta,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
