

Technical Site Visit Report

Prepared for: BHAWANI SINGH VISHEN - Site 8

PROJECT INFORMATION

Report Number	ESV-2026-0016
Project ID	3C246881
Project Name	BHAWANI SINGH VISHEN
Building Name	Site 8
Billing Name	BHAWANI SINGH VISHEN
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju
Site Address	SITE 8, CENTRAL AVENUE PHASE 2 , PIONIER LAKE DISTRICT , GATTAHALLI, SARJAPUR, BANGALORE, KARNATAKA 560099
GPS Coordinates	12.86834388163449, 77.70140811893845
Google Maps	https://www.google.com/maps?q=12.868343881634491,77.70140811893845
Visit Date	2026-03-14
Visited By	K Naveen
Revision	Rev 2

CLIENT INFORMATION

Client Name	BHAWANI SINGH VISHEN
Contact	9650201988

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	8.4
Module Make & Capacity	Waaree bifacial Non DCR 700 W

Module Length (mm)	2384
Module Width (mm)	1304
Number of Panels	12
Inverter Type	Hybrid (String)
Inverter Brand	Deye 8 kW 3phase hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	SE-F5plus
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstruction in the roof are lift headroom water tanks columns that could affect the solar installation.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	HDGI Elevated Structure
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	Yes	The building is under construction
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	At the time of site visit site is in under construction, client will give the provision for DC cables

#	Question	Answer	Notes
13	What is the height of the building and how many floors does it have?	G+3+Headroom is approximately 20 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	N/A	-

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	N/A	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The inverter, DCDB, ACDB, Battery will be place client store room which is located inside the headroom.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located rear side of the building.	-
6	Where is the Internet Router located?	Under construction	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	-	Building is under construction. Main meter is not yet installed.
2	Is the Meter cubicle photo matching with the previous answer?	No	Under construction
3	Has the termination point in the Main meter panel been identified?	No	Not Available
4	Is the Termination Point easily visible or sealed?	-	Not Available
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	No	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Not Applicable	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Not Available
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	Not Available

#	Question	Answer	Notes
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	No	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 2000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 2000, width: 1500	-
22	Is LAN cable under customer scope?	N/A	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).





This route (using Staircase) will be followed to carry Small items



Staircase Details



Meter Box



Material Storage



Proposed PV Area





Cable Routing




DC Cable & DC Earthing routing



DC Cable will run through the conduit pipe

Equipment Location

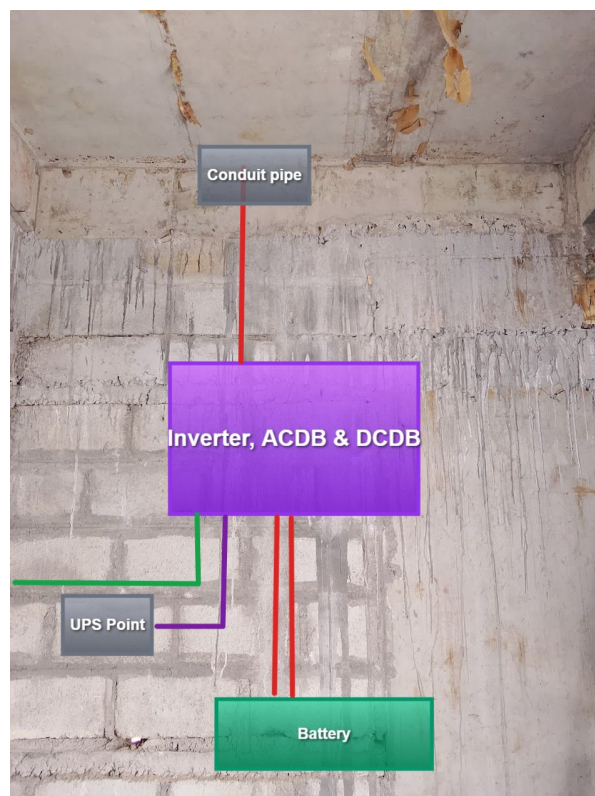




AC Earthing Cable Will run through this provision


Earth Pit Location




Site Layout - Top View

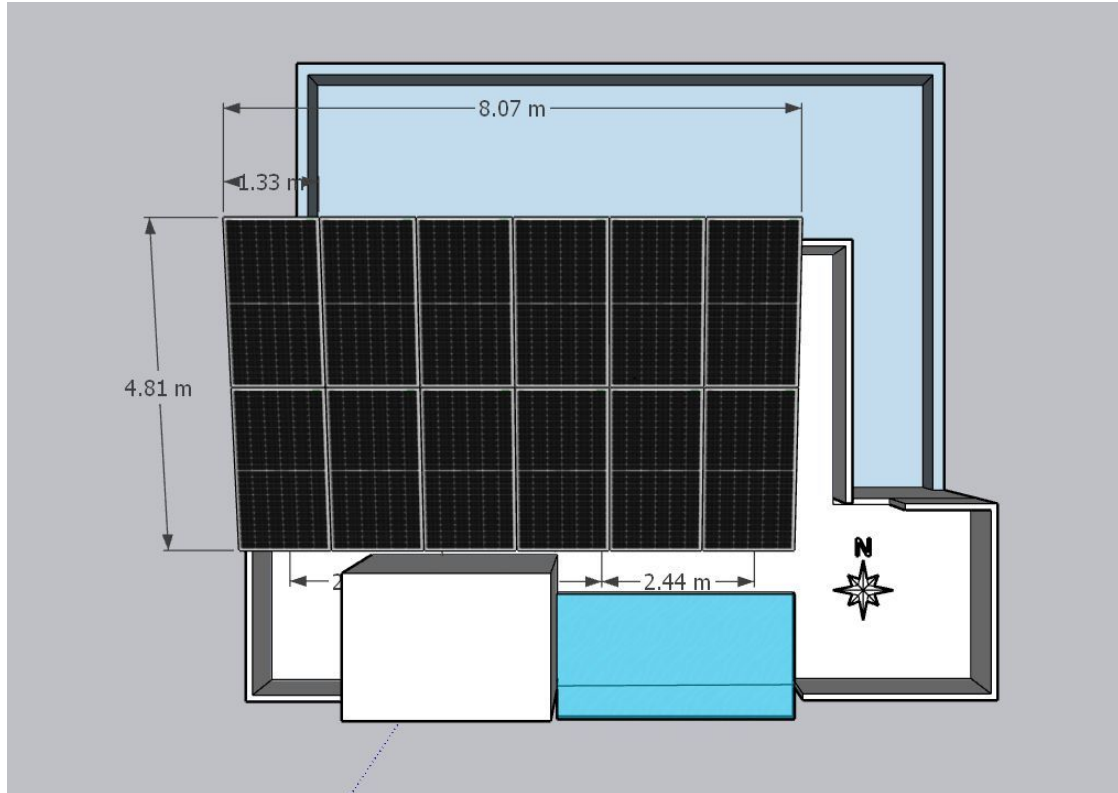


Top View

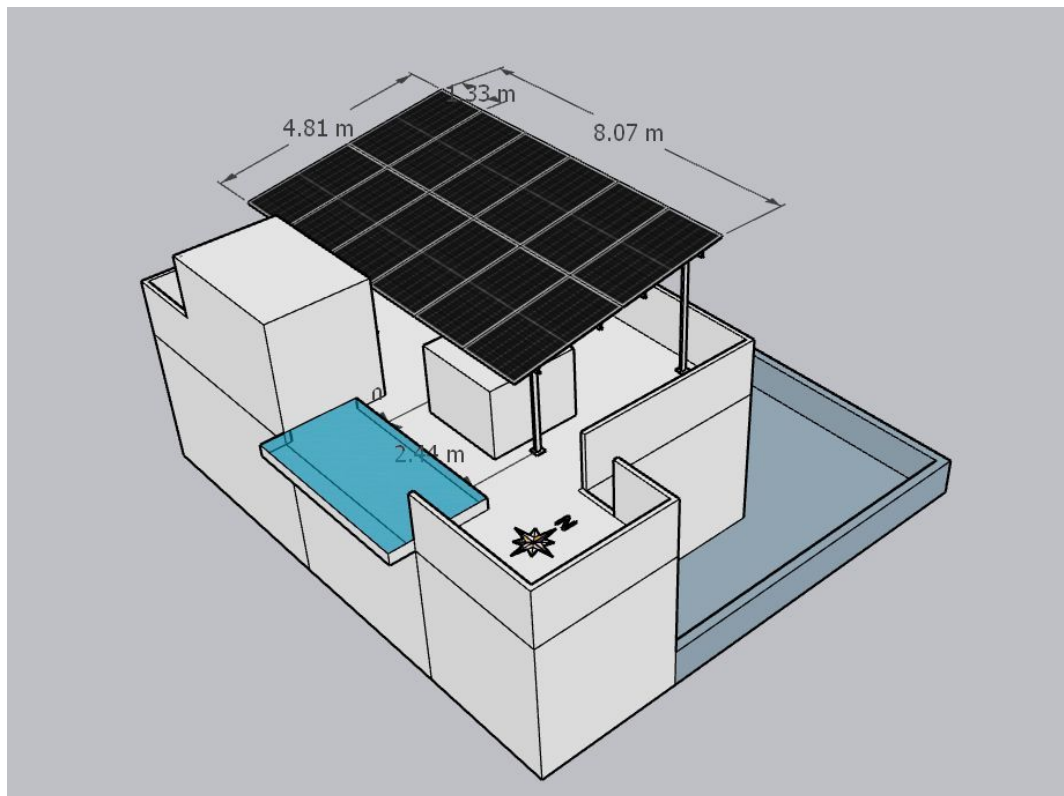

Side View

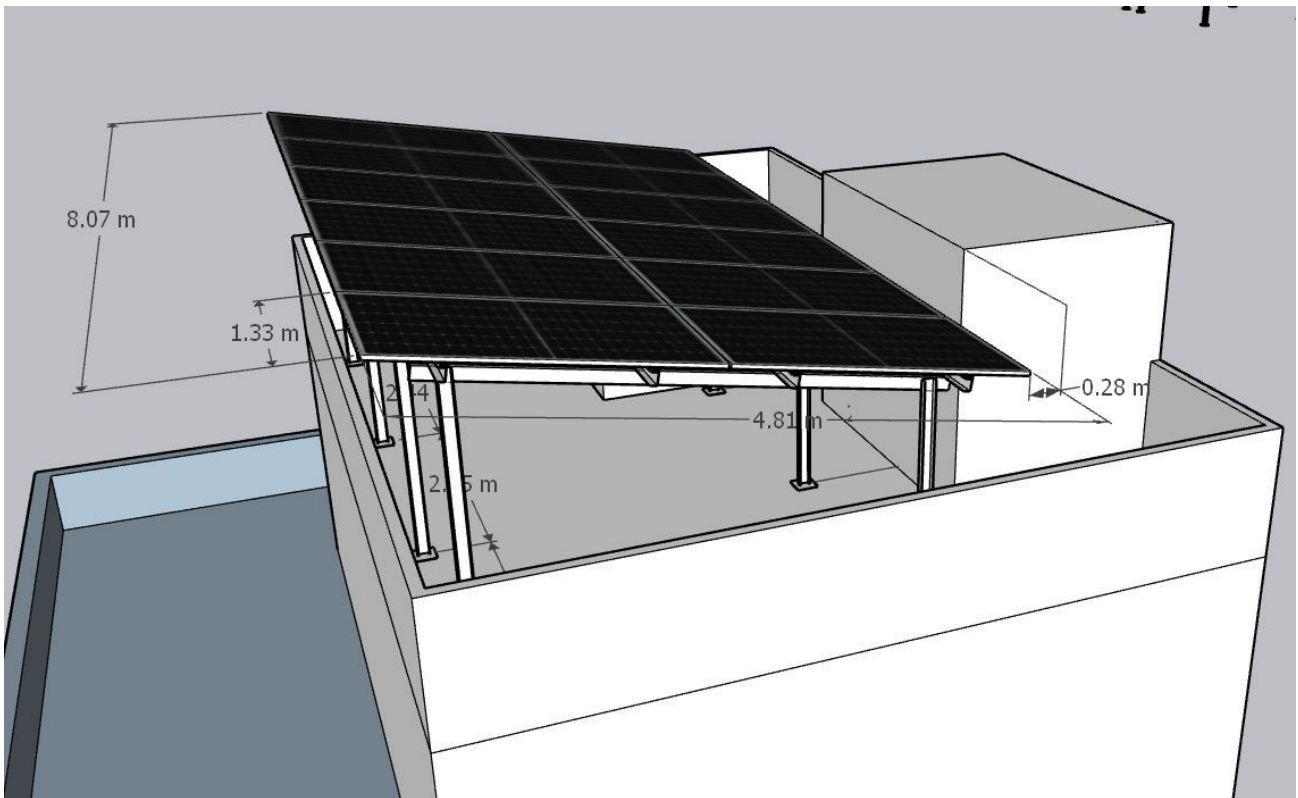

Iso view

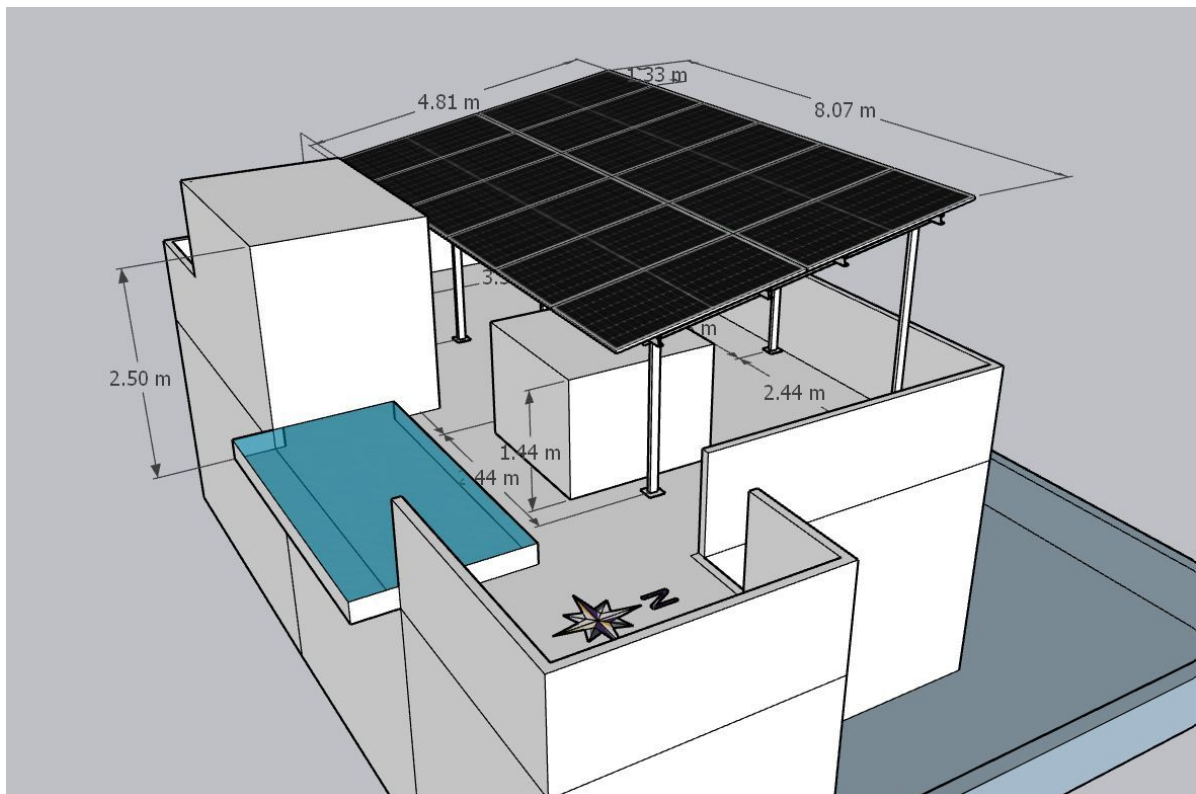

Side View

OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the solar meter location is under customer scope
2	UPS point near the inverter location is under customer scope.
3	As per customer suggestions only the routing and panel layout has been finalised
4	As per the customer inputs only the lift headroom 4 ft has been considered
5	Before installing the panels customer needs to cut the reinforcement rebars
6	During the site visit the site is fully under construction
7	https://photos.app.goo.gl/PQCeHpP3FcRz5HDJ6
8	Since the site is in under construction the meter is not yet installed

THANK YOU

Dear BHAWANI SINGH VISHEN,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
