

Technical Site Visit Report

Prepared for: Aravinth Kumar_Aashritha Honey Dell Layout_3.1kWp_String

PROJECT INFORMATION

Report Number	ESV-2026-0205
Project ID	0EAD4817
Project Name	Aravinth Kumar_Aashritha Honey Dell Layout_3.1kWp_String
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	HARIOM PATEL
Site Address	Villa 32, Aashritha Honey Dell Layout, Opposite to Celebrity Nature Habitat, Silkfarm road, Bidaraguppe, Sarjapur Attibele Road, Bengaluru 562107.
GPS Coordinates	12.818133, 77.793015
Google Maps	https://www.google.com/maps?q=12.818133,77.793015
Visit Date	2026-09-15
Visited By	ABILASH N K
Revision	Rev 1

CLIENT INFORMATION

Client Name	Aravinth Kumar
Contact	+91 9632916467

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	3.10
Sanction Load (kW)	3
Module Make & Capacity	Premier 620Wp Topcon Bi-Facial DCR
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	5
Inverter Type	String
Inverter Brand	Deye: 3KW - 48V - LV - Single Phase
Number of Inverters	1
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The inverter, DCDB and ACDB can be mounted on the wall in the ground-floor car porch.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, discussed with the customer and finalised the location for earthing.	-
6	Where is the Internet Router located?	Ground floor.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	3 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-

#	Question	Answer	Notes
8	What type of mounting structure is planned?	Elevated	<i>Elevated HDGI - 2m Front Leg (Single Row, Portrait) with Drilling & Only Base Plate Cement Covering</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	8 meters. (G + 1)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999)	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	<i>The existing RCC tank tower close to the planned installation is suitable for mounting the lightning arrester (LA).</i>
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>Space for digging the earth pit is available in the car porch floor of the building. The tiles have to be removed as per the requirement.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	No	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-



#	Question	Answer	Notes
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 3000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout - Top View

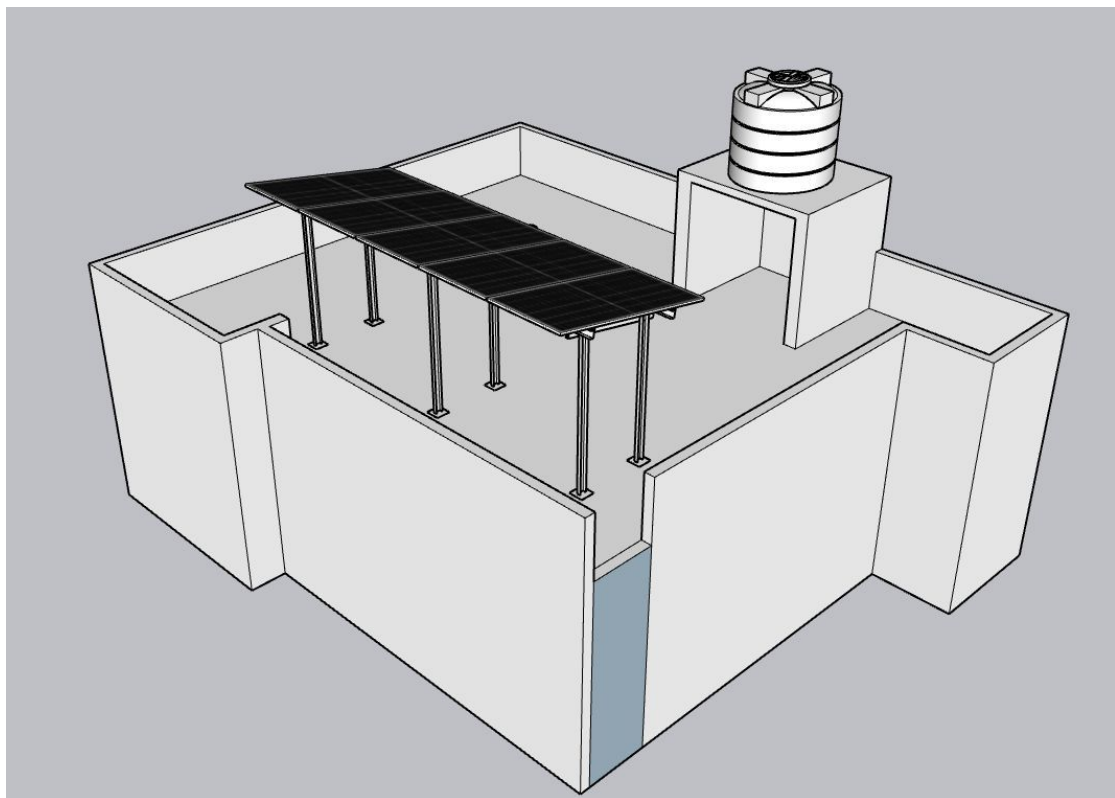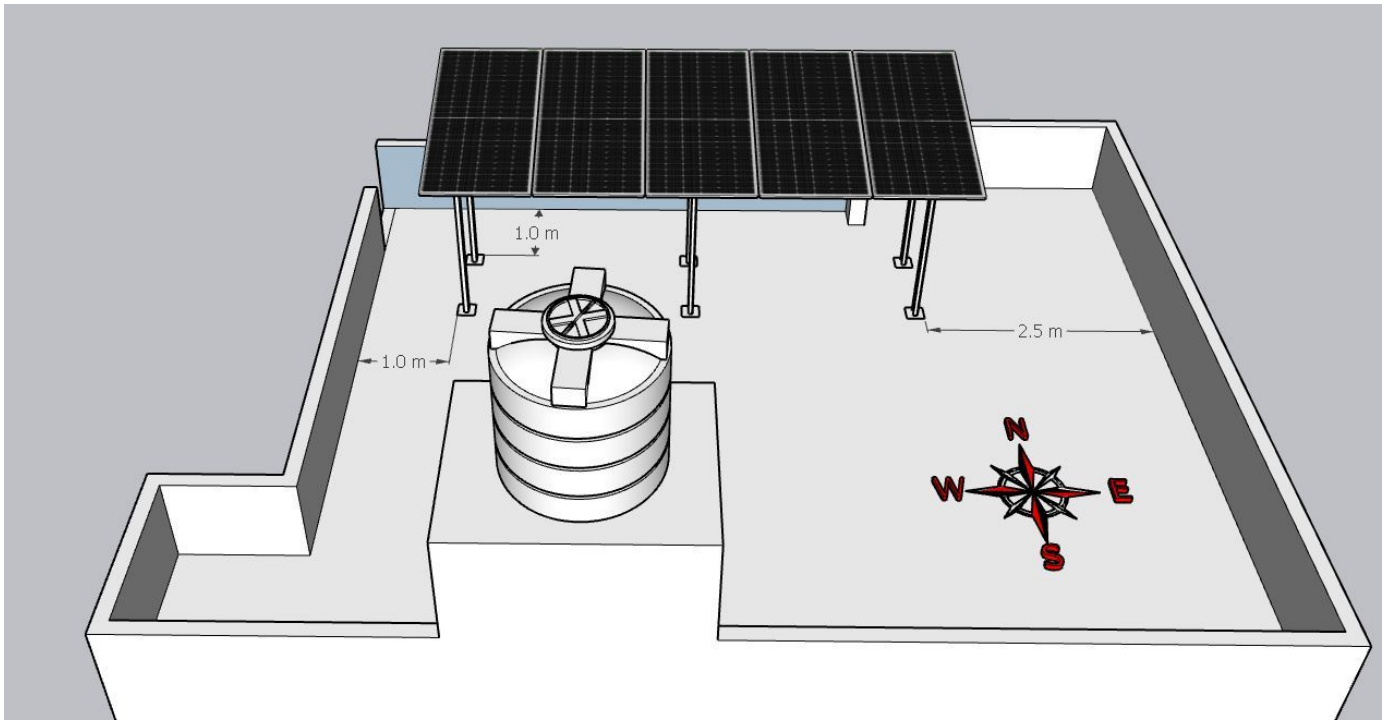

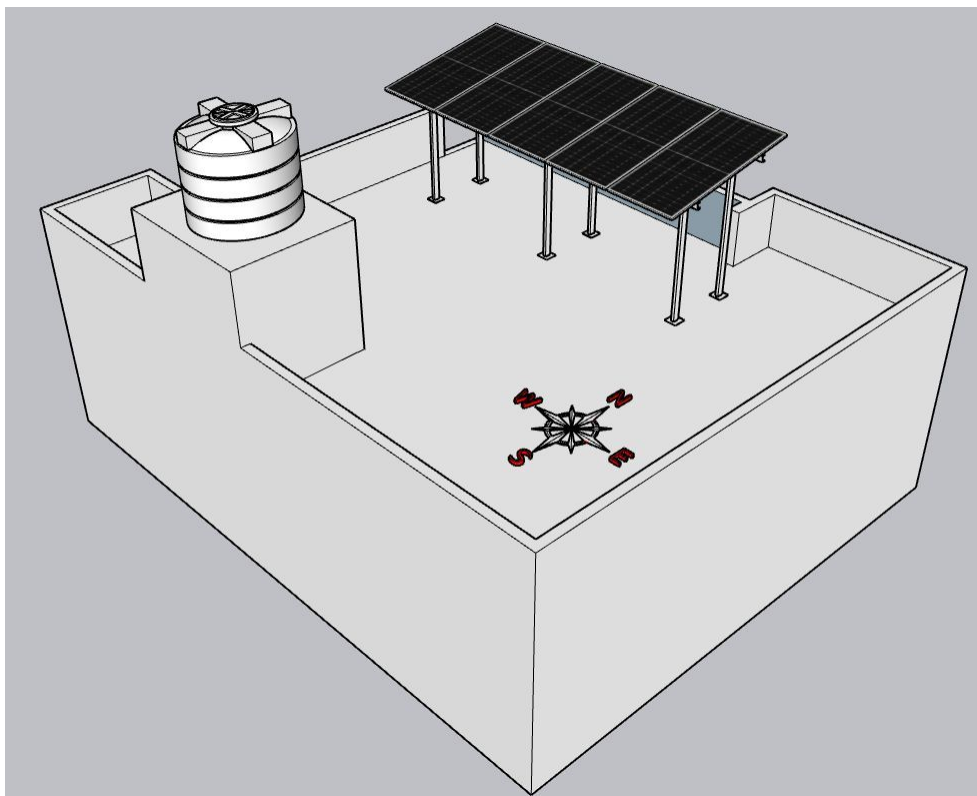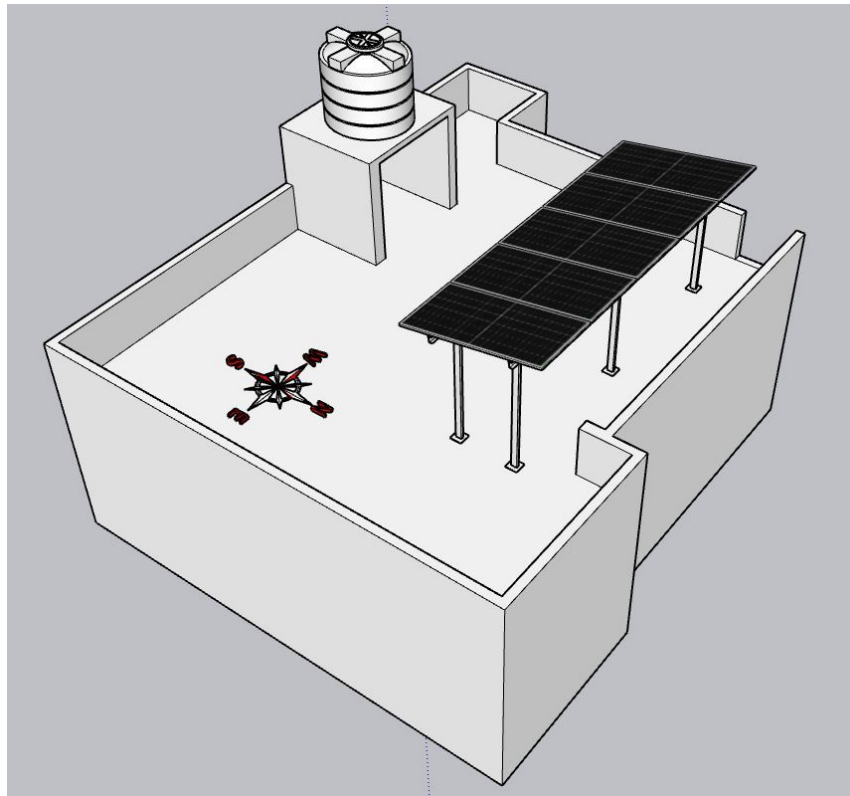

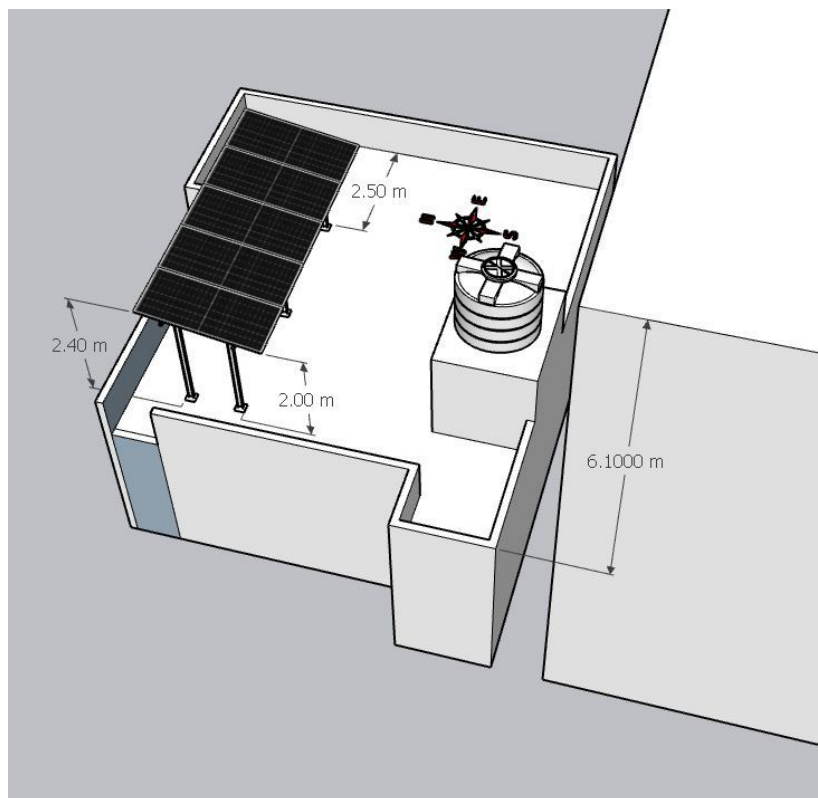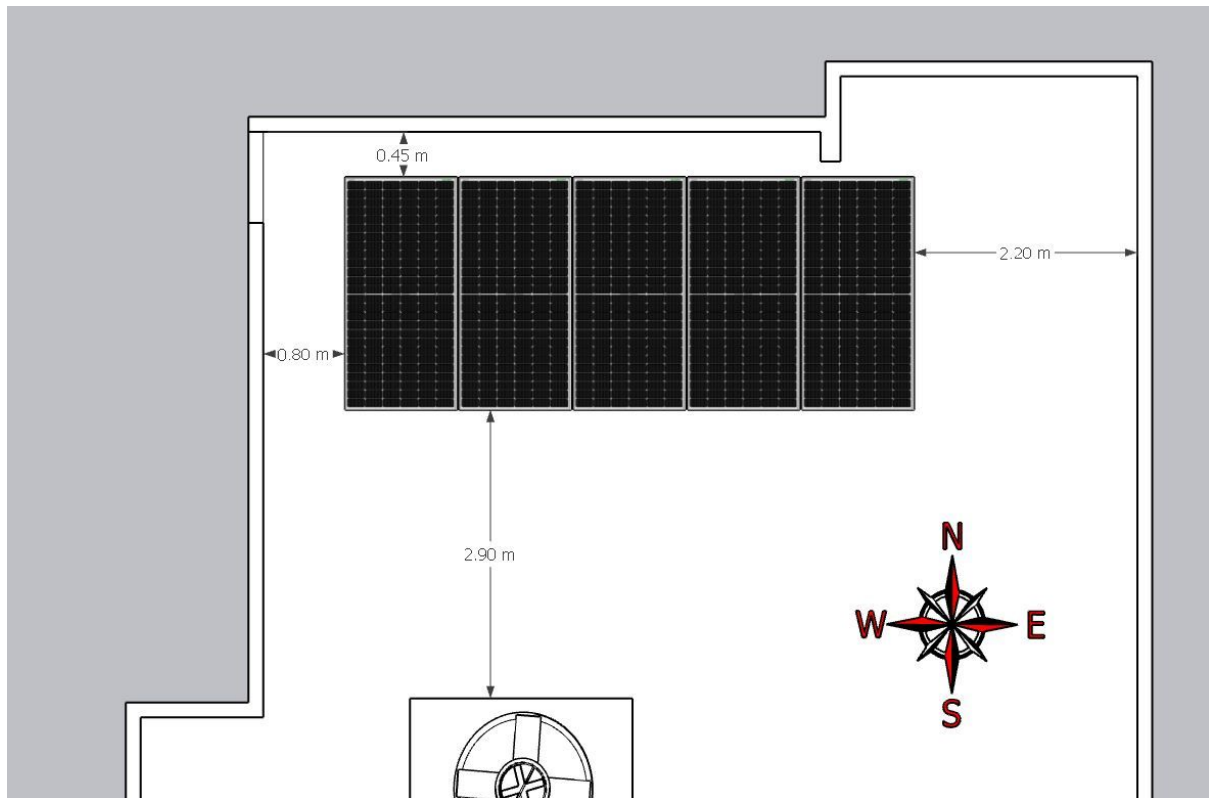

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



The materials can follow the stairs until reaching the terrace.




The materials can follow the stairs until reaching the terrace.



The materials can follow the balcony stairs until reaching the terrace.

Staircase Details

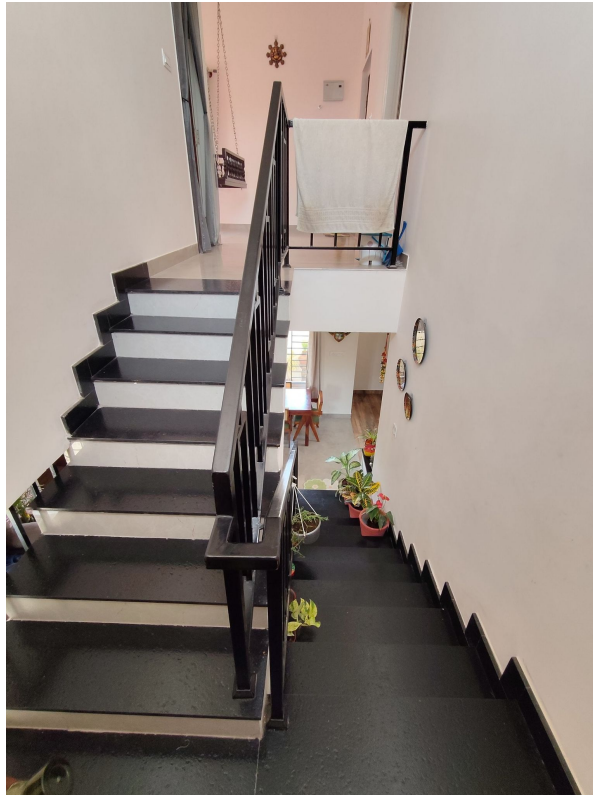

Staircase width: 900 mm

Proposed PV Area





Cable Routing







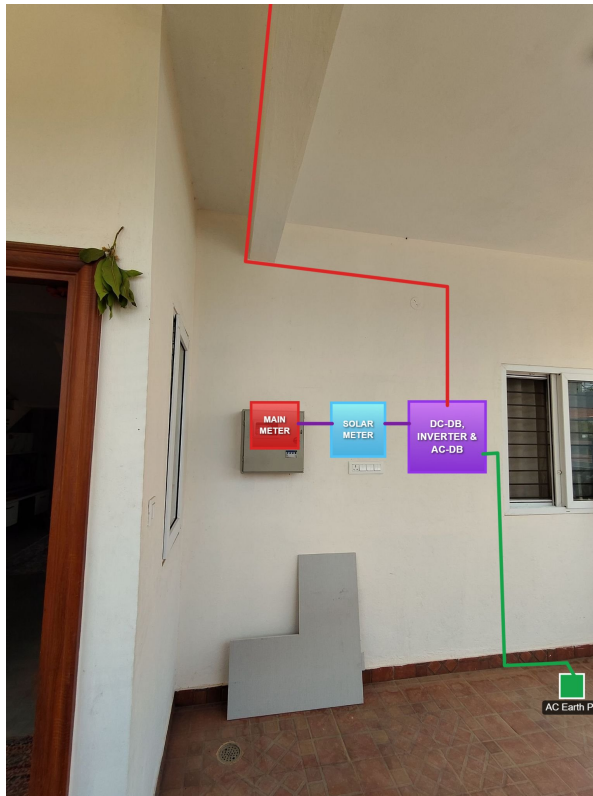


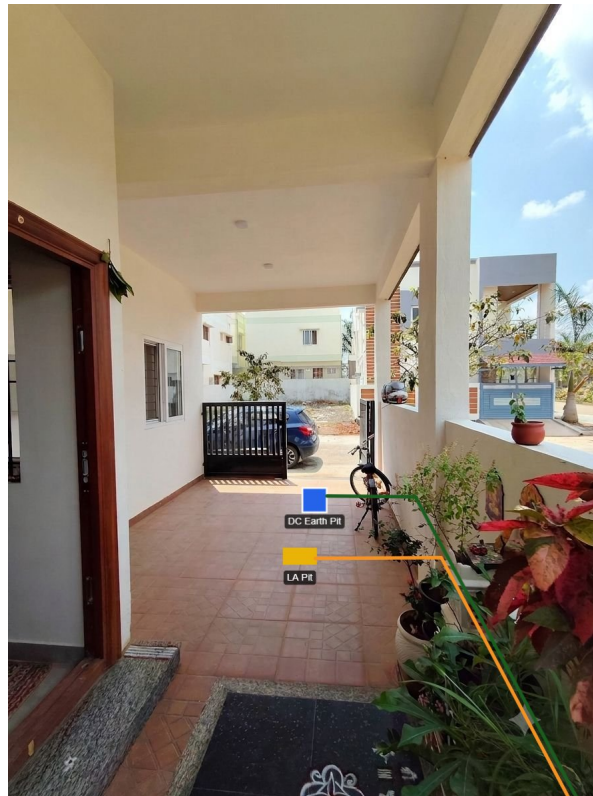

Meter Box



Shadow Analysis

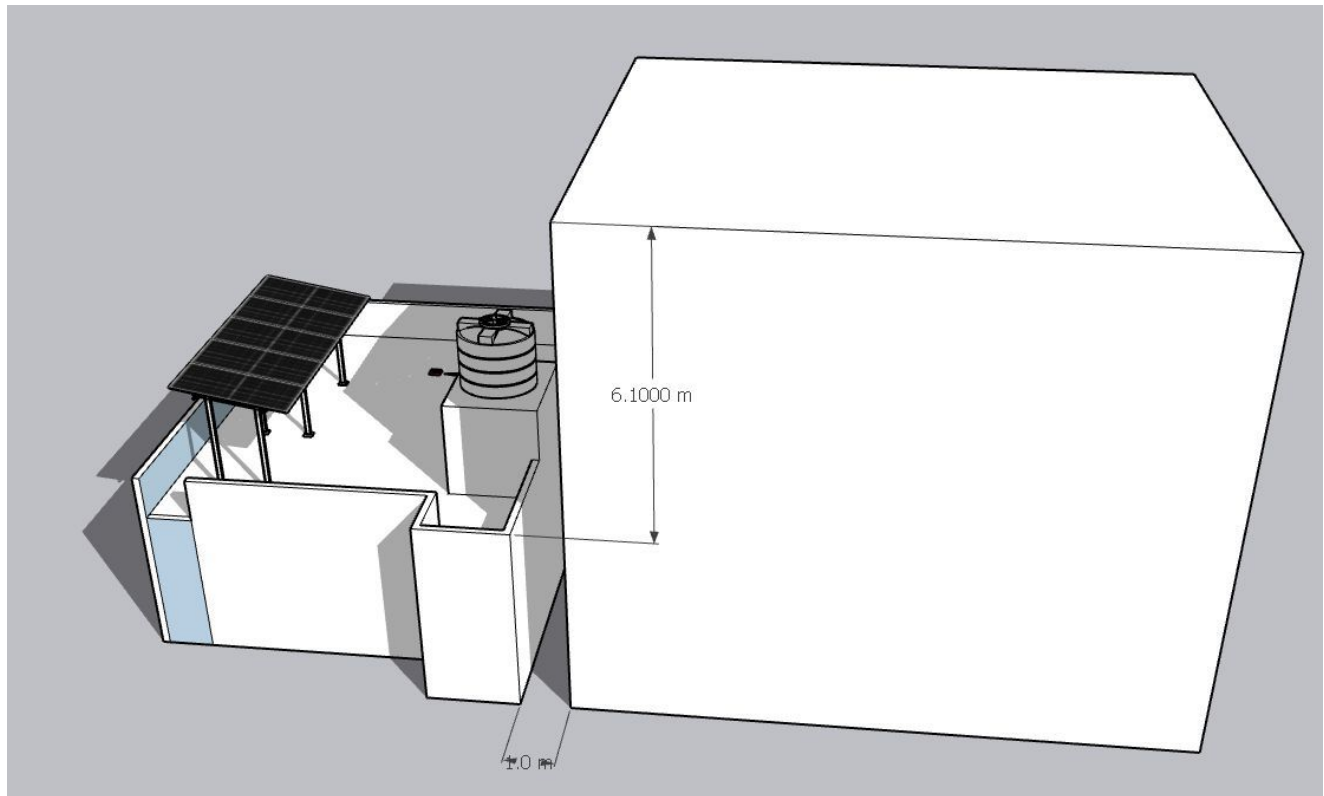

Shadow view (Nov - Jan at 3pm)

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 3.1 kWp On-Grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCO regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.

THANK YOU

Dear Aravinth Kumar,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
