

Technical Site Visit Report

Prepared for: Vani Kolla_Banneragatta Road Non Subsidy_10.4kWp_Microinverter (IQ Series)

PROJECT INFORMATION

Report Number	ESV-2026-0219
Project ID	EVDMUJDD
Project Name	Vani Kolla_Banneragatta Road Non Subsidy_10.4kWp_Microinverter (IQ Series)
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju JS
Site Address	901/97/196, Eastern Portion, Sun City Layout, 1st Main Road, 2nd Cross, Santhruptunagar, Near The South School, J.P Nagar, 7th Phase, Bangalore, Karnataka,560078
GPS Coordinates	12.885073, 77.585478
Google Maps	https://www.google.com/maps?q=12.885073,77.585478
Visit Date	2026-09-19
Visited By	ABHILASH R S
Revision	Rev 5

CLIENT INFORMATION

Client Name	Vani Kolla
Contact	'+91 9789099841

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	10.455
Sanction Load (kW)	10
Module Make & Capacity	Premier 615Wp Topcon Bi-Facial Non-DCR
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	17
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	17
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Enphase accessories and the solar meter provision have been given to the existing LT panel near the main meter box located on the ground floor of the building.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes. The customer will be providing all the earthings pits as well as pulling the cables upto the points where the respective earthings are to be terminated.	-
6	Where is the Internet Router located?	Wi-Fi/Internet router not yet installed. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	An HDGI-elevated customised structure will be provided at the proposed premises by the customer.
9	What is the orientation of the solar panels?	["East"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	The conduits to pull the cables from the roof terrace to the ground will be provided by the customer.
13	What is the height of the building and how many floors does it have?	24 metres (G + 5)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	An LT panel with the provisions for the main meter, solar meter and the Enphase accessories box have been provided by the customer.
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	The earthing strip for the lightning arrester has been pulled from the earthing pit to the tank tower location by the customer.
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-



#	Question	Answer	Notes
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	Yes	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>The spare earthing pits have been made by the customer at the premises, and the earthing cables have been pulled upto the necessary termination points.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	Not Applicable	<i>HDGI structure will be provided by the customer at the proposed premises as per the design given by ECOSCH.</i>
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 400, width: 400	<i>The solar meter fixing provision is available in the new LT panel installed by the customer.</i>
21	Provide the dimension for earth pits location (L x W of available space).	-	<i>Earthing pits are made by the customer and are ready for the cable termination.</i>
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable

Site Layout - Top View

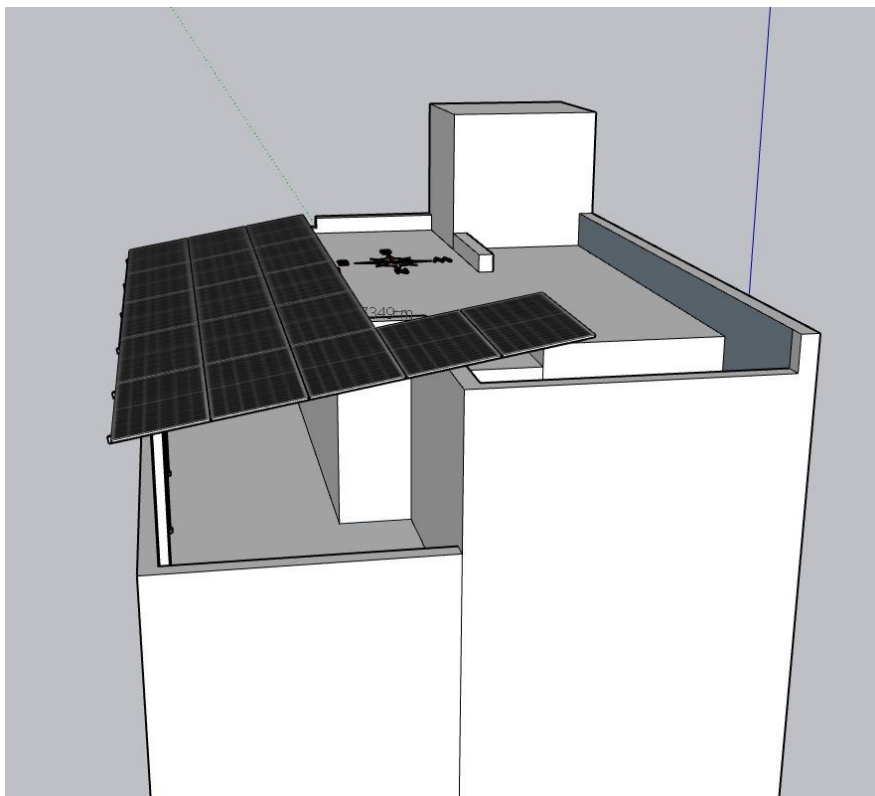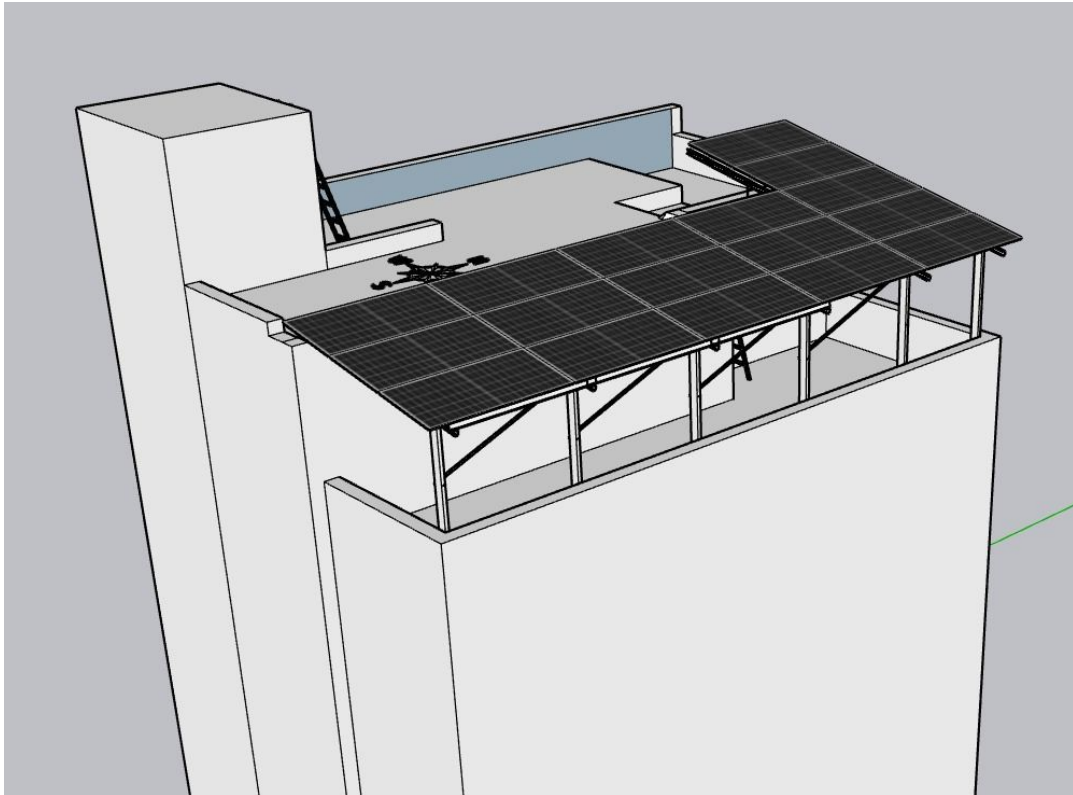

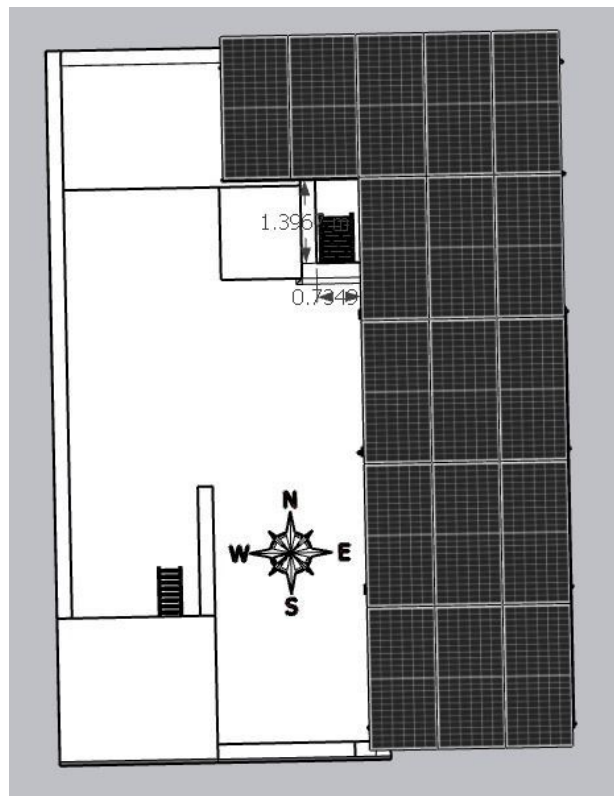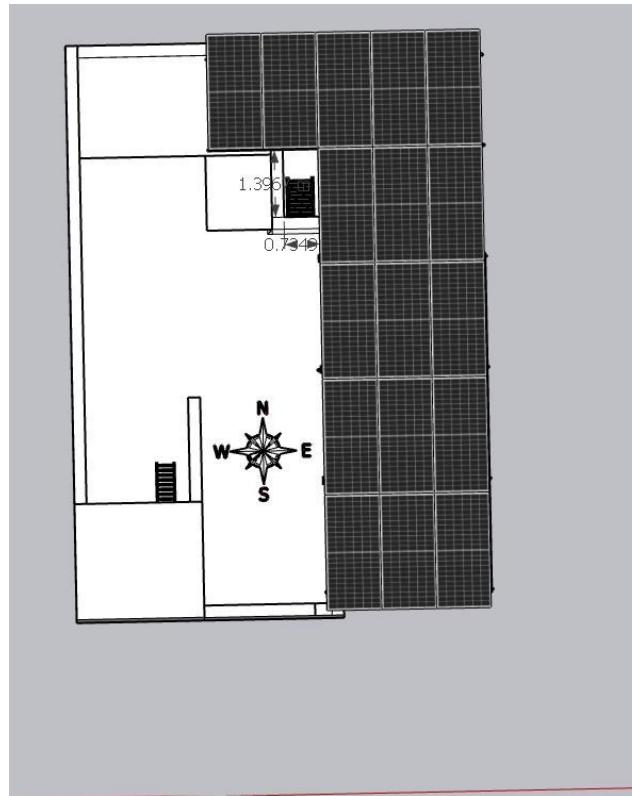

Building Exterior



Material Delivery Route



The materials can be shifted to the terrace via the inner staircase.



The materials can follow the stairs.



The materials reaching the terrace floor




The materials can be stored here until the installation begins.

Staircase Details




Staircase width: 1000 mm


Proposed PV Area

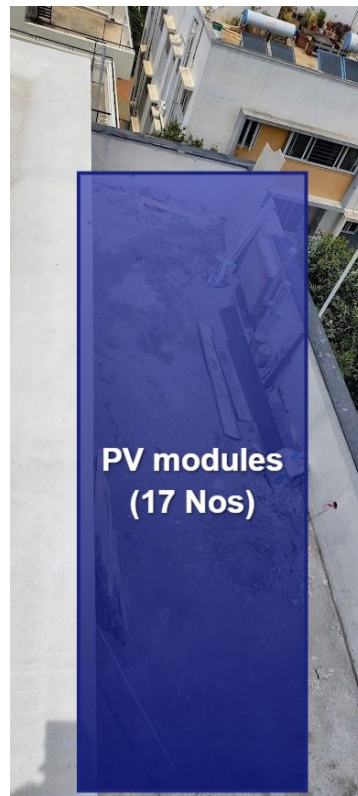

Cable Routing

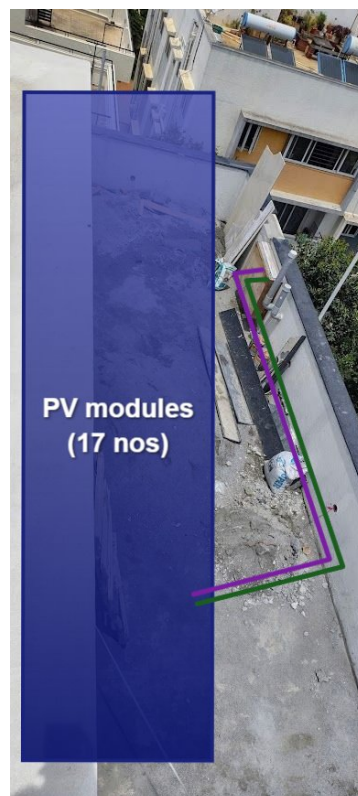


The AC cable and the structure earthing cables can be pulled upto the looping box provided at the terrace floor by the customer.

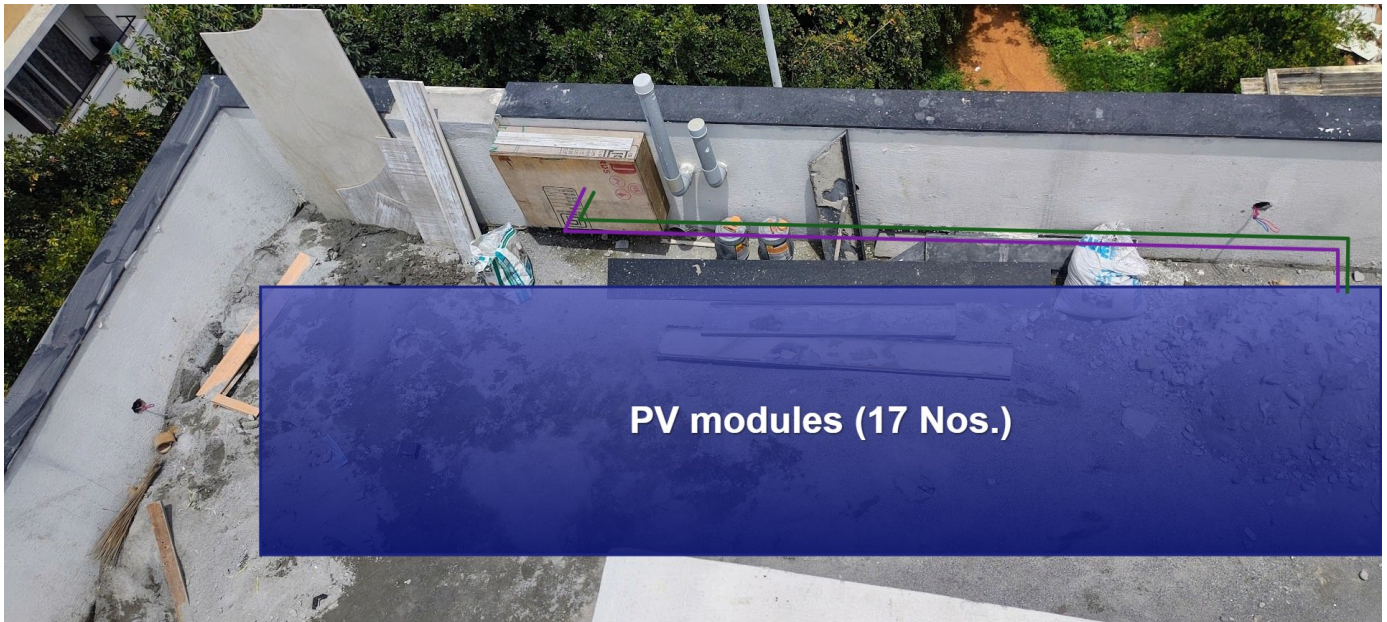

the looping box allows the AC cable and the structure earthing cable to reach the LT panel cabin at the ground floor.




Two separate cabins allocated for the solar meter and the Enphase accessories box.

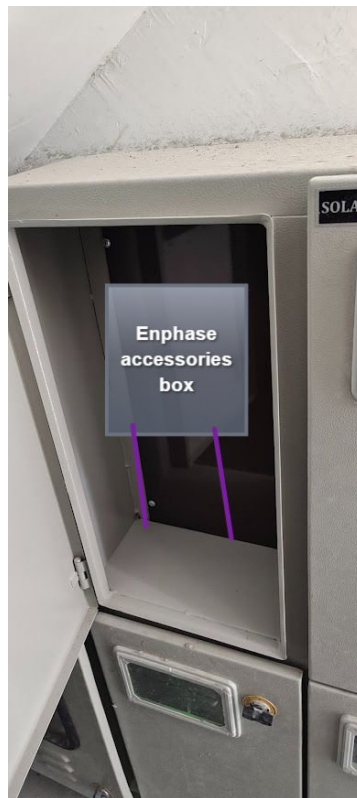

Initially the AC cable from the looping box at the terrace floor will be given to the enphase accessories box



The AC cables from the enphase accessories box will be given to the solar meter

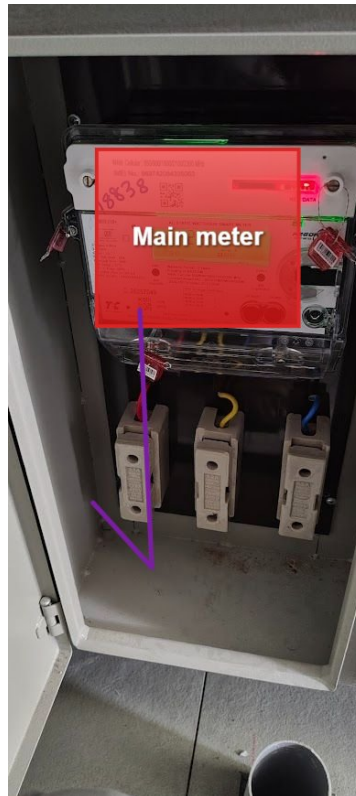

finally the AC cable from the solar meter will be connected to the main meter.



The lightning arrester can be connected to the earthing cable already given by the customer.



The DC earthing cable can be terminated at this cabin where two set of earthing cables available.

Meter Box



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 10.455kWp, On-grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the Enphase Accessories box location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.
3	Ensuring the existing concealed conduits are reliable enough to pull the cables.
4	All earthings (including AC, DC & LA) up to the required termination points will be provided by the customer.
5	HDGI structure will be provided by the customer at the proposed premises as per the design given by ECOSOCH.
6	Providing the AC cable from the solar array to the LT panel at the ground floor.

THANK YOU

Dear Vani Kolla,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
