

Technical Site Visit Report

Prepared for: Mukunda_Hassan_9.84kWp_IQ8P

PROJECT INFORMATION

Report Number	ESV-2026-0135
Project ID	B8FECEC3
Project Name	Mukunda_Hassan_9.84kWp_IQ8P
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Mahantayya
Site Address	Behind Bhanu Theathre Bhimmayya colony Hassan - 573201
GPS Coordinates	13.00124492310548, 76.10559377400712
Google Maps	https://www.google.com/maps?q=13.001244923105478,76.10559377400712
Visit Date	2026-06-05
Visited By	Charan
Revision	Rev 0

CLIENT INFORMATION

Client Name	Mukunda
Contact	96324 80228

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	9.84
Sanction Load (kW)	10
Module Make & Capacity	Waaree Bi-facial Non DCR and 615Wp
Module Length (mm)	2382
Module Width (mm)	1134

Number of Panels	16
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	16
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Earthing is already completed but we have to take a cable from it.	-
6	Where is the Internet Router located?	Under Construction	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	<i>Puff Sheet roof</i>
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	2	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Other	<i>(Landscape Orientation on Metal Sheet with Trapezoidal Profile)</i>
9	What is the orientation of the solar panels?	["South"]	-

#	Question	Answer	Notes
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	G+4 with 18m height	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	More than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	-
11	Is there space available to dig DC, AC and LA earth pits?	No	Earthing is already completed
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2500, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	N/A	-
22	Is LAN cable under customer scope?	No	-



#	Question	Answer	Notes
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-


PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout

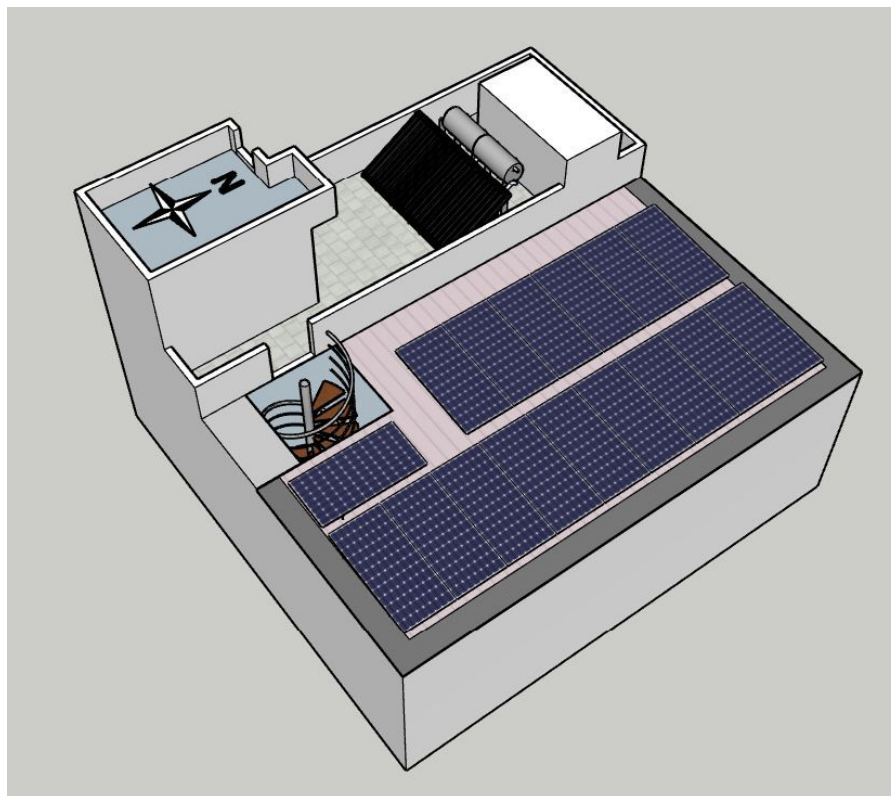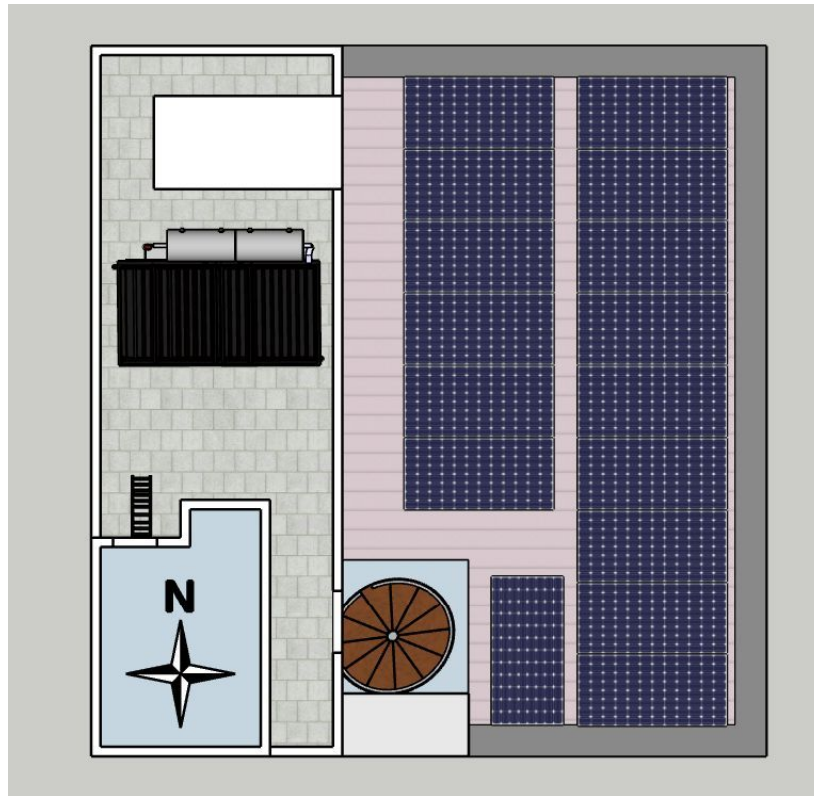

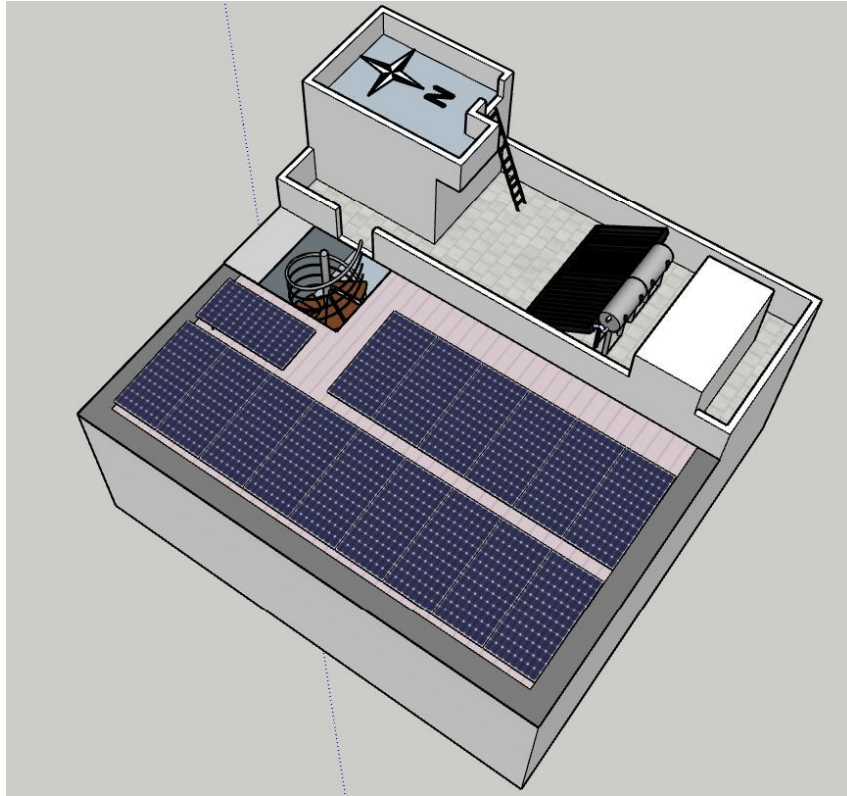

Building Exterior



Material Delivery Route




This route (using staircase) will be followed to carry all items.



We have to take the panels from the outside, as there is no other way to move them to the terrace.

Staircase Details

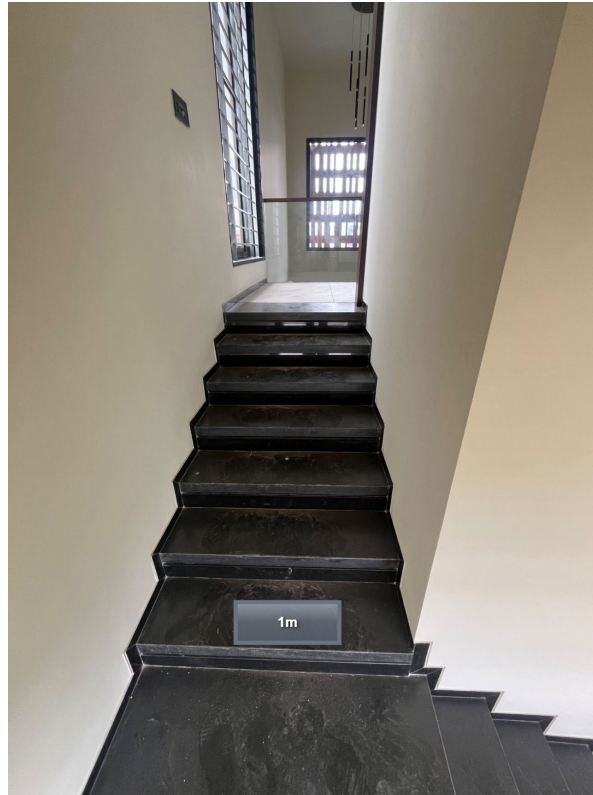

Material Storage



Inside this room we can store the panels and all other materials



Proposed PV Area



Cable Routing




We have to make hole to pass AC cable.




Enphase accessories should be installed in the terrace room.



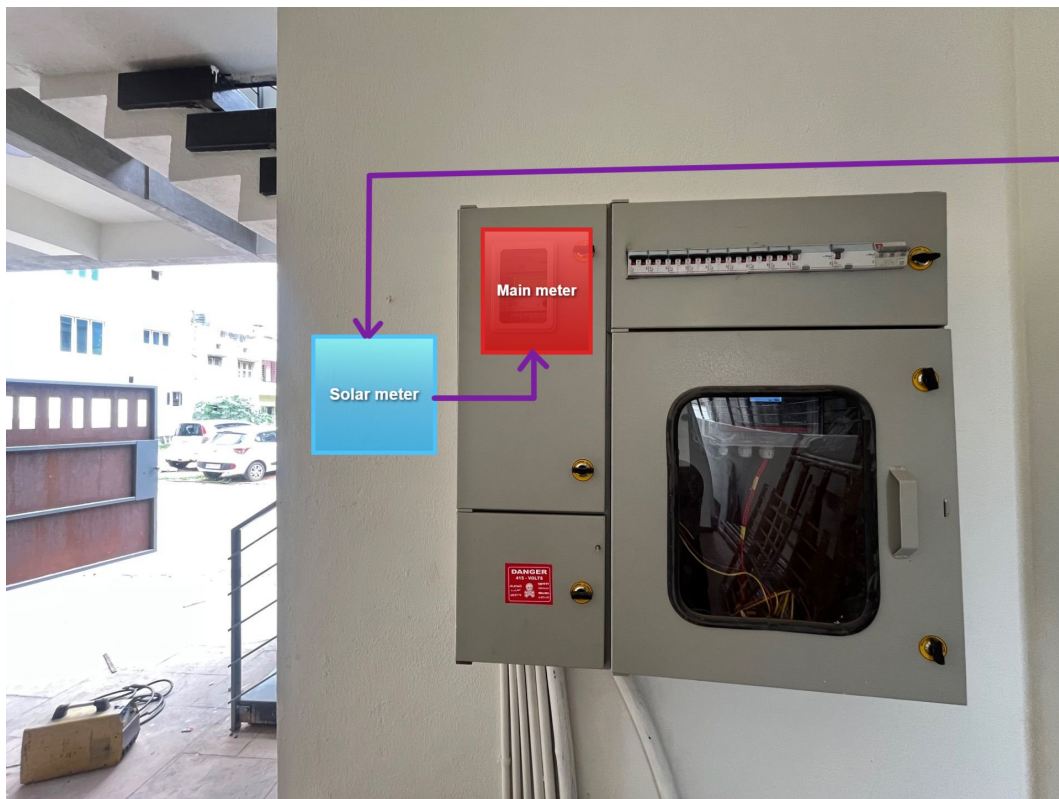





Earthing Routing

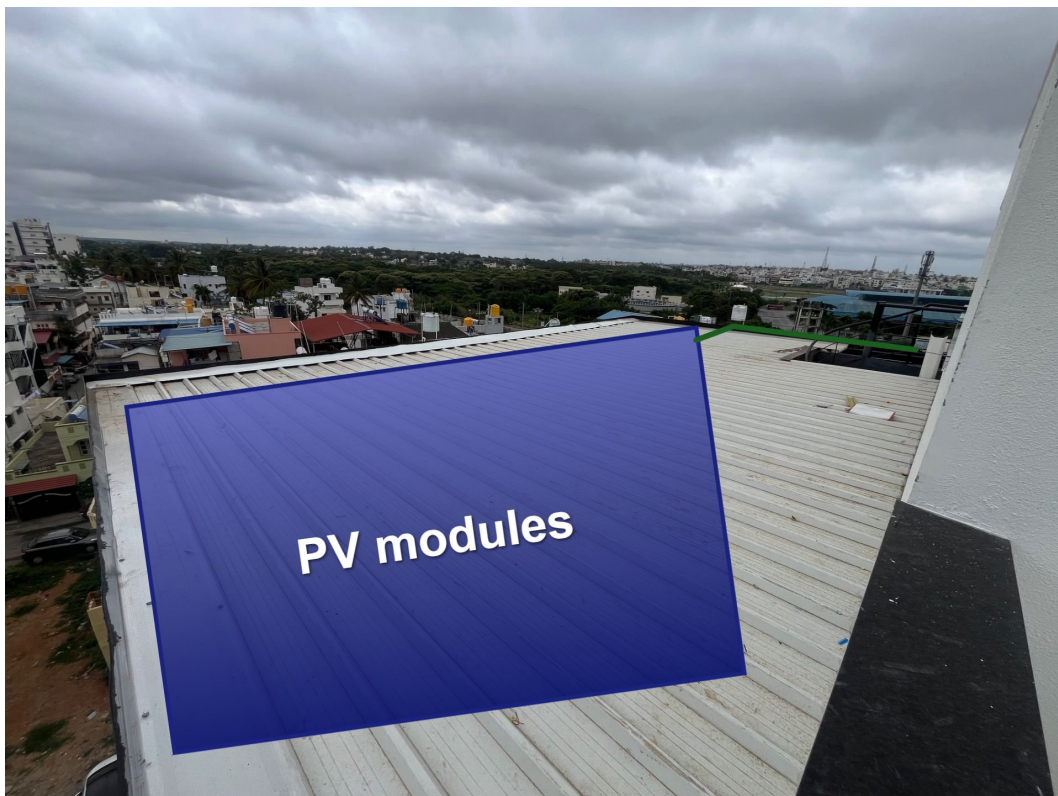



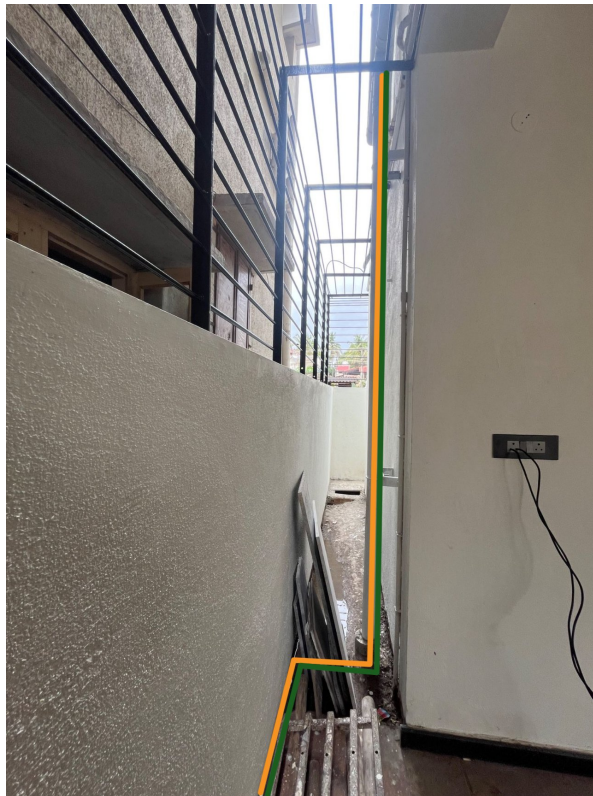

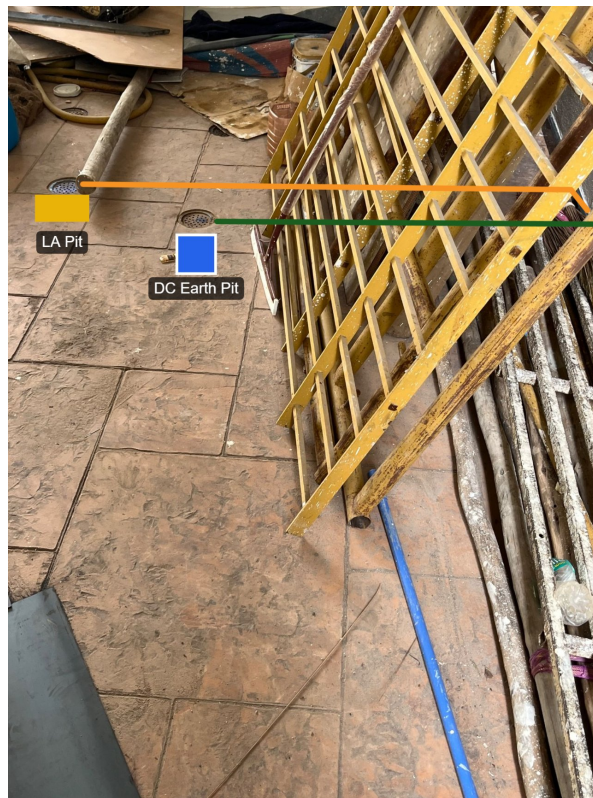

Chipping work is required to route the earthing cable from the earth pits.

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	The Enphase accessories should be installed in the terrace room.
2	Chipping work is required to route the earthing cable from the earth pits.

Customer Scope

#	Observation
1	Wi-Fi up to solar meter location.
2	After laying the earthing cable, the chipped area should be covered with concrete.

THANK YOU

Dear Mukunda,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
