

Technical Site Visit Report

Prepared for: Deepa Jayamani Pillai and Kailash Nadh Balakumaran Nair_Classic Orchards Susbidy_7.995kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0209
Project ID	00WHXTAR
Project Name	Deepa Jayamani Pillai and Kailash Nadh Balakumaran Nair_Classic Orchards Susbidy_7.995kWp_Hybrid
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Govindaraju JS
Site Address	House No 0D, Site No 80/2AClassic Orchards Layout Phase 2 main road behind Meenakshi Temple Bannerghatta Road.
GPS Coordinates	12.874328, 77.588501
Google Maps	https://www.google.com/maps?q=12.874328,77.588501
Visit Date	2026-09-22
Visited By	ABILASH N K
Revision	Rev 1

CLIENT INFORMATION

Client Name	Deepa Jayamani Pillai and Kailash Nadh Balakumaran Nair
Contact	+91 8971546660

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	7.995
Sanction Load (kW)	10
Module Make & Capacity	Premier 615Wp Topcon Bi-Facial DCR
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	13
Inverter Type	Hybrid (Enphase)
Inverter Brand	Enphase IQ8P
Number of Inverters	13
Battery	Needed
Number of Batteries	1
Capacity of each Battery (kWh)	5
Battery Model No.	IQ5P 5kWh LFP Battery with 3.8 kW continuous output.
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Enphase system controller, Enphase accessories and the battery can be mounted on the wall (on the east side of the building), opposite to the existing main meter box in the ground floor.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	details: A reliable canopy with enough ventilation from the sides has to be provided by the customer in order to protect the Enphase system controller, the battery and the related accessories.	-
5	Did you discuss the location of the earth pits with the customer?	Yes, discussed with the customer and finalised the location for earthing.	-

#	Question	Answer	Notes
6	Where is the Internet Router located?	Wi-Fi/Internet router not yet installed. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Other	<i>The PV modules have to be mounted in the special MS structure to be fabricated by the customer on the walls at the roof terrace.</i>
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	<i>one roof, but the structure is mounted on three different walls.</i>
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Other	<i>The PV modules have to be mounted in the special MS structure to be fabricated by the customer on the wall.</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	<i>In order to access the PV array, the walkway and ladder provision have to be made by the customer prior to the installation.</i>
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	<i>The customer will be providing the conduits to bring the AC cables and the earthing cables from the top terrace to the bottom until the Enphase controller location.</i>
13	What is the height of the building and how many floors does it have?	10 (G + 1 + headroom)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	The building and the LT panel are under construction. The customer will be providing a solar meter box in the LT panel that they would be fabricating.
2	Is the Meter cubicle photo matching with the previous answer?	No	The building and the LT panel are under construction.
3	Has the termination point in the Main meter panel been identified?	No	The building and the LT panel are under construction.
4	Is the Termination Point easily visible or sealed?	-	The building and the LT panel are under construction.
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	The building and the LT panel are under construction. The customer will be providing a solar meter box in the LT panel that they would be fabricating.
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	There is no reliable ladder provision at present. The ladder provision to access the roof will be provided at the site by the customer prior to the installation.
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	-	The MS fabrication will be done by the customer. The aluminium long rails supplied by Ecosoch will be fixed on top of the L-clamps (being welded by the fabrication team from the customer side).
18	Is ventilation available in the battery location?	Yes	The battery will be mounted on the outer boundary walls of the building, and the sides will be covered with the necessary fabricated shield.



#	Question	Answer	Notes
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	All accessories are to be wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 5000, width: 2000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout - Top View

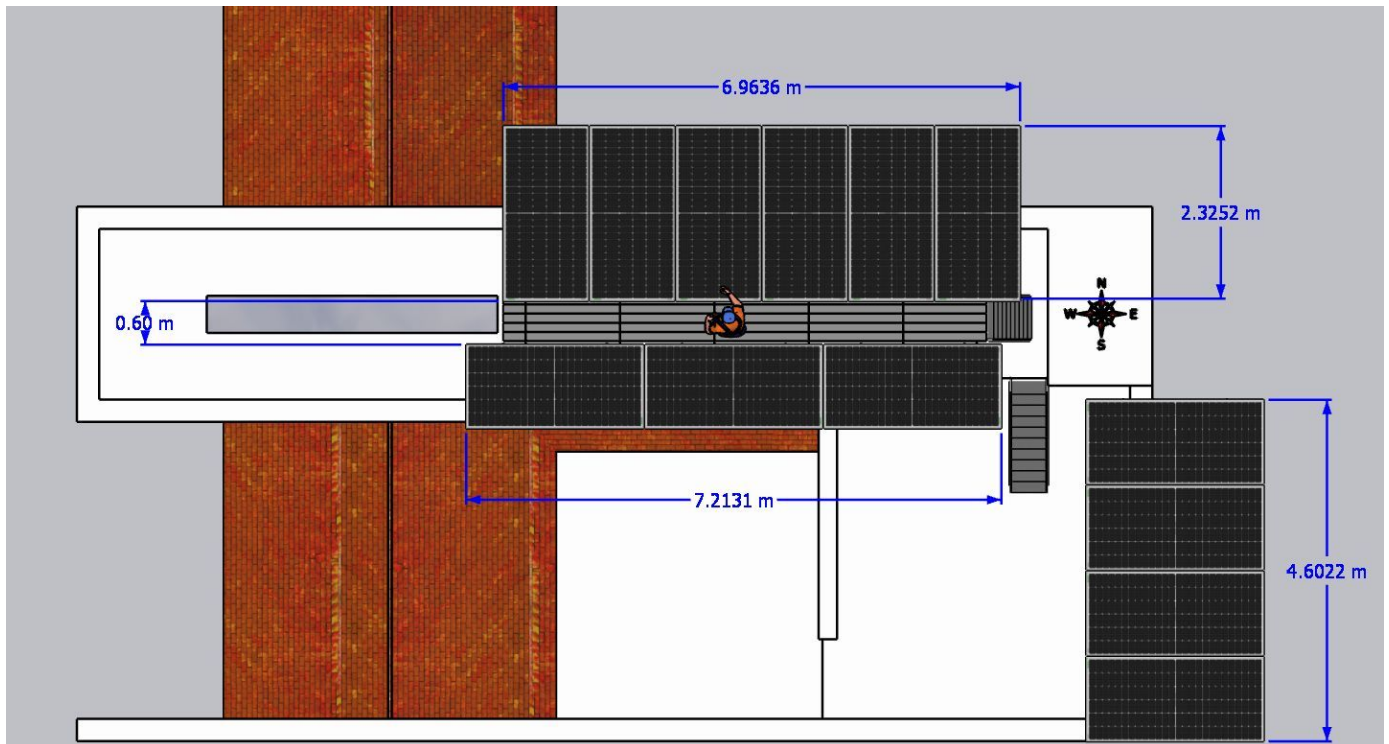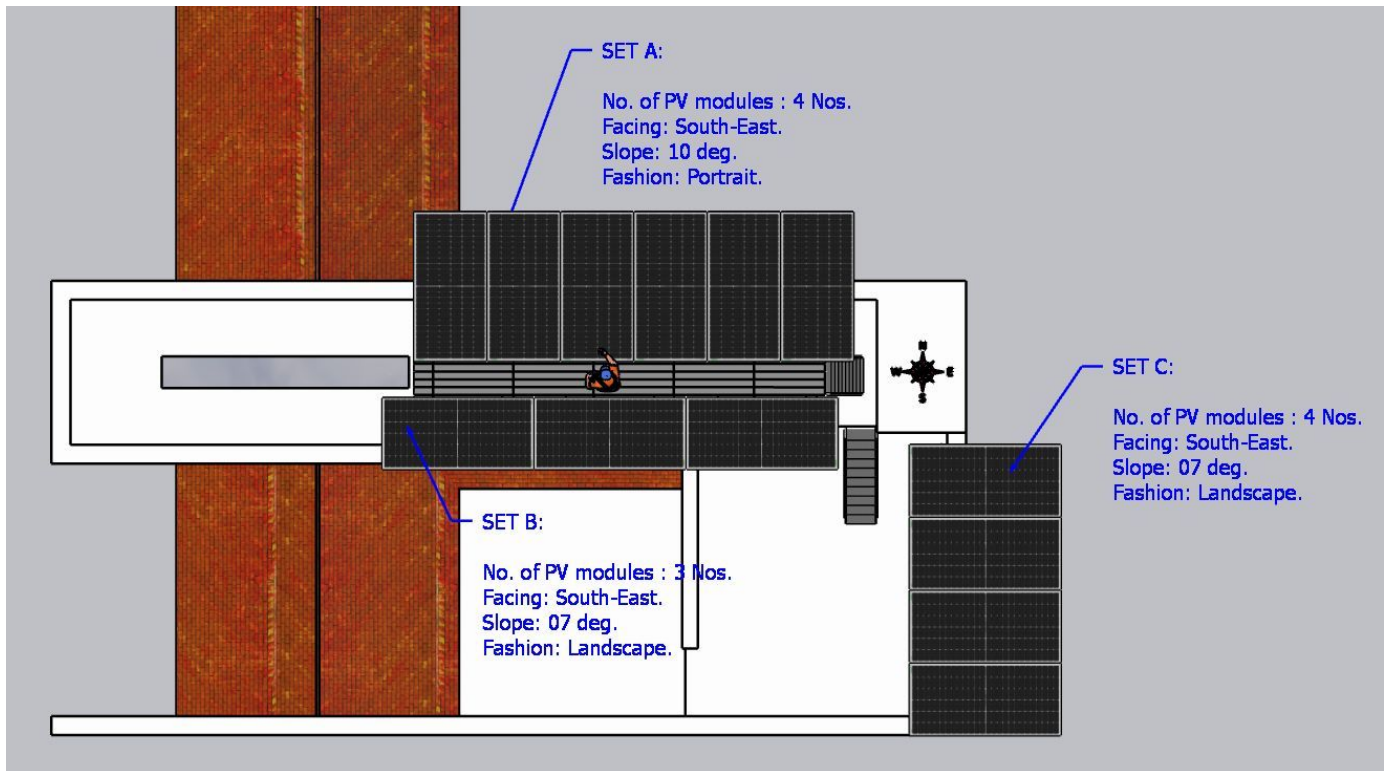


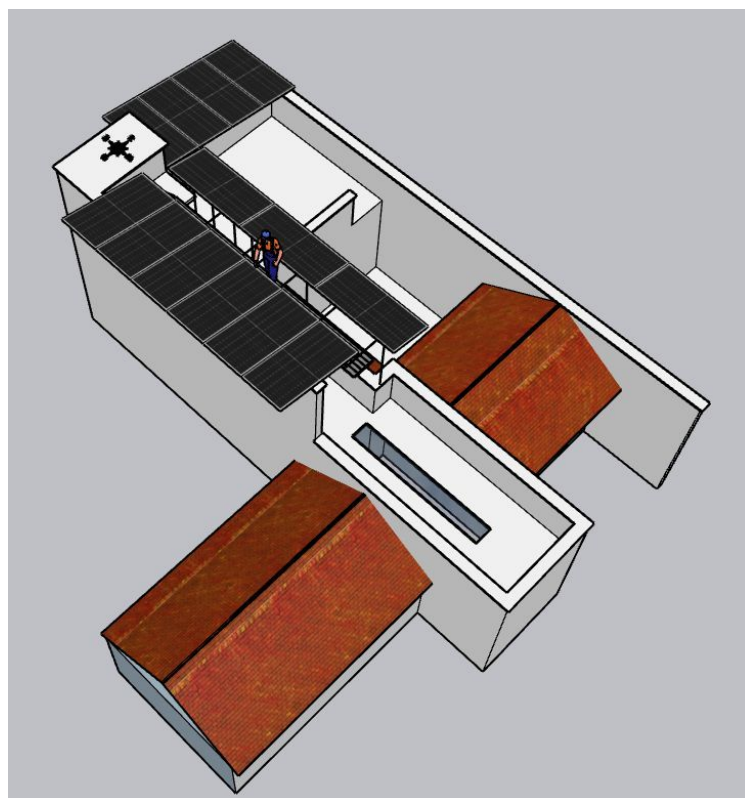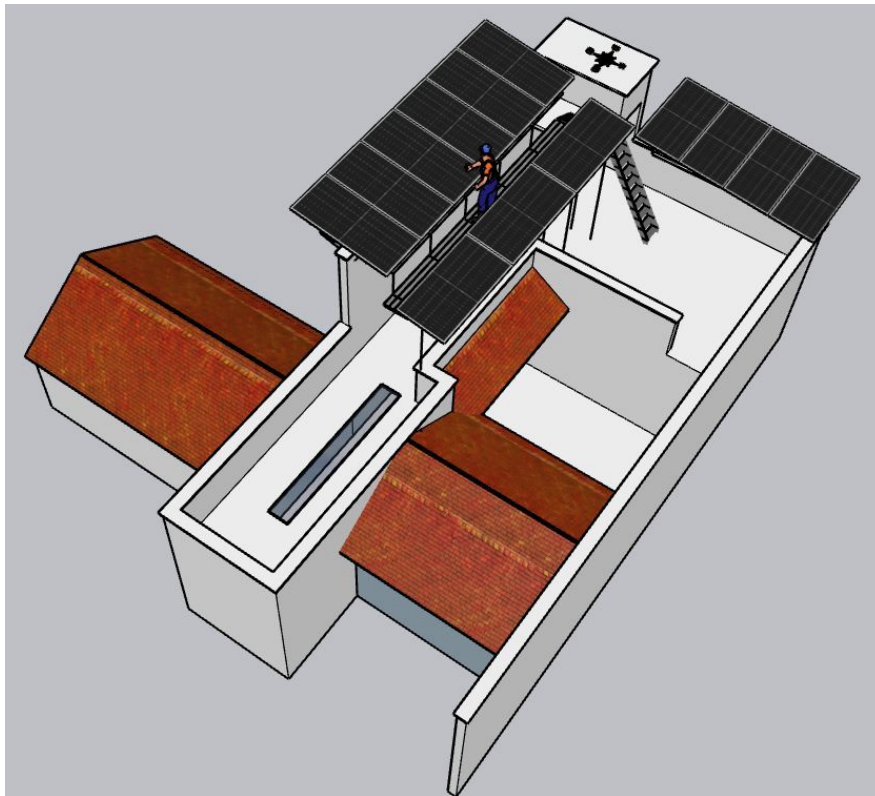

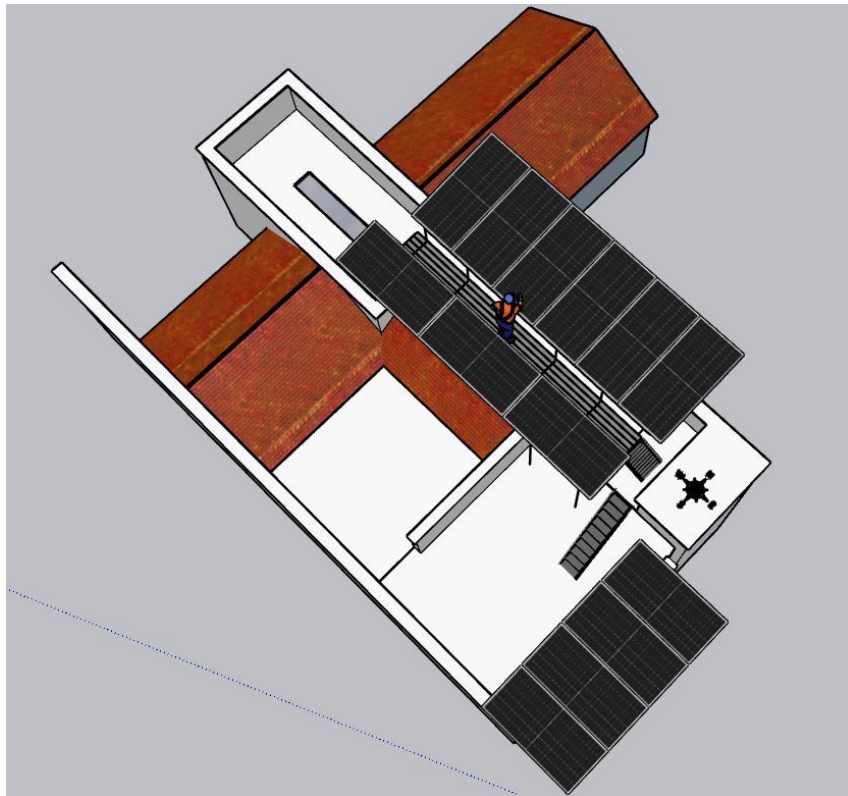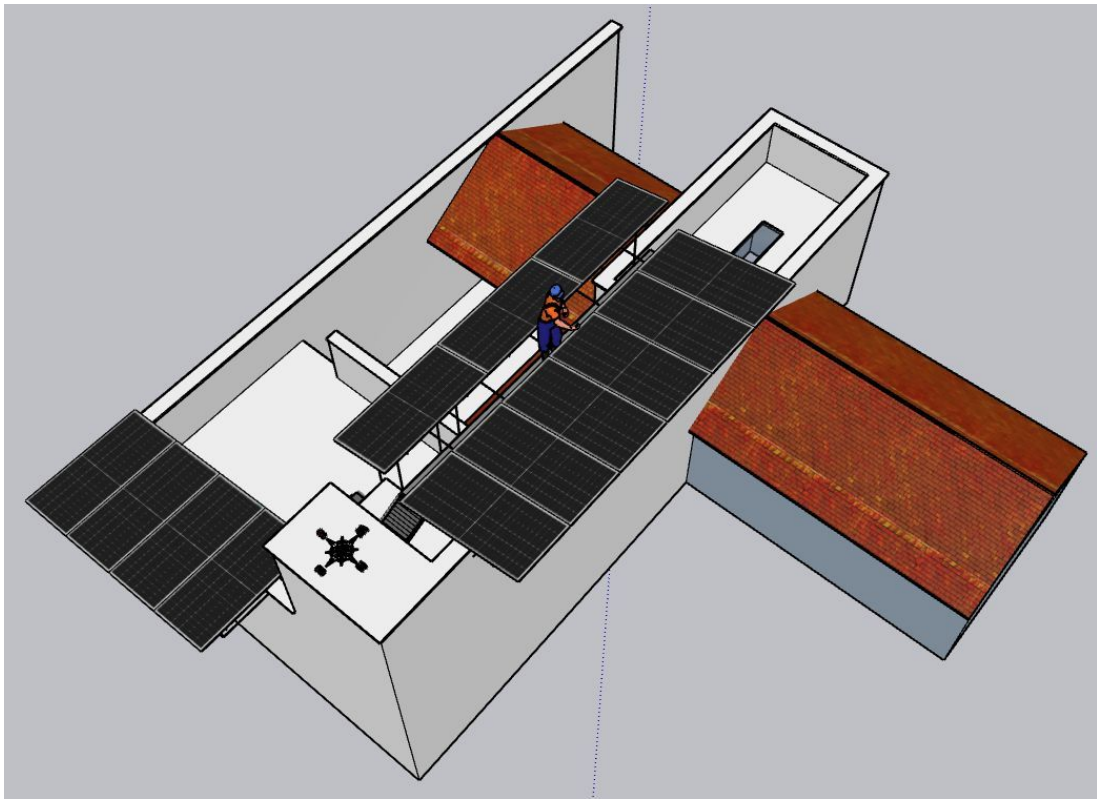

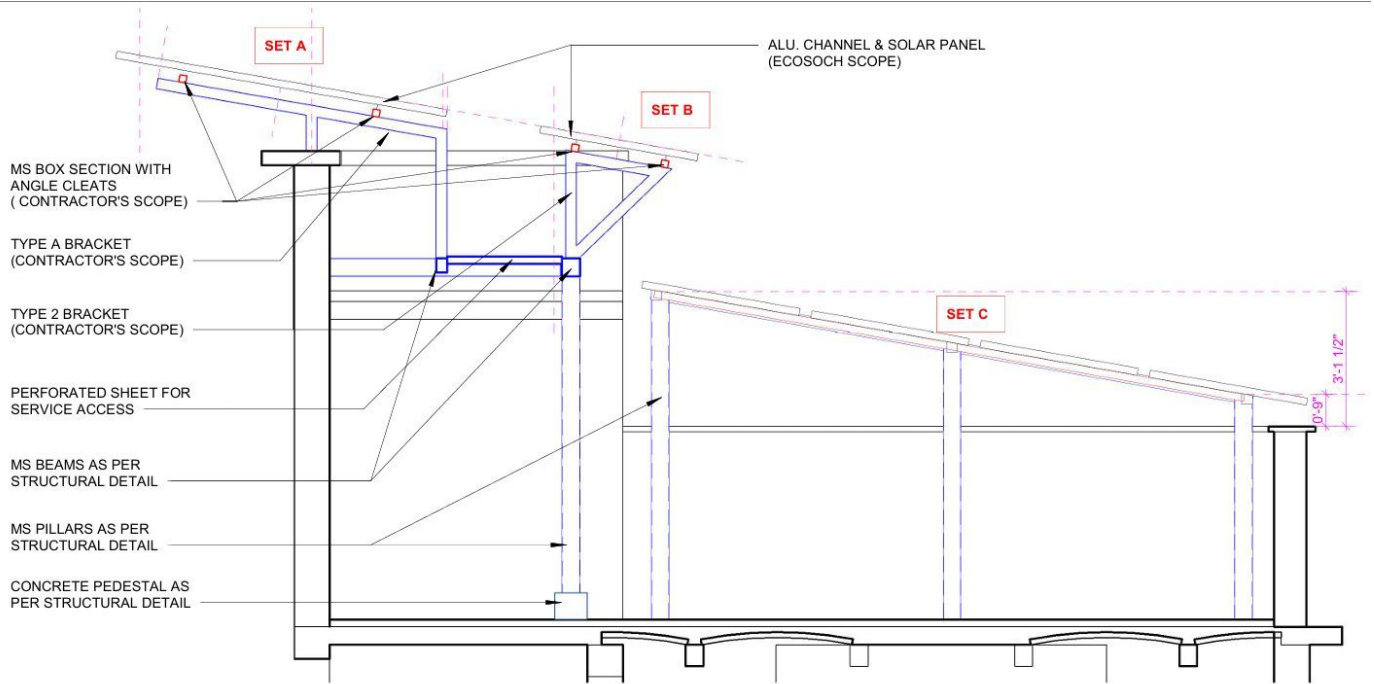


BB SS- SECTION B
1 : 35

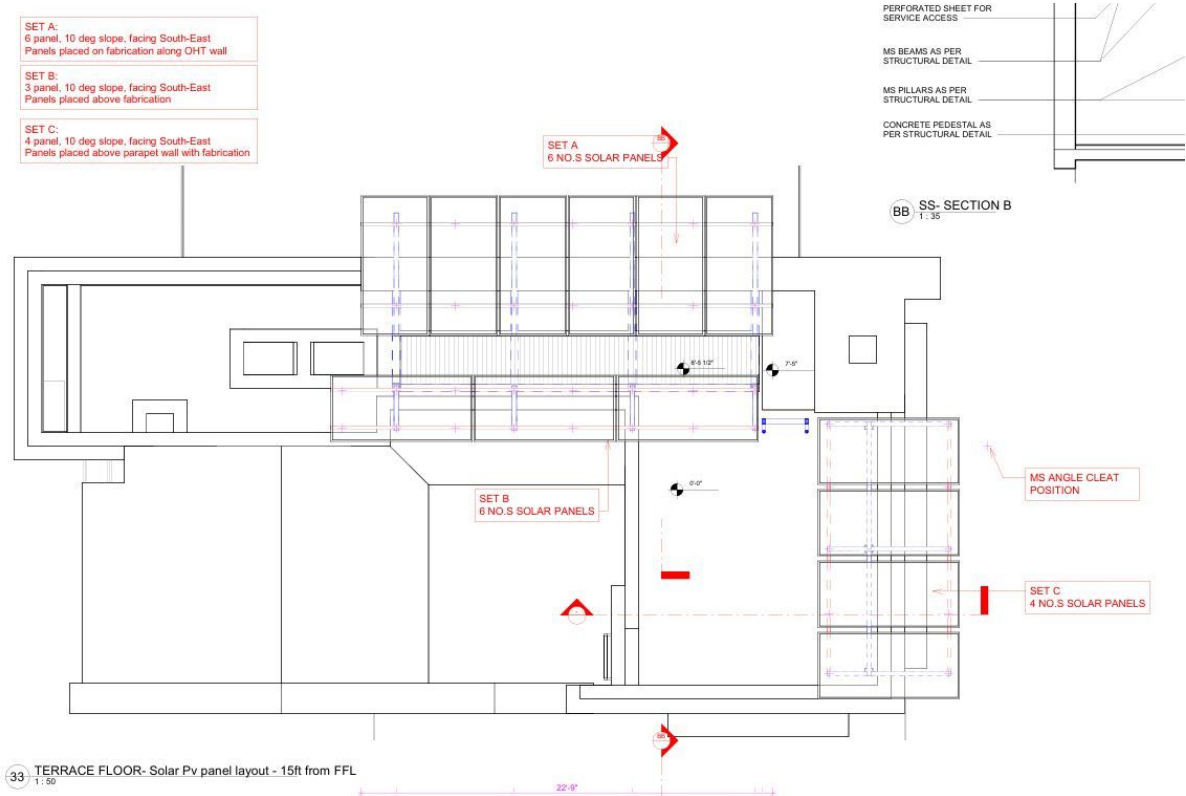


33 TERRACE FLOOR- Solar Pv panel layout - 15ft from FFL
1 : 50


33 TERRACE FLOOR- Solar Pv panel layout - 15ft from FFL
1:50

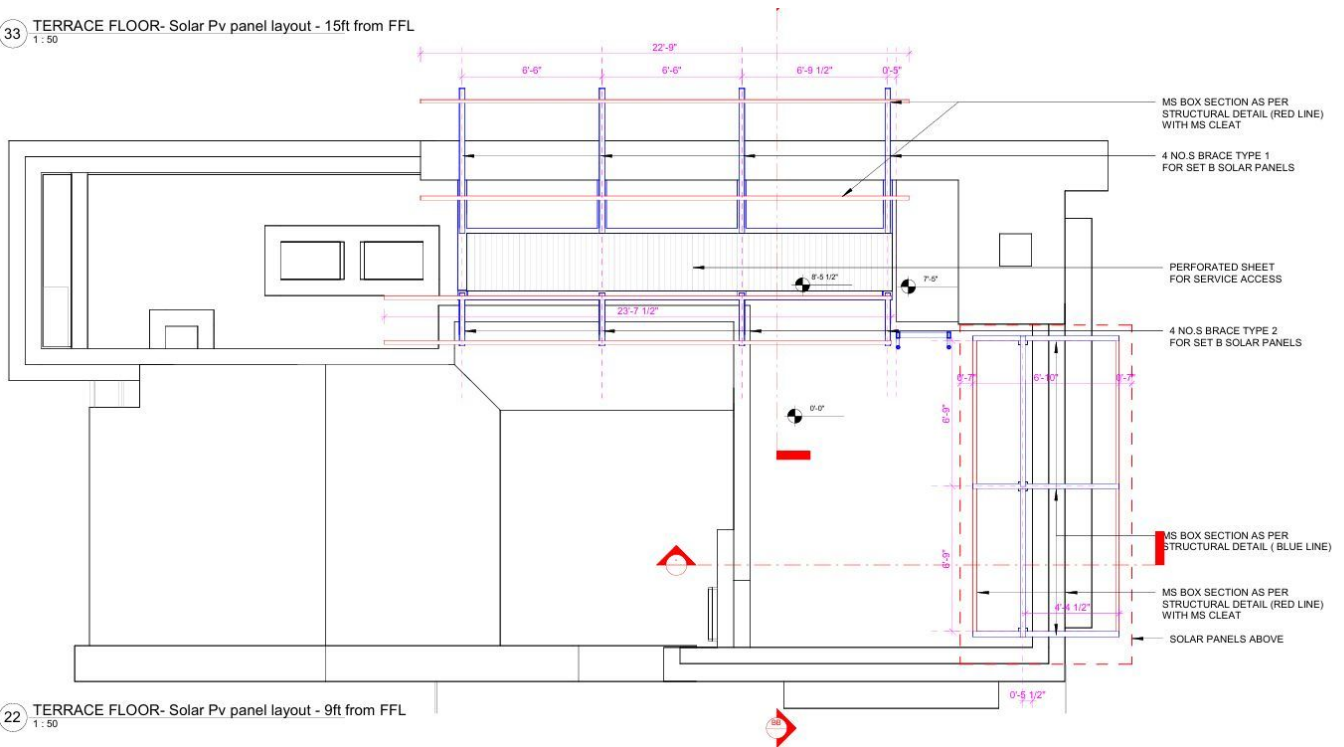


22 TERRACE FLOOR- Solar Pv panel layout - 9ft from FFL
1:50

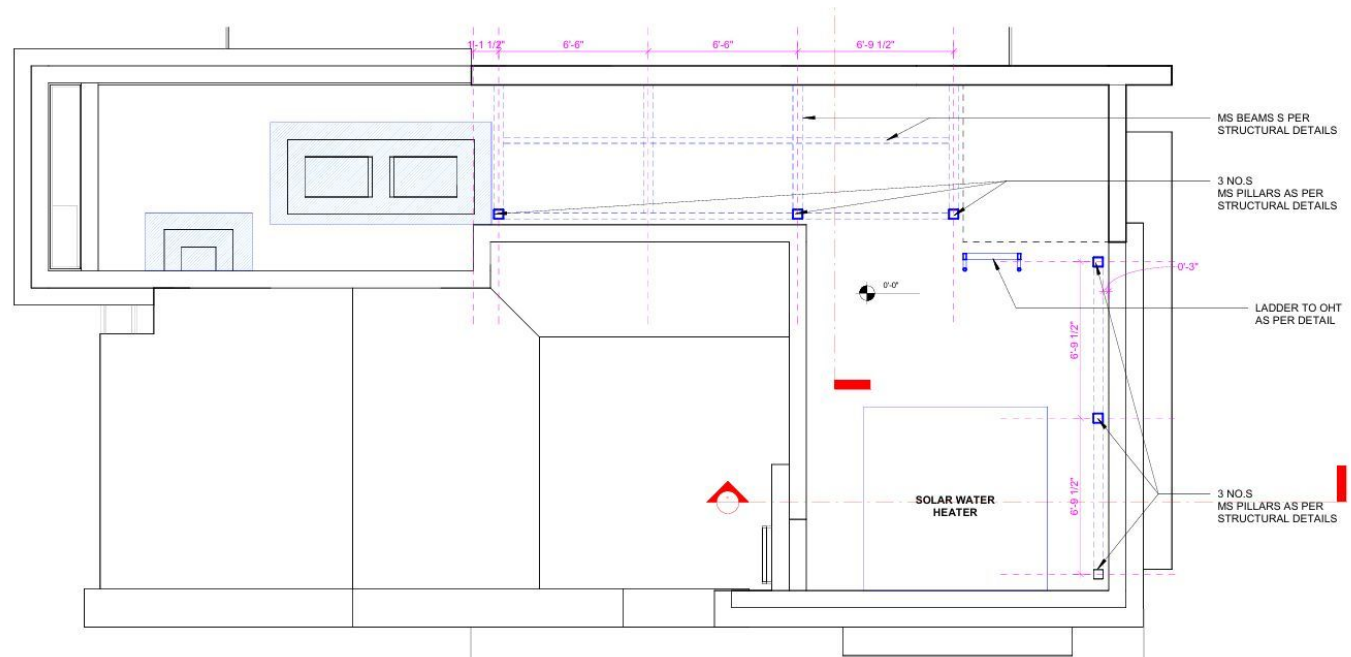

1 TERRACE FLOOR- Solar Pv panel layout - 5ft from FFL
1:50

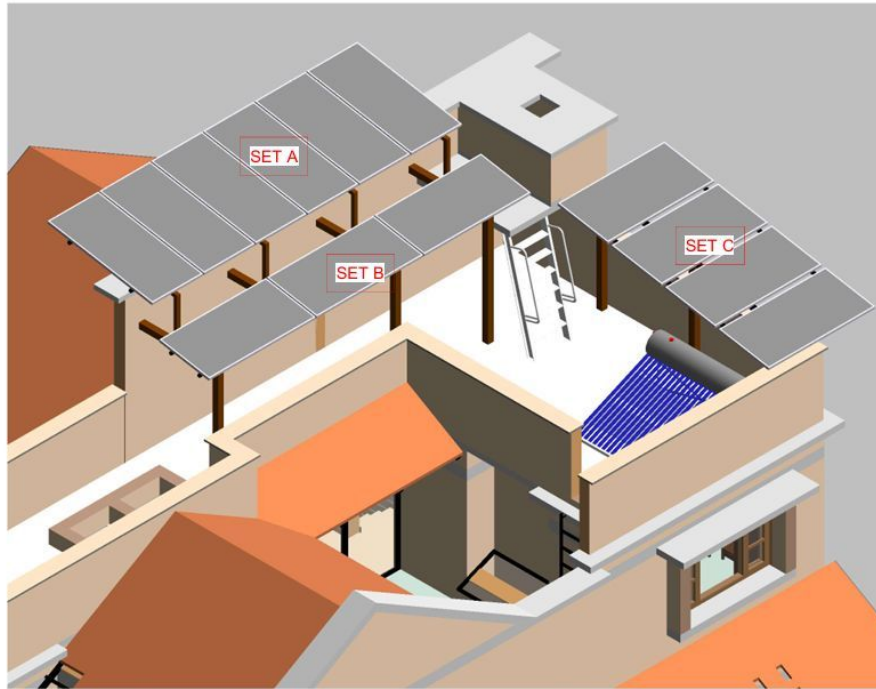

4 SOLAR PV PANELS

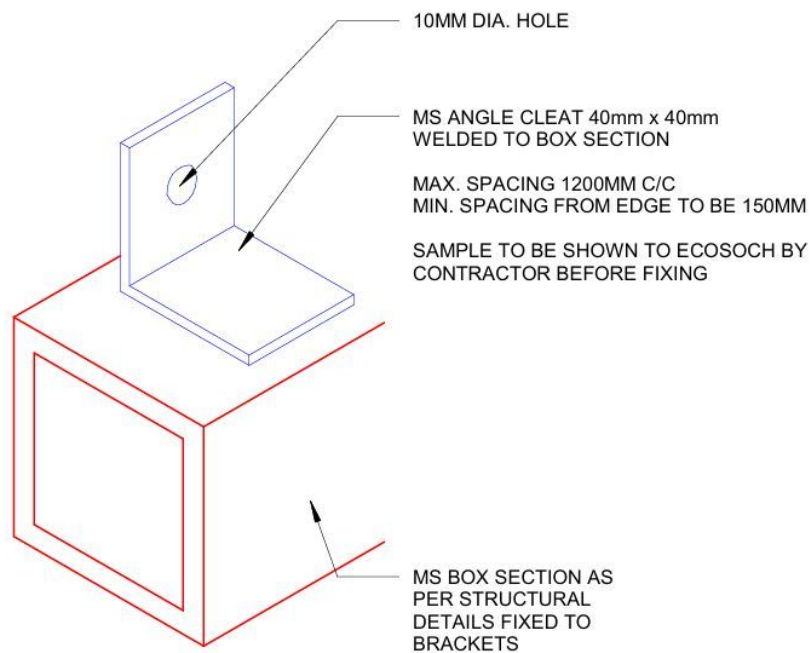

2 MS ANGLE CLEAT DETAIL
1:2

Building Exterior



Front view



Side view

Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Panels can be stored here.




Light weight materials can be shifted to the terrace via this back entry.



The materials can follow the corridor inside until reaching the middle yard.



The materials reaching the middle yard can be shifted to the terrace via the ladder.

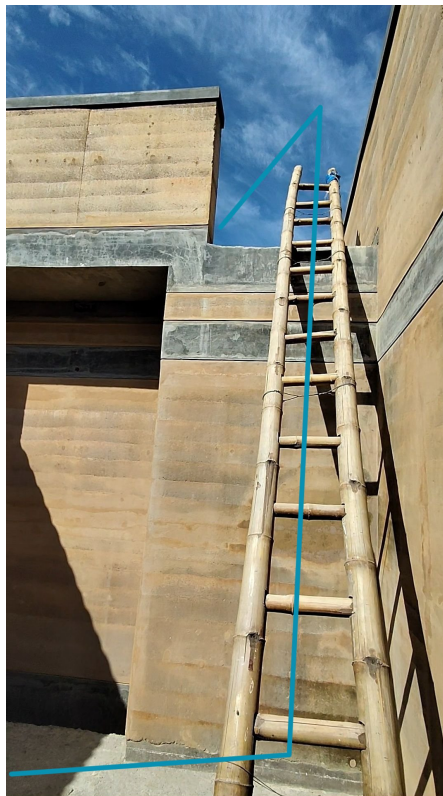

The materials can be shifted using a reliable ladder provided by the customer prior to the installation.



The materials can be stored here.,

Material Storage





The materials can be stored here either vertically leaning on the wall or lay horizontally on the floor.

Proposed PV Area



Cable Routing

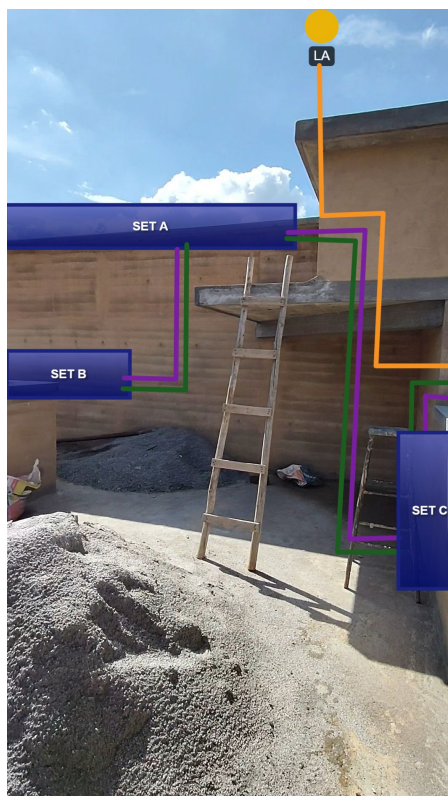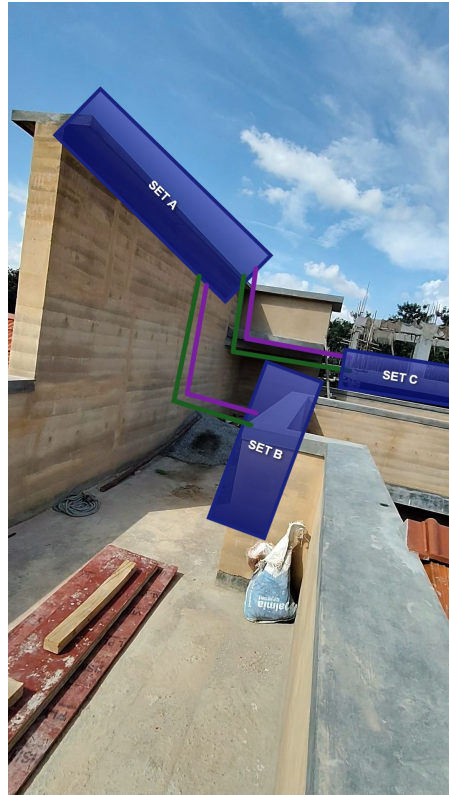





OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 7.995kWp, Enphase Hybrid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing a MS structure at the premises as per the approved design.
2	Providing input and output cables as per the requirements as in the SLD.
3	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
4	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.
5	Providing UPS point near the Inverter and battery location.
6	Fabrication of a canopy to protect the Enphase accessories and the battery installed at the premises.
7	Ensuring the Inverter-Battery room has adequate ventilation.

THANK YOU

Dear Deepa Jayamani Pillai and Kailash Nadh Balakumaran Nair,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
