

Technical Site Visit Report

Prepared for: Julius Amrit_Prestige Oasis 49 B Sunsidy_4.88kWp_Microinverter (IQ Series) - Villa #49

PROJECT INFORMATION

Report Number	ESV-2026-0194
Project ID	5BCF51DC
Project Name	Julius Amrit_Prestige Oasis 49 B Sunsidy_4.88kWp_Microinverter (IQ Series)
Building Name	Villa #49
Billing Name	Julius Amrit
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Govindaraju
Site Address	5HJ3+4M Prestige Oasis Villa-49, Vaishnavi Layout, Adde Vishwanathapura, Adde Viswanathapura, Karnataka 560119
GPS Coordinates	13.18035323847023, 77.5542901594767
Google Maps	https://www.google.com/maps?q=13.180353238470229,77.5542901594767
Visit Date	2026-08-28
Visited By	K Naveen
Revision	Rev 0

CLIENT INFORMATION

Client Name	Julius Amrit
Contact	9810198140

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	4.88
Module Make & Capacity	Premier DCR Bifacial 610

Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	8
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	8
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located in the corridor which is near to the car parking area.	-
6	Where is the Internet Router located?	Customer scope	Under construction
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	corrugated sheet roof with 5 degree slope on east side and 4 degree slope on west side.
2	Are there any obstructions on the roof that could affect the solar installation?	details: Manglore tile roof are the obstructions that could affect the solar installtion.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	5	For east side corrugated sheet roof has 5 degree and west side corrugated has 4 degree slope

#	Question	Answer	Notes
5	On how many roofs at the site are we installing solar?	2	Combination of 2 different directions
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Other	Aluminum short rail structure
9	What is the orientation of the solar panels?	["East", "West"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	Conduits are not available, but electrician they will provide the access up to the main meter location.
13	What is the height of the building and how many floors does it have?	The height of the building is G+1 +Headroom is approximately 15 meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	N/A	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	details: Still the site conditions have congested space take precautions	-

#	Question	Answer	Notes
		during installing the panels.	
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	For East side sheet roof rafter to rafter is 1240,1190,1265,1140 mm and Purlin to purlin is 760,1060 &1050	For East side sheet roof rafter to rafter is 1240,1190,1265,1140 mm and Purlin to purlin is 760,1060 &1050 For West side sheet roof rafter to rafter is 1075,1250,1260,1205,1160 mm and Purlin to purlin is 760,1060 &1050
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1100, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 800, width: 1200	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).









This route (using Staircase) will be followed to carry Small items.



Staircase Details



Meter Box



Material Storage



Proposed PV Area



East side corrugated sheet roof with 5 degree slope



West side corrugated sheet roof with 4 degree slope

Cable Routing








Pulling the AC cable from here to bottom main meter location is under customer scope.





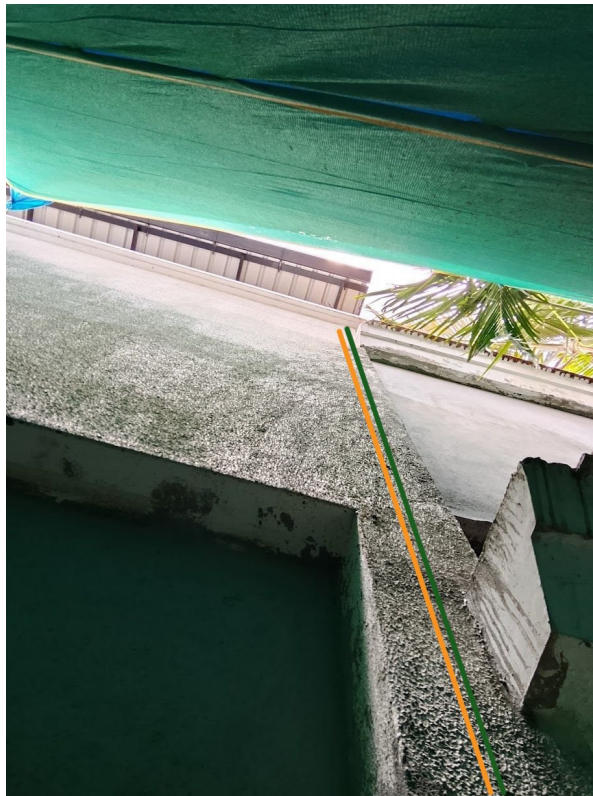






Sheet roof profile pitch 0.2m


Equipment Location


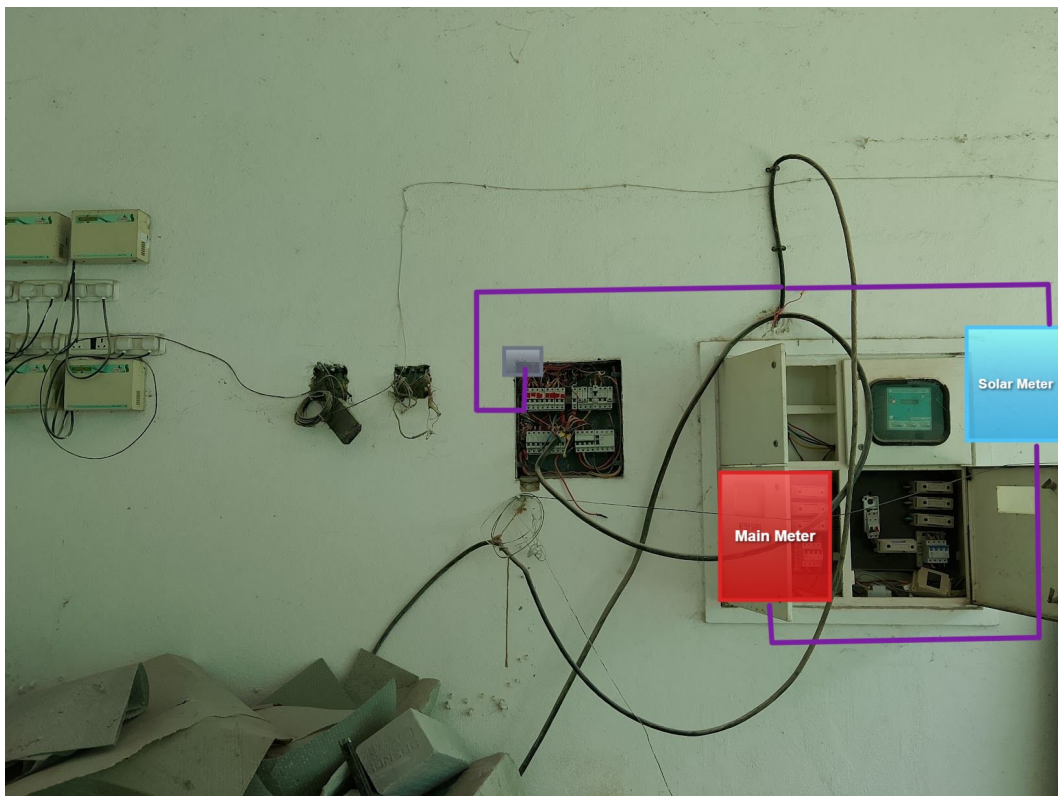


Earth Pit Location



Site Layout - Top View

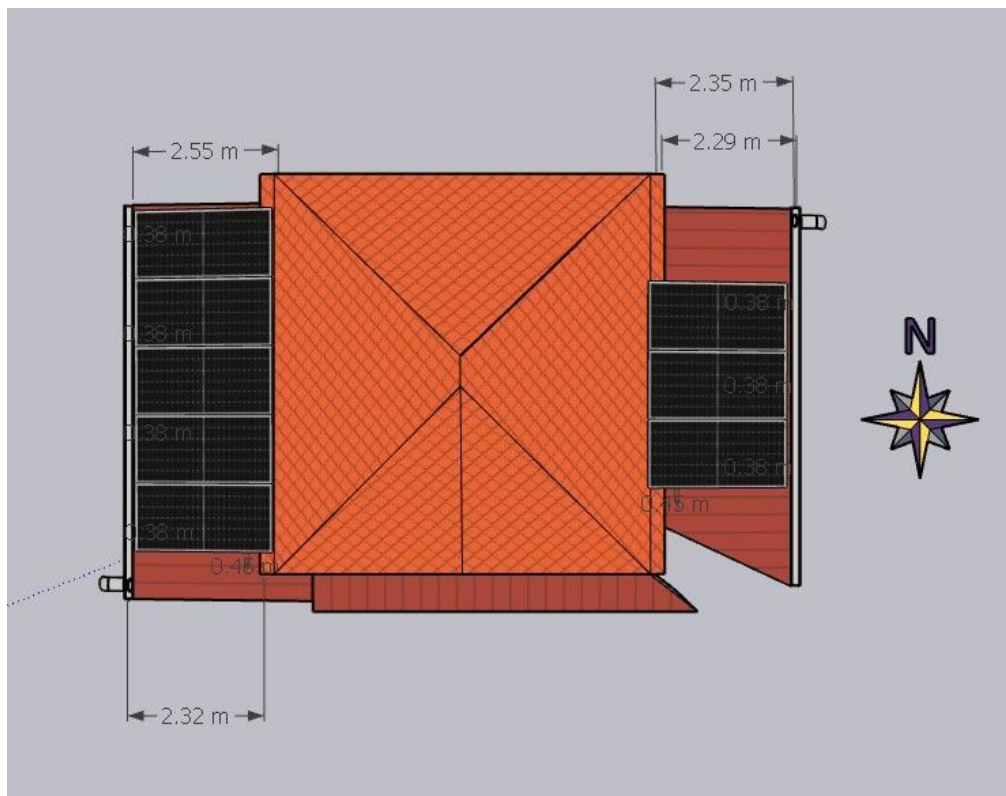


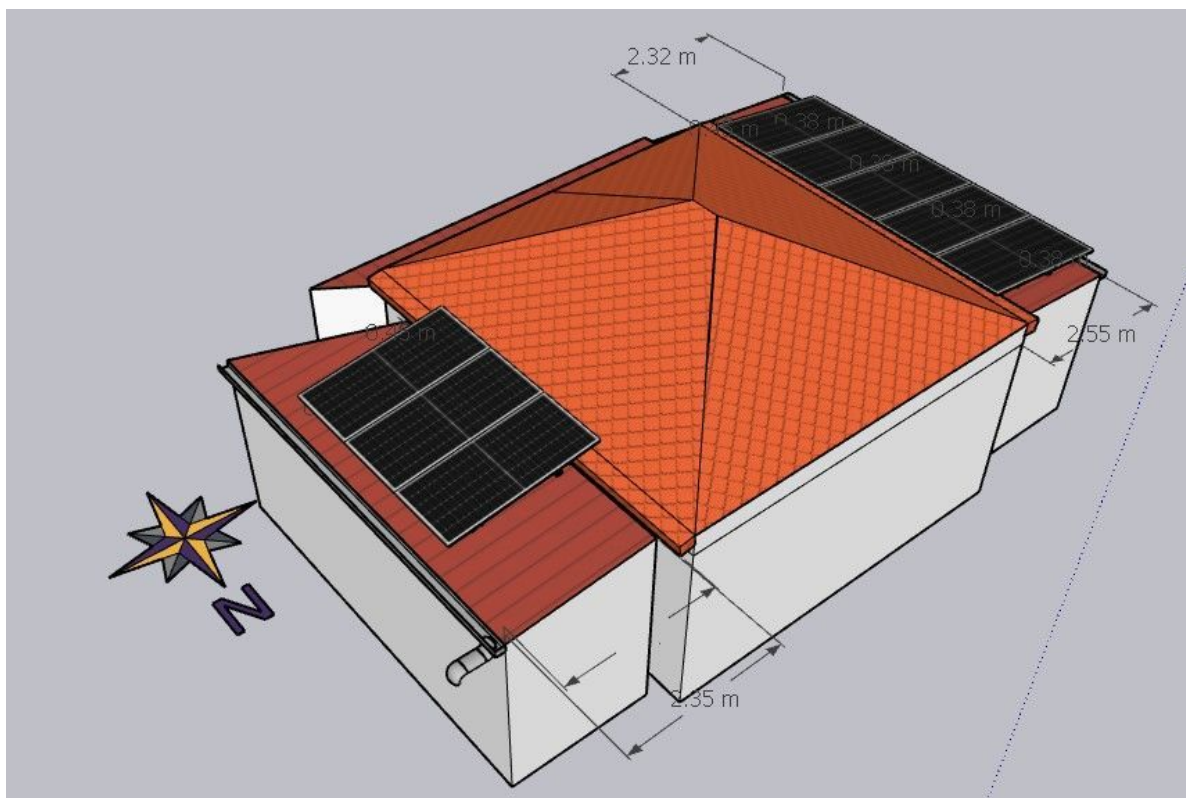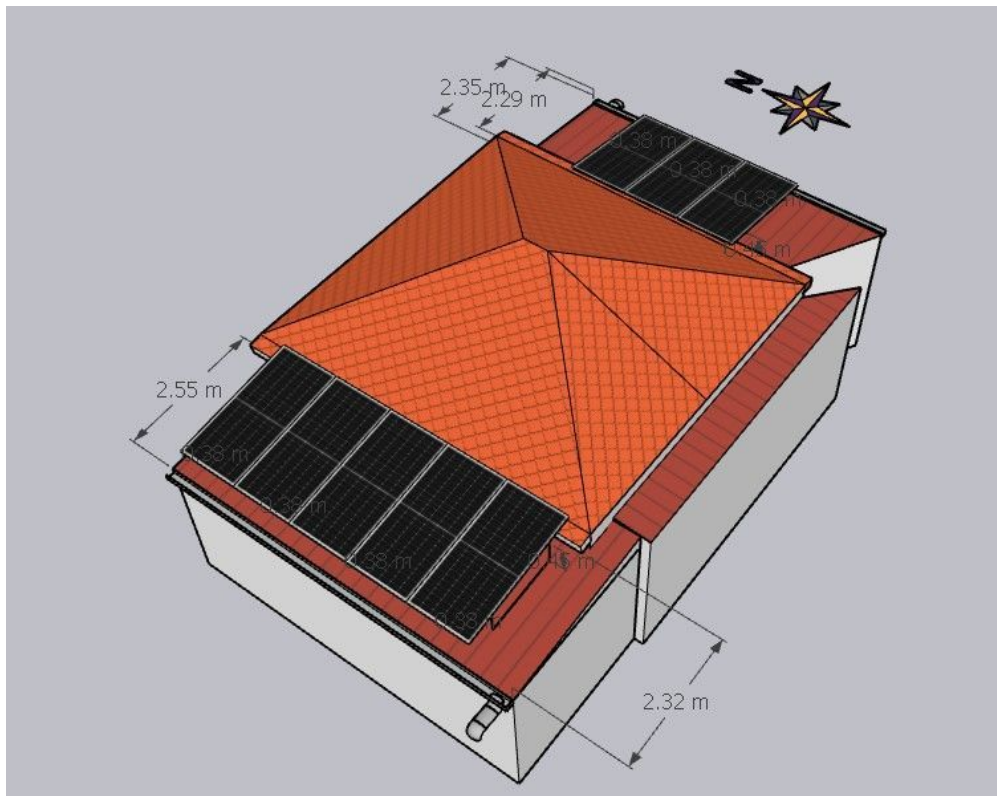

Building Exterior



Existing Electrical

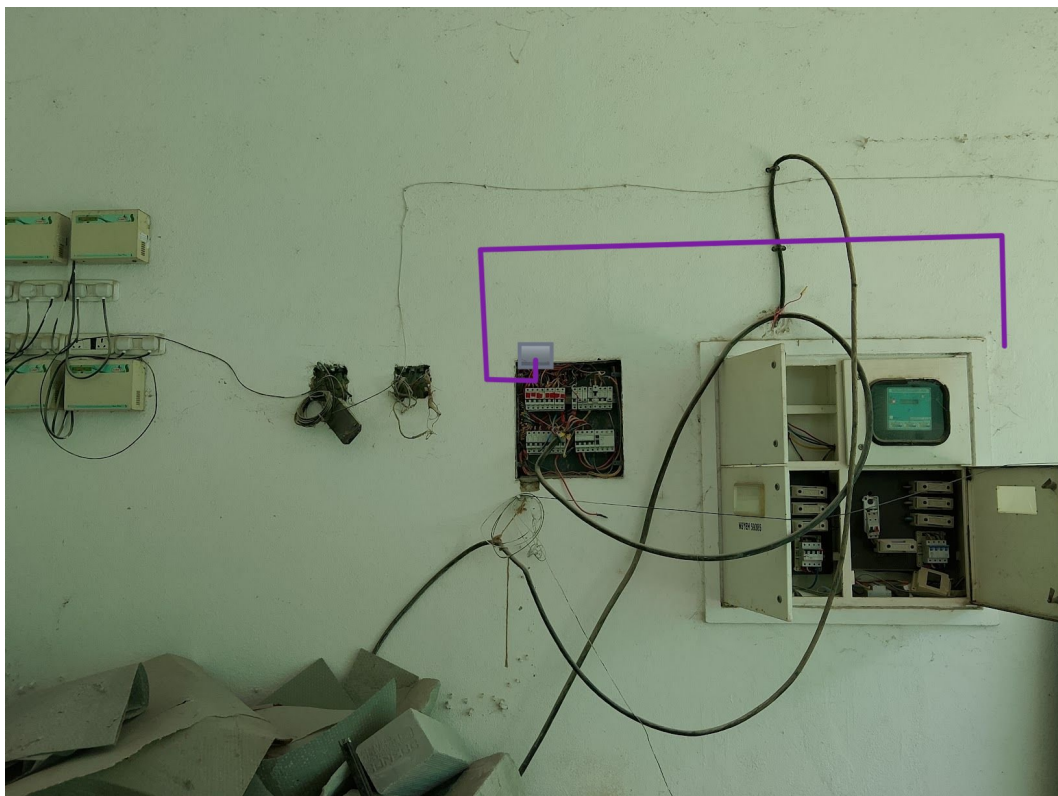

As discussed with the electrician they will give thrprovision for AC conduit pipe up to the meter location is under customer scope.

OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the solar meter location is under customer scope.
2	As discussed with client the panel layout,cable routing, earthing location has been finalized.
3	Pulling the AC cable from the top terrace down to the bottom main meter location will be under the customer's scope.

THANK YOU

Dear Julius Amrit,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
