

## Technical Site Visit Report

Prepared for: Baby Usha Murlidhar\_Kalyananagara Subsidy\_5.5kWp\_Optimizer - House No: 511

### PROJECT INFORMATION

|                 |                                                                                                                                                     |
|-----------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0120                                                                                                                                       |
| Project ID      | 1544A4C7                                                                                                                                            |
| Project Name    | Baby Usha Murlidhar_Kalyananagara Subsidy_5.5kWp_Optimizer                                                                                          |
| Building Name   | House No: 511                                                                                                                                       |
| Billing Name    | Baby Usha Murlidhar_Kalyananagara Subsidy_5.5kWp_Optimizer                                                                                          |
| Project Sector  | Residential                                                                                                                                         |
| Project Type    | With Subsidy                                                                                                                                        |
| Sales Lead      | Govindaraju                                                                                                                                         |
| Site Address    | #511, 4th E Cross HRBR layout, Kalyananagar 560043                                                                                                  |
| GPS Coordinates | 13.02387099613392, 77.64153970777792                                                                                                                |
| Google Maps     | <a href="https://www.google.com/maps?q=13.023870996133915,77.64153970777792">https://www.google.com/maps?q=13.023870996133915,77.64153970777792</a> |
| Visit Date      | 2026-05-26                                                                                                                                          |
| Visited By      | sai                                                                                                                                                 |
| Revision        | Rev 2                                                                                                                                               |

### CLIENT INFORMATION

|             |                     |
|-------------|---------------------|
| Client Name | Baby Usha Murlidhar |
| Contact     | 7624858081          |

### PROJECT DETAILS

|                           |                           |
|---------------------------|---------------------------|
| Solar Rooftop System Type | On-Grid                   |
| System Capacity (kWp)     | 5.54                      |
| Sanction Load (kW)        | 10                        |
| Module Make & Capacity    | Adani DCR bifacial 615 Wp |

|                         |                                 |
|-------------------------|---------------------------------|
| Module Length (mm)      | 2382                            |
| Module Width (mm)       | 1133                            |
| Number of Panels        | 09                              |
| Inverter Type           | SolarEdge                       |
| Inverter Brand          | Solaredge 5kW 3 phase optimizer |
| Number of Inverters     | 01                              |
| Number of Optimizers    | 09                              |
| Mounting Structure Type | RCC Flat Roof                   |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                                                               | Notes |
|---|----------------------------------------------------------------------------|--------------------------------------------------------------------------------------|-------|
| 1 | Can the delivery van/truck reach the material unloading point?             | Yes                                                                                  | -     |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | No                                                                                   | -     |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | Inverter, DCDB, ACDB is located near the terrace area (towards south east direction) | -     |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | Yes                                                                                  | -     |
| 5 | Did you discuss the location of the earth pits with the customer?          | Earth pits are located near the ground area                                          | -     |
| 6 | Where is the Internet Router located?                                      | customer scope                                                                       | -     |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | N/A                                                                                  | -     |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                                                                  | -     |

### Roof Details

| # | Question                                                                         | Answer                                                                                   | Notes |
|---|----------------------------------------------------------------------------------|------------------------------------------------------------------------------------------|-------|
| 1 | What type of roof is present at the site?                                        | RCC Flat Roof                                                                            | -     |
| 2 | Are there any obstructions on the roof that could affect the solar installation? | details: The plumbing line on the roof could obstruct and affect the solar installation. | -     |
| 3 | What is the angle of the panels? (in degrees)                                    | 10                                                                                       | -     |
| 4 | In case of sloped roof, what is the slope angle of the roof? (in degrees)        | N/A                                                                                      | -     |

| #  | Question                                                                                                 | Answer                                             | Notes                                                                         |
|----|----------------------------------------------------------------------------------------------------------|----------------------------------------------------|-------------------------------------------------------------------------------|
| 5  | On how many roofs at the site are we installing solar?                                                   | 1                                                  | -                                                                             |
| 6  | If it is a Tiled roof, what is underneath the tiles?                                                     | N/A                                                | -                                                                             |
| 7  | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?                     | N/A                                                | -                                                                             |
| 8  | What type of mounting structure is planned?                                                              | Elevated                                           | <i>Solarfit structure with 2m front clearance is planned for this project</i> |
| 9  | What is the orientation of the solar panels?                                                             | ["South"]                                          | -                                                                             |
| 10 | How can the roof be accessed?                                                                            | Ladder                                             | -                                                                             |
| 11 | Is the building currently under construction?                                                            | No                                                 | -                                                                             |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | N/A                                                | -                                                                             |
| 13 | What is the height of the building and how many floors does it have?                                     | Height of the building is 14m; it has G+2+headroom | -                                                                             |
| 14 | Is the site photo matching with the building description?                                                | Yes                                                | -                                                                             |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                                                 | -                                                                             |

## Residential / Electrical

| #  | Question                                                                                                | Answer                                                                           | Notes |
|----|---------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------|-------|
| 1  | What type of energy meter is currently installed?                                                       | Phase: Three<br>Phase, Type:<br>Analog, If<br>3-phase: LT w/o<br>CT (5 - 34.999) | -     |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes                                                                              | -     |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes                                                                              | -     |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible                                                                          | -     |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No                                                                               | -     |
| 6  | Is space available for CT within Energy meter panel?                                                    | N/A                                                                              | -     |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | N/A                                                                              | -     |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A                                                                              | -     |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | No                                                                               | -     |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | N/A                                                                              | -     |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | Yes                                                                              | -     |
| 12 | In case of elevated structures, is an LA extension provided at the far end?                             | Yes                                                                              | -     |
| 13 | In case of elevated structures, is it with or without grouting?                                         | Without Grouting                                                                 | -     |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                       | No                                                                               | -     |
| 15 | Are there any safety risks associated with accessing the roof for installation?                         | No                                                                               | -     |
| 16 | Is space present in rooftop to store the panels?                                                        | Horizontally                                                                     | -     |

| #  | Question                                                                                          | Answer                                                                                       | Notes |
|----|---------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------|-------|
|    |                                                                                                   | sleeping                                                                                     |       |
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin. | N/A                                                                                          | -     |
| 18 | Is ventilation available in the battery location?                                                 | N/A                                                                                          | -     |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                       | Inverters/ACDB/DCDB be installed on a wall mount                                             | -     |
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).                         | length: 600, width: 400                                                                      | -     |
| 21 | Provide the dimension for earth pits location (L x W of available space).                         | length: 500, width: 500                                                                      | -     |
| 22 | Is LAN cable under customer scope?                                                                | No                                                                                           | -     |
| 23 | Is there any shadow that affects the solar installation?                                          | No                                                                                           | -     |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location?                  | details: Trench work has to be done to carry the earthing cables to the earth pits location. | -     |

## PHOTO DOCUMENTATION


### Cable Routing Legend

| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|  | Proposed PV Module Array |
|  | Main Meter Location      |
|  | Solar Meter              |
|  | Battery                  |
|  | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |
|  | LA Pit                   |
|  | LA                       |

## Building Exterior



## Material Delivery Route

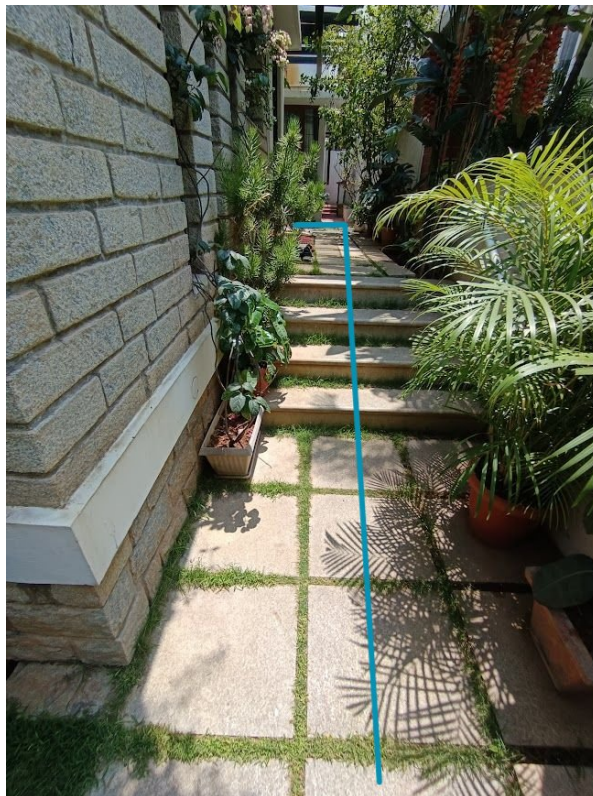





*This route will carry the small items*




*This route will carry the large items (like panels)*

## Meter Box



## Staircase Details

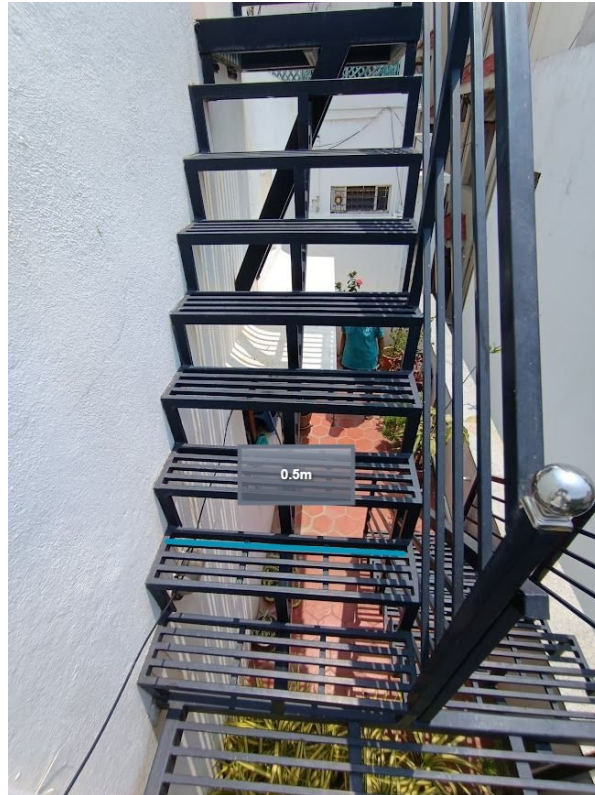


## Material Storage







## Site Layout - Top View

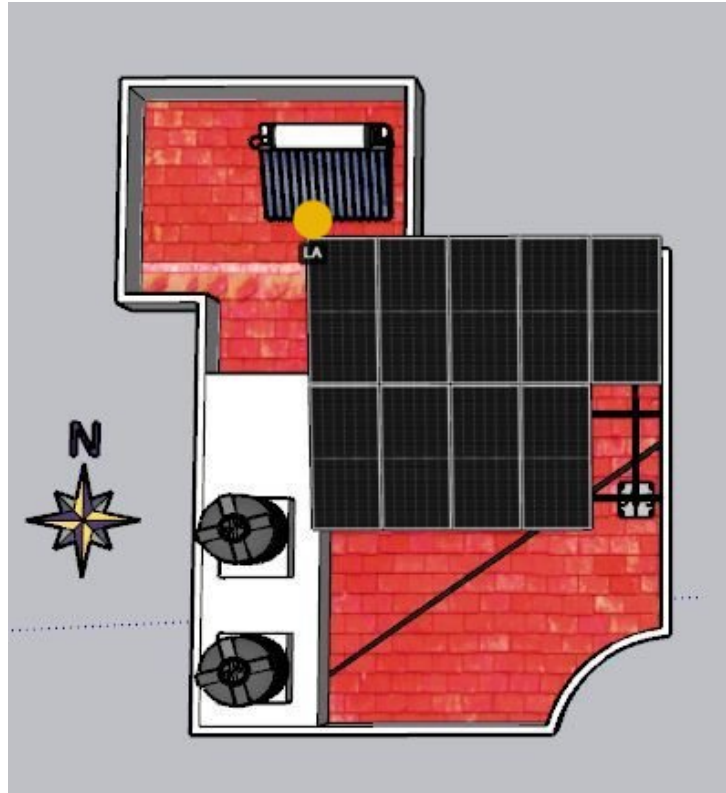


Top view

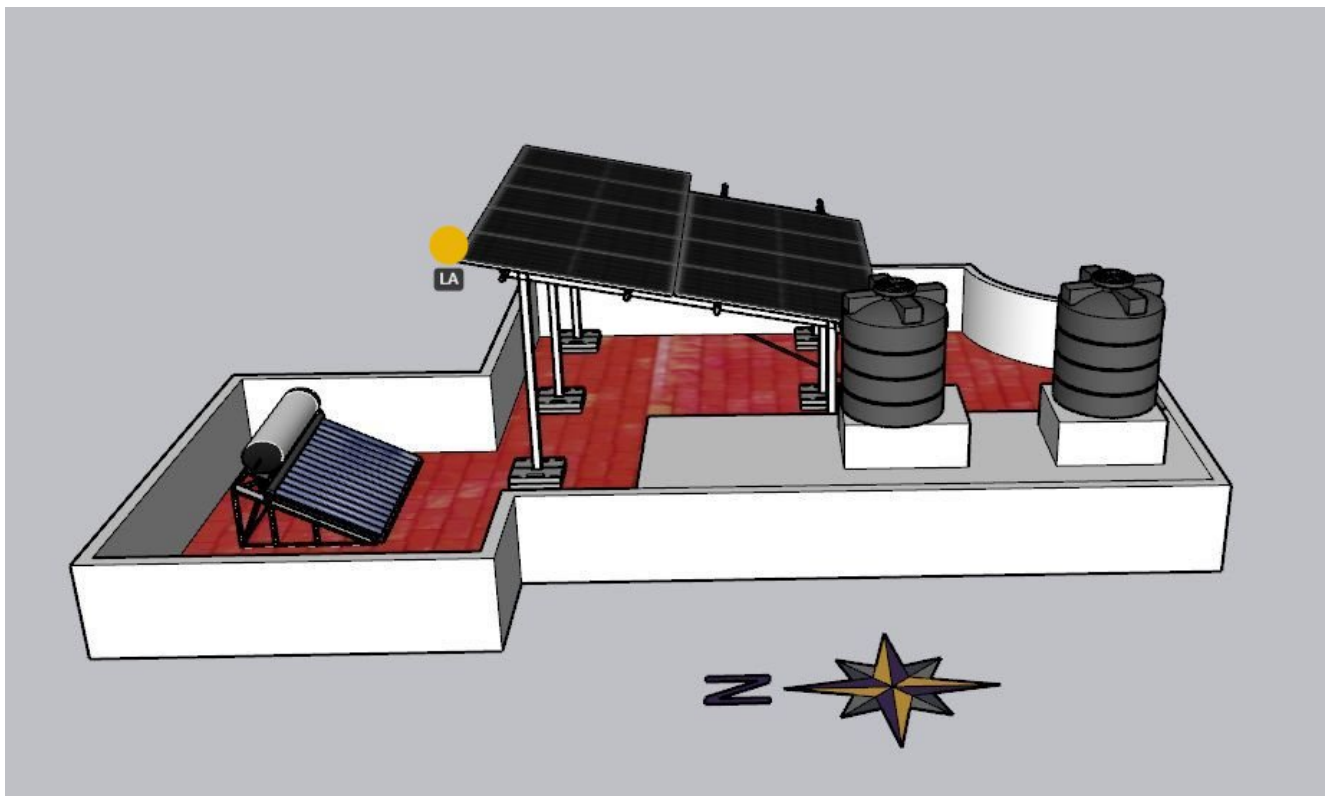


Side view (1)

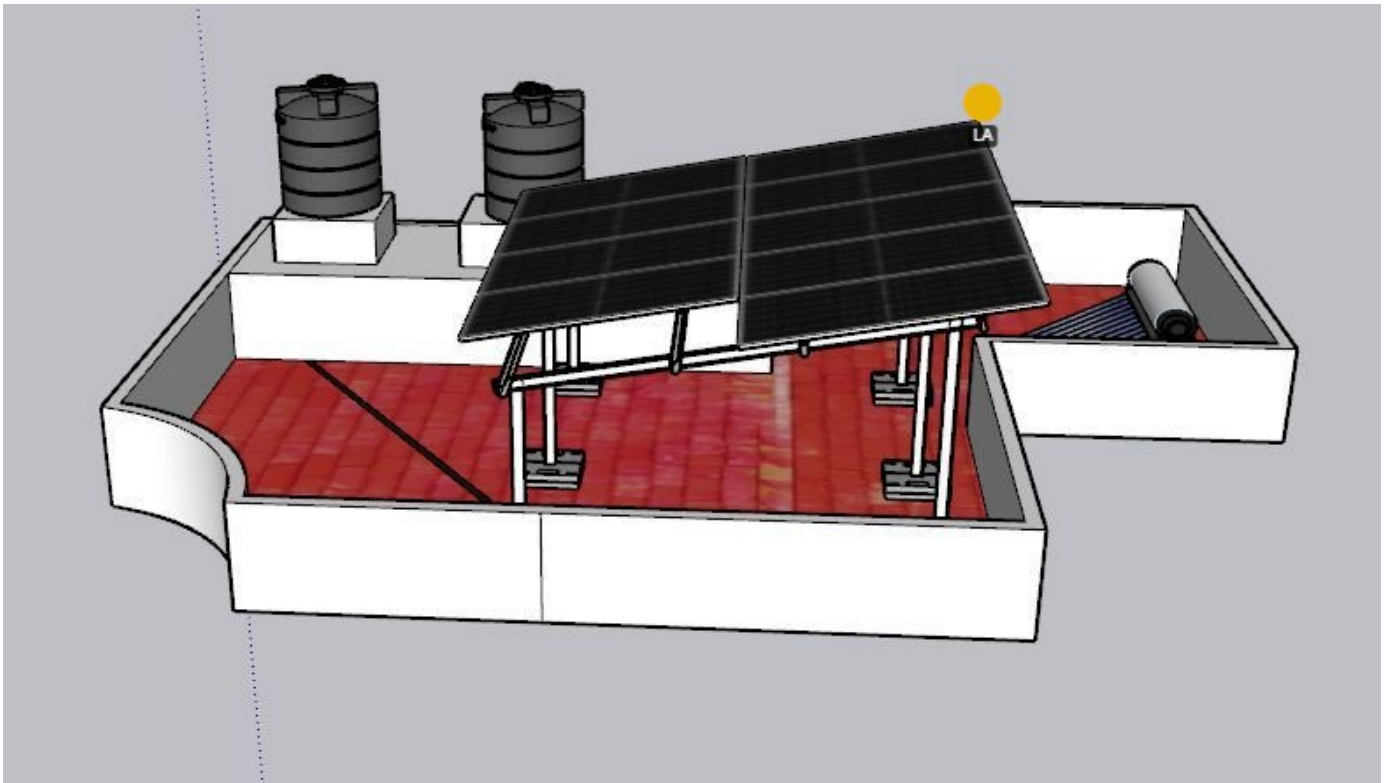


Side view (2)

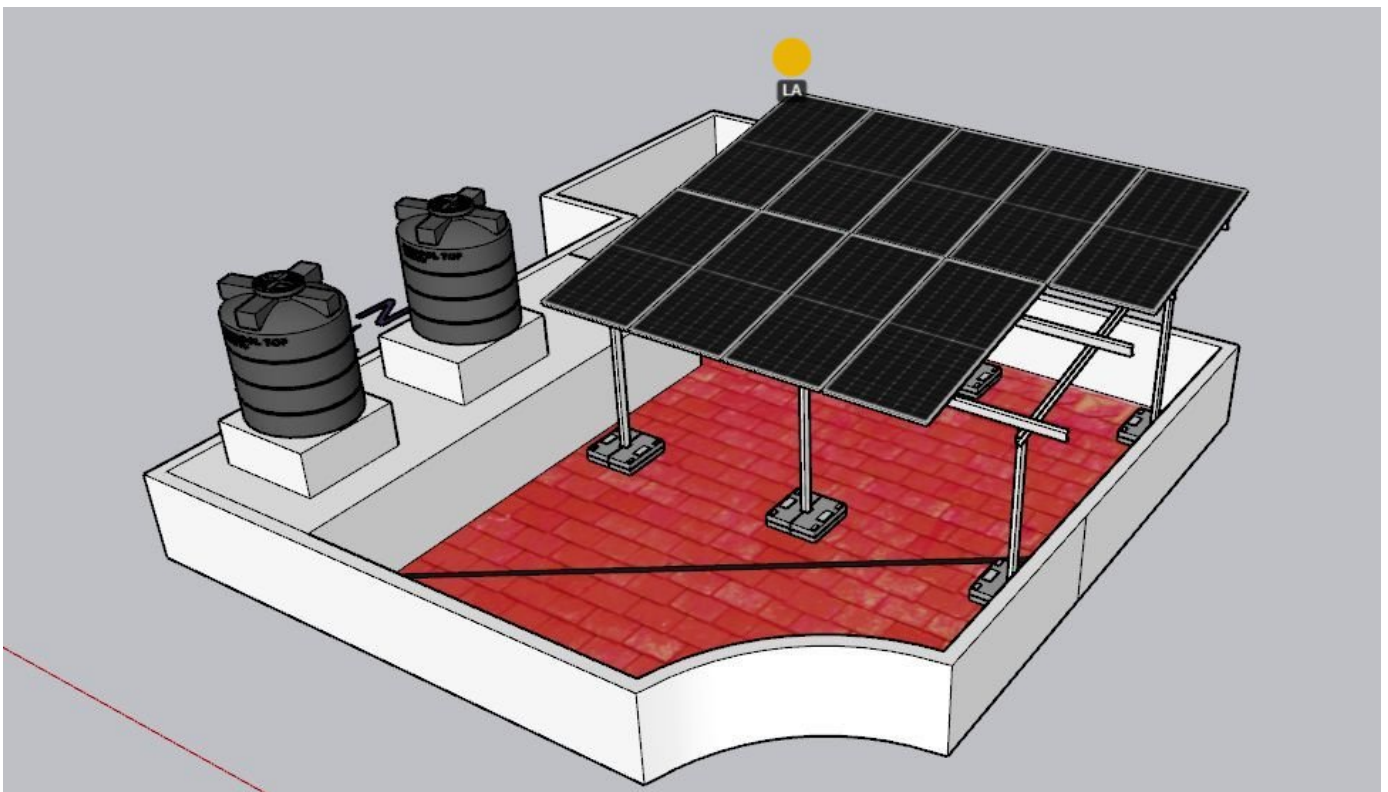

Side view (3)

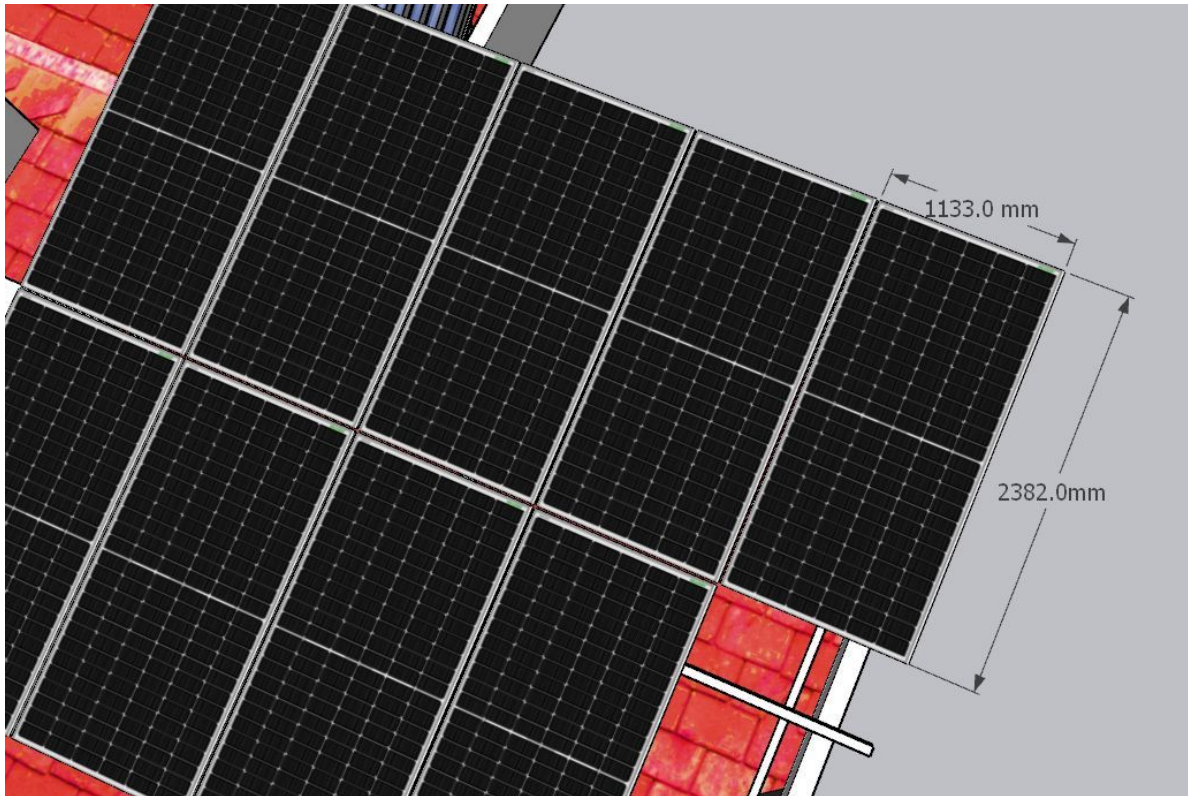

*Panel dimensions*

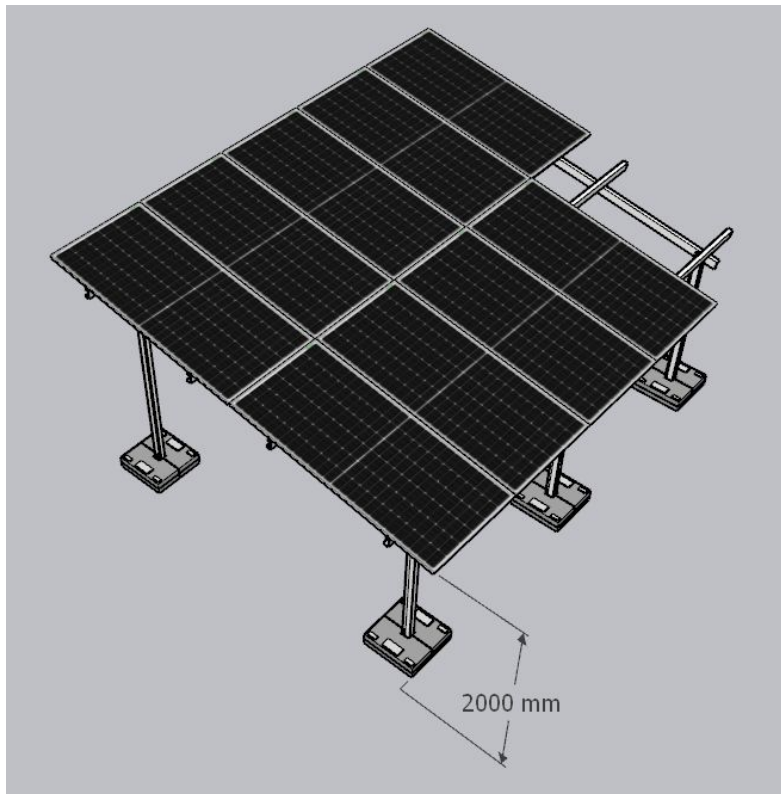

*Structure details*




## Proposed PV Area




## Cable Routing






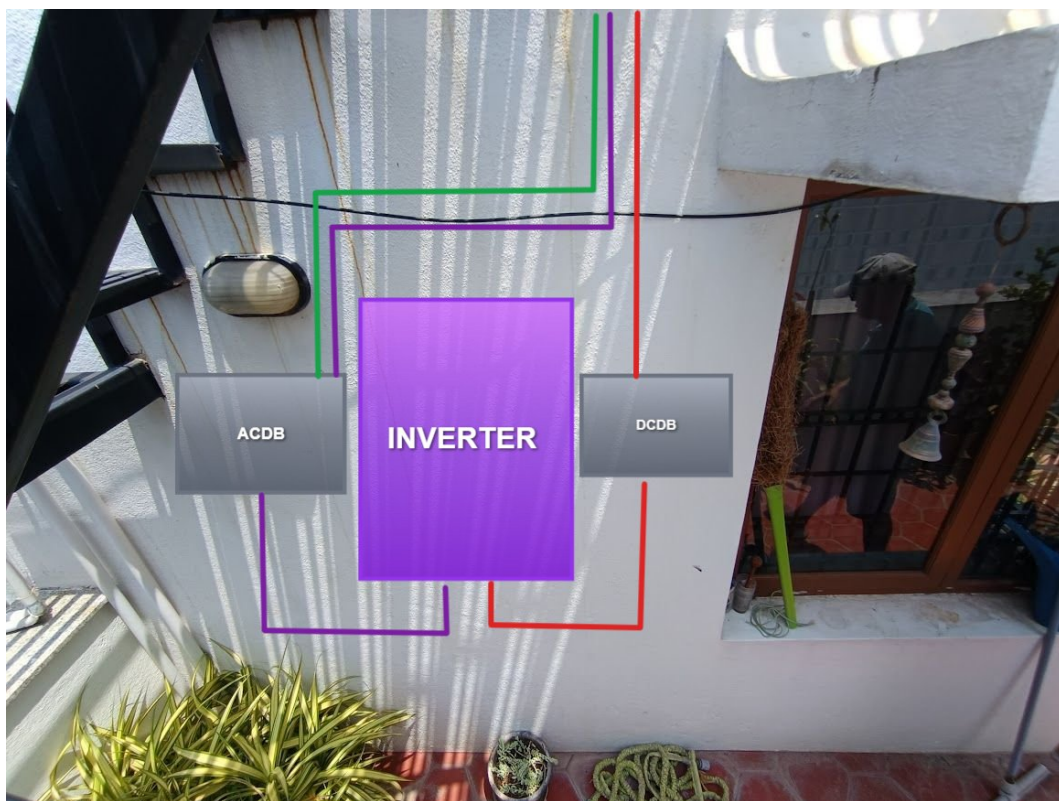

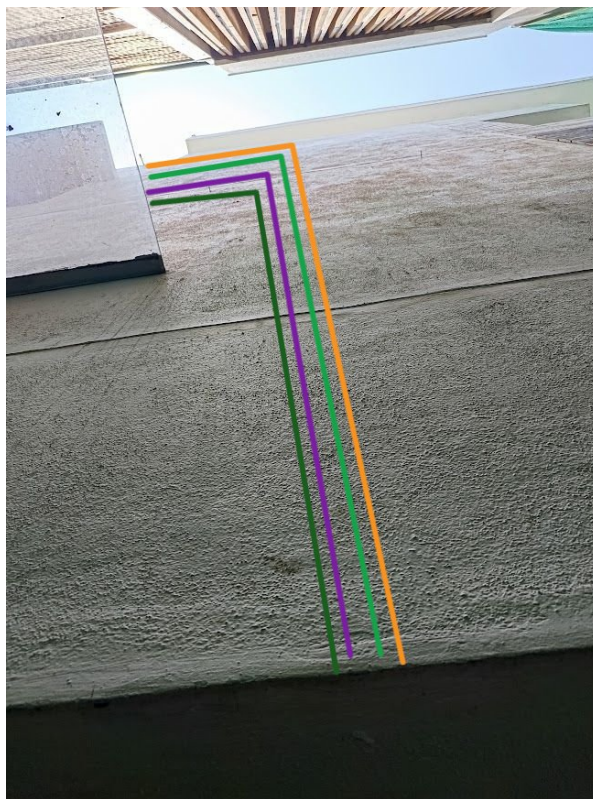



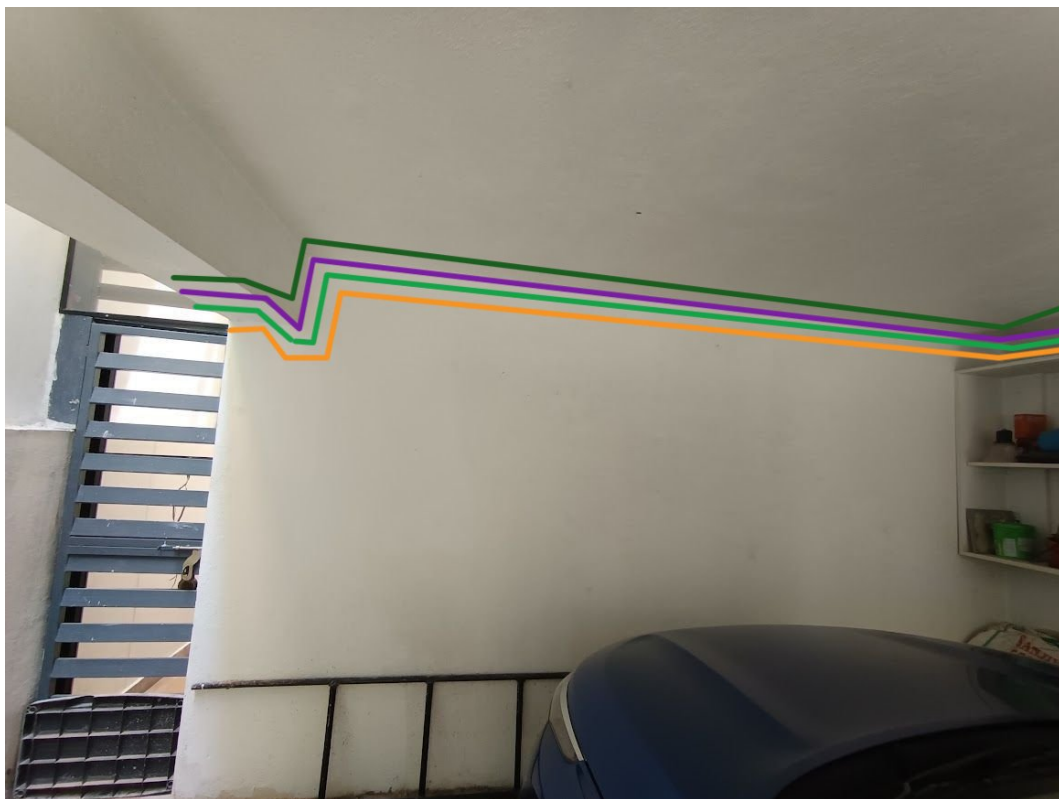



## Equipment Location





#### Earth Pit Location

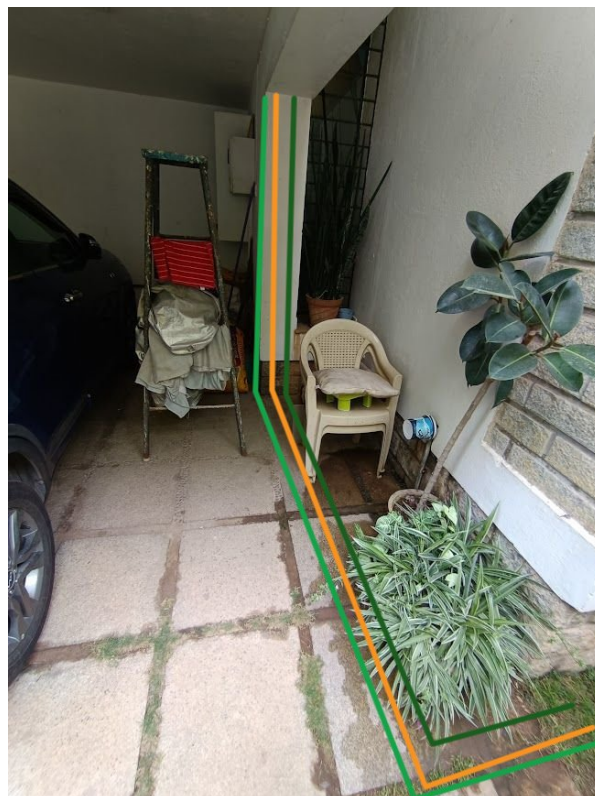

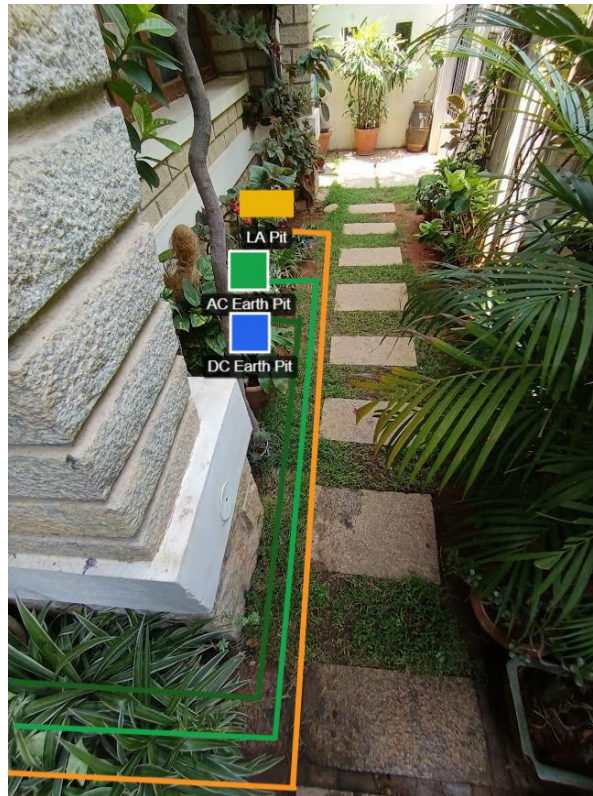

## OBSERVATIONS & RECOMMENDATIONS

### EcoSoch Scope

| # | Observation                                                                                                                    |
|---|--------------------------------------------------------------------------------------------------------------------------------|
| 1 | As discussed with the customer, the routing, cable earthing, inverter location, and solar meter location have been considered. |

### Customer Scope

| # | Observation                                    |
|---|------------------------------------------------|
| 1 | Wi-Fi upto solar meter is under customer scope |

## THANK YOU

Dear Baby Usha Murlidhar,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
