

Technical Site Visit Report

Prepared for: Raghu B P_Sahakarnagar_ Non Subsidy_7.44kWp_String - SRI RANGA 1998 C-BLOCK

PROJECT INFORMATION

Report Number	ESV-2026-0215
Project ID	6ZHVCJIF
Project Name	Raghu B P_Sahakarnagar_ Non Subsidy_7.44kWp_String
Building Name	SRI RANGA 1998 C-BLOCK
Billing Name	Raghu B P
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Mahantayya
Site Address	Raghu .B.P, 1998, 'SRI RANGA', 2nd Main Road C - Block, Near Mangalore Brick House Sahakarnagar BENGALURU - 560092.
GPS Coordinates	13.0615368, 77.5793983
Google Maps	https://www.google.com/maps?q=13.0615368,77.5793983
Visit Date	2026-09-26
Visited By	K Naveen
Revision	Rev 0

CLIENT INFORMATION

Client Name	Raghu B P
Contact	'+91 9980142381

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	7.44
Sanction Load (kW)	8

Module Make & Capacity	Premier Bifacial Non DCR 620
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	12
Inverter Type	String
Inverter Brand	Deye 8 kW 3phase Hybrid
Number of Inverters	1
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter,DCD B,ACDB will be installed near the main meter location	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the basement which is near to the parking area.	-
6	Where is the Internet Router located?	First floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	2 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstructions on the roof is flower pots, solar water heaters, sky lights could affect the solar installation.	-
3	What is the angle of the panels? (in degrees)	7	-

#	Question	Answer	Notes
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	AL Short Rail - Elevated Structure
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	N/A	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	The height of the building is G+3 is approximately 14 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-

#	Question	Answer	Notes
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall Mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 750, width: 950	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1200, width: 1400	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	N/A	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).






This route (using Staircase) will be followed to carry Small items.



Staircase Details

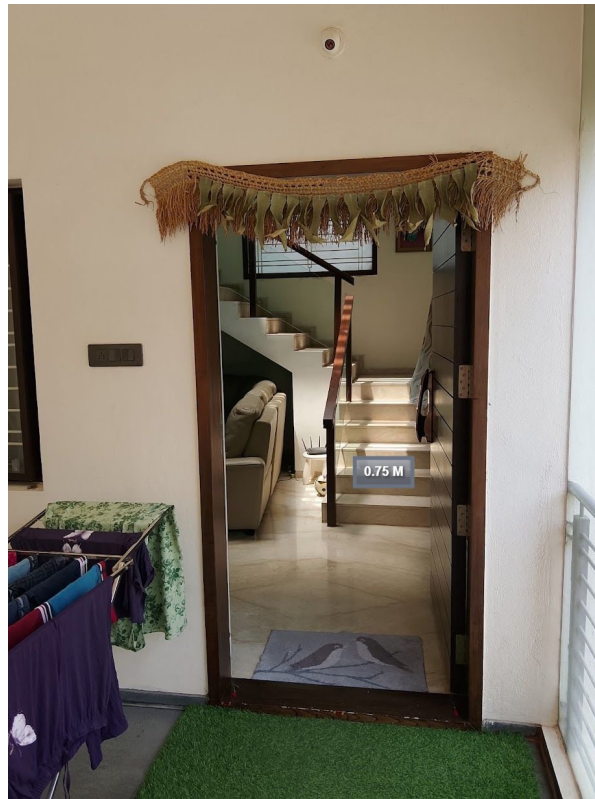

Meter Box




Material Storage



Proposed PV Area



Cable Routing

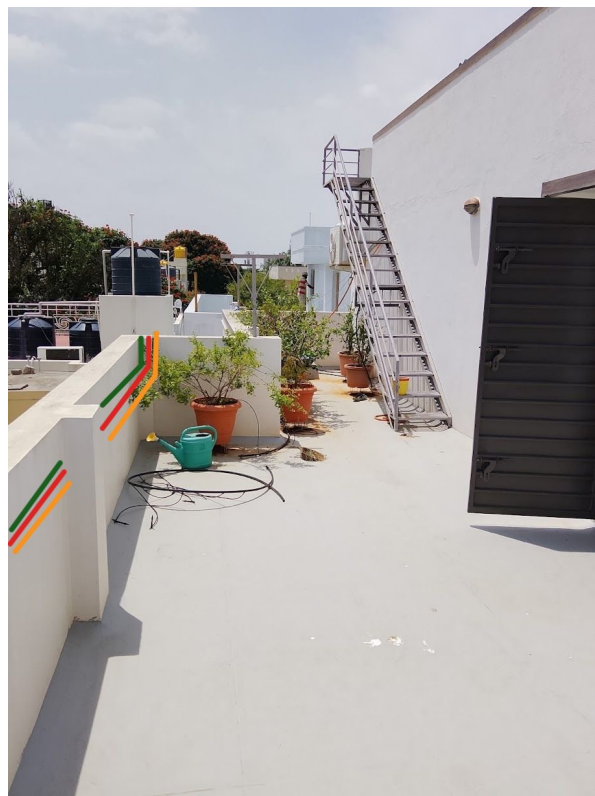













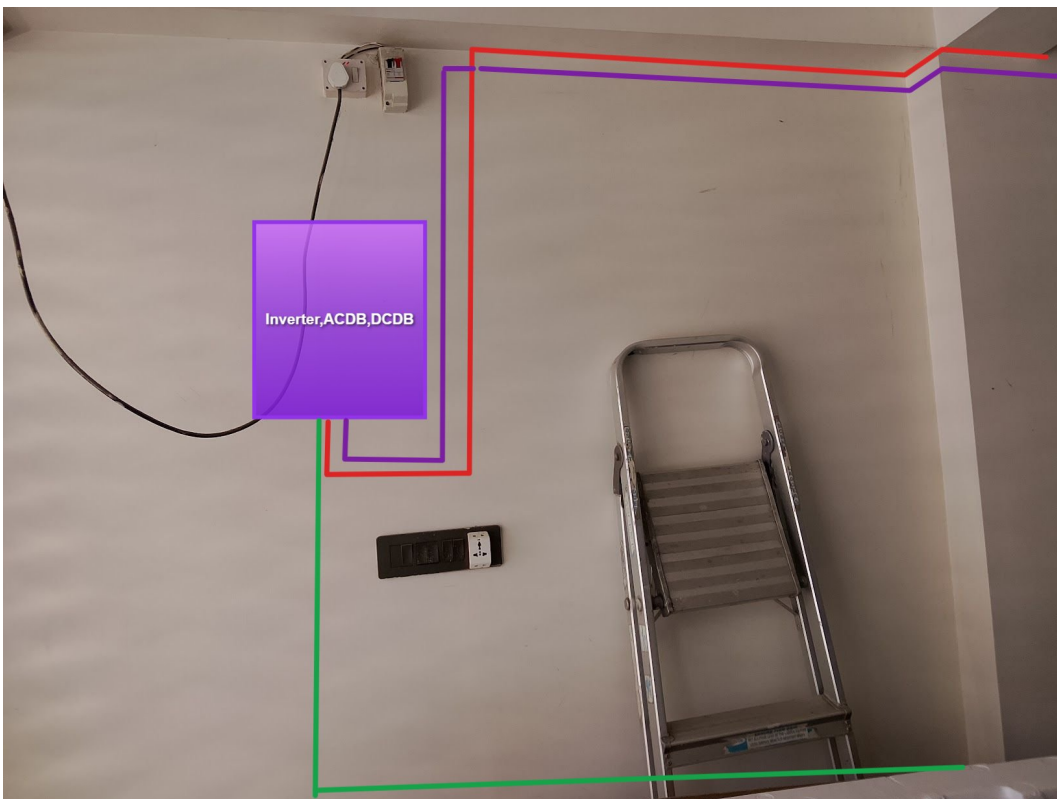





Equipment Location

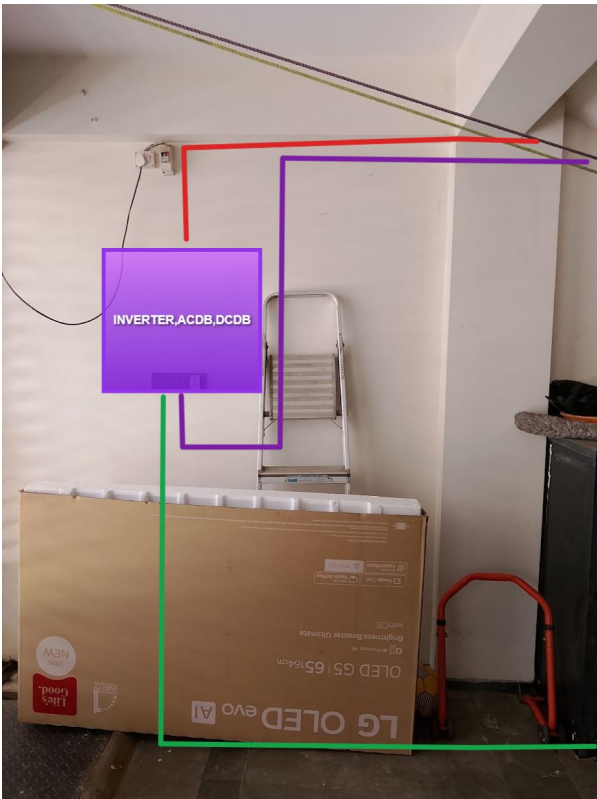






Earth Pit Location






Site Layout - Top View

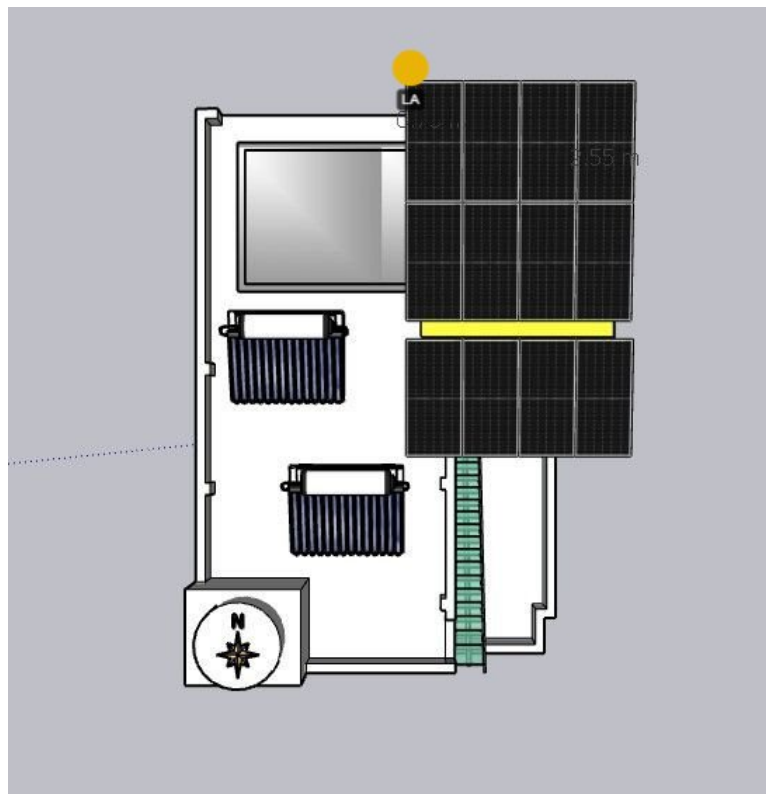

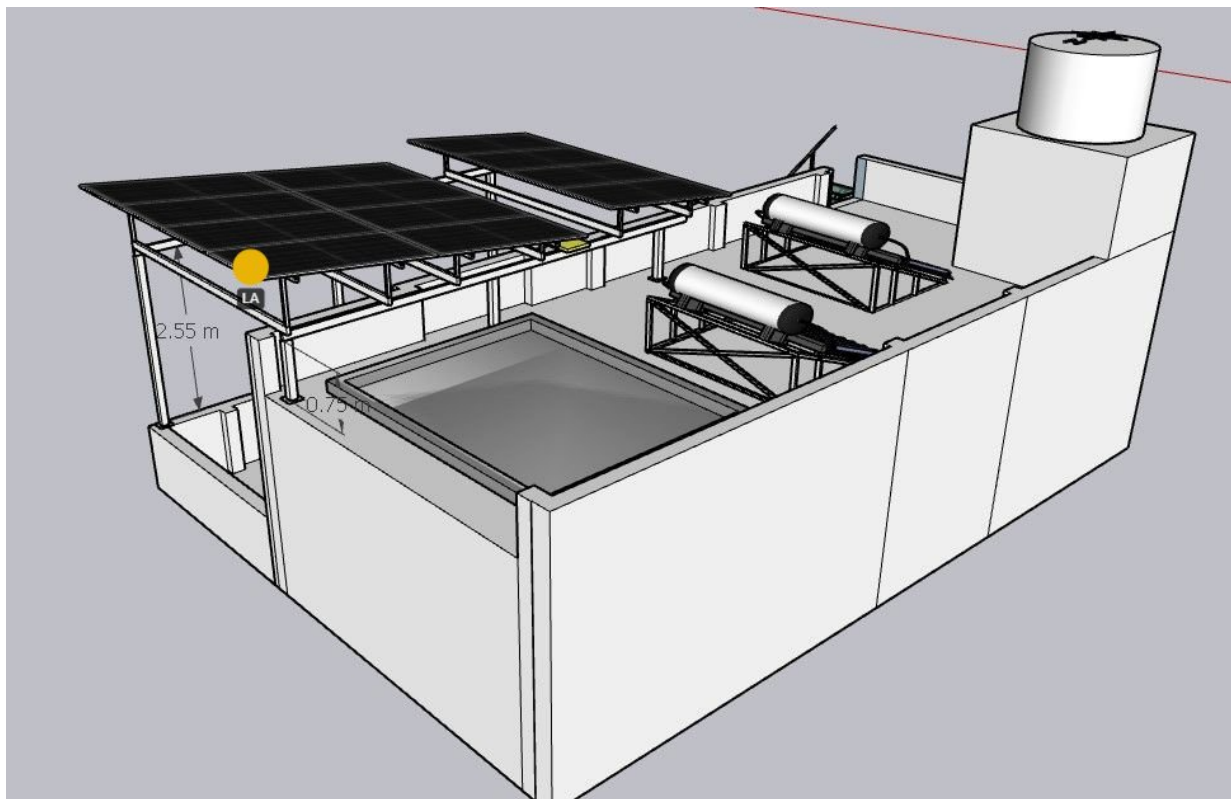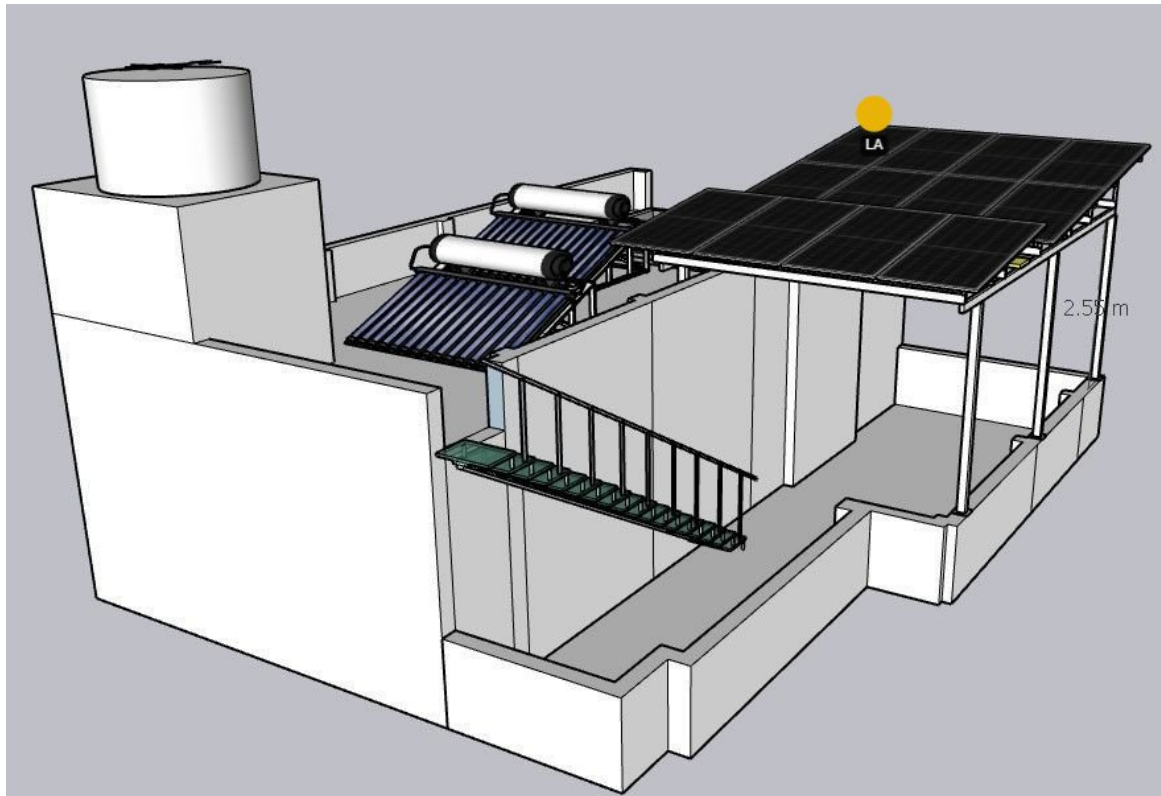

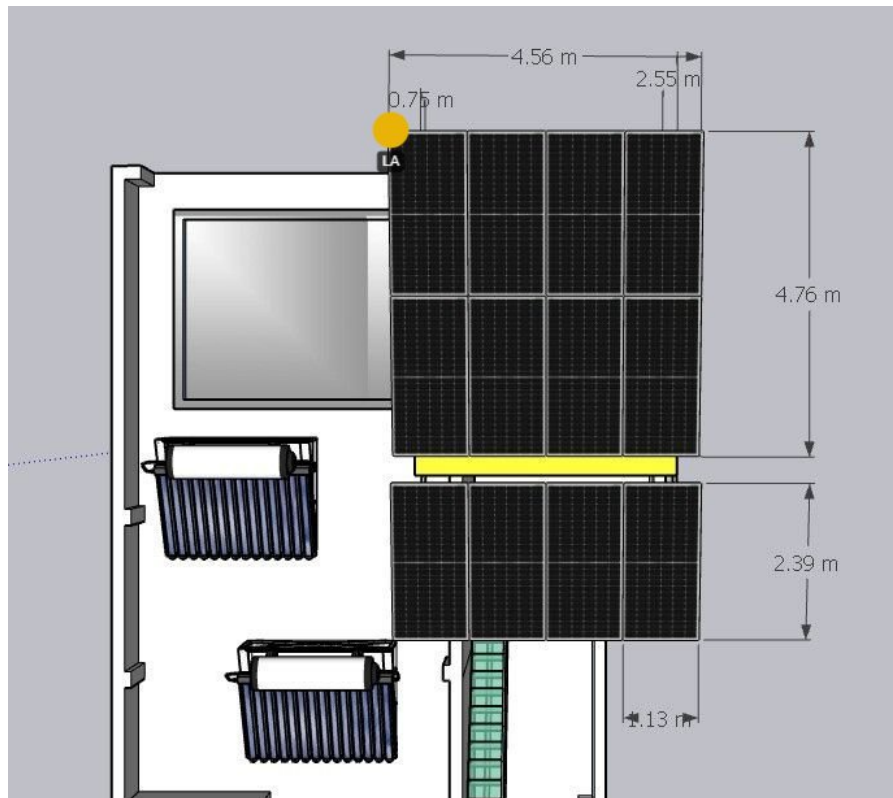

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi upto the inverter location is under customer scope.
2	MS Fabrication is under customer scope.
3	As per the customer suggestions only the panel layout, earthing, cable routing has been considered.

THANK YOU

Dear Raghu B P,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
