

Technical Site Visit Report

Prepared for: Gandharv_felicity_8.4kWp_Hybrid - Villa #51

PROJECT INFORMATION

Report Number	ESV-2026-0191
Project ID	045EF512
Project Name	Gandharv_felicity_8.4kWp_Hybrid
Building Name	Villa #51
Billing Name	Gandharv
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Hariom
Site Address	Villa 51, Felicity by Bricks and Milestones, Kada Agrahara, Sree Narayana Nagar, Sompura Gate, Sarjapur Road, Bengaluru, Karnataka, Bengaluru-562125
GPS Coordinates	12.8605796, 77.7540579
Google Maps	https://www.google.com/maps?q=12.8605796,77.7540579
Visit Date	2026-08-22
Visited By	K Naveen
Revision	Rev 1

CLIENT INFORMATION

Client Name	Gandharv
Contact	+91 89515 75180

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	8.4
Module Make & Capacity	Waaree bifacial Non DCR - 700 Wp

Module Length (mm)	2382
Module Width (mm)	1303
Number of Panels	12
Inverter Type	Hybrid (String)
Inverter Brand	Deye 8 kW 3phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter,DCDB,ACDB,Battery will be placed near the electrical room	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the parking area which is located beside the electrical room	-
6	Where is the Internet Router located?	Customer scope	<i>Under construction</i>
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstructions on the roof are raised reinforcement that could slightly disturb the solar installation.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	Elevated HDGI 2P4 Structure and 1P4 structure with 2m front clearance
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	The existing 1 inch conduit pipe are available at the site for DC cable routing
13	What is the height of the building and how many floors does it have?	The height of the building is Parking+G+2+headroom is approximately 15 meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	Temporary 3 phase meter is available at the site
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	No	Under construction
4	Is the Termination Point easily visible or sealed?	-	Under construction
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	No	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-

#	Question	Answer	Notes
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Under construction
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1500, width: 1500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1500, width: 2000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).








This route (using Staircase) will be followed to carry Small items.



Staircase Details



Meter Box

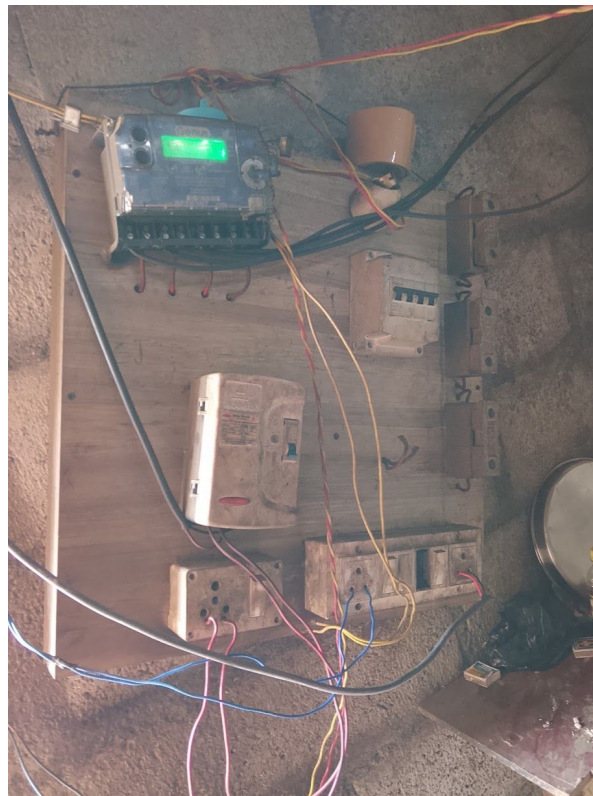




Material Storage




Proposed PV Area

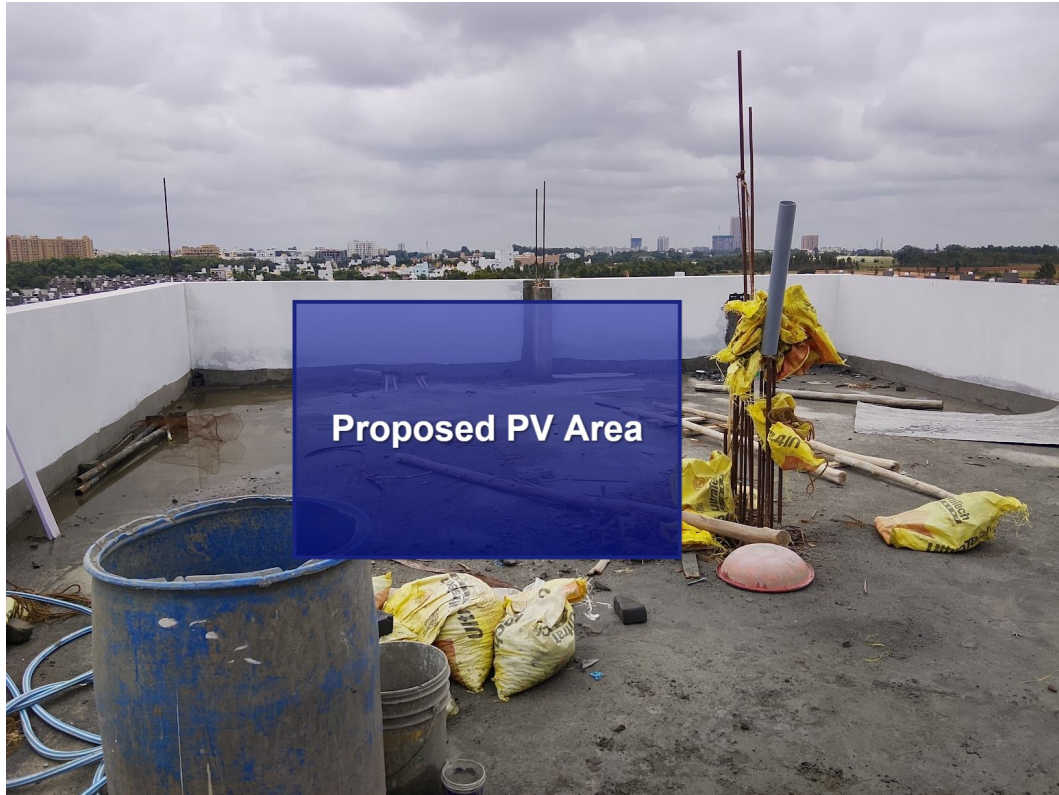


Cable Routing



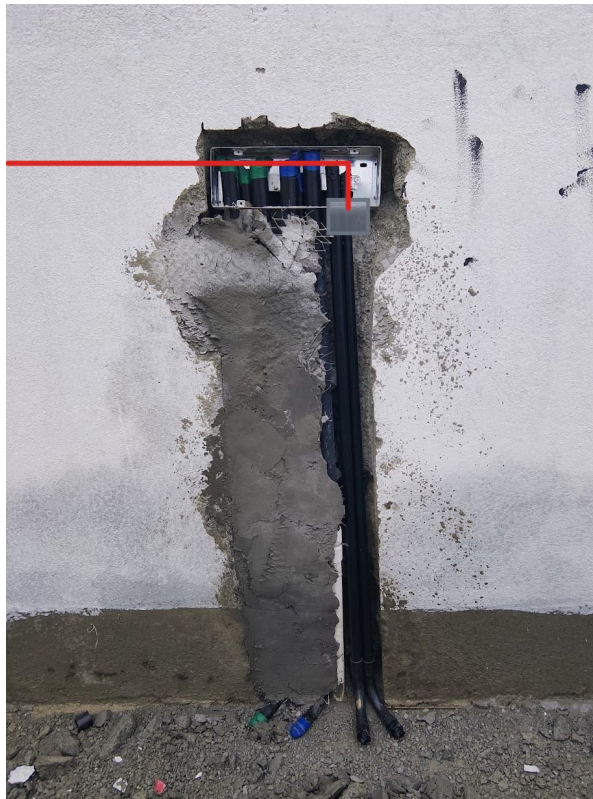






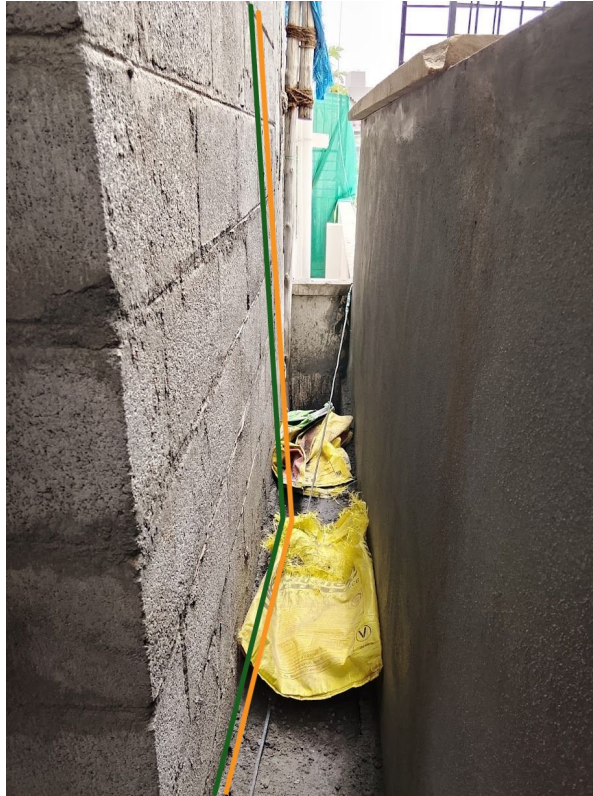

Equipment Location


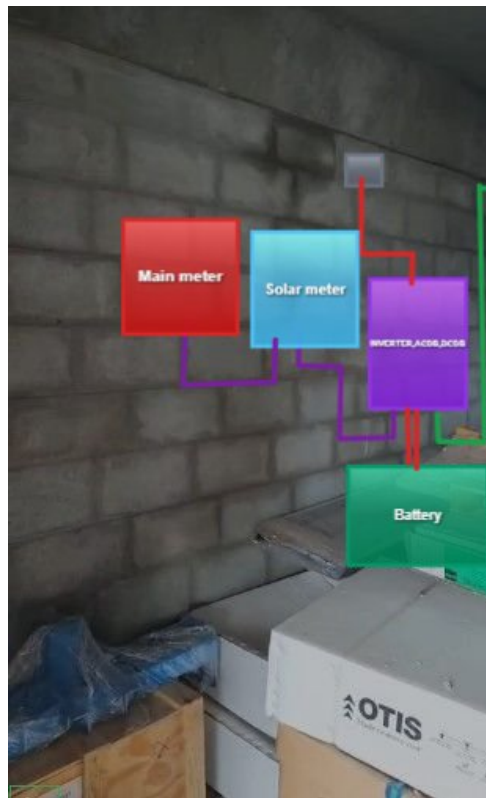



Make a hole to run the AC earthing up to the earthing location

Earth Pit Location



Site Layout - Top View

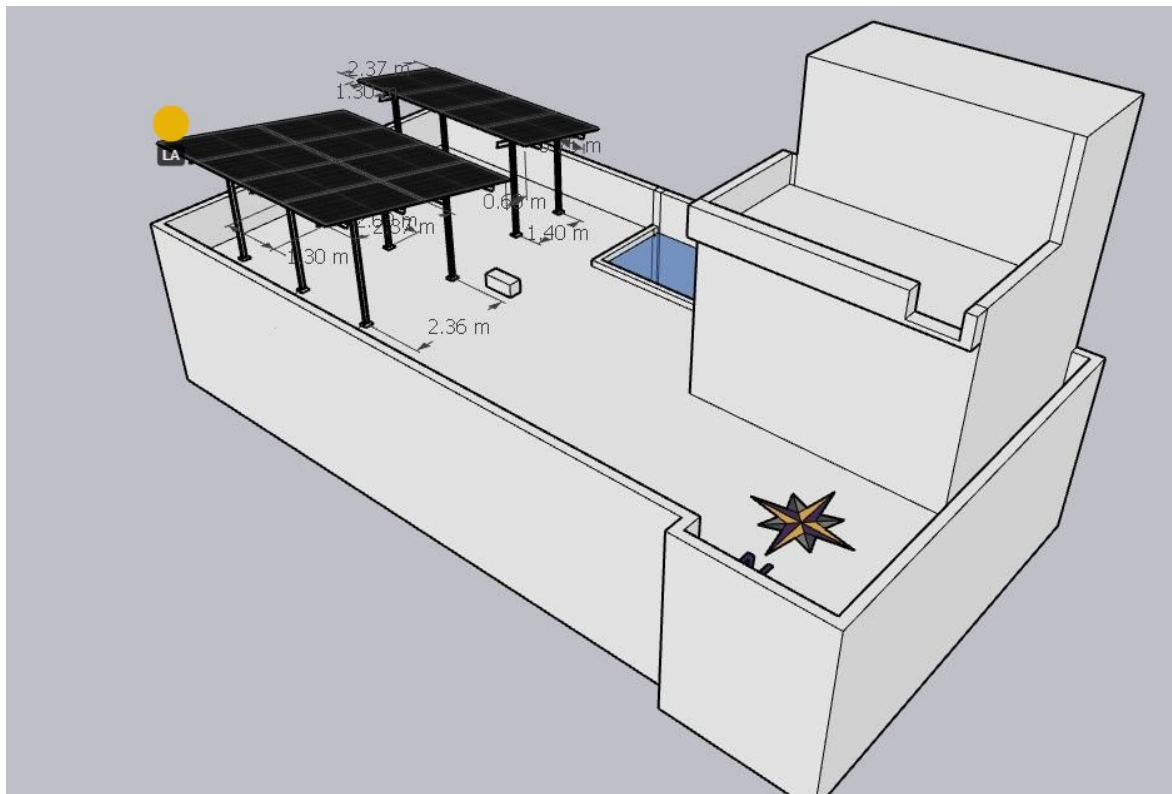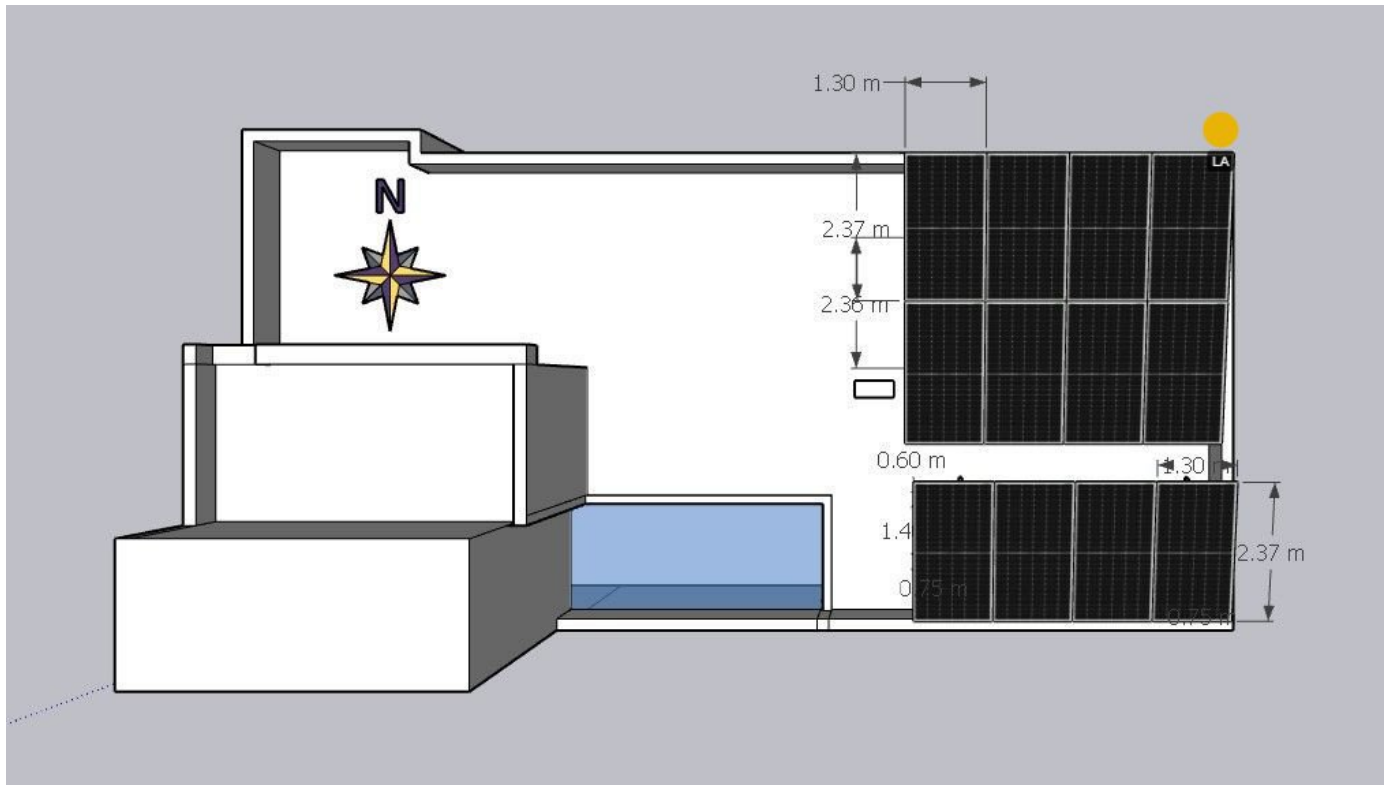

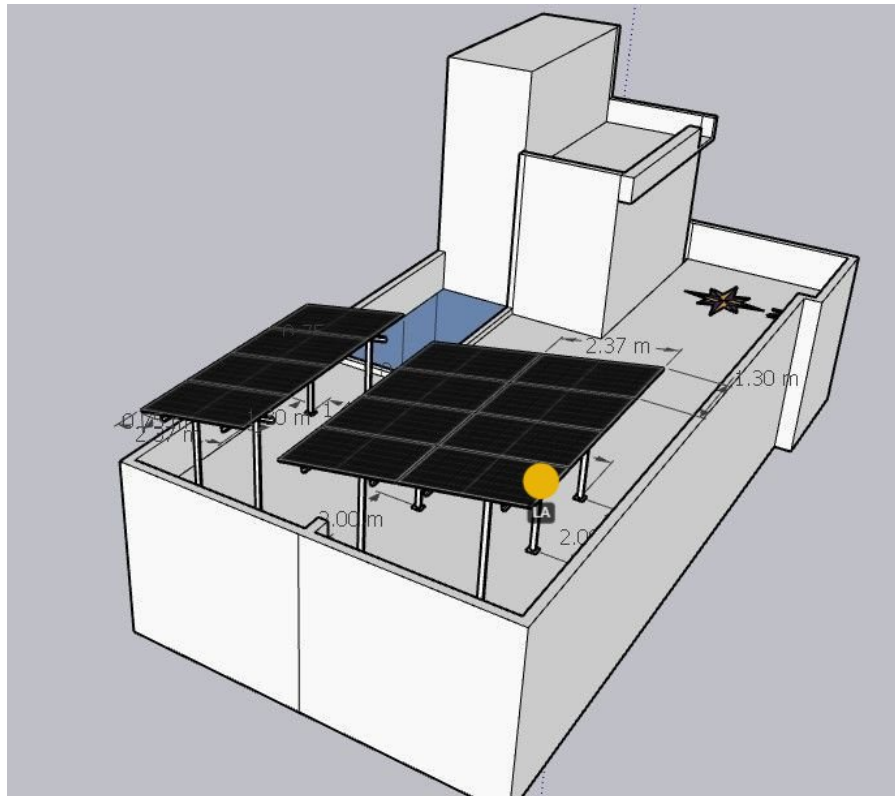

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	Ups point near the inverter location is under customer scope.
3	As per the client concern the 2P6 HDGI structure is changed to 2P4 and 1P4 structure with 2m front clearance.
4	As per the customer suggestions only the panel layout, cable routing, earthing has been considered.
5	To avoid the installation disturbances to cut raised reinforcement is under construction.

THANK YOU

Dear Gandharv,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
