

Technical Site Visit Report

Prepared for: Bharathi s murthy - Baohukla 159

PROJECT INFORMATION

Report Number	ESV-2026-0138
Project ID	9B4422B0
Project Name	Bharathi s murthy
Building Name	Baohukla 159
Billing Name	Bharathi s murthy
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Govindaraju
Site Address	No133, Vashishta, 1st cross Royal Residency Layout sir M V Road BTM 4thstage Bangalore 560076
GPS Coordinates	12.8832475740197, 77.61097068128714
Google Maps	https://www.google.com/maps?q=12.883247574019702,77.61097068128714
Visit Date	2026-06-08
Visited By	K Naveen
Revision	Rev 0

CLIENT INFORMATION

Client Name	Bharathi s murthy
Contact	9845234634

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	4.88
Module Make & Capacity	Premier DCR Bifacial 610

Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	8
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	8
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The chajjas are the obstacles that could hinder the material lifting	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the corridor which is front side of the house.	-
6	Where is the Internet Router located?	Ground floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	3 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	RCC Flat roof with laid of tiles and uneven surfac roof area.
2	Are there any obstructions on the roof that could affect the solar installation?	details: The obstructions on the roof are solar waterheater and watertanks	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-

#	Question	Answer	Notes
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	<i>SolrFit X-Series-Elevated HDGI with ballast and Adhesive</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	G+1+Headroom is approximately 15 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	N/A	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	Yes	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	Without Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-

#	Question	Answer	Notes
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 600, width: 400	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1500, width: 600	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route




This route (using lifting) will be followed to carry large items (like Panels).




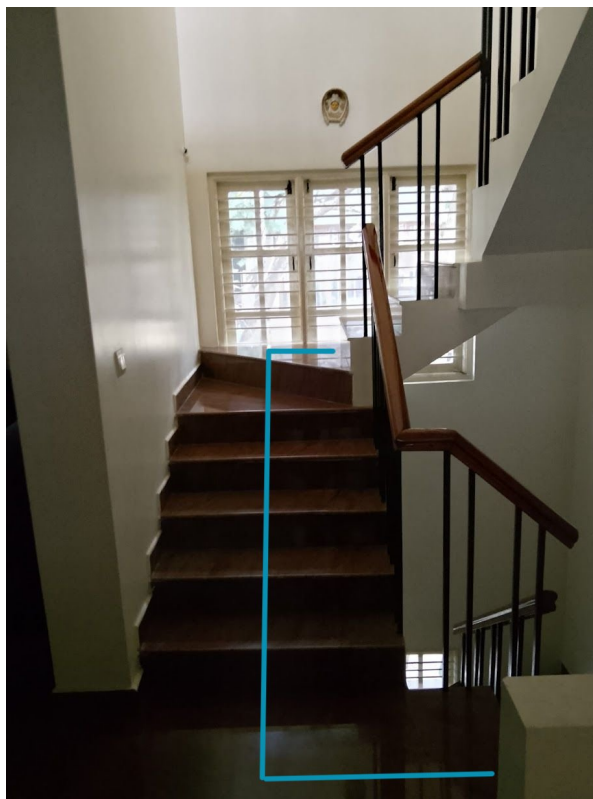


This route (using Staircase) will be followed to carry Small items.

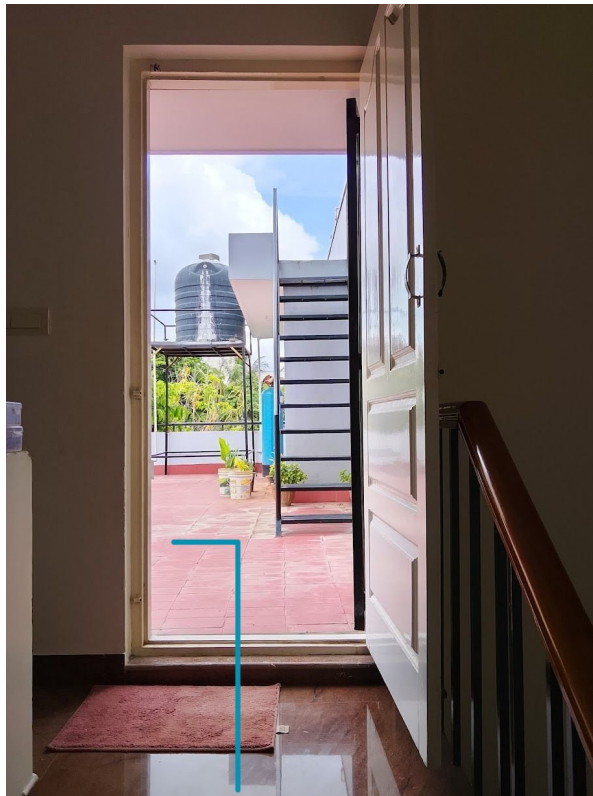

Staircase Details

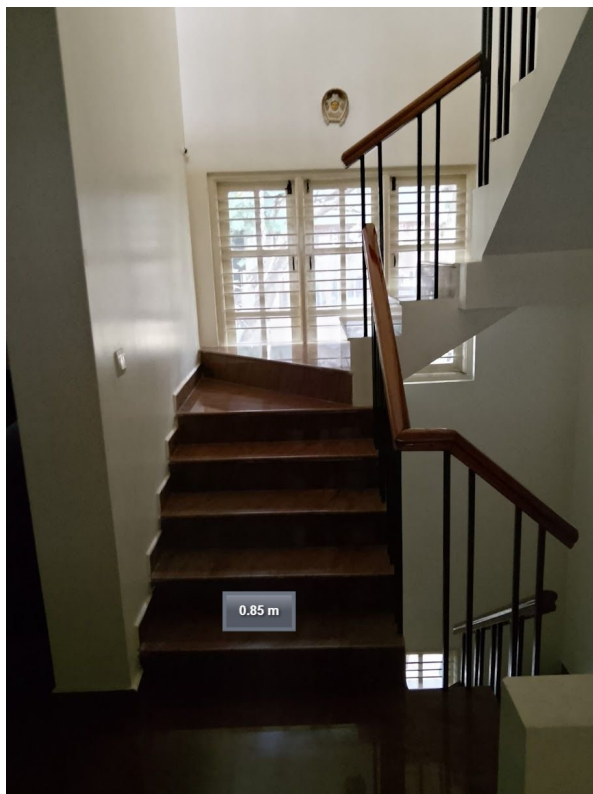

Meter Box

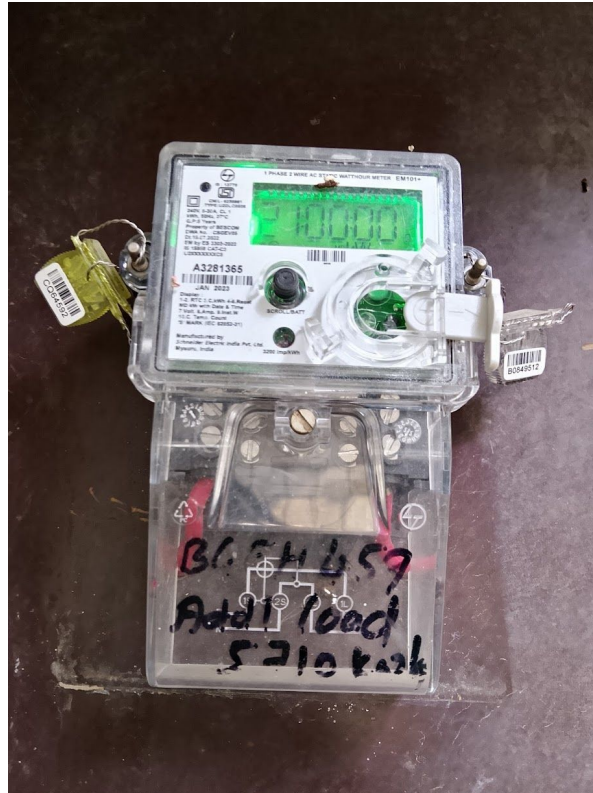

Material Storage





Proposed PV Area



At the time of installation make sure that levelling the roof surface


Cable Routing

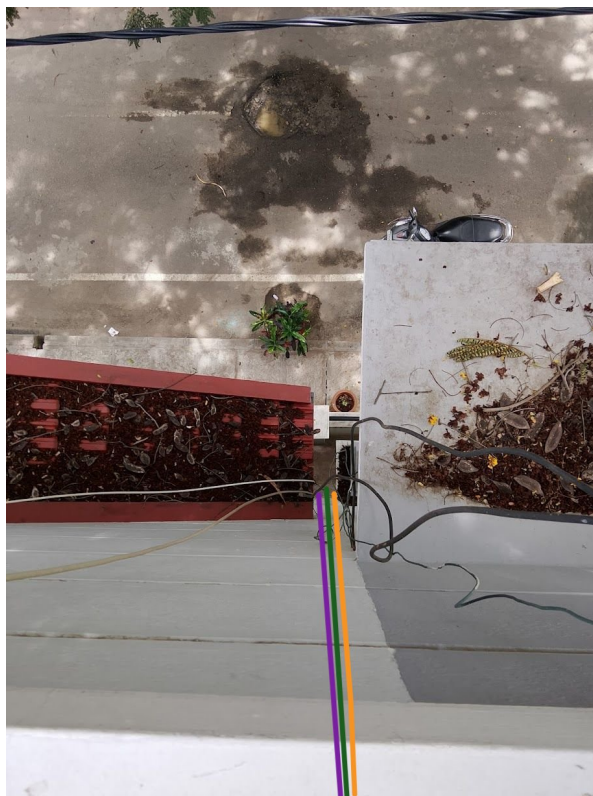

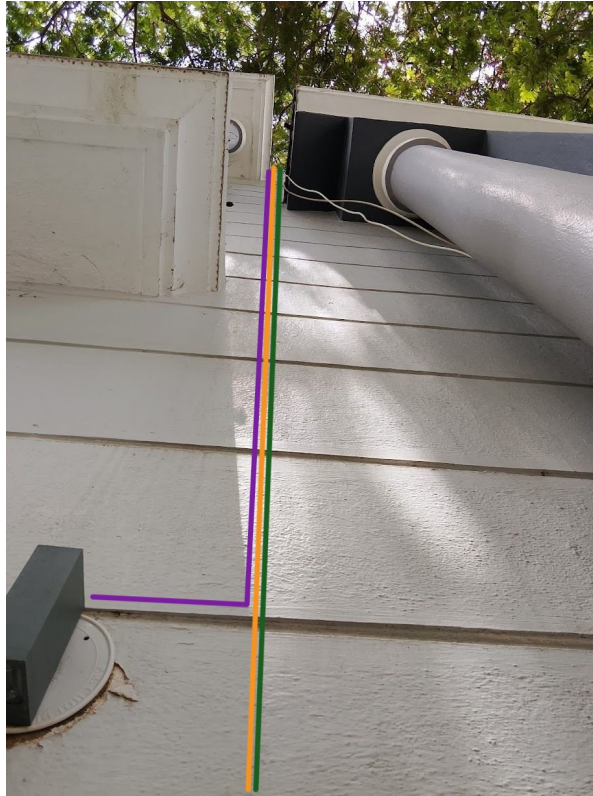






Equipment Location


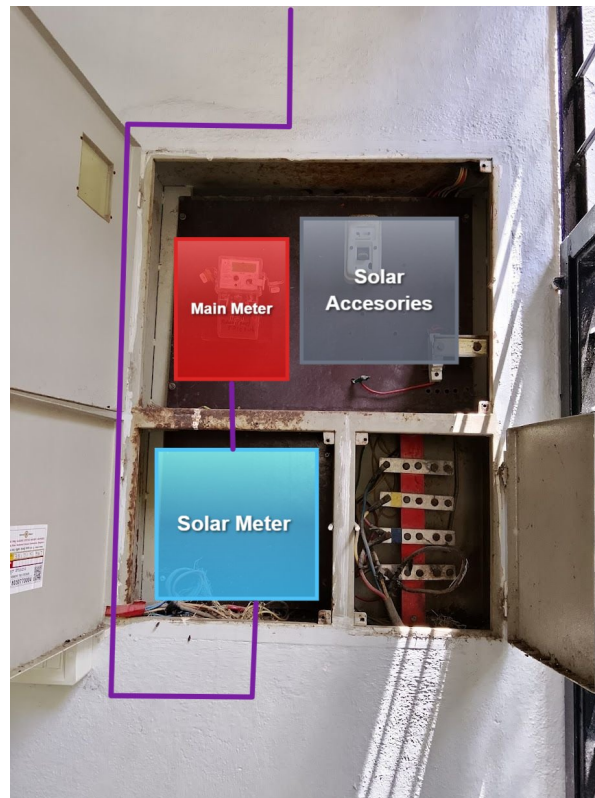


Earth Pit Location

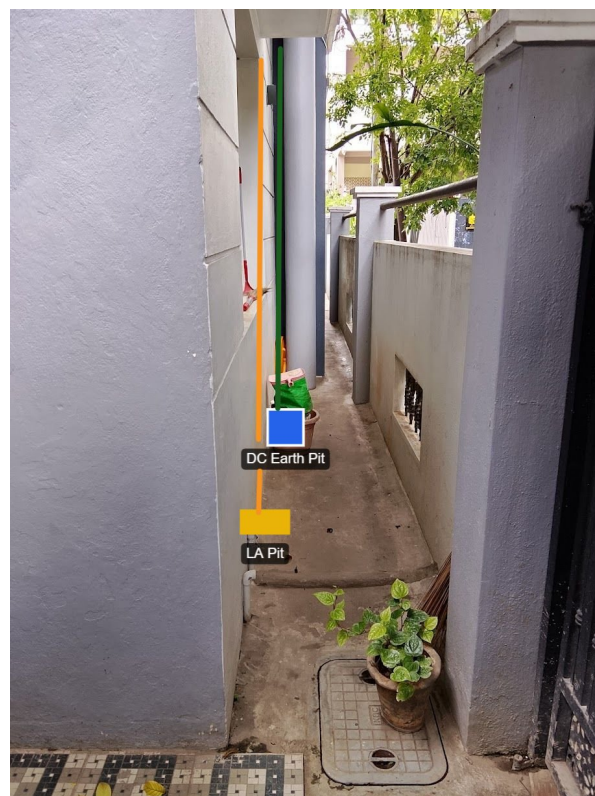

Site Layout - Top View

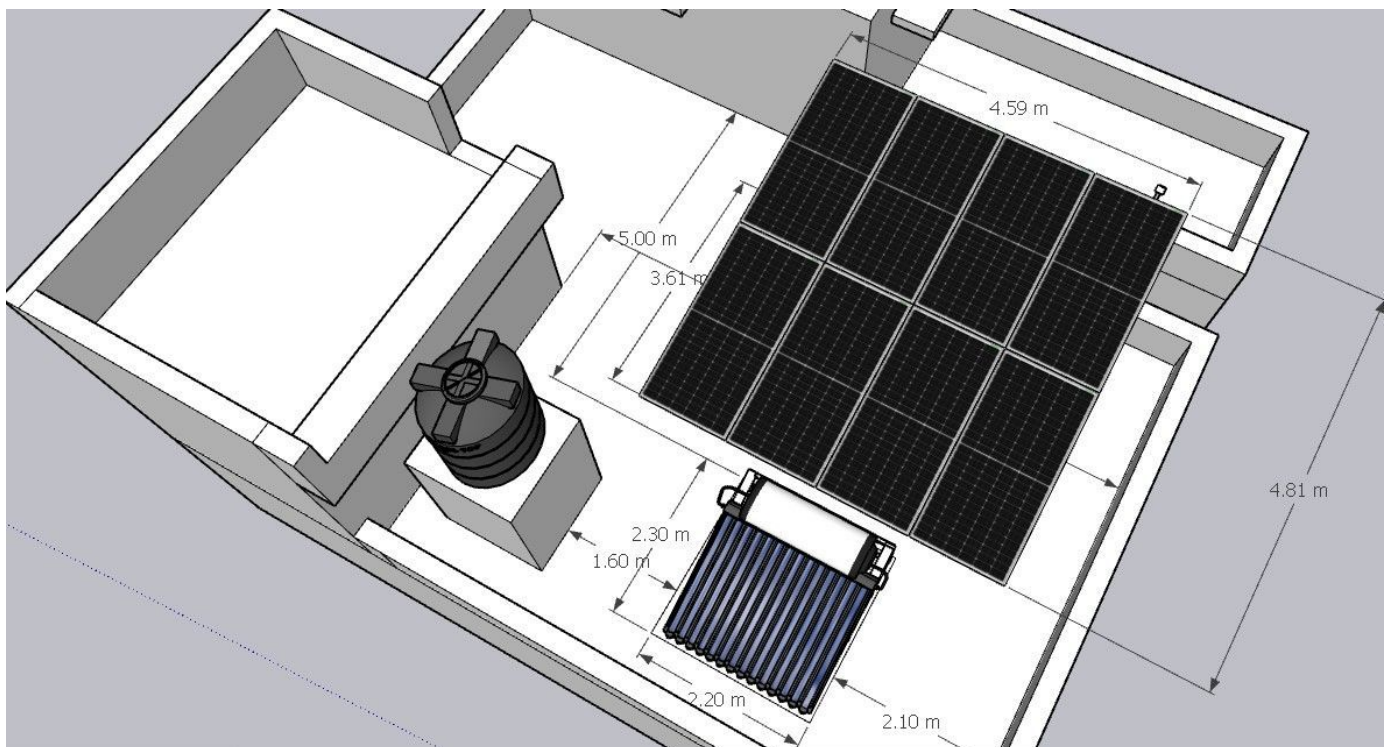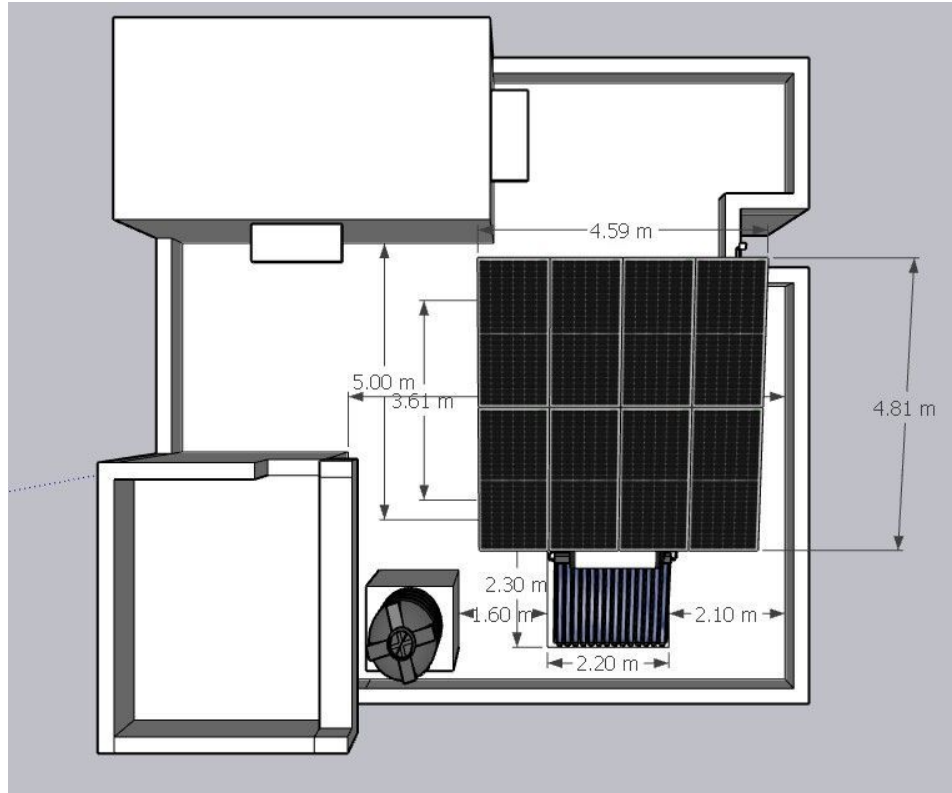

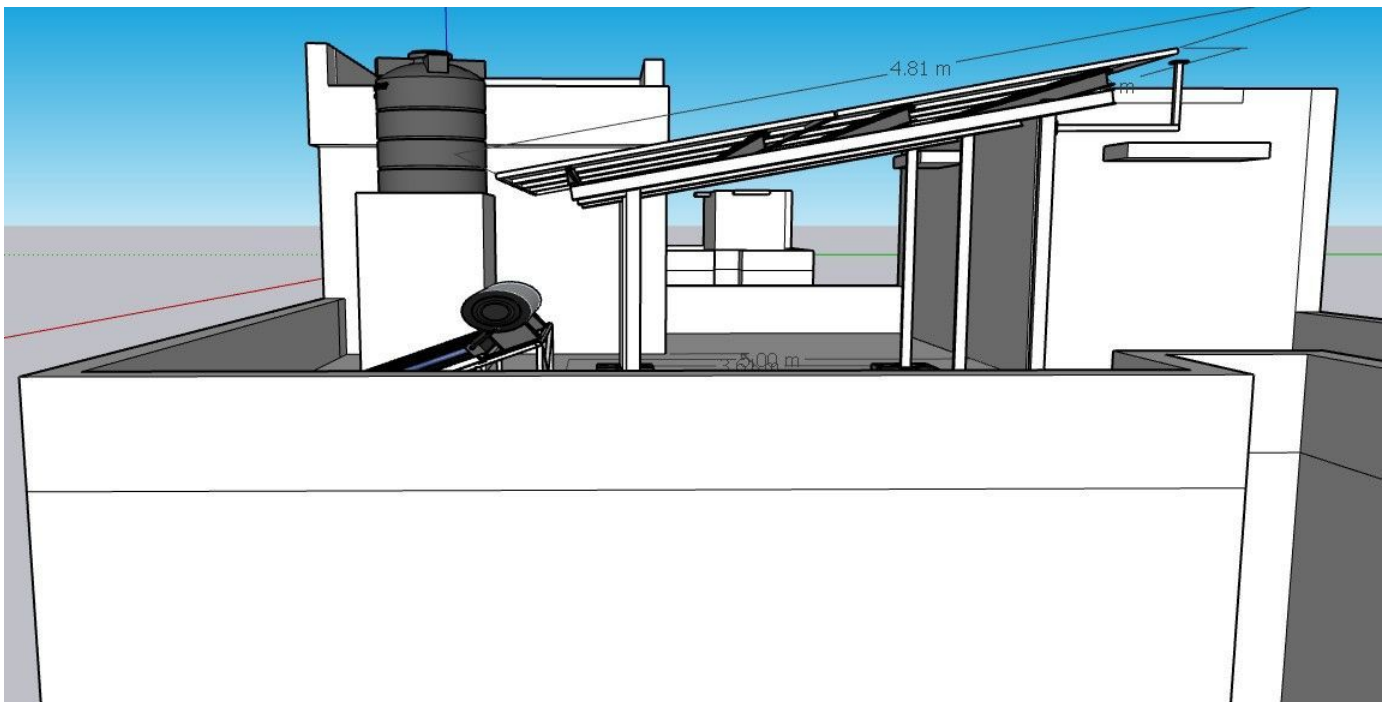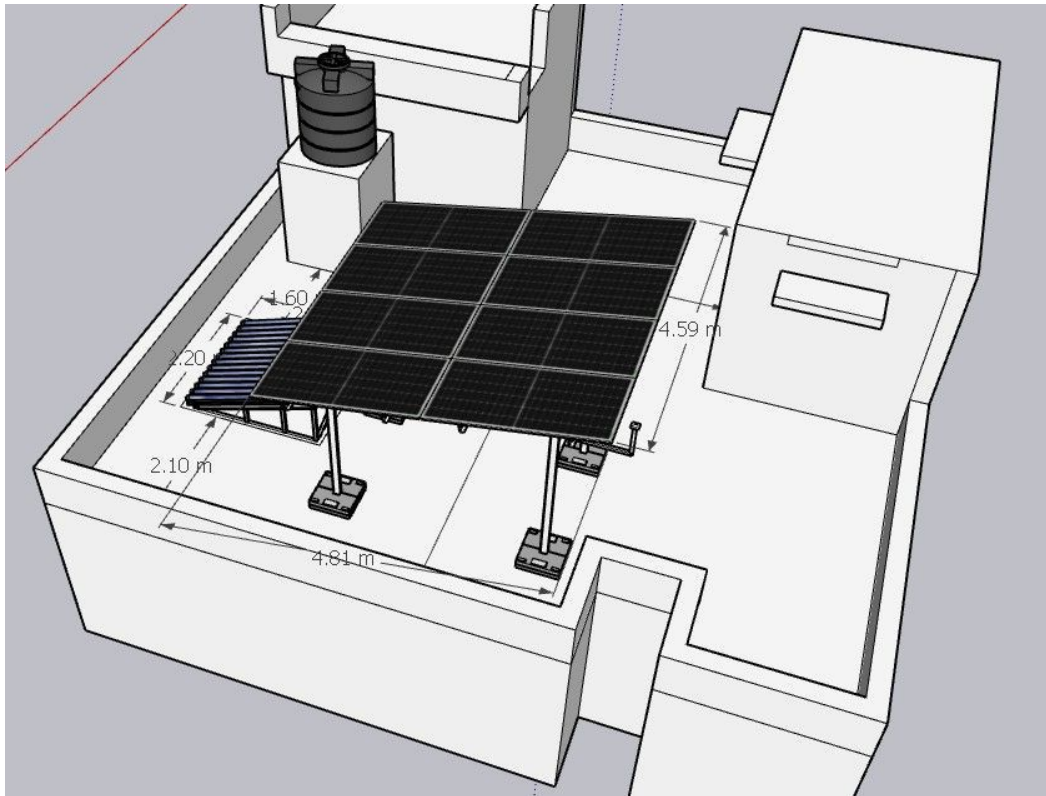

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	The proposed roof is tiled and has an uneven surface. It is recommended to level the roof area, if possible, prior to installation to facilitate proper system mounting and alignment.
2	The allocated area for the solar meter cubicle in the main meter section is approximately 0.6 m × 0.4 m. The necessary accessories can be accommodated within this space, with the solar system interconnection installed below the meter cubicle.

Customer Scope

#	Observation
1	Wi-Fi up to the solar meter location is under customer scope.
2	As per the customer scope only panel layout, cable routing, earthing location has been finalised

THANK YOU

Dear Bharathi s murthy,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
