

## Technical Site Visit Report

Report for: Nischal Dutta\_Subsidy\_Adarsh palm retreat\_7.38kWp\_Microinverter (IQ Series) - Villa 511, Lane 1N, Phase 3, Adarsh Palm Retreat Villas

### PROJECT INFORMATION

|                 |                                                                                                                                                     |
|-----------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0178                                                                                                                                       |
| Project ID      | B55AA886                                                                                                                                            |
| Project Name    | Nischal Dutta_Subsidy_Adarsh palm retreat_7.38kWp_Microinverter (IQ Series)                                                                         |
| Building Name   | Villa 511, Lane 1N, Phase 3, Adarsh Palm Retreat Villas                                                                                             |
| Billing Name    | Nischal Dutta_Subsidy_Adarsh palm retreat_7.38kWp_Microinverter (IQ Series)                                                                         |
| Project Sector  | Residential                                                                                                                                         |
| Project Type    | With Subsidy                                                                                                                                        |
| Sales Lead      | Mahantayya                                                                                                                                          |
| Site Address    | Nischal Dutta Villa 511, Lane 1N, Phase 3, Adarsh Palm Retreat Villas DevaraBeesanHalli, Outer Ring Road BENGALURU, KARNATAKA 560103                |
| GPS Coordinates | 12.91829680005437, 77.69228460121654                                                                                                                |
| Google Maps     | <a href="https://www.google.com/maps?q=12.918296800054373,77.69228460121654">https://www.google.com/maps?q=12.918296800054373,77.69228460121654</a> |
| Visit Date      | 2026-07-25                                                                                                                                          |
| Visited By      | Sai                                                                                                                                                 |
| Revision        | Rev 2                                                                                                                                               |

### CLIENT INFORMATION

|             |               |
|-------------|---------------|
| Client Name | Nischal Dutta |
| Contact     | 9945512727    |

### PROJECT DETAILS

|                           |         |
|---------------------------|---------|
| Solar Rooftop System Type | On-Grid |
| System Capacity (kWp)     | 7.38    |
| Sanction Load (kW)        | 10      |

|                         |                           |
|-------------------------|---------------------------|
| Module Make & Capacity  | Adani DCR bifacial 615 Wp |
| Module Length (mm)      | 2382                      |
| Module Width (mm)       | 1133                      |
| Number of Panels        | 12                        |
| Inverter Type           | Micro                     |
| Inverter Brand          | Enphase IQ8P              |
| Number of Inverters     | 12                        |
| Mounting Structure Type | Elevated                  |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                         | Notes |
|---|----------------------------------------------------------------------------|------------------------------------------------|-------|
| 1 | Can the delivery van/truck reach the material unloading point?             | No                                             | -     |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | No                                             | -     |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | N/A                                            | -     |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | N/A                                            | -     |
| 5 | Did you discuss the location of the earth pits with the customer?          | Earth pits are located near the basement area. | -     |
| 6 | Where is the Internet Router located?                                      | Customer scope                                 | -     |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | N/A                                            | -     |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                            | -     |

### Roof Details

| # | Question                                                                             | Answer        | Notes                                                                                                                |
|---|--------------------------------------------------------------------------------------|---------------|----------------------------------------------------------------------------------------------------------------------|
| 1 | What type of roof is present at the site?                                            | RCC Flat Roof | -                                                                                                                    |
| 2 | Are there any obstructions on the roof that could affect the solar installation?     | No            | -                                                                                                                    |
| 3 | What is the angle of the panels? (in degrees)                                        | 9             | -                                                                                                                    |
| 4 | In case of sloped roof, what is the slope angle of the roof? (in degrees)            | N/A           | -                                                                                                                    |
| 5 | On how many roofs at the site are we installing solar?                               | 0             | -                                                                                                                    |
| 6 | If it is a Tiled roof, what is underneath the tiles?                                 | -             | The posts (legs) have been positioned beneath the tiled roof, where a concrete slab is present underneath the tiles. |
| 7 | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled? | N/A           | -                                                                                                                    |

| #  | Question                                                                                                 | Answer                                             | Notes                  |
|----|----------------------------------------------------------------------------------------------------------|----------------------------------------------------|------------------------|
| 8  | What type of mounting structure is planned?                                                              | Elevated                                           | MS Elevated structure. |
| 9  | What is the orientation of the solar panels?                                                             | ["South"]                                          | -                      |
| 10 | How can the roof be accessed?                                                                            | Staircase                                          | -                      |
| 11 | Is the building currently under construction?                                                            | Yes                                                | -                      |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | No                                                 | -                      |
| 13 | What is the height of the building and how many floors does it have?                                     | Height of the building is 10m; it has G+1+Headroom | -                      |
| 14 | Is the site photo matching with the building description?                                                | Yes                                                | -                      |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                                                 | -                      |

## Residential / Electrical

| #  | Question                                                                                                | Answer                            | Notes                           |
|----|---------------------------------------------------------------------------------------------------------|-----------------------------------|---------------------------------|
| 1  | What type of energy meter is currently installed?                                                       | Phase: Three Phase, Type: Digital | Building is under construction. |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes                               | -                               |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes                               | -                               |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible                           | -                               |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No                                | -                               |
| 6  | Is space available for CT within Energy meter panel?                                                    | No                                | -                               |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | Less than 50m                     | -                               |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A                               | -                               |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | Yes                               | Building is under construction. |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | Yes                               | Building is under construction. |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | Yes                               | -                               |
| 12 | In case of elevated structures, is an LA extension provided at the far end?                             | Yes                               | -                               |
| 13 | In case of elevated structures, is it with or without grouting?                                         | N/A                               | -                               |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                       | No                                | -                               |
| 15 | Are there any safety risks associated with accessing the roof for installation?                         | No                                | -                               |
| 16 | Is space present in rooftop to store the panels?                                                        | Horizontally sleeping             | -                               |
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.       | N/A                               | -                               |
| 18 | Is ventilation available in the battery location?                                                       | N/A                               | -                               |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                             | N/A                               | -                               |

| #  | Question                                                                         | Answer                       | Notes                                  |
|----|----------------------------------------------------------------------------------|------------------------------|----------------------------------------|
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).        | length: 800,<br>width: 498   | <i>Building is under construction.</i> |
| 21 | Provide the dimension for earth pits location (L x W of available space).        | length: 1000,<br>width: 1000 | -                                      |
| 22 | Is LAN cable under customer scope?                                               | No                           | -                                      |
| 23 | Is there any shadow that affects the solar installation?                         | No                           | -                                      |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location? | No                           | -                                      |

## PHOTO DOCUMENTATION

### Cable Routing Legend

| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|    | Proposed PV Module Array |
|    | Main Meter Location      |
|    | Solar Meter              |
|    | Battery                  |
|    | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |
|  | LA Pit                   |
|  | LA                       |

### Building Exterior



### Material Delivery Route








*This route carry the small items*



*This route carry the large items (like panels)*

## Meter Box

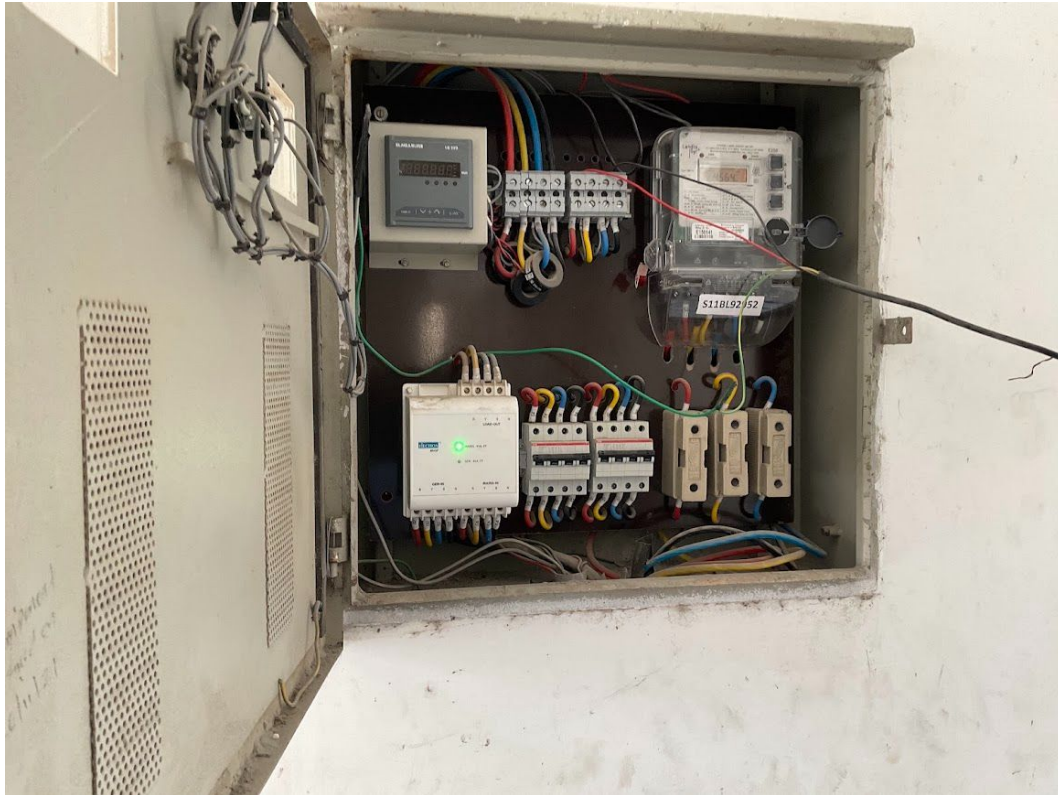


## Staircase Details






## Site Layout - Top View

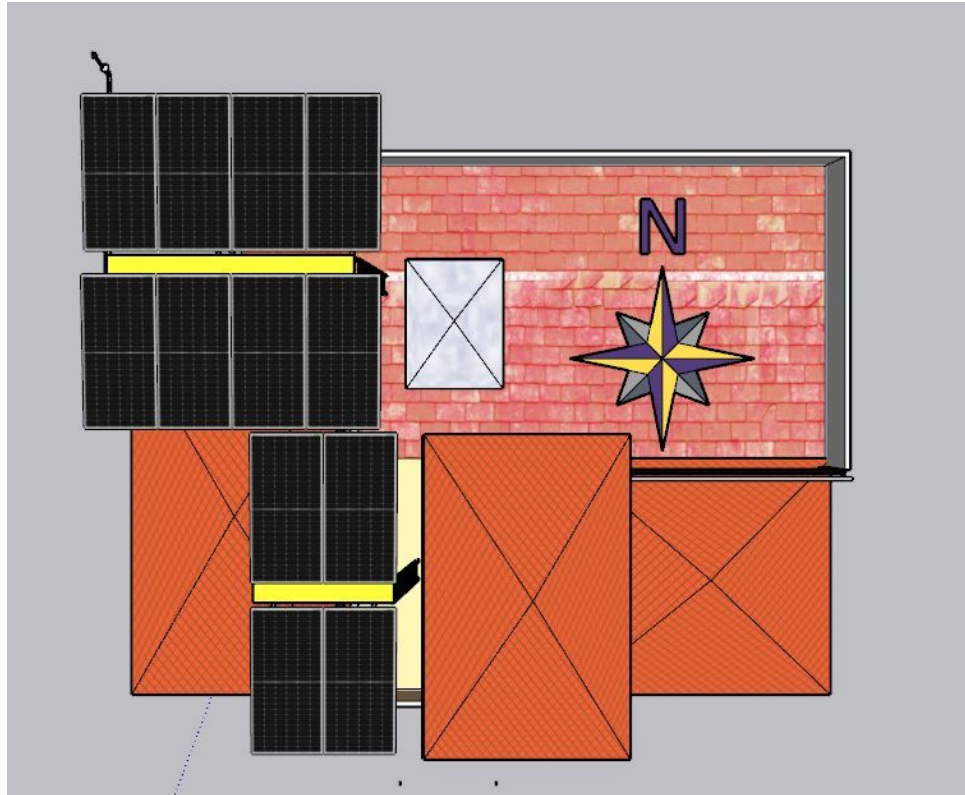


Top View

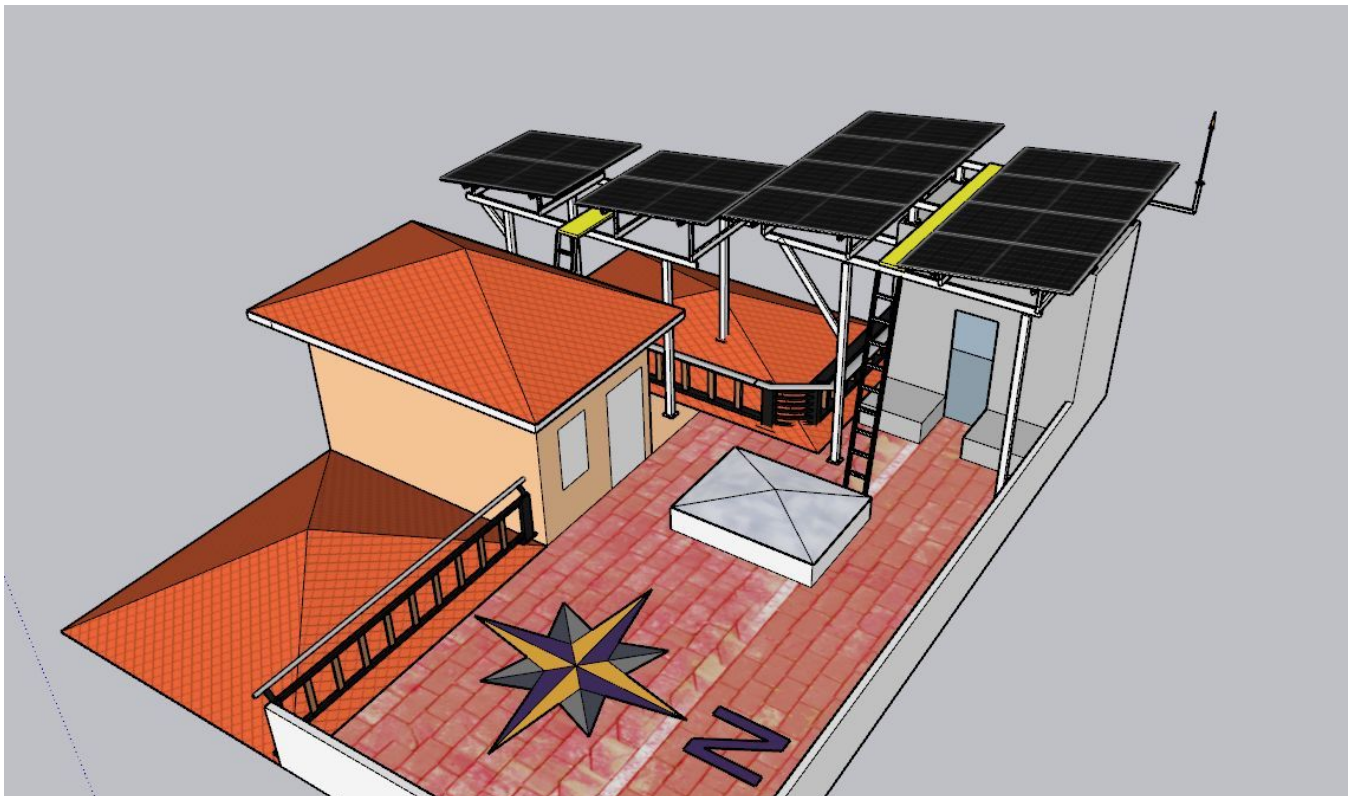


Side View (1)




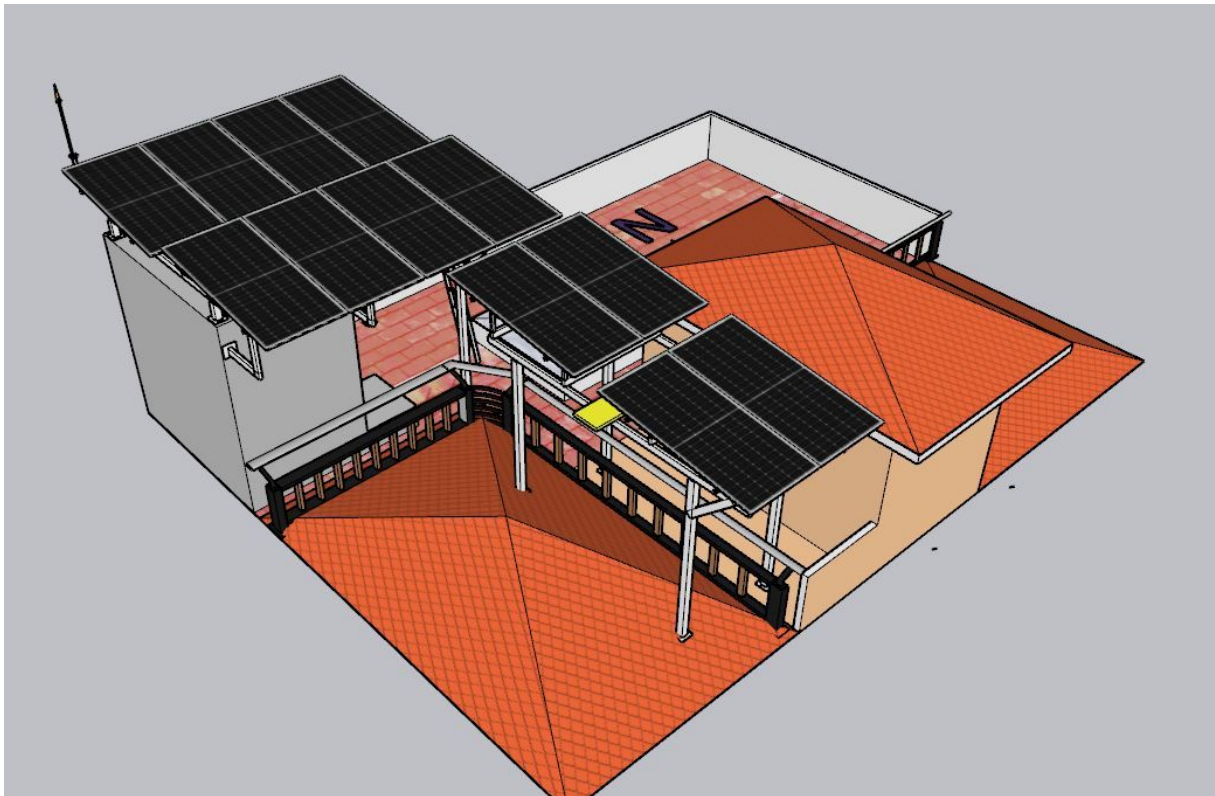


Side View (2)

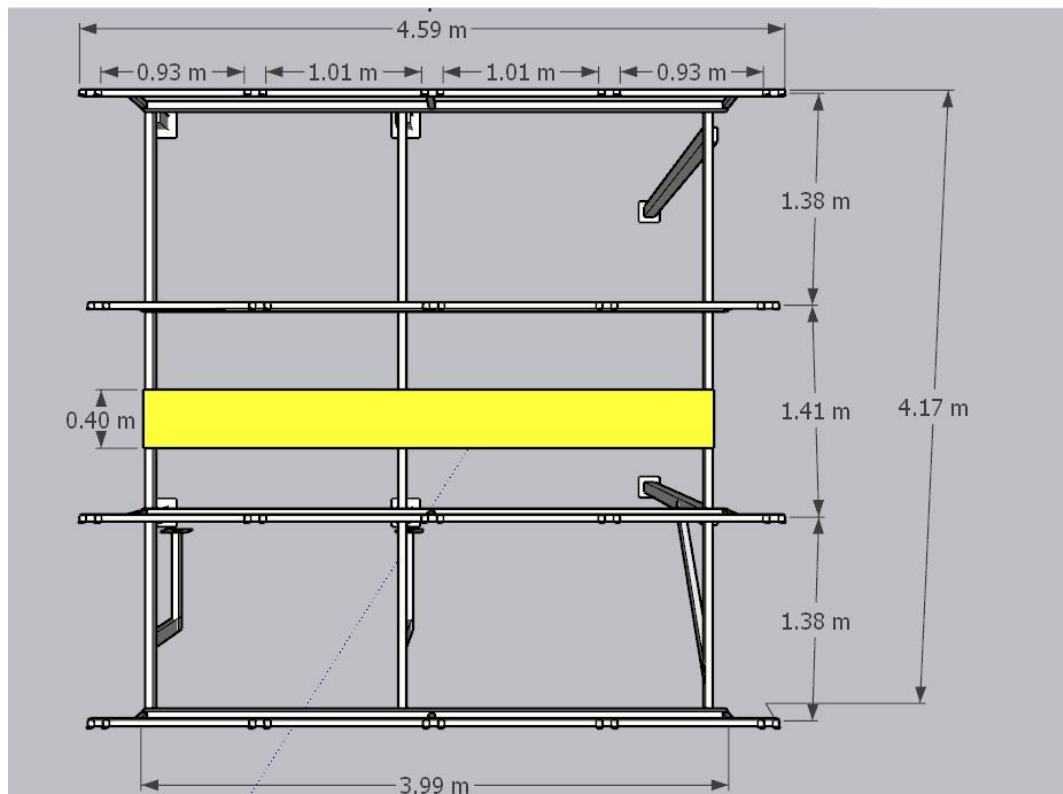


Structure details (1)

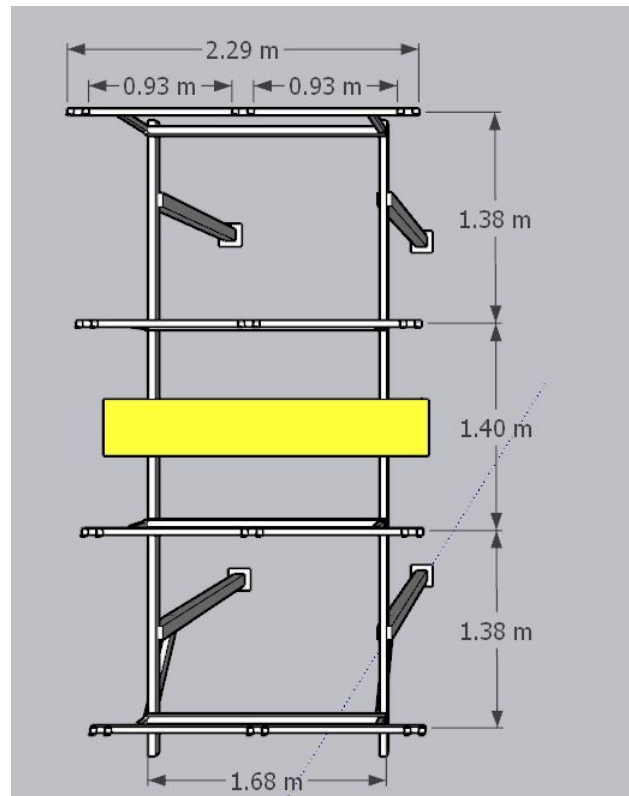


Structure details (2)

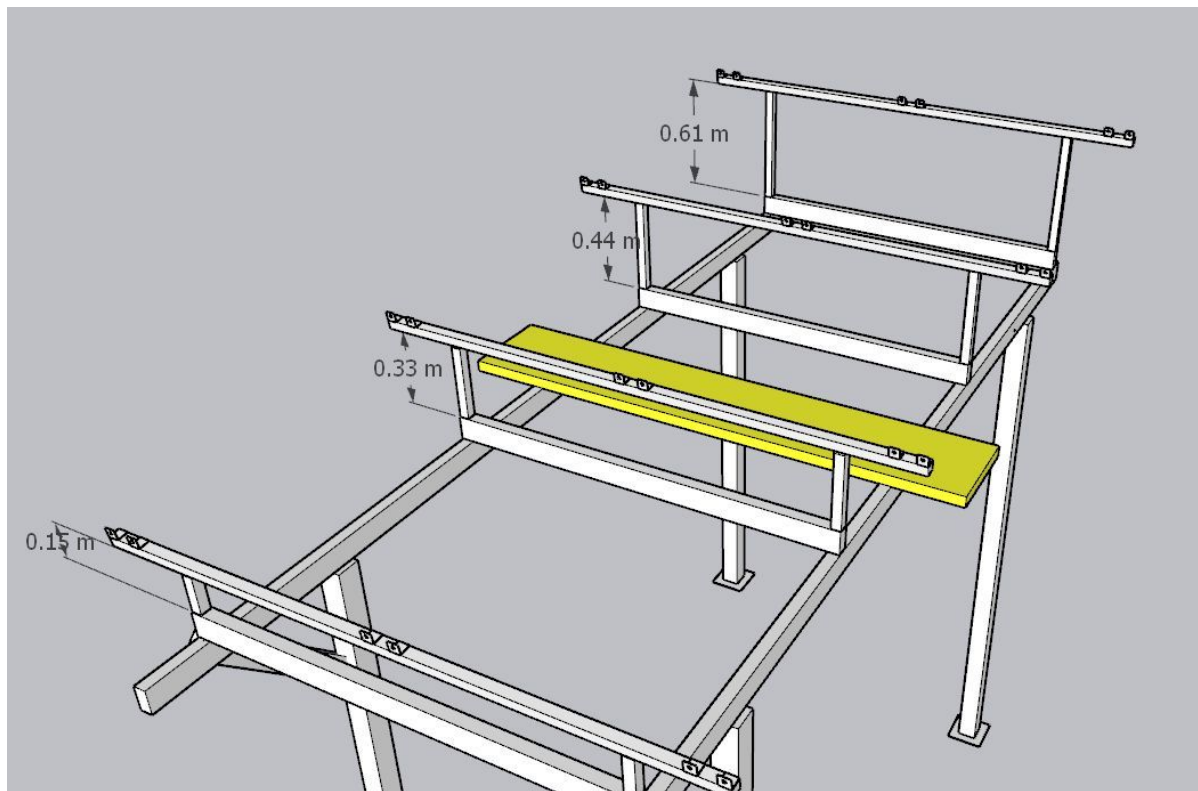

Structure details (3)

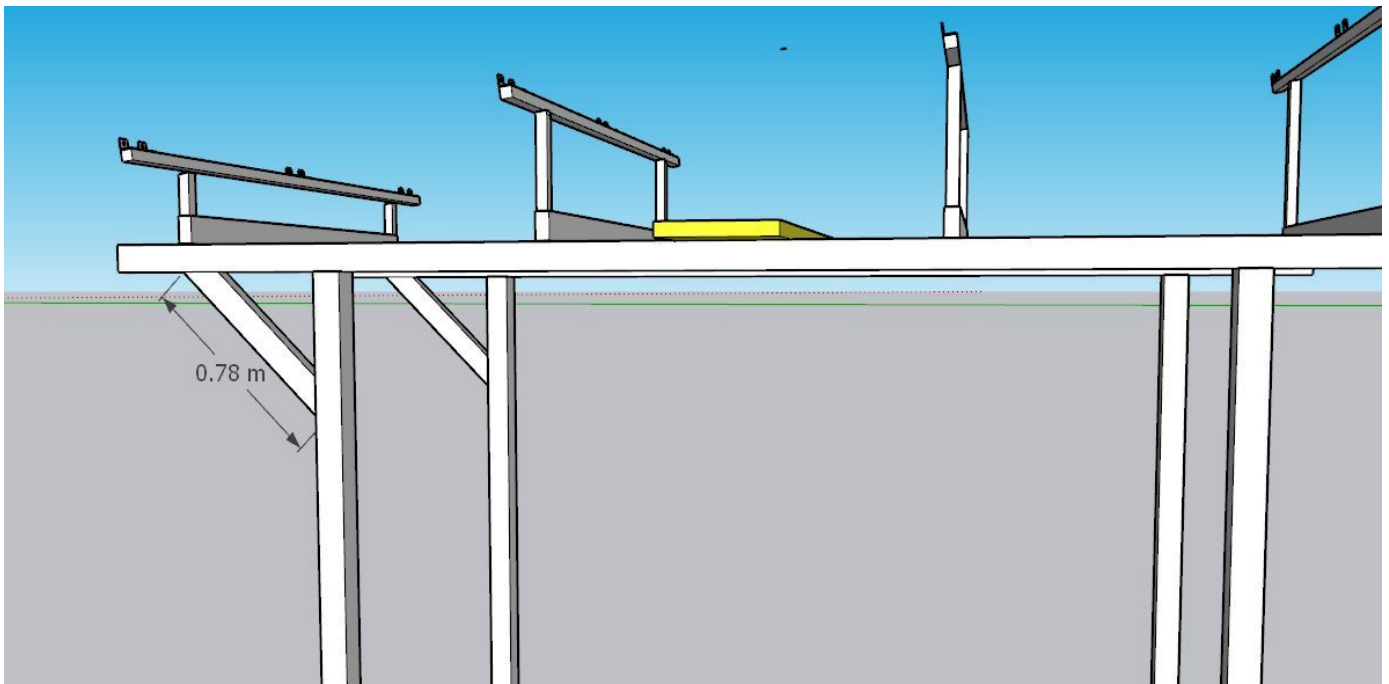


Structure details (4)

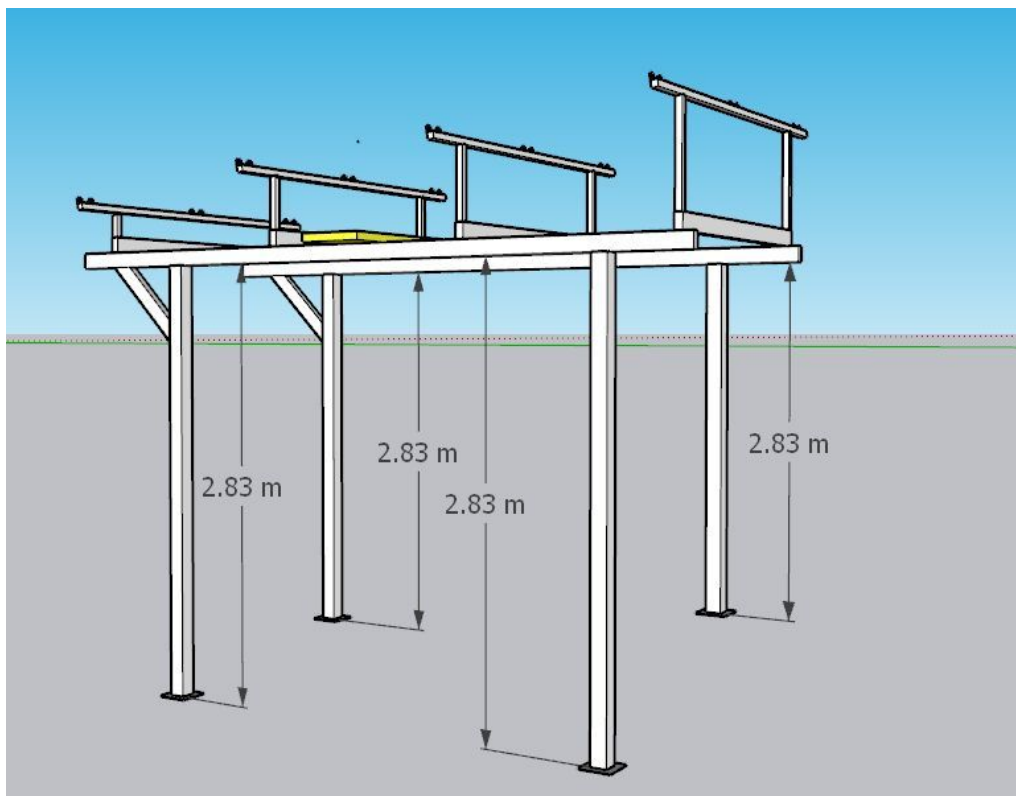


Structure details (5)




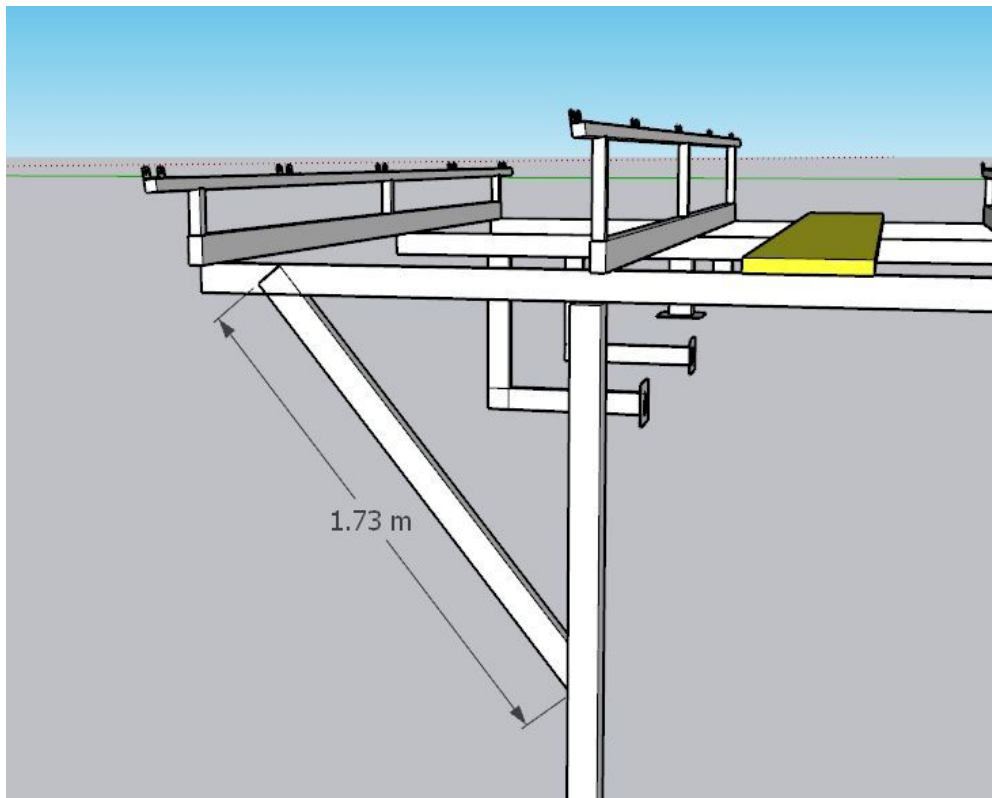


Structure details (6)

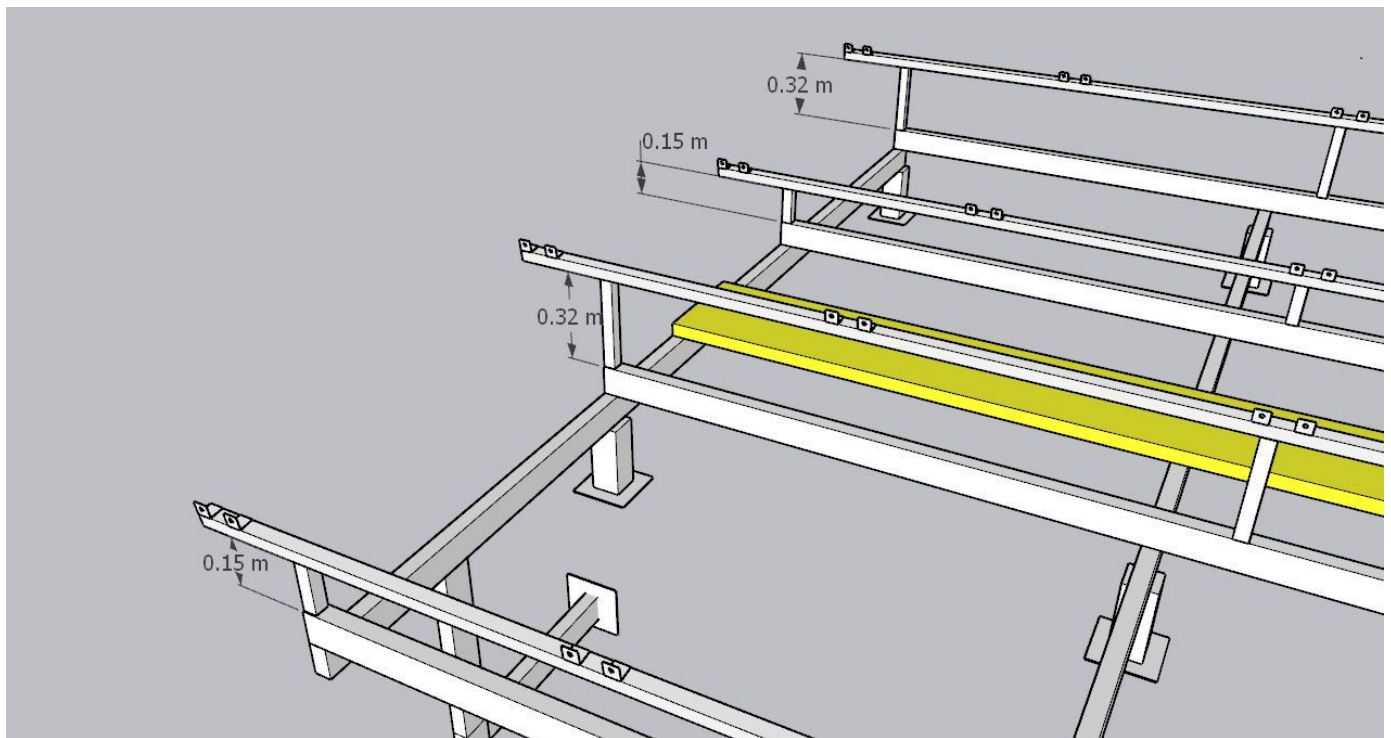


Structure details (7)

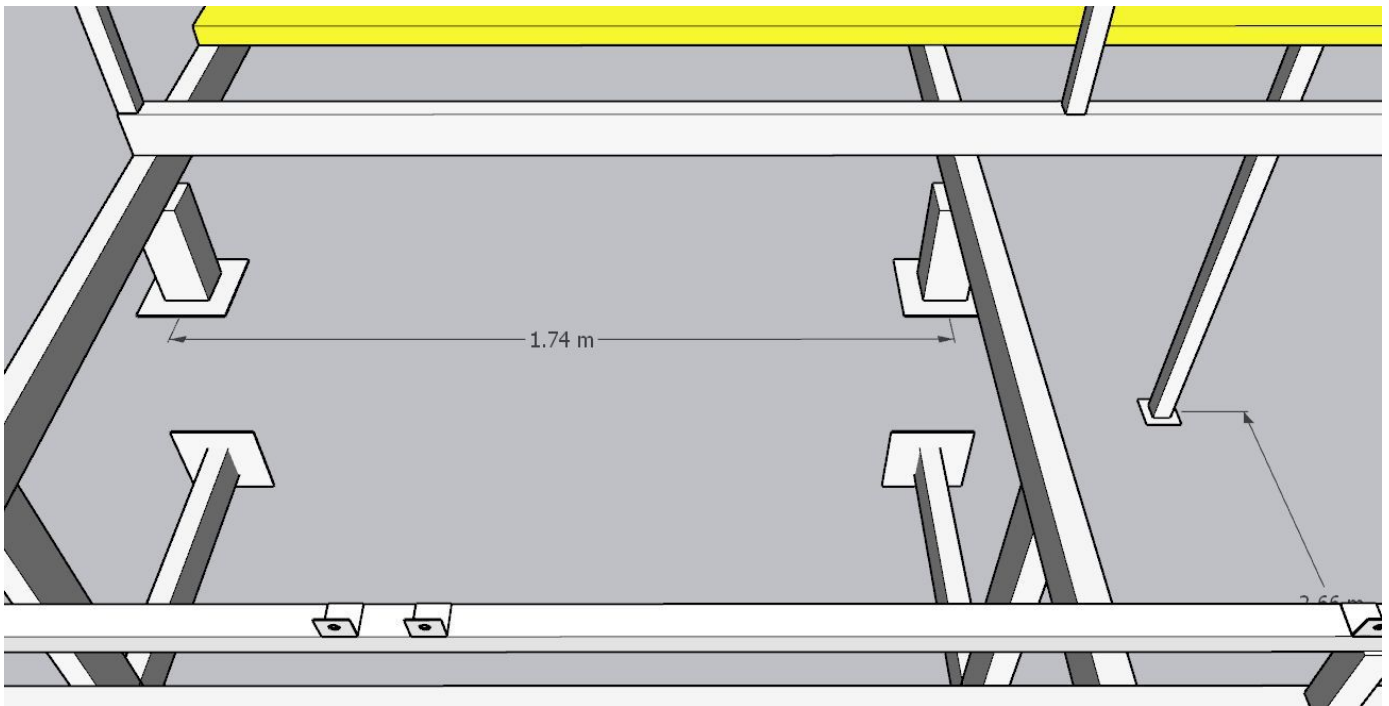


Structure details (8)

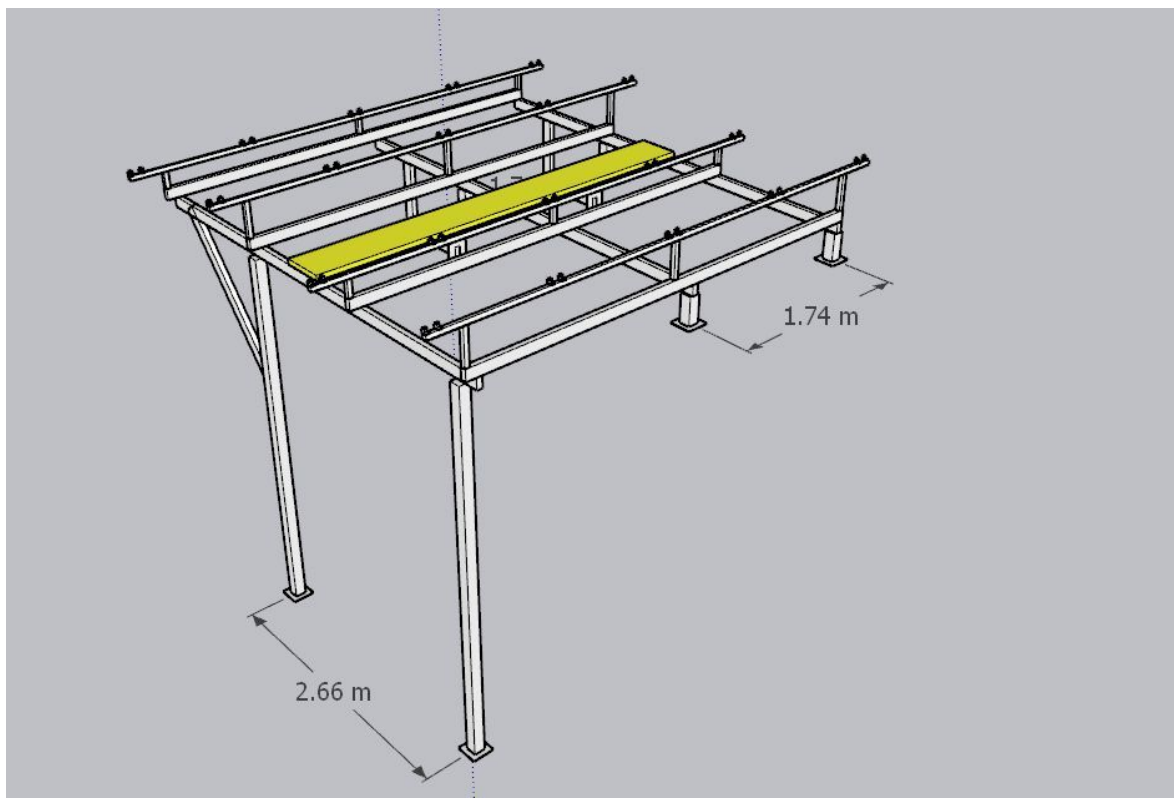

Structure details (9)

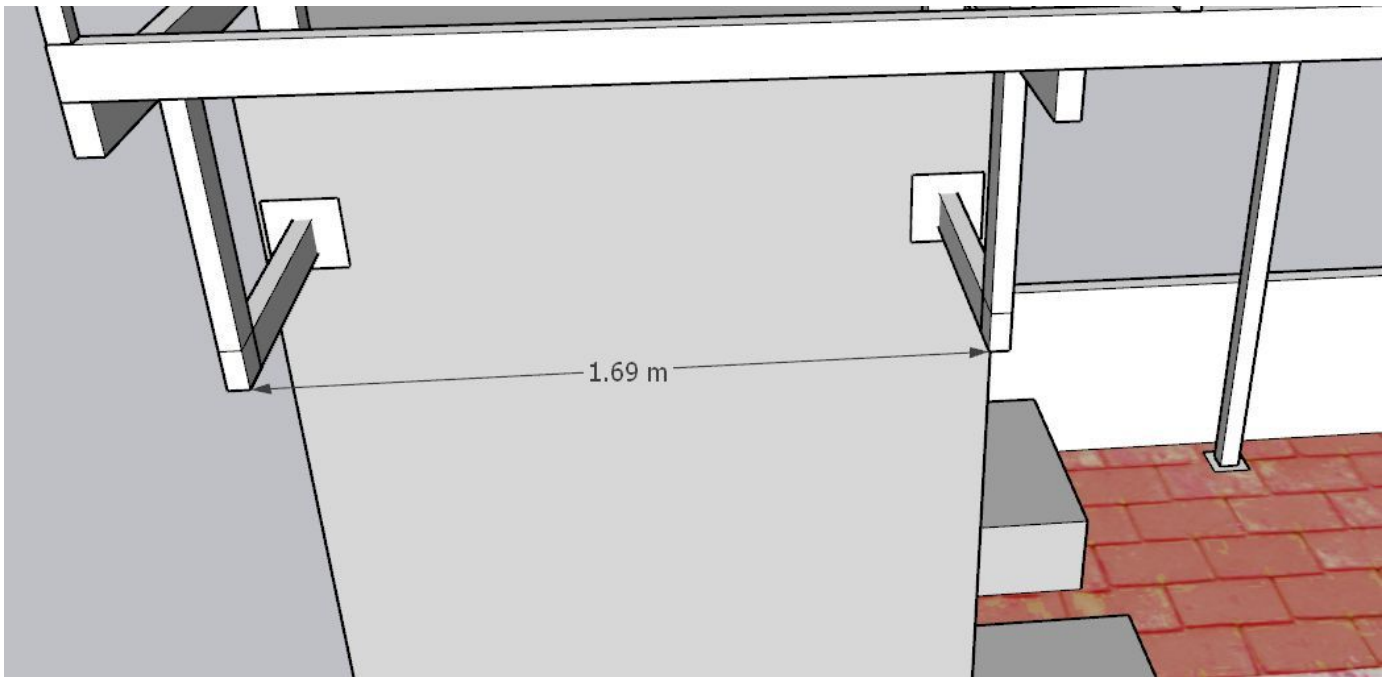


Structure details (10)

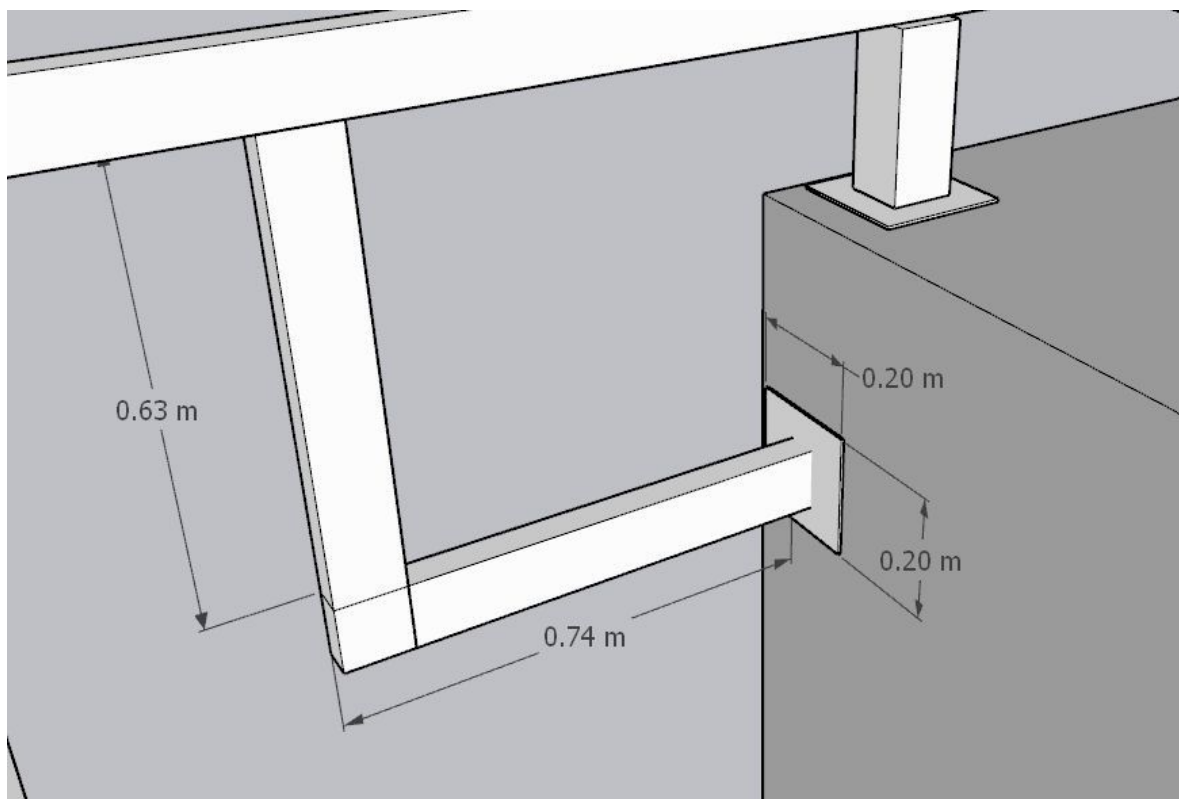


Structure details (11)




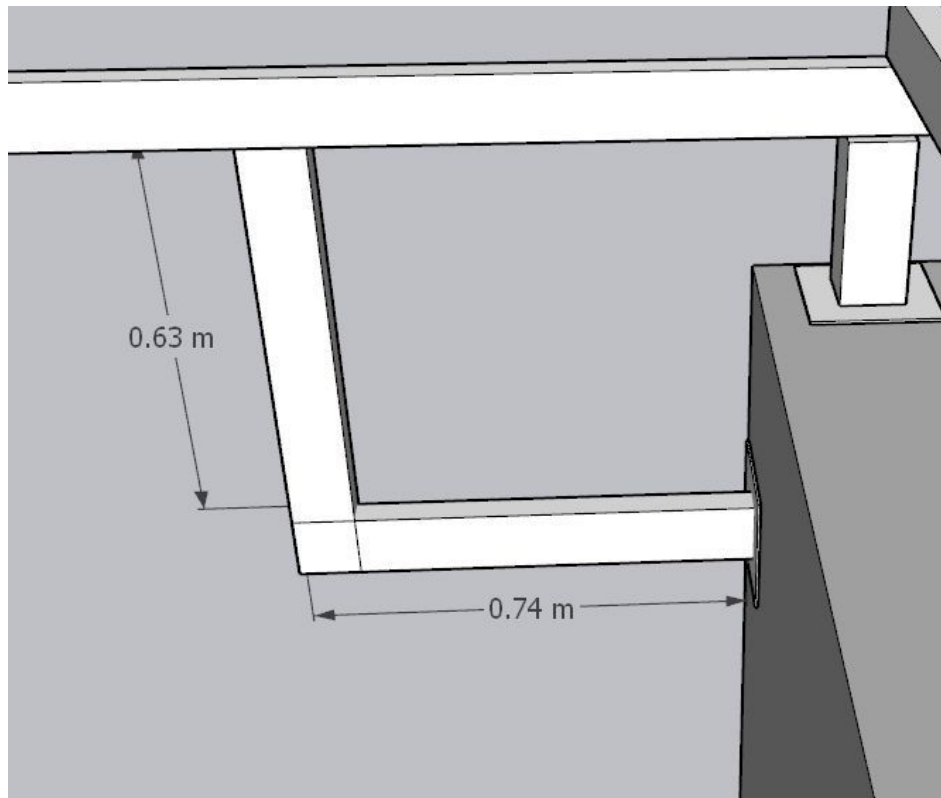


Structure details (12)

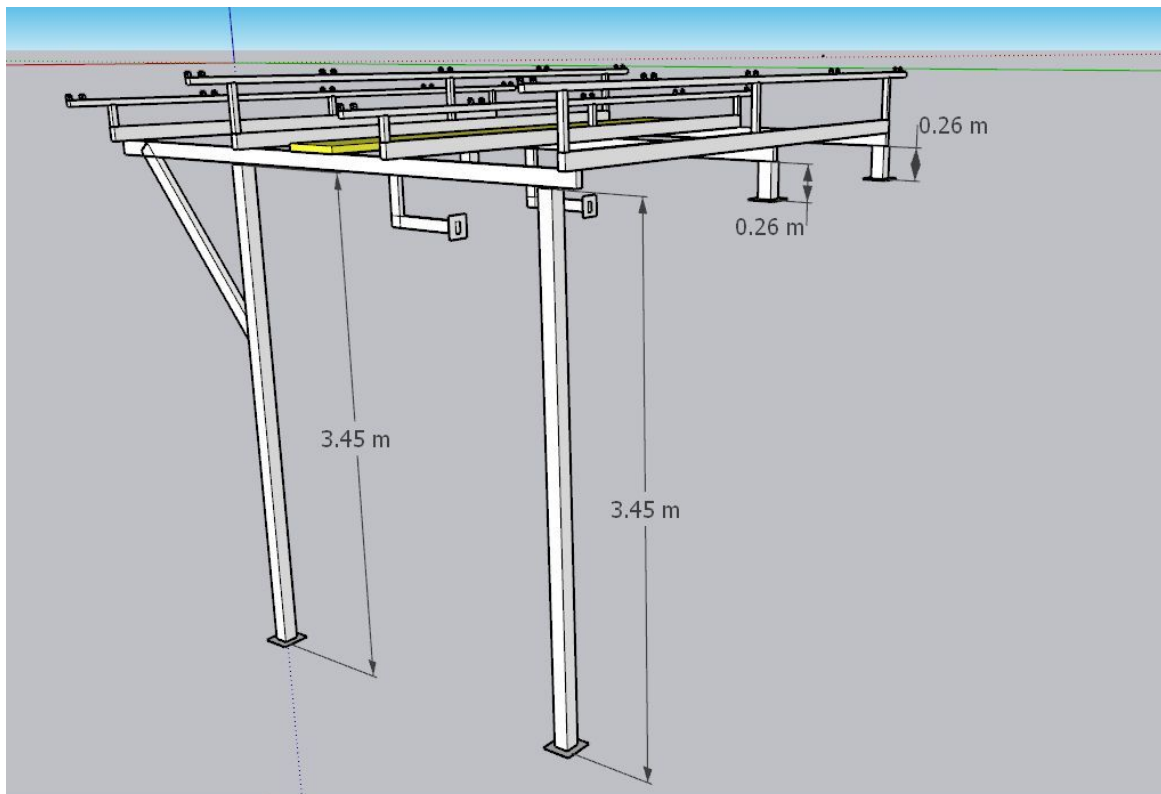


Structure details (13)

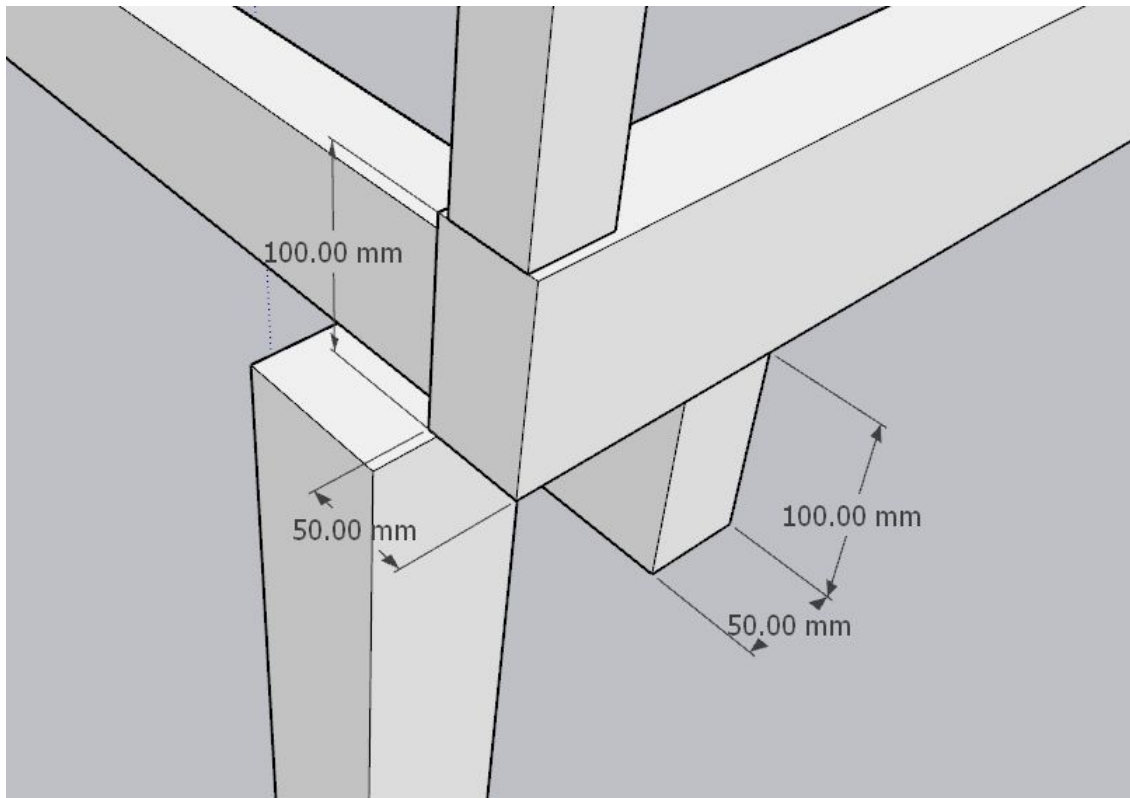


Structure details (14)

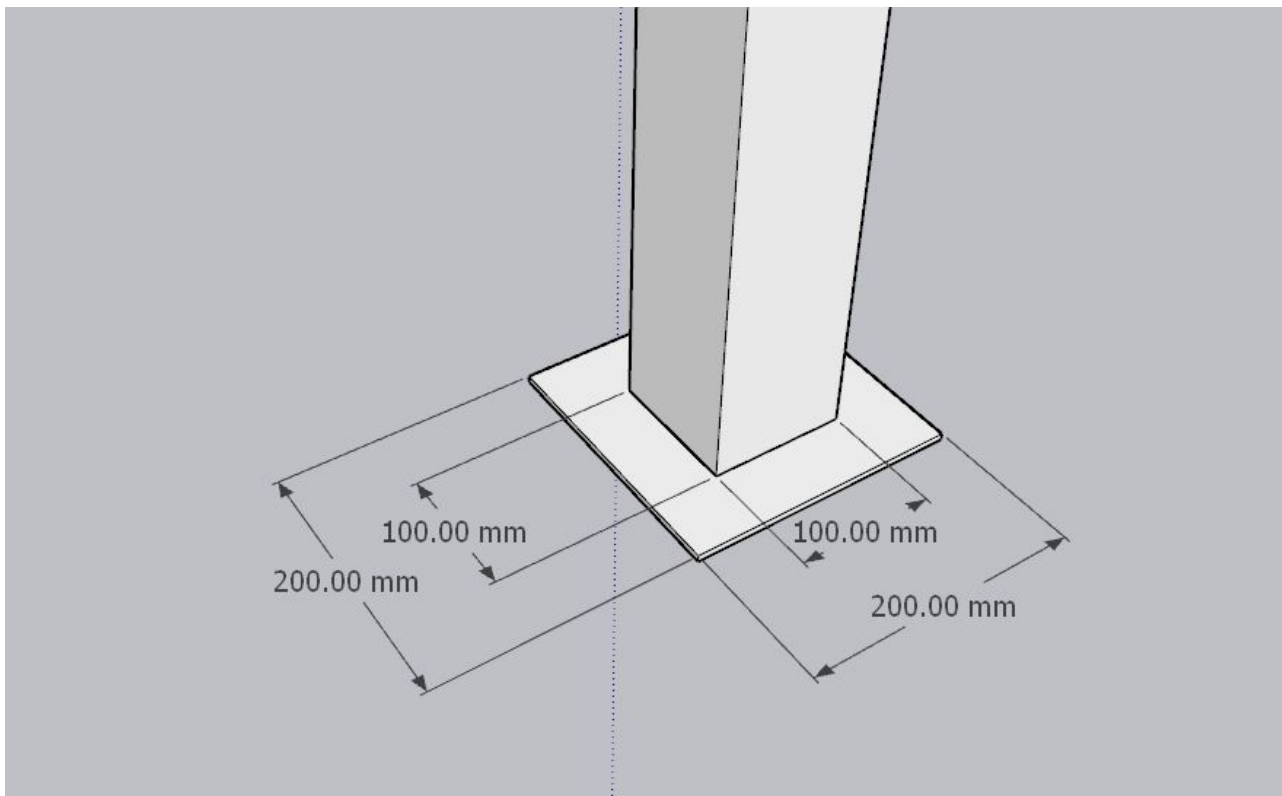


Structure details (15)

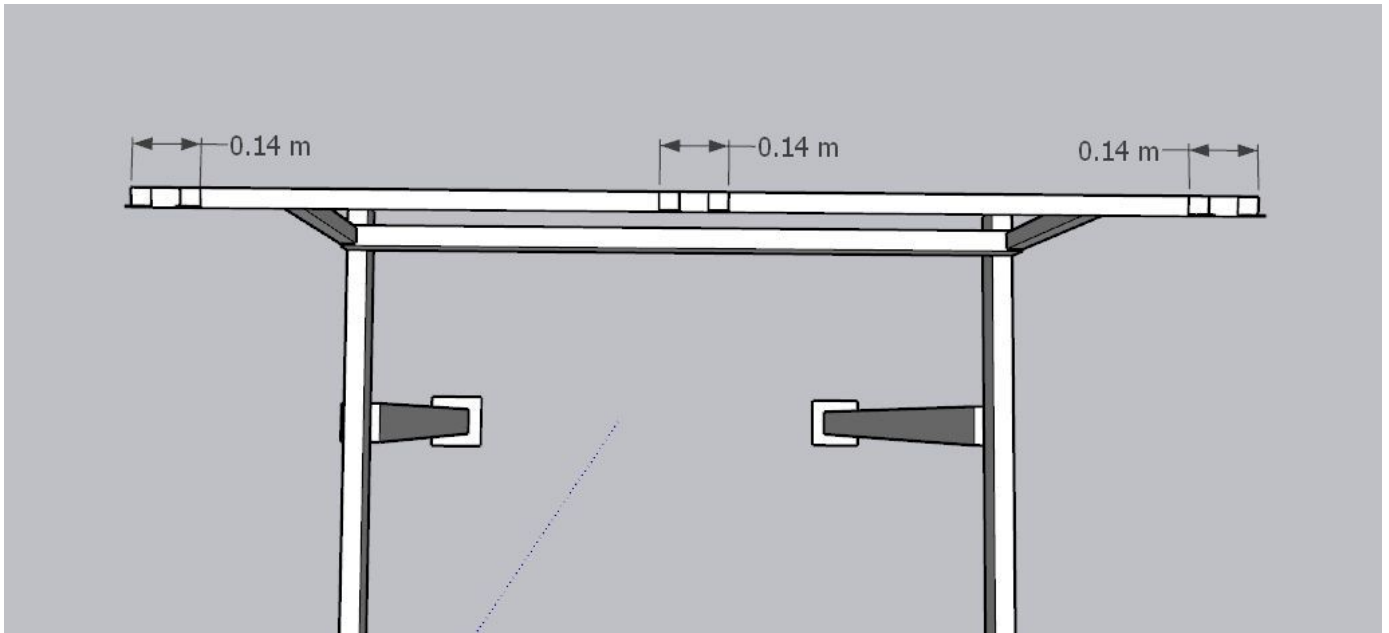


Structure details (16)

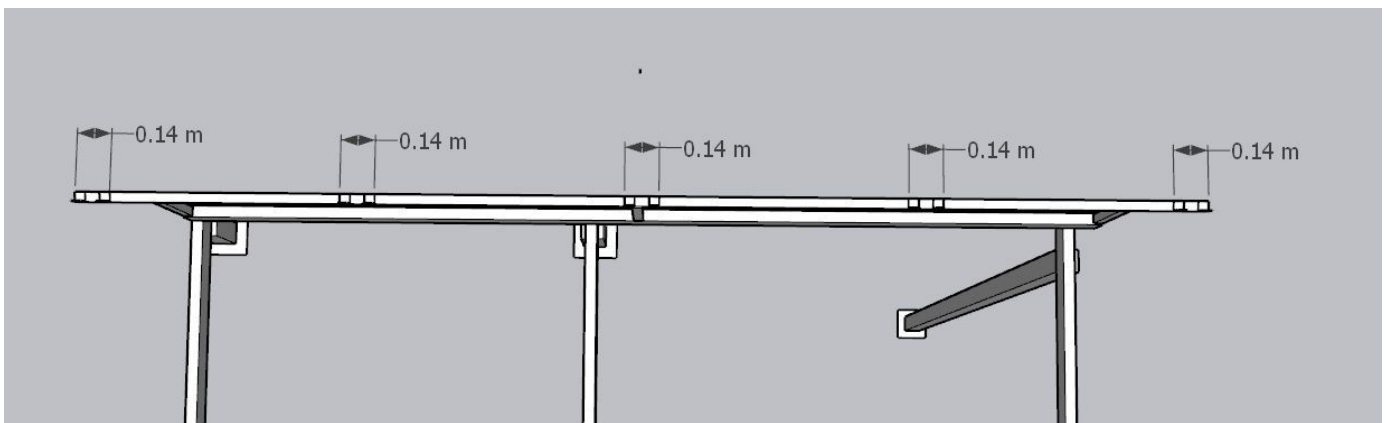

Structure details (17)

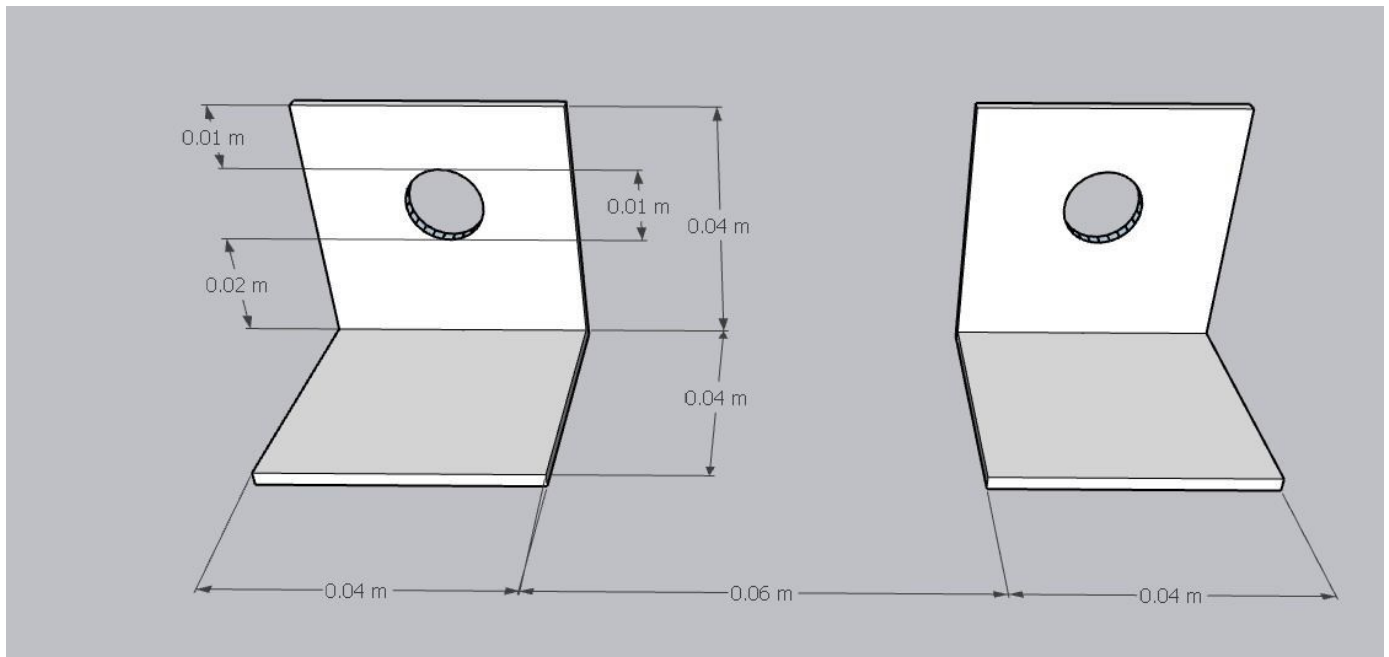

Structure details (18)

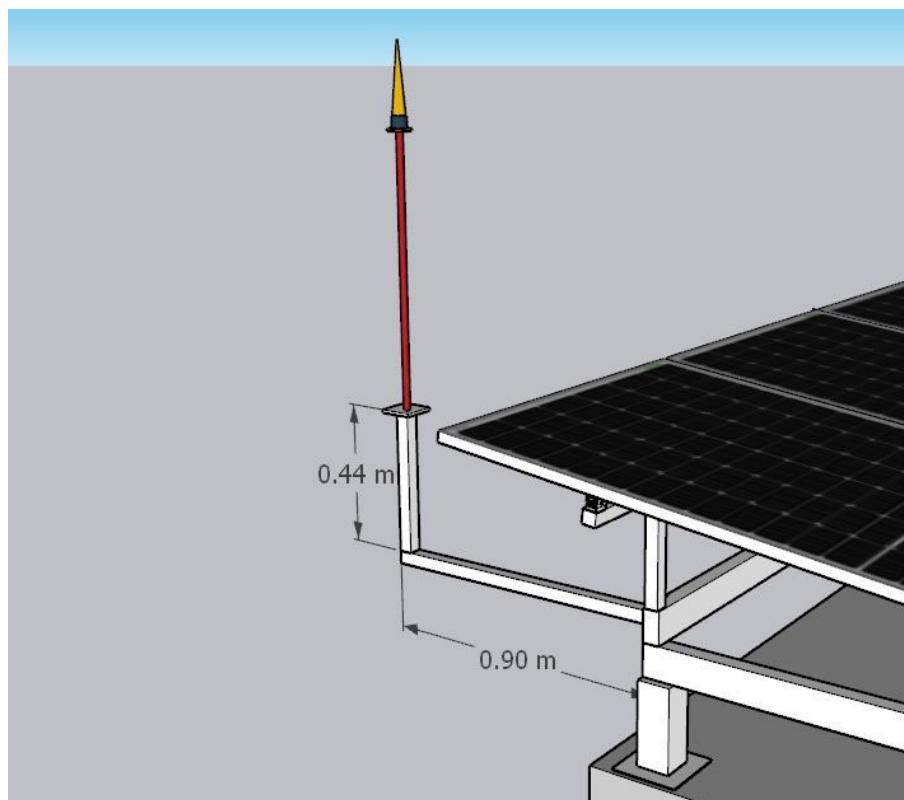


Structure details (19)

## Material Storage





### Proposed PV Area

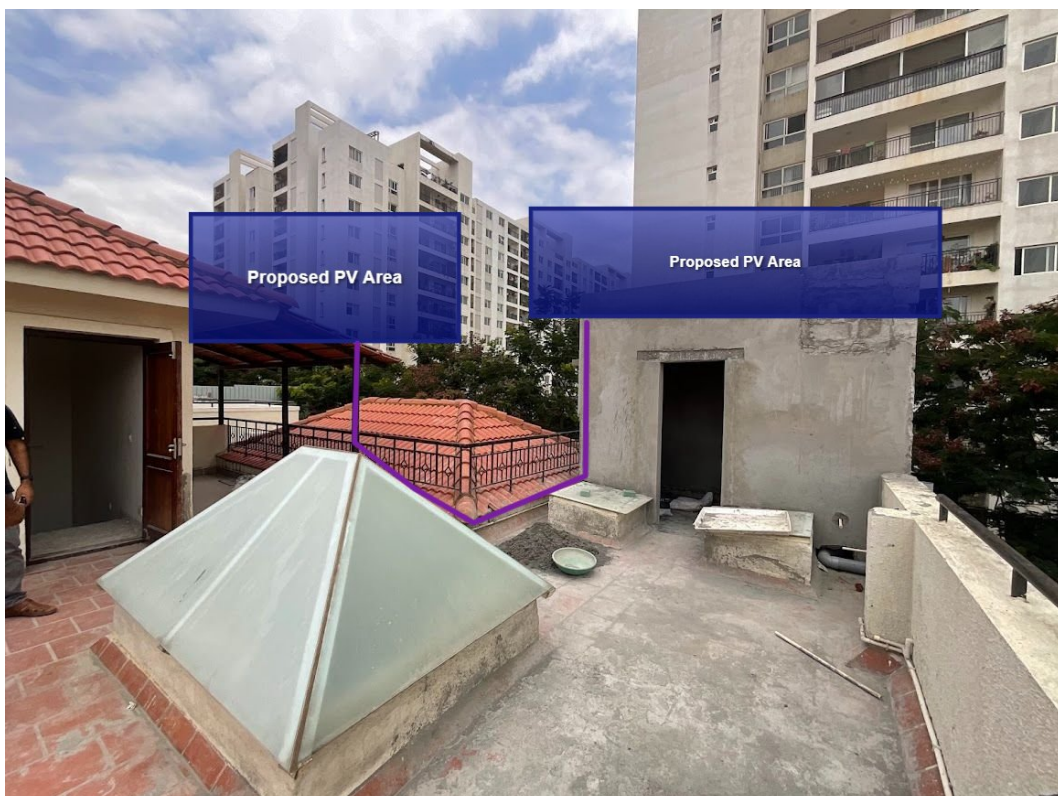



## Cable Routing








## Equipment Location



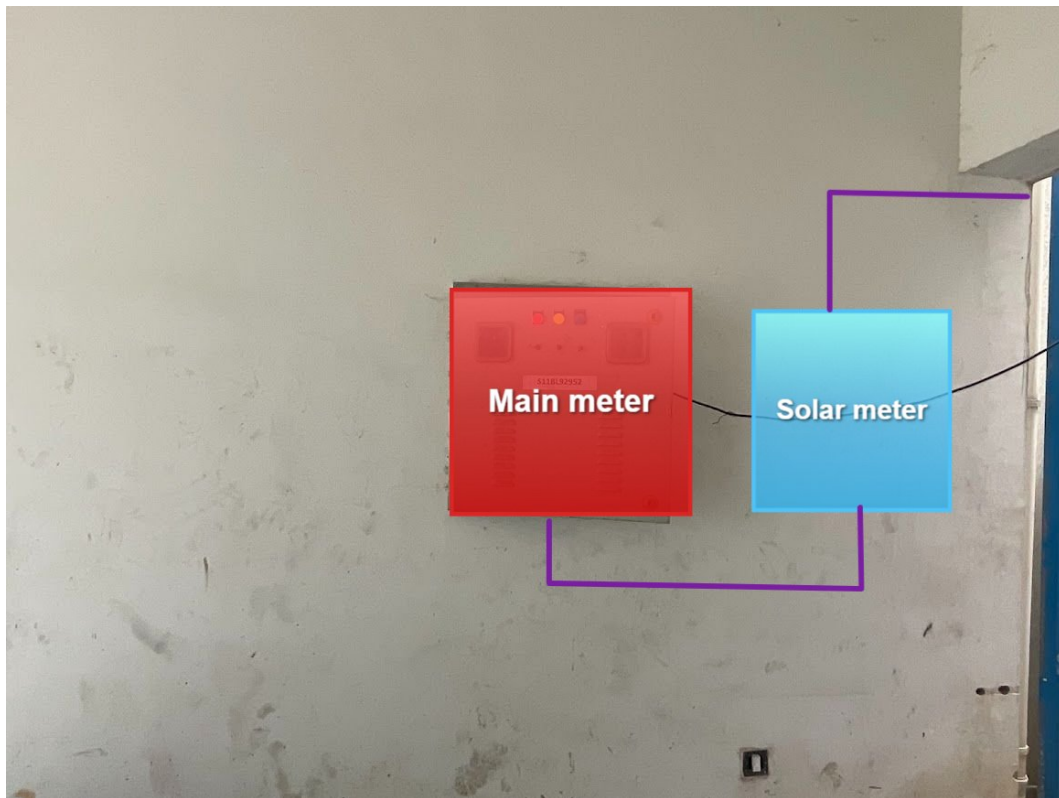

#### Earth Pit Location







## OBSERVATIONS & RECOMMENDATIONS

### EcoSoch Scope

| # | Observation                                                                                                                                                                                                                                                                 |
|---|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1 | As per the customer's suggestion, the routing, cable earthing and also solar meter location have been considered.                                                                                                                                                           |
| 2 | At the time of installation, the tiled roof adjacent to the headroom area must be removed. Additionally, the tiles on the west side of the roof must be removed to facilitate the installation of the posts (legs). Both activities are under the customer's scope of work. |

### Customer Scope

| # | Observation                            |
|---|----------------------------------------|
| 1 | Wi-Fi is under the customer scope      |
| 2 | MS fabrication is under customer scope |

## THANK YOU

Dear Nischal Dutta,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
