

Technical Site Visit Report

Prepared for: Ravi Srinivasa Rao_Embassy Spring Non Subsidy_14.6kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0177
Project ID	619B885C
Project Name	Ravi Srinivasa Rao_Embassy Spring Non Subsidy_14.6kWp_Hybrid
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju
Site Address	Site No 10-29, Embassy Springs, Nagamangala Village, Kundana Hobli, Devanahalli Tq, Bengaluru- 562110
GPS Coordinates	13.21258307132766, 77.61981189854708
Google Maps	https://www.google.com/maps?q=13.212583071327657,77.61981189854708
Visit Date	2026-07-20
Visited By	Charan
Revision	Rev 0

CLIENT INFORMATION

Client Name	Ravi Srinivasa Rao
Contact	98493 45319

PROJECT DETAILS

Solar Rooftop System Type	Off-Grid
System Capacity (kWp)	14.88
Sanction Load (kW)	15
Module Make & Capacity	Premier DCR Bi-facial and 620Wp
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	24
Inverter Type	Hybrid (String)
Inverter Brand	Deye 15 kW 3-Ph
Number of Inverters	1
Battery	Needed
Number of Batteries	3
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	On basement	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, on backside of the building	-
6	Where is the Internet Router located?	Under Construction	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-

#	Question	Answer	Notes
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	HDGI structure
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	Conduit pipes are available for DC cables and Earthing cables
13	What is the height of the building and how many floors does it have?	15m with B+G+2 floors	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	-
2	Is the Meter cubicle photo matching with the previous answer?	N/A	-
3	Has the termination point in the Main meter panel been identified?	N/A	-
4	Is the Termination Point easily visible or sealed?	N/A	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	No	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	No	-



#	Question	Answer	Notes
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1500, width: 1500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 2000, width: 2000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-


PHOTO DOCUMENTATION

Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout

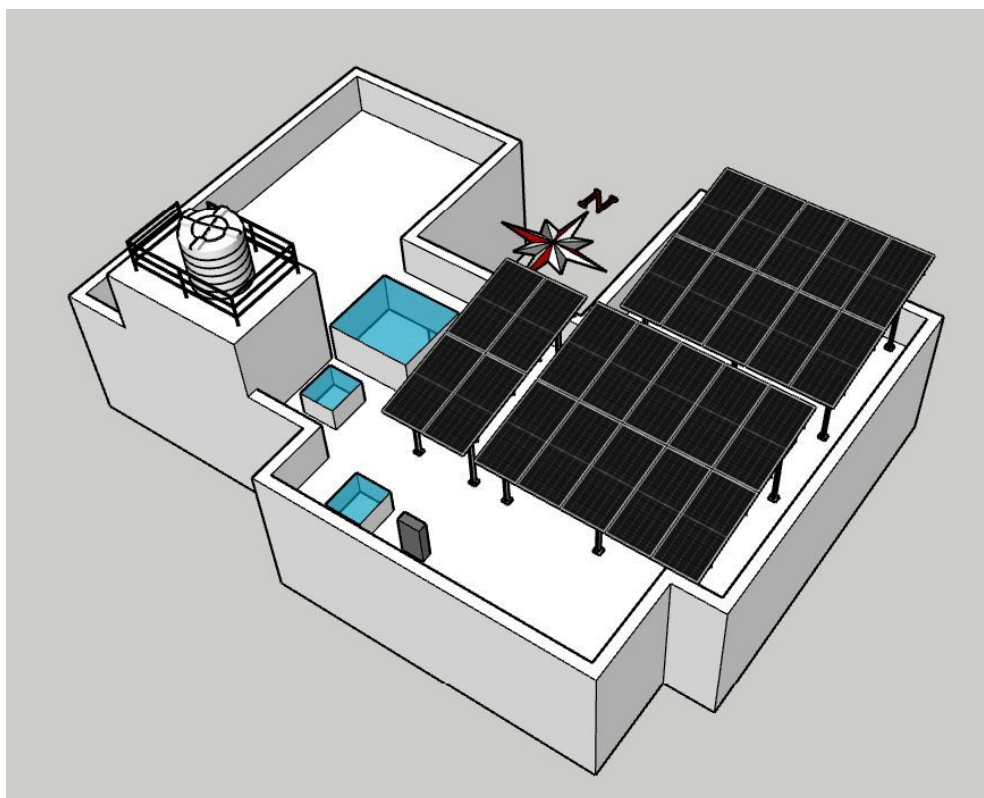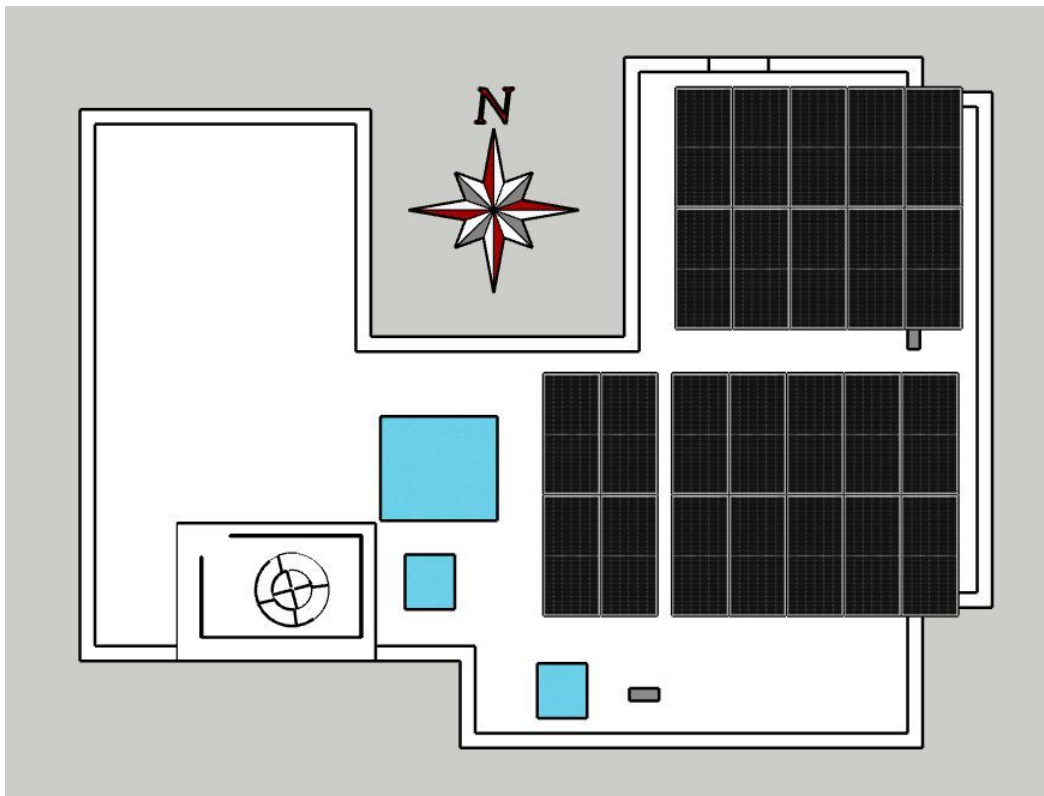


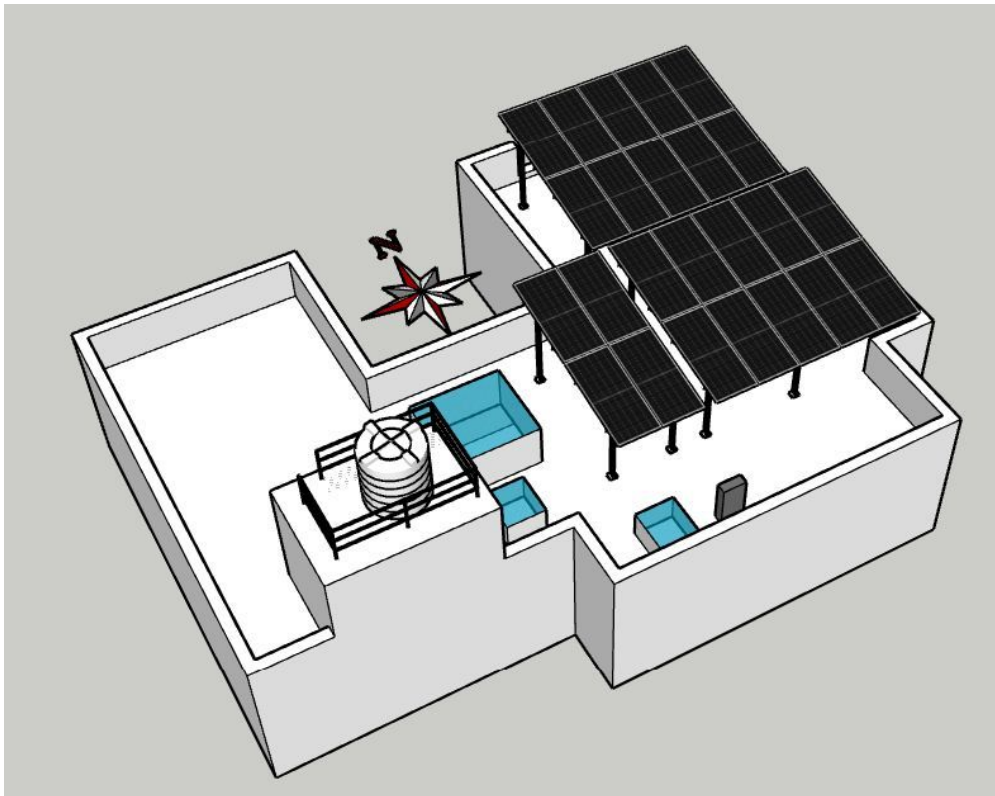

Structure Details

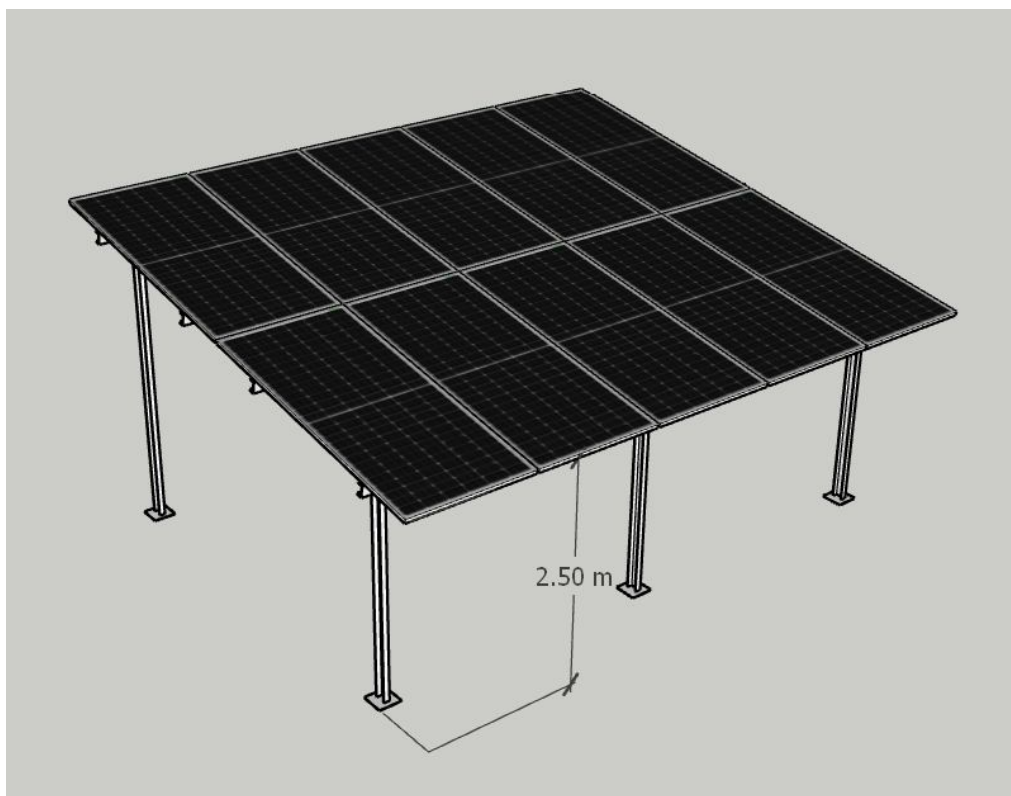

5P2 HDGI structure with 2.5m height - 2No.s

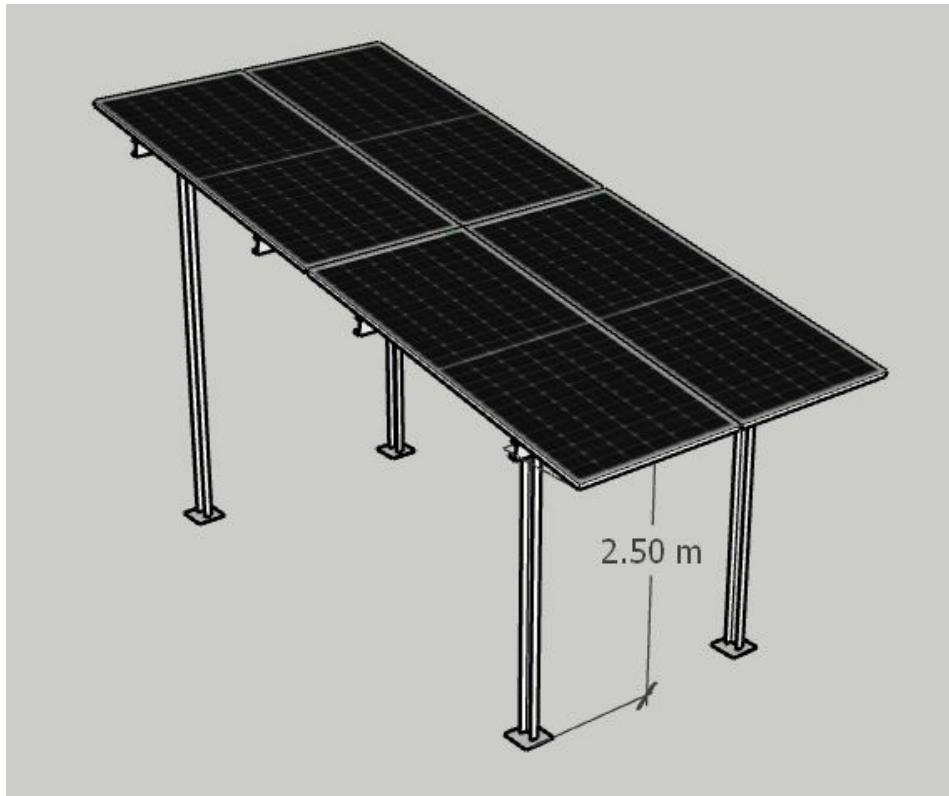

2P2 HDGI structure with 2.5m height - 1No.

Building Exterior



Material Delivery Route



This route (using staircase) will be followed to carry all items.



Staircase Details




Material Storage





Proposed PV Area




Cable Routing

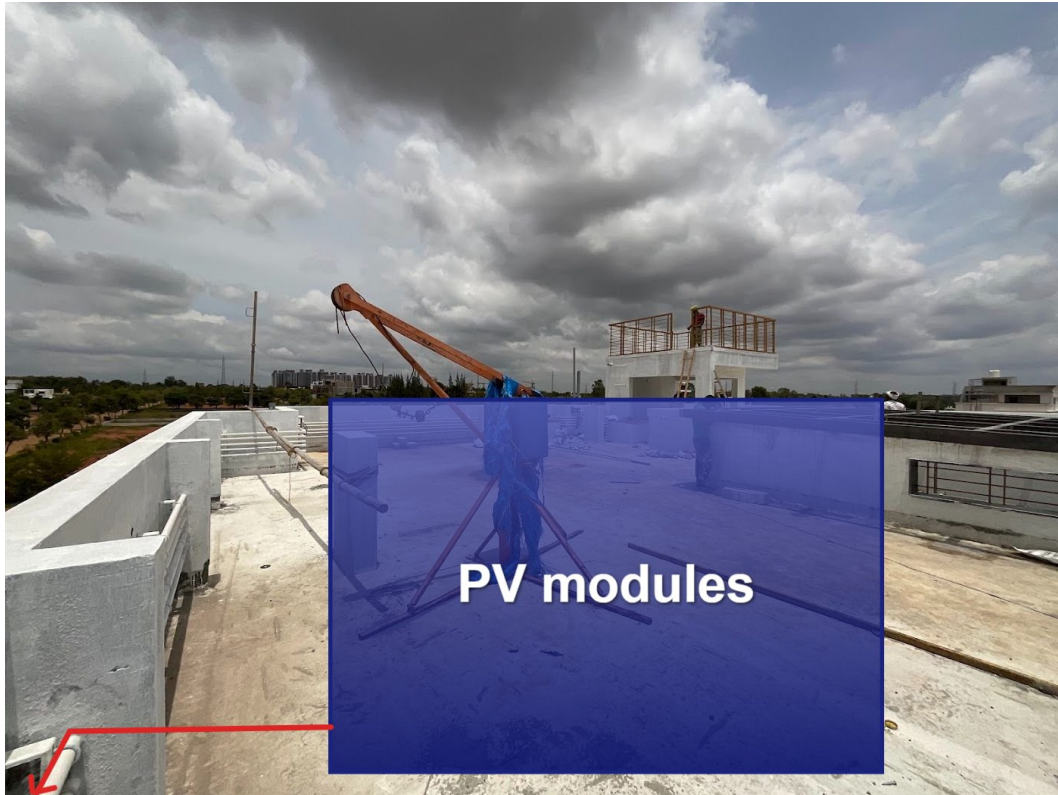


Conduit pipes for the DC cable

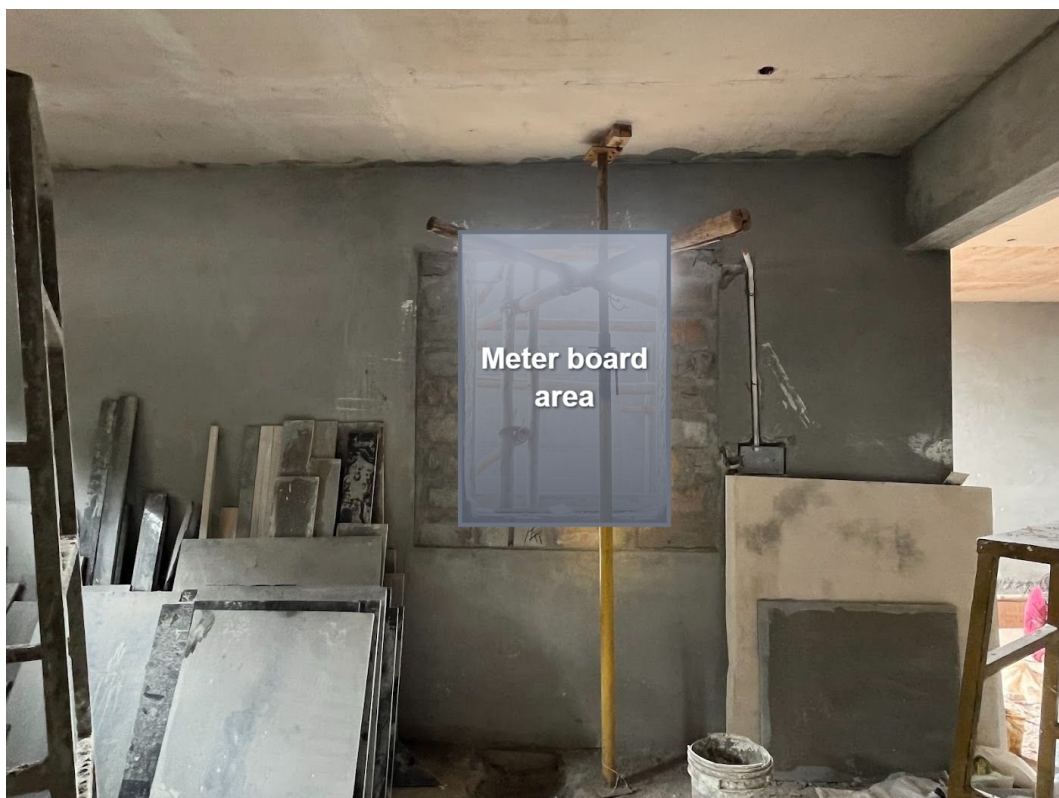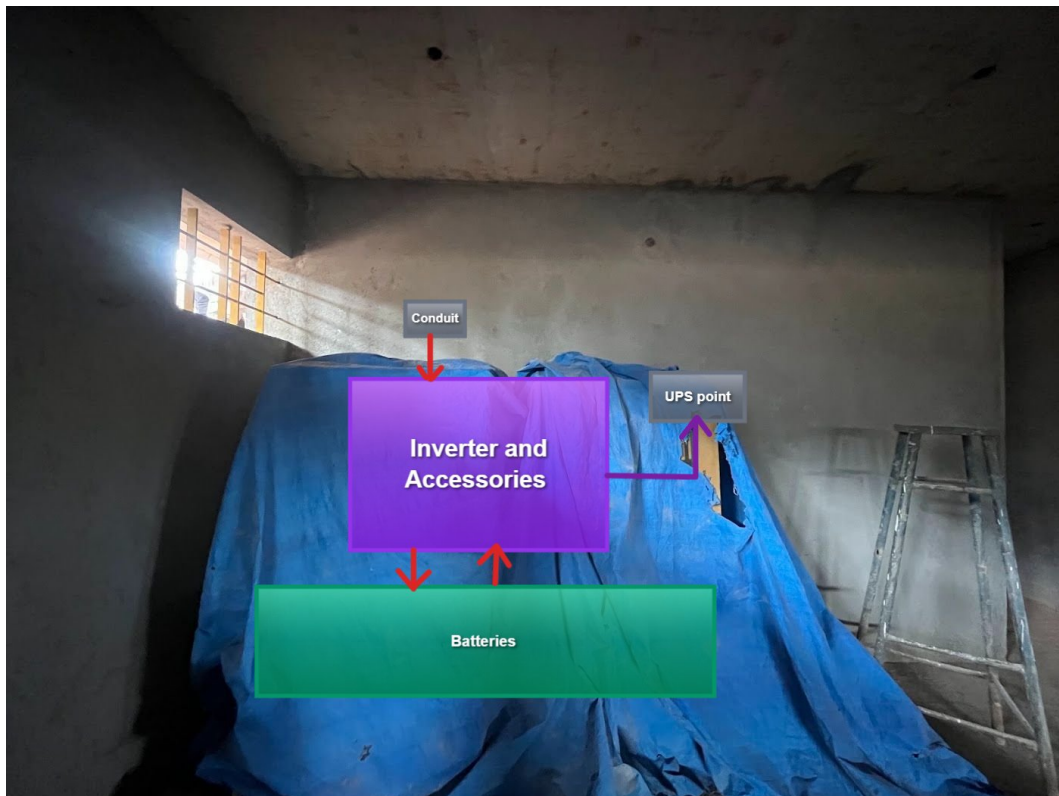

Earthing Routing

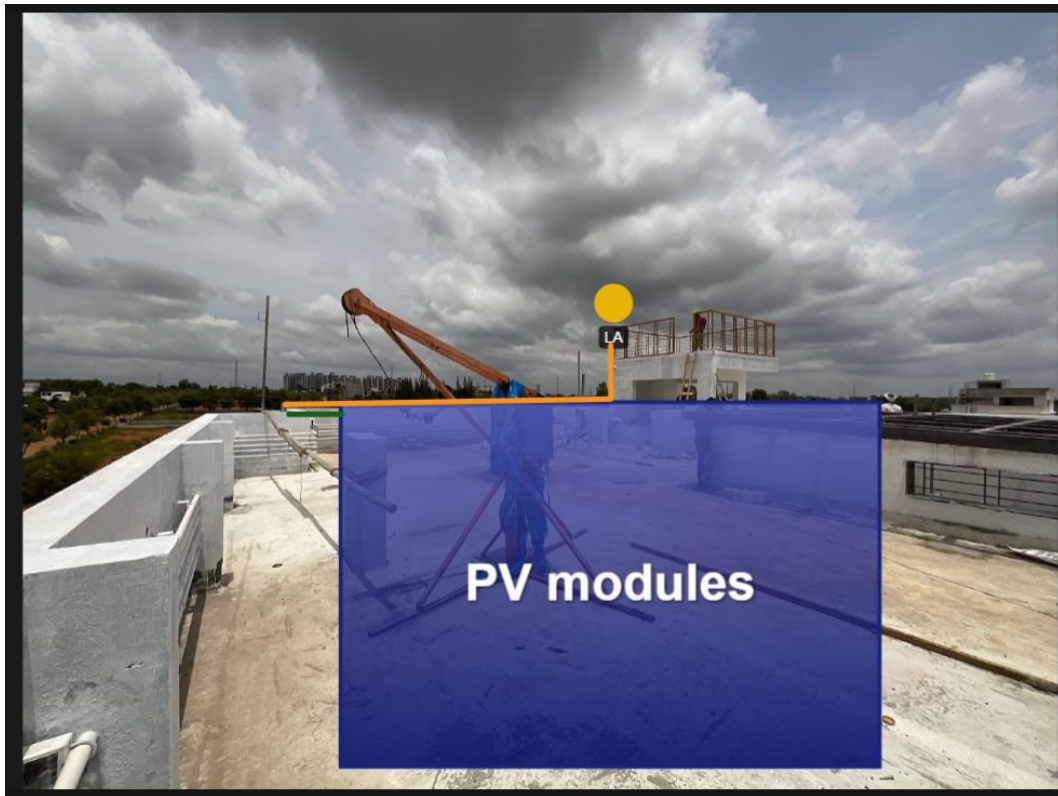



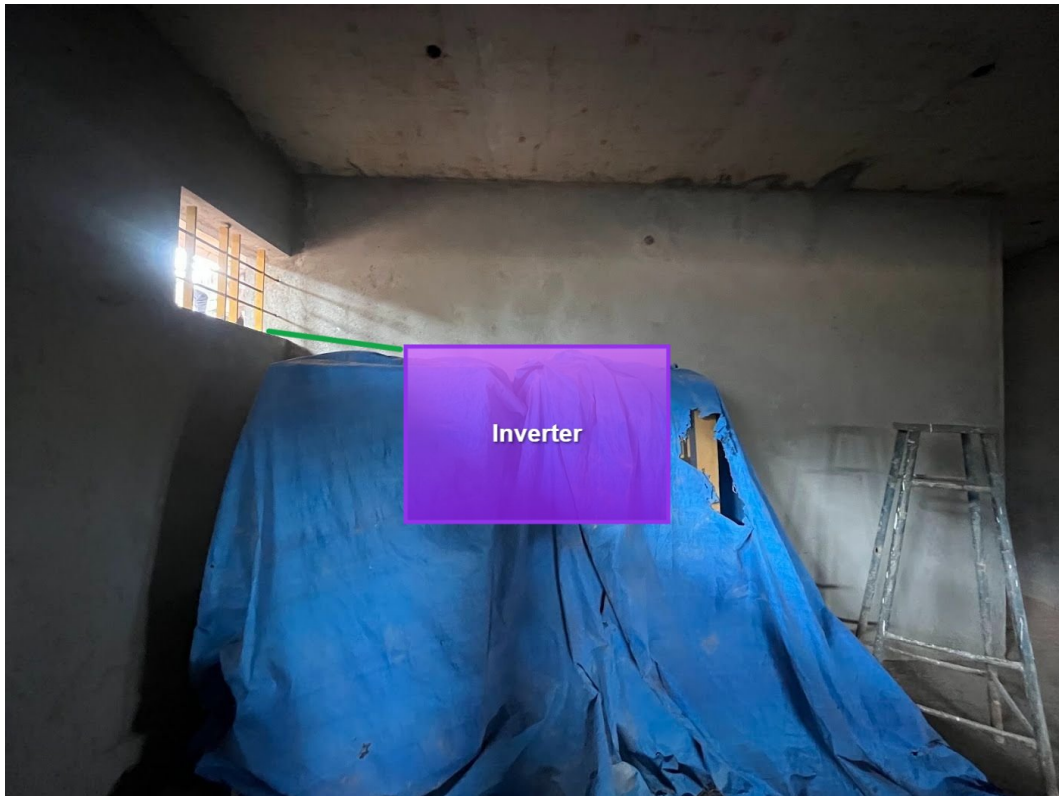

OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to Inverter location.
2	UPS point (In/Out) near Inverter.
3	Conduit pipes for the DC cable and earthing.

THANK YOU

Dear Ravi Srinivasa Rao,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
