

Technical Site Visit Report

Client: Bala Mukund

Site Visit Done By:

Charan P

Contact: 77609 00833

GMap Coordinates: 12.873270104901211,
77.55399600302385

Site Address: 410, 6th B Cross, 7th Main road,
Narayana Nagar 2nd Block, 560062

Site Visit Date : 18/06/2025

www.ecosoch.com

System Type	On-Grid
System capacity	3.3 kWp
Module Make and capacity	Novasys Mono DCR Bi-facial and 550Wp
Number of panels	06
Inverter	Micro Inverter
Inverter Brand	Enphase
Number of inverters	06
Battery	IQ 5P LFP Battery – 1no.
Mounting Structure	Mini rails with MS Elevated structure

What type of roof is present at the site? (e.g., RCC Flat Roof, Corrugated Sheet Roof, Tiled Roof, etc.)

Ans: RCC Flat Roof

Are there any obstructions on the roof that could affect the solar installation? (e.g., Water tanks, HVAC units, Skylights, Chimney, Dish Antenna, etc). If yes, provide details.

Ans: No

What is the angle of the panels? Mention in degrees.

Ans: 7 degrees

In case of sloped roof (like Tiled, RCC sloped, etc.), what is the slope angle of the roof? Mention in degrees.

Ans: Not applicable

On how many roofs at the site are we installing solar?

Ans: 01

If it is a Tiled roof, what is underneath the tiles? Is it RCC, MS Rafter, Wooden Rafter, etc.? Provide details.

Ans: Not applicable

If it is a Tiled roof with MS or Wooden rafters underneath, is it a Single-tiled or Double-tiled roof? Provide details.

Ans: Not applicable

What type of mounting structure is planned (e.g., Ballast, Elevated, Mini-rails, Long rails with L clamps)? Provide details.

Ans: MS Elevated structure

What is the orientation of the solar panels? (e.g., North, South, East, West). Provide details in case of multiple orientations.

Ans: South orientation

How can the roof be accessed? (e.g., Ladder, Staircase). Provide details.

Ans: Staircase

Is the building currently under construction?

Ans: Yes

In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?

Ans: Yes, available only for the AC cable.

What is the height of the building (in metres), and how many floors does it have? Mention like (G+1, G+2, etc.). Note that headroom is not a floor. So if there are 3 floors and a headroom, then mention as G+2+Headroom

Ans: 11m and G+2

Is the site photo matching with the previous answer?

Ans: Yes

Is there an overhead HT line passing within a 10-meter radius of the site?

Ans: No

Site visit Inspection Checklist – General

Can the delivery van/truck reach the material unloading point?

Ans: Yes

Are there any obstacles at the site that could hinder material lifting? Provide details.

Ans: No

Where will the Inverter, DCDB, ACDB, Battery, etc. be located? Provide details for the applicable components.

Ans: Not applicable

Is a canopy required for protecting the Inverters/ACDB/DCDB? If so, is it under customer scope? Provide images and details.

Ans: No

Should the Inverters/ACDB/DCDB be installed on a metal grill? If so, are slotted C channels required? Provide images and details.

Ans: Not applicable

Did you discuss the location of the earth pits with the customer? (e.g., Basement, Outside Garden Area)

Ans: Yes, at ground floor

Where is the Internet Router located?

Ans: Not yet installed because it is under construction.

What's the Wi-Fi strength of the router near to the String inverter/Envoy? How many signal bars?

Ans: Not applicable

Did you pin the site location in your WhatsApp when you were at the site?

Ans: Yes

What type of energy meter is currently installed?

- Is it Single or Three Phase?
- Is it Digital or Analog?
- In case of 3-phase meter, Is it LT CT Meter or Normal Three Phase?

Ans: Not yet installed because it is under construction.

Is the Meter cubicle photo matching with the previous answer?

Ans: No

Has the termination point in the Main meter panel been identified? Provide details.

Ans: No because meter is not yet installed.

Is the Termination Point easily visible or sealed?

Ans: No because meter is not yet installed.

Is a Lightning Arrestor (LA) already available at the site?

Ans: No

Is there an existing AC earth pit available? If so, what's its age and condition?

Ans: No

Is space available for CT within Energy meter panel?

Ans: Not applicable

In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?

Ans: No

Provide details of the existing CT ratings (if applicable).

Ans: Not applicable

In Main meter panel, is empty space available for solar meter?

Ans: The main meter panel is not yet installed, but a bigger one is planned, which will also include a solar meter and its accessories.

In Main meter panel, is empty space available to house the Enphase accessories (in case of an Enphase system) or the ACDB components (in case of a string inverter system)?

Ans: Not applicable

Is there space available to dig DC, AC and LA earth pits?

Ans: Yes

In case of elevated structures, is an LA extension provided at the far end (if there is no other higher point to install the LA)?

Ans: No

Are there any challenges with respect to Installation and Maintenance activities (for Solar Care) like dangerous drop, slope too steep, safety of installation personnel, unavailability of anchor points, etc.?

Ans: No

Are there any safety risks associated with accessing the roof for installation (like Monkey ladder, more than 20° slope, etc.)?

Ans: No

Is space present in rooftop to store the panels in a horizontally sleeping or vertically leaning against the wall position? Need details.

Ans: Panels can be stored in a horizontal position.

In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin, and rafter & purlin square box dimension

Ans: Not applicable

Is ventilation available in the battery location?

Ans: Not applicable

Should the Inverters/ACDB/DCDB be installed on a metal grill? If so, are slotted C channels required? Provide images and details.

Ans: Not applicable

Provide the dimensions for solar meter cubicle placement (Length and width of the wall)

Ans: 3m and 2m

Provide the dimension for earth pits location (Length and width of the available space)

Ans: 5m and 1m

Is LAN cable under customer scope?

Ans: No

Is there any shadow that affects the solar installation?

Ans: No

MATERIAL DELIVERY ROUTE (Photos)






This route (using staircase) will be followed to carry all items.


MATERIAL STORAGE AND DELIVERY (Photos)





ECO SOCH
Sunny Living


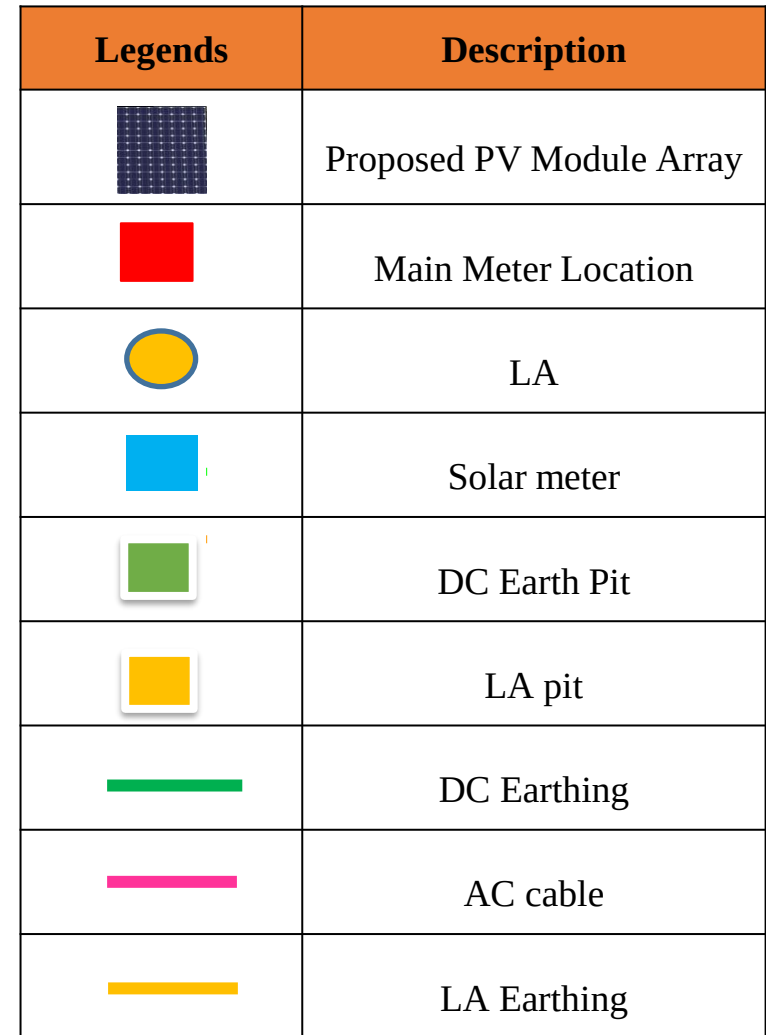


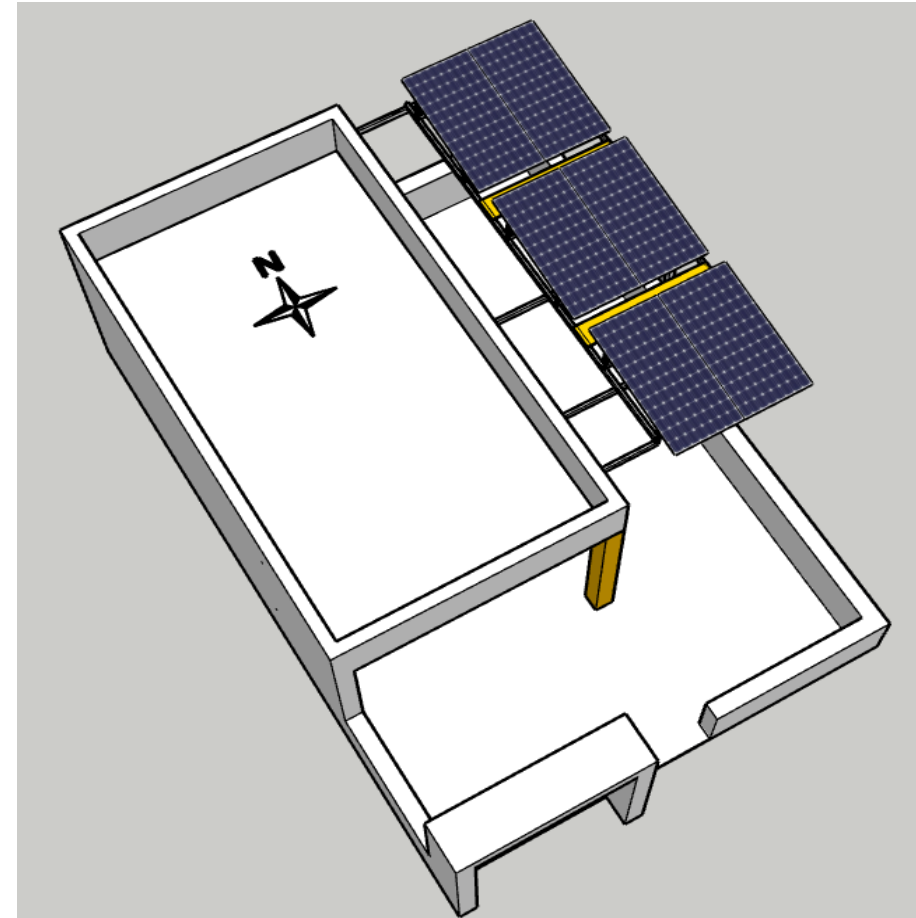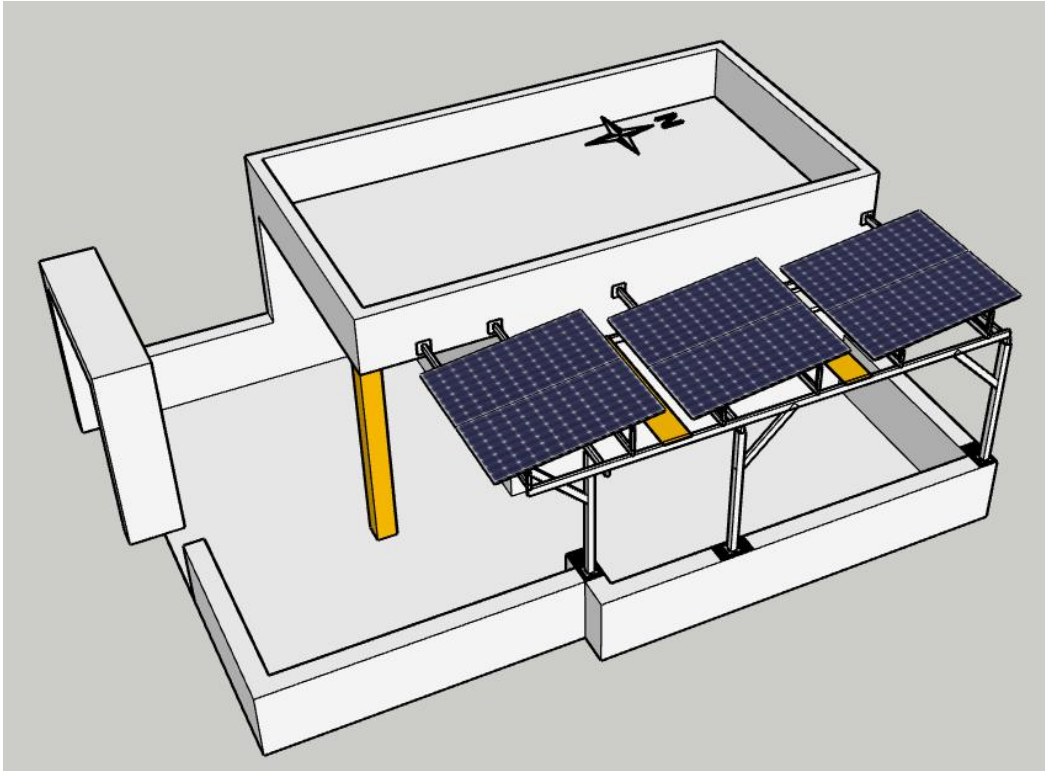




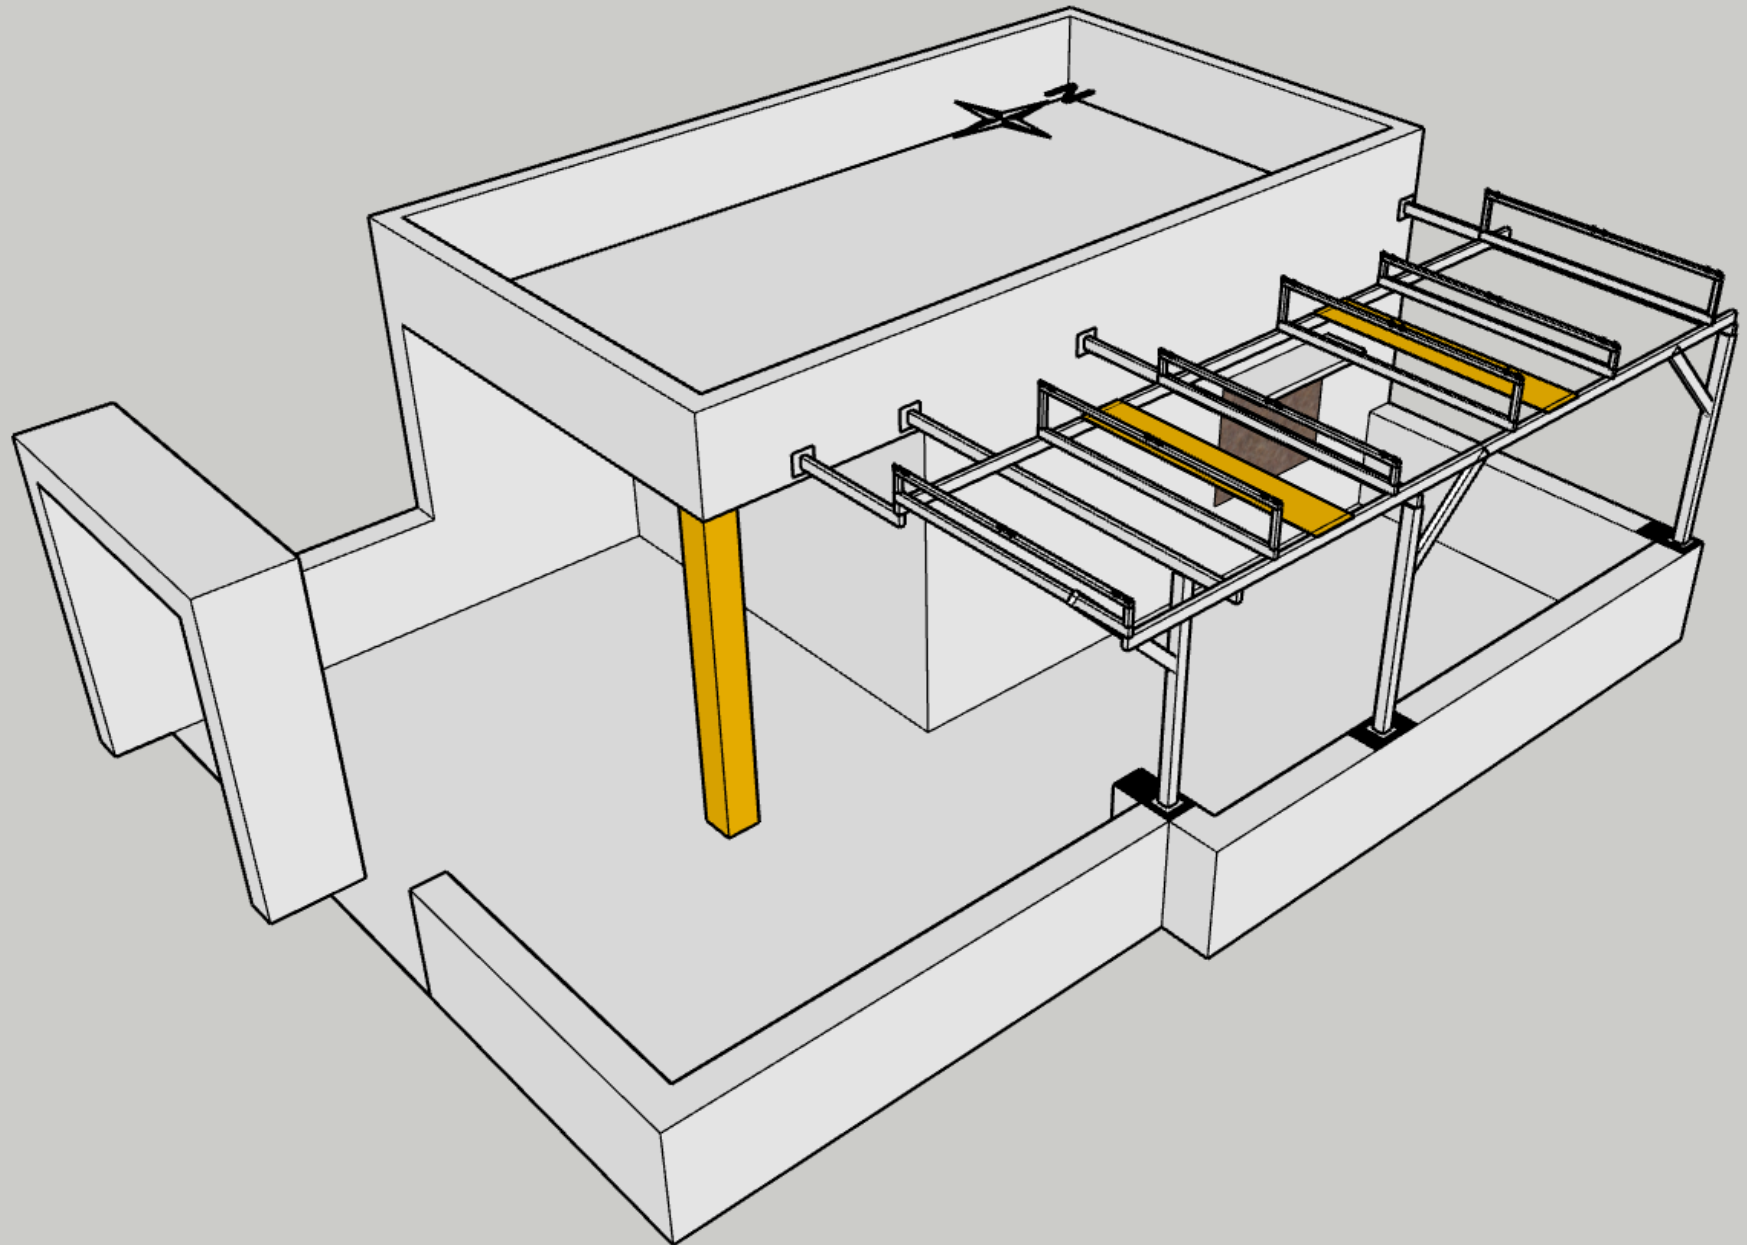


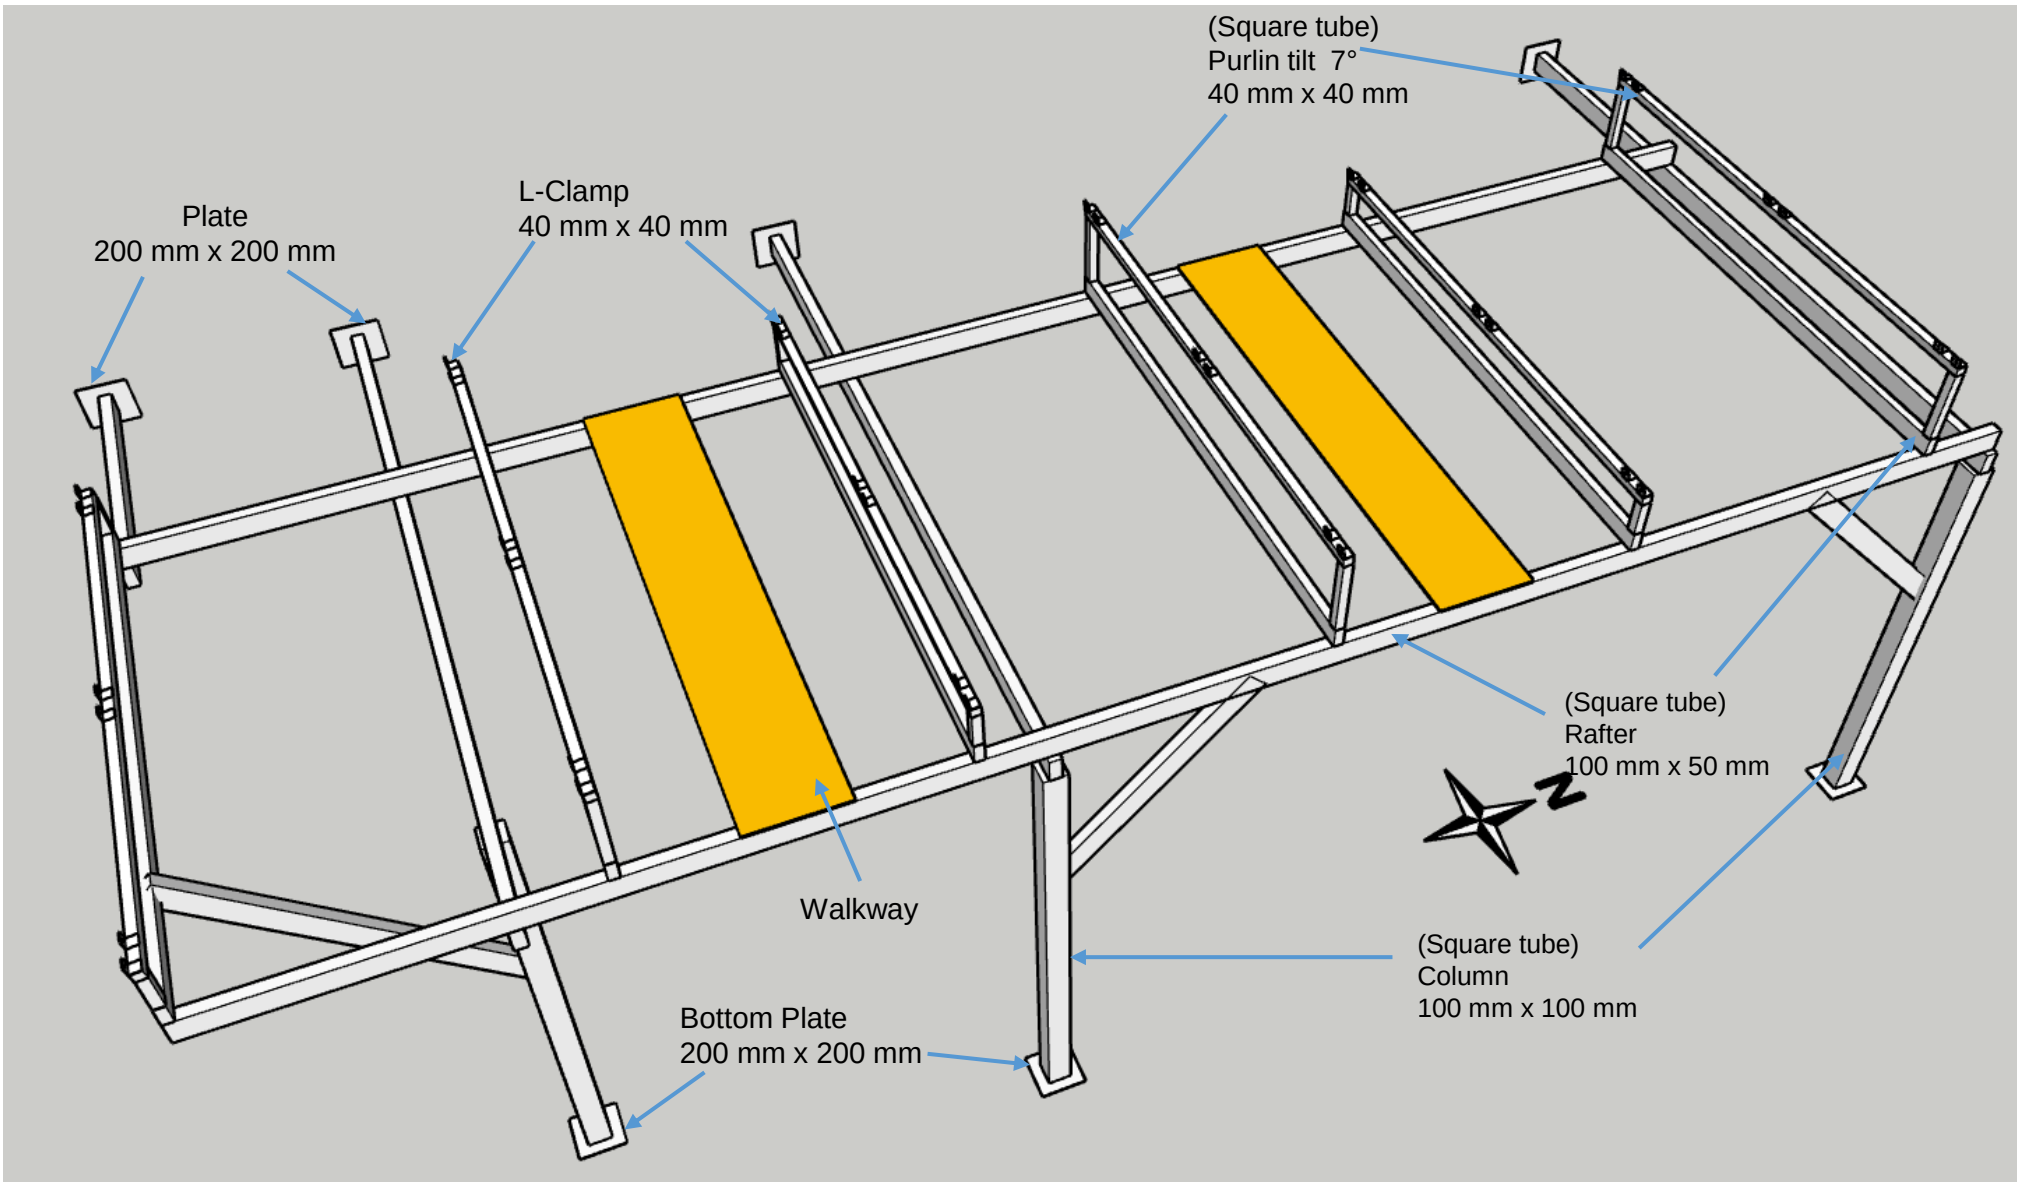

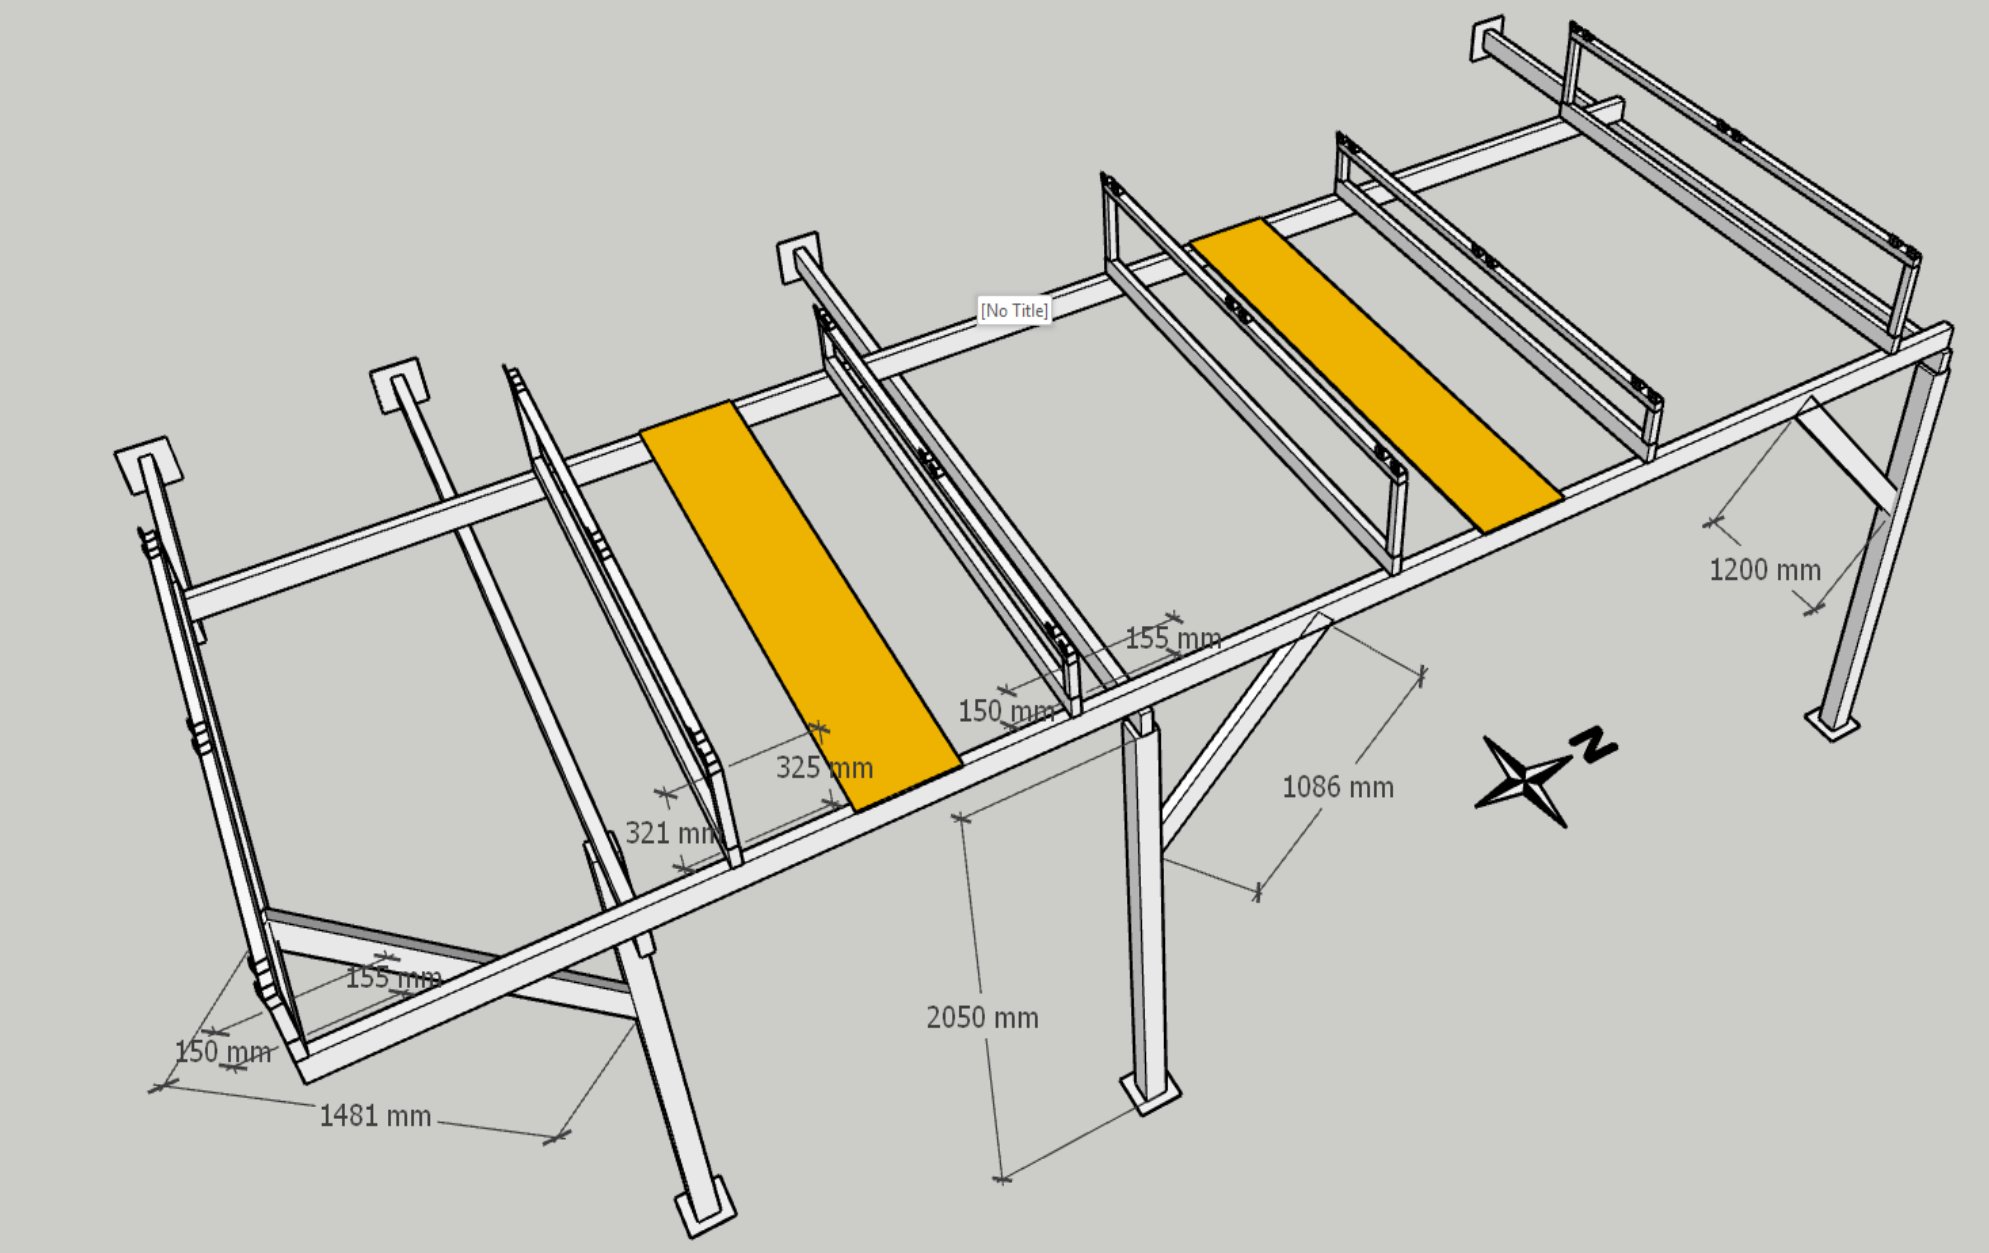

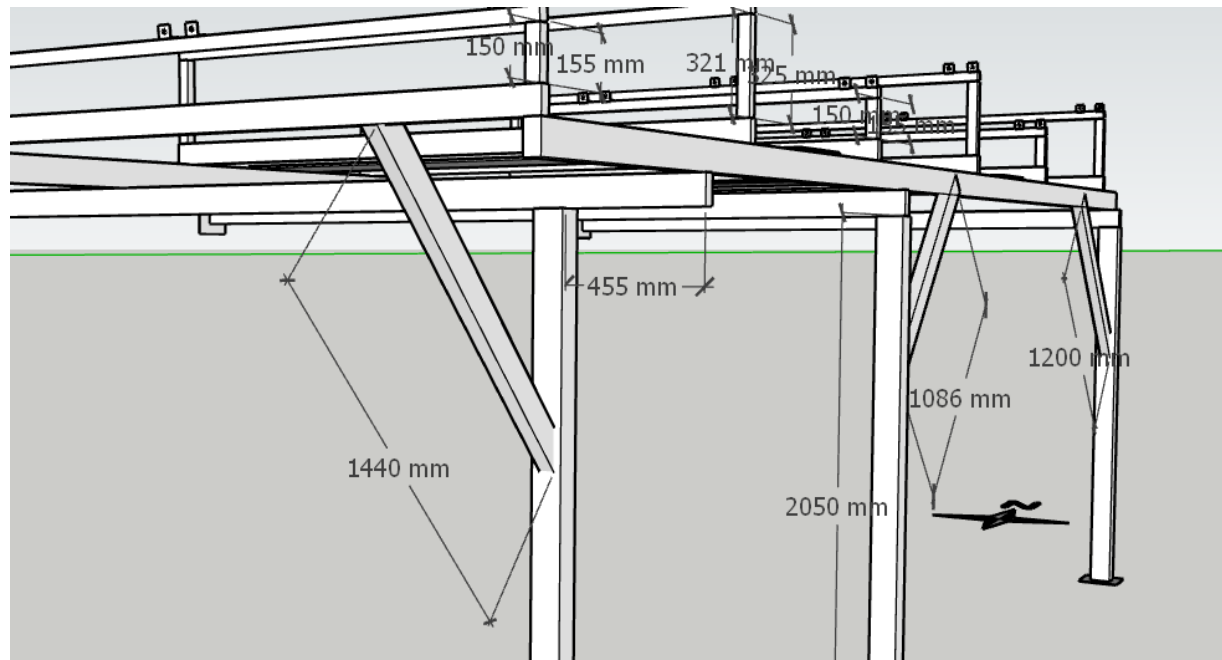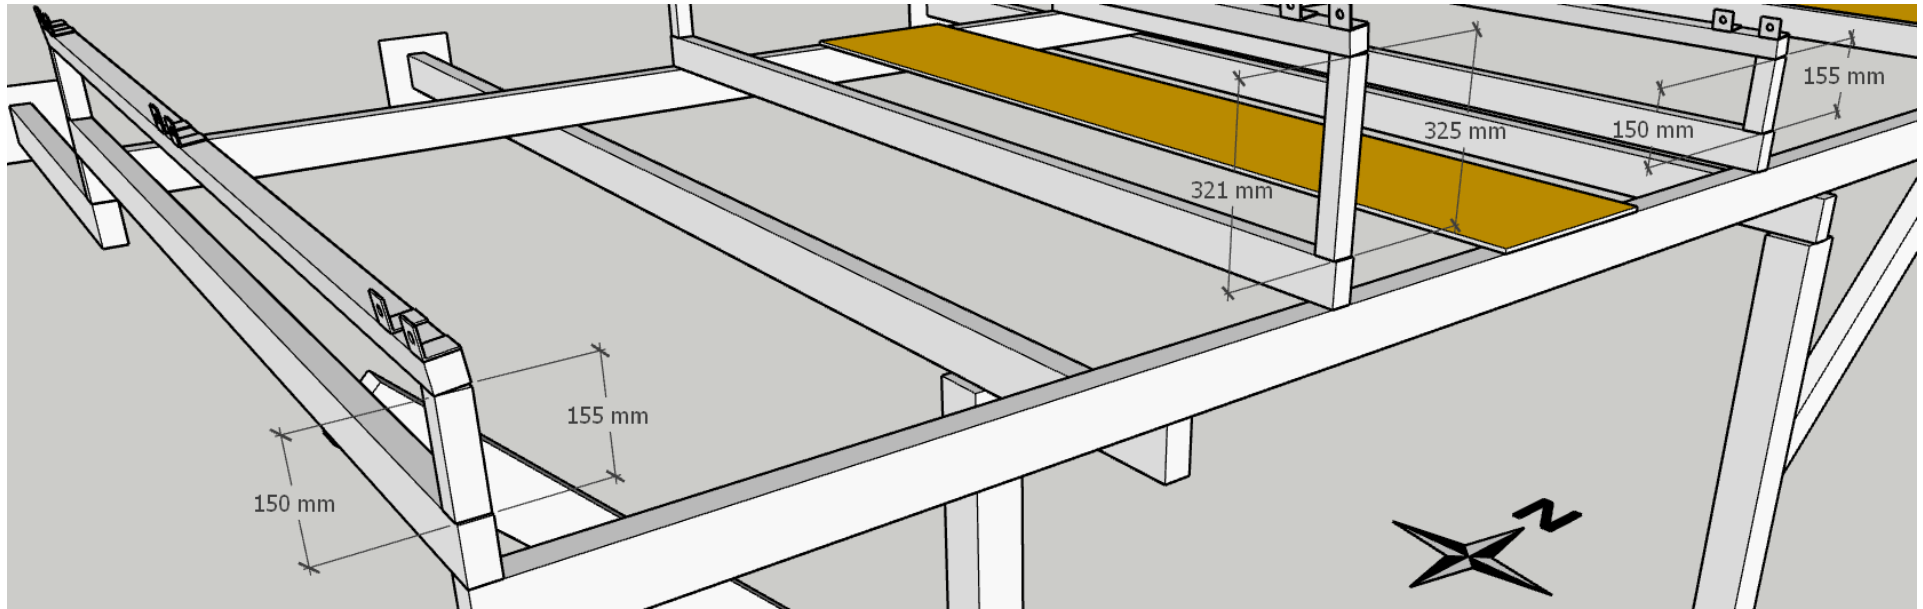



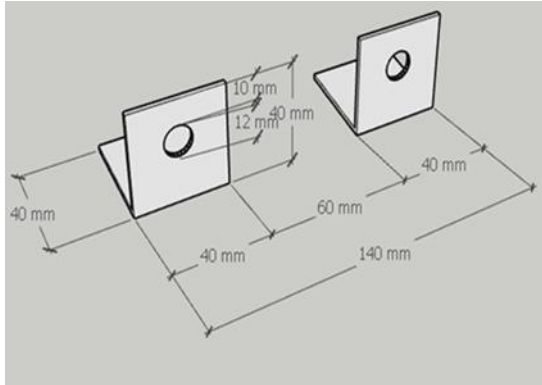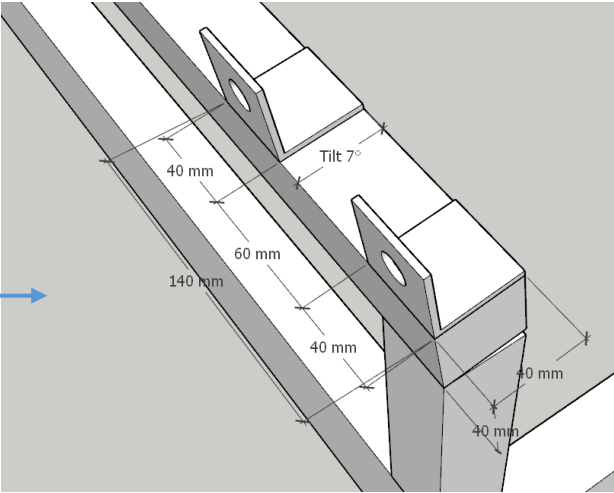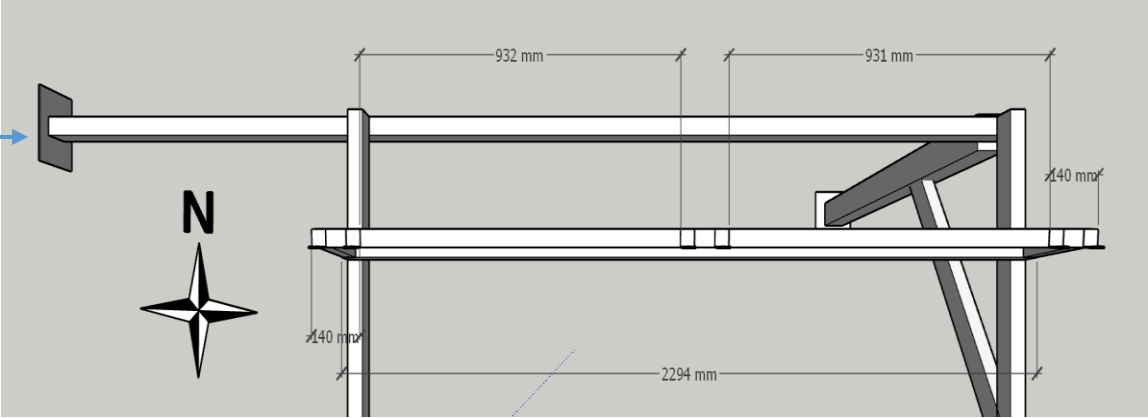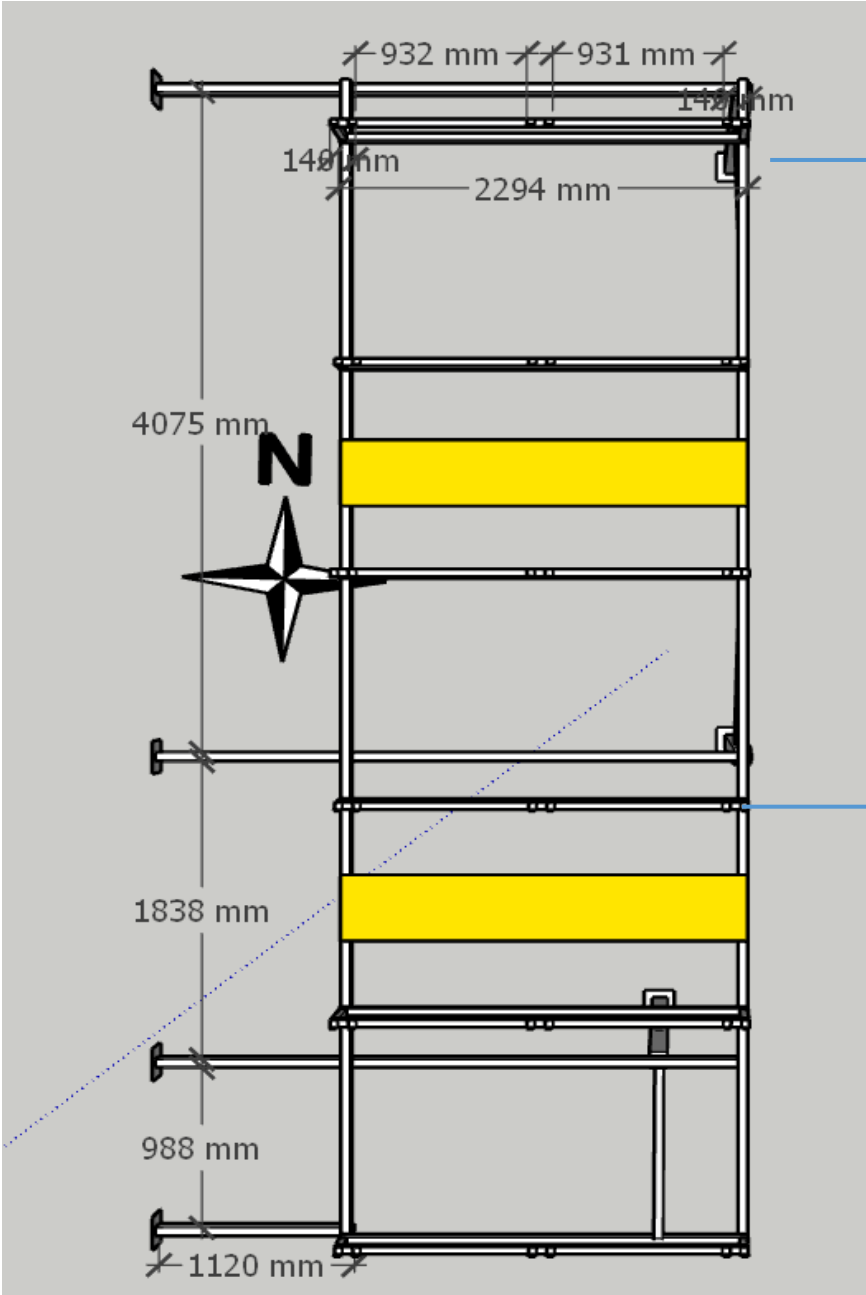


Proposed PV Area (Roof Image)




Panels to be placed in this blue marked area.





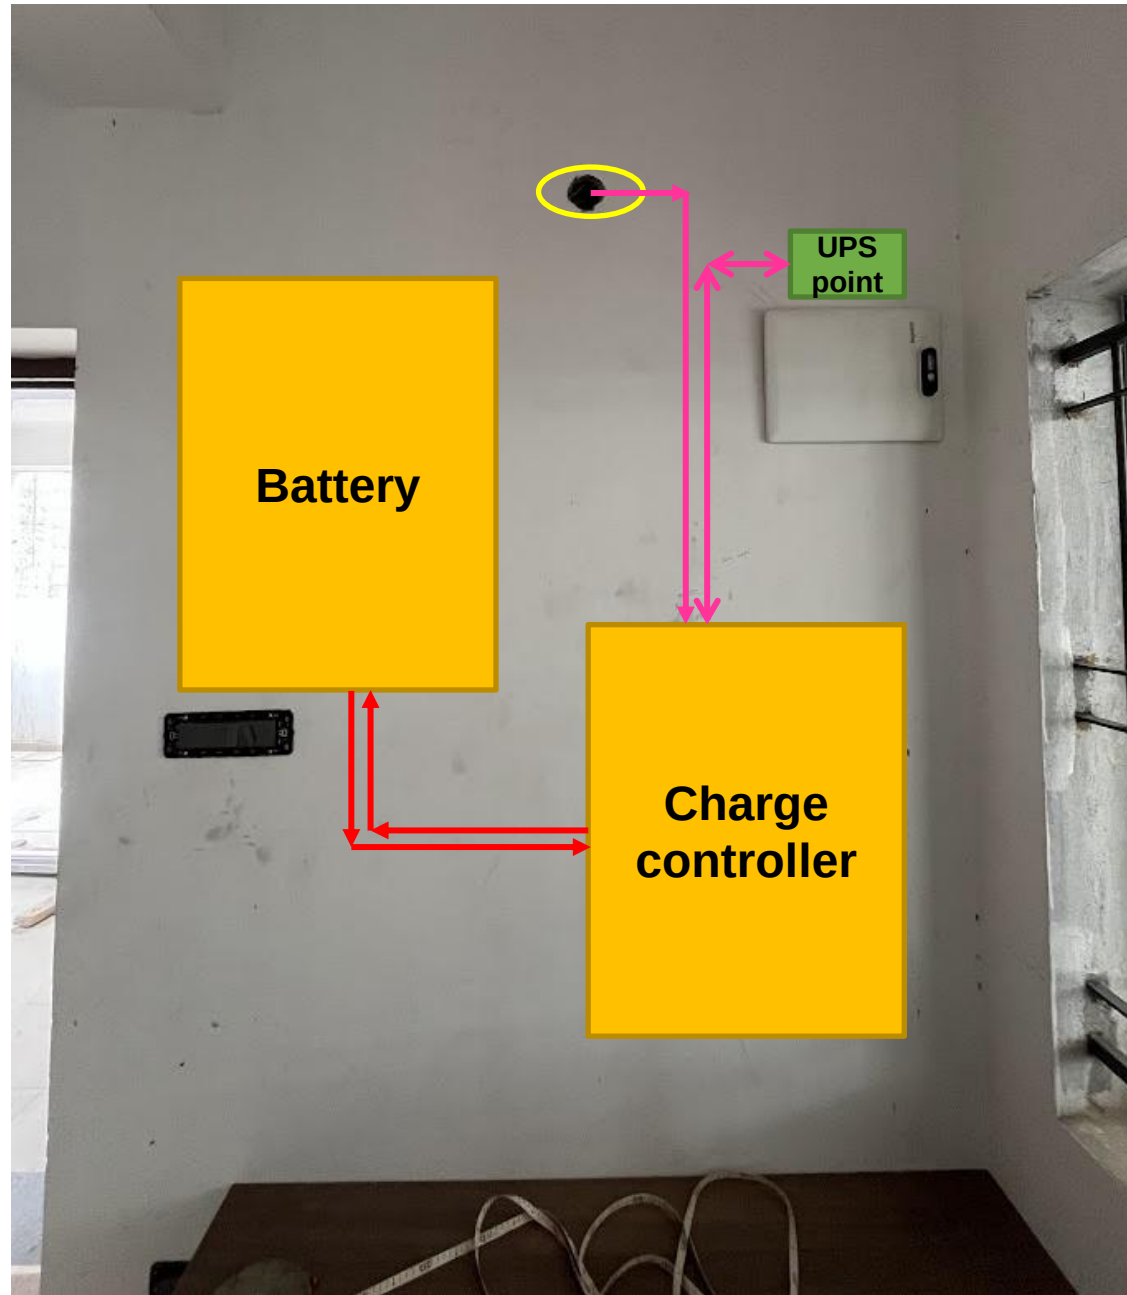

Main meter and Solar meter location:

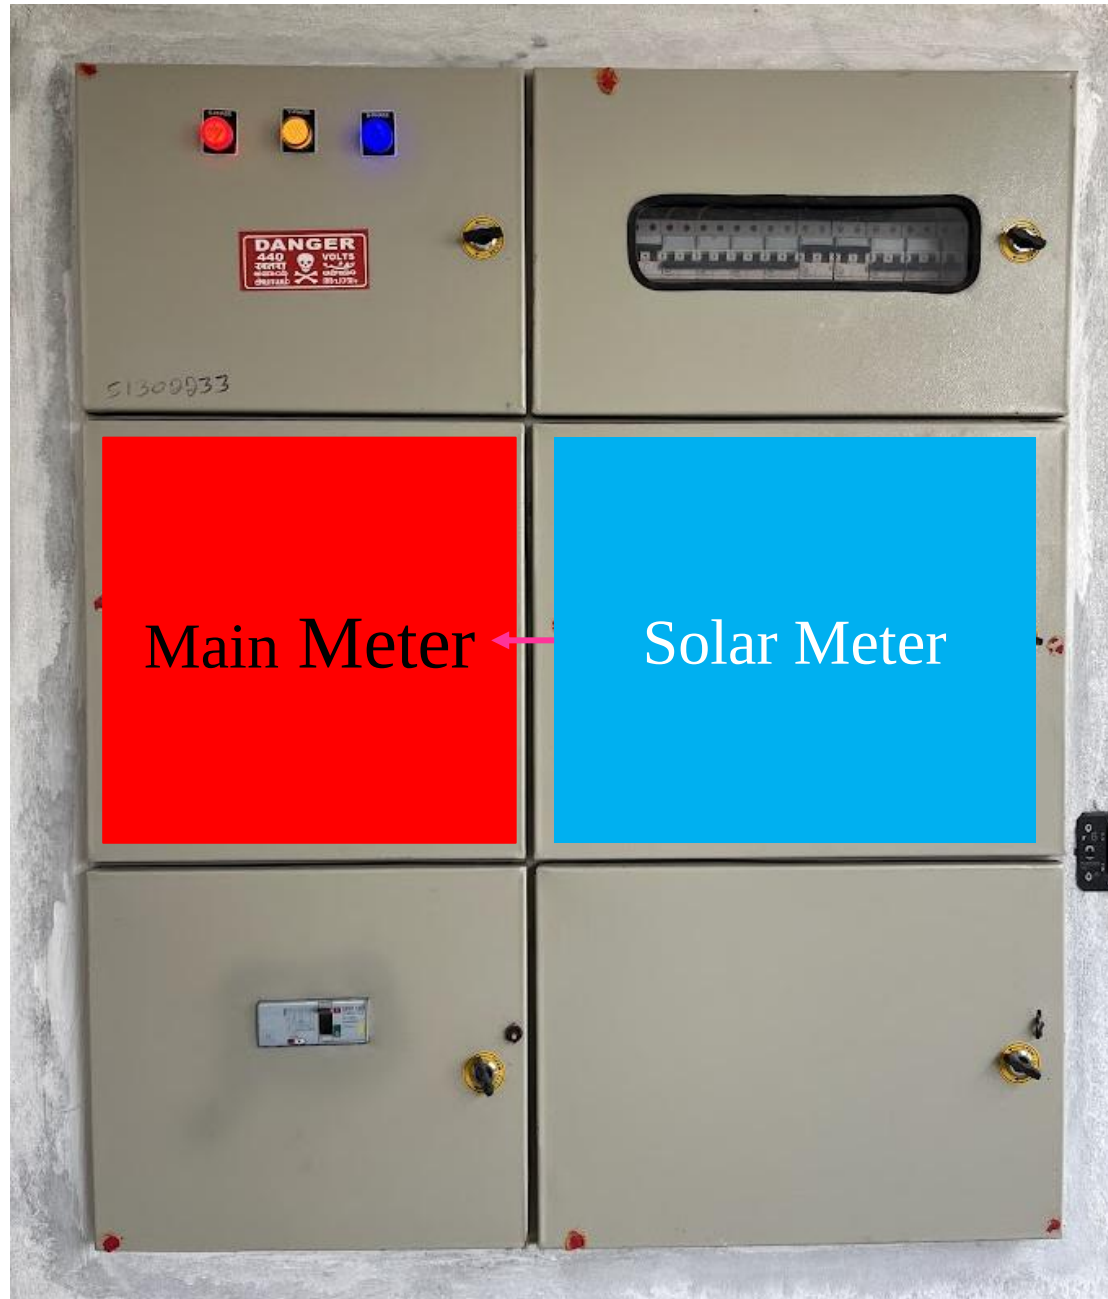

General:

- A conduit pipe is available for the AC cable. In case of any blockage, external routing can be used. (1 inch Conduit)

Customer scope:

- Wi Fi connectivity up to the solar meter.
- MS fabrication work and provision of a ladder for accessing the solar panels.

THANK YOU FOR PARTNERING WITH US



www.ecosoch.com

#940, Sha Arcade, 2nd Phase, NTI Layout, Rajiv Gandhi Nagar, Kodigehalli, Bangalore, 560097
CONTACT US: +91-8123410101, 8123420202
