

Technical Site Visit Report

Prepared for: JEEVANKUMAR VAKATI AND M SOHITHA - #21

PROJECT INFORMATION

Report Number	ESV-2026-0111
Project ID	67EDE3F9
Project Name	JEEVANKUMAR VAKATI AND M SOHITHA
Building Name	#21
Billing Name	JEEVANKUMAR VAKATI AND M SOHITHA
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	JEEVANKUMAR VAKATI AND M SOHITHA #21,2nd floor, Brindavanam Layout Horamavu Agra Main Road Bangalore-560043
GPS Coordinates	13.0309937, 77.6599852
Google Maps	https://www.google.com/maps?q=13.0309937,77.6599852
Visit Date	2026-05-16
Visited By	K NAVEEN
Revision	Rev 0

CLIENT INFORMATION

Client Name	JEEVANKUMAR VAKATI AND M SOHITHA
Contact	99019 60949

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	6.20
Sanction Load (kW)	6.6

Module Make & Capacity	Adani DCR bifacial 620
Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	10
Inverter Type	Micro
Inverter Brand	Enphase
Number of Inverters	10
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	while construction client made two earthing for solar	-
6	Where is the Internet Router located?	Third	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	4	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	0	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-

#	Question	Answer	Notes
8	What type of mounting structure is planned?	Mini-rails	Short Rail - Sheet Roof (Special structure)
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	G+3+Hedroom is approximately 15 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	The dimensions of empty box for solar meter is 0.3 X 0.5 m
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	N/A	-
15	Are there any safety risks associated with accessing the roof for installation?	N/A	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-

#	Question	Answer	Notes
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 300, width: 500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1000, width: 1000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	Yes	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA


Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).





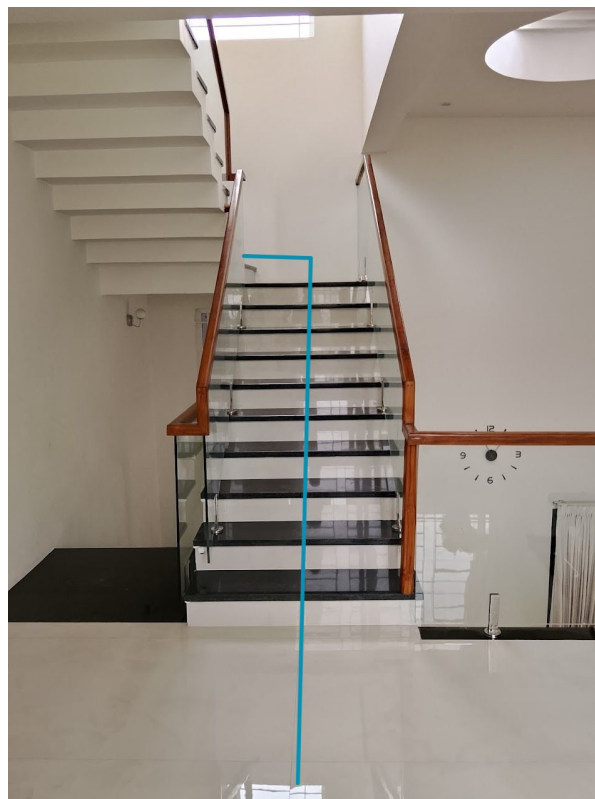

This route (using Staircase) will be followed to carry Small items

Staircase Details



Meter Box




Material Storage




Proposed PV Area



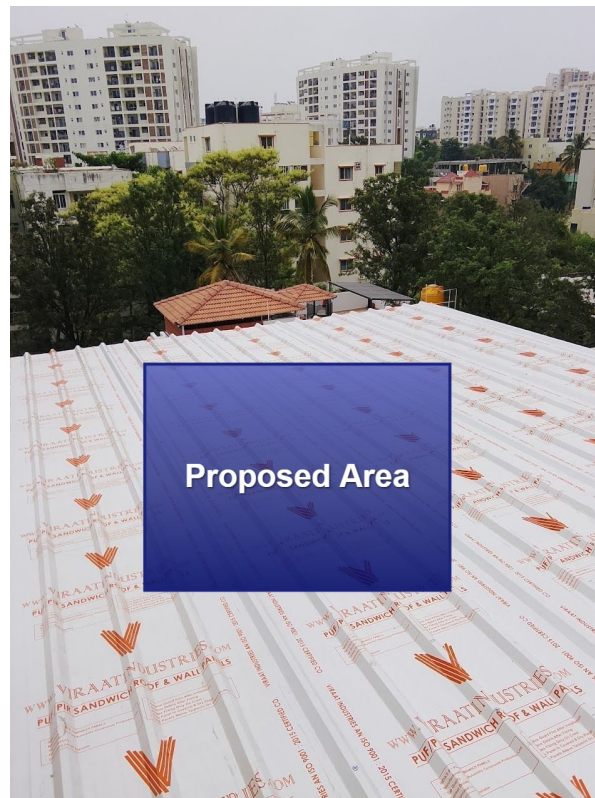

Cable Routing



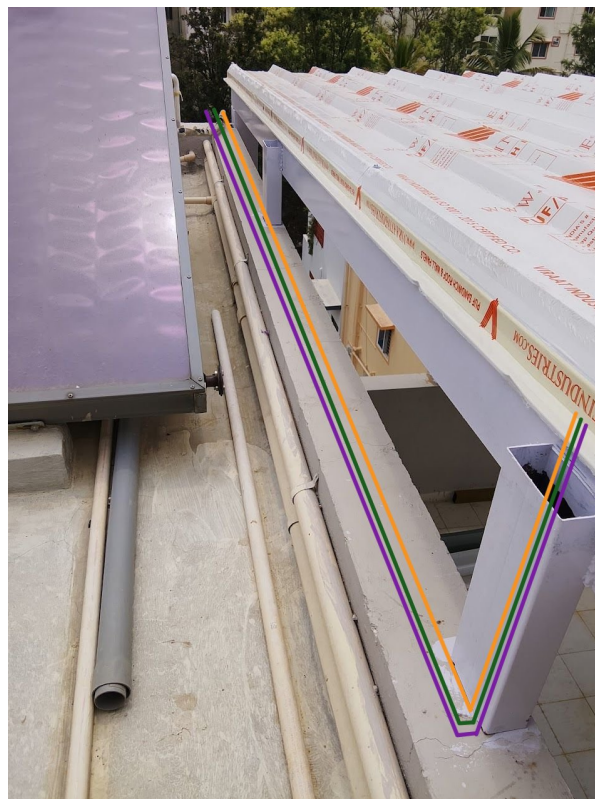







Make a hole to run the AC Cable, LA & DC Earthing routing till the meter location


Equipment Location

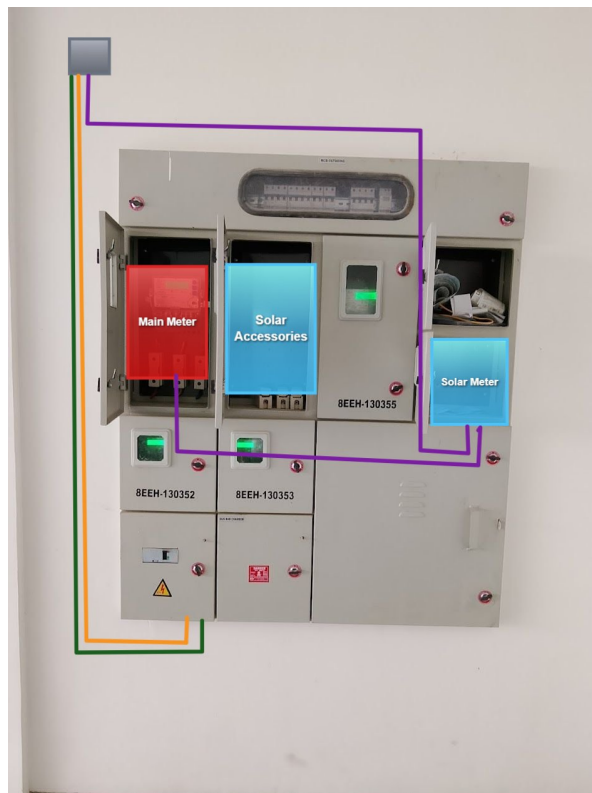

Earth Pit Location


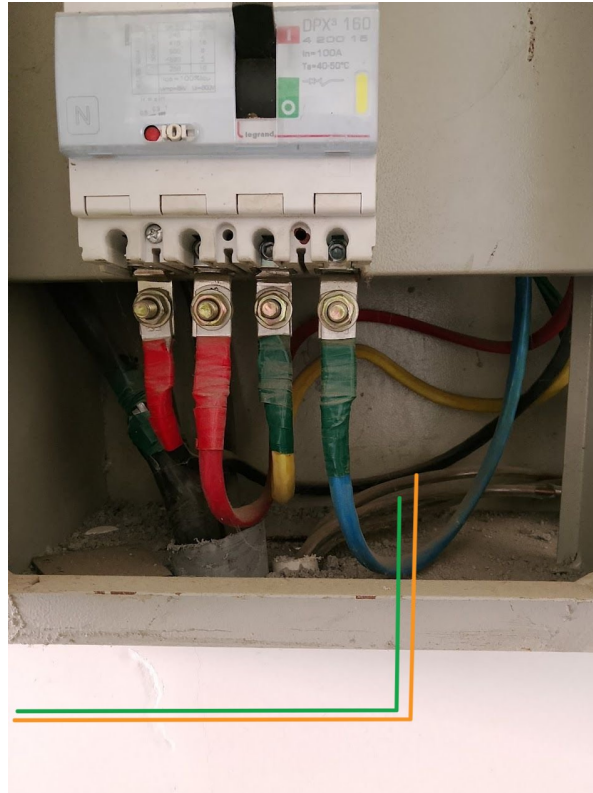



The existing earthing rods are available at the meter panel board; we can tap them for both DC and AC earthing.

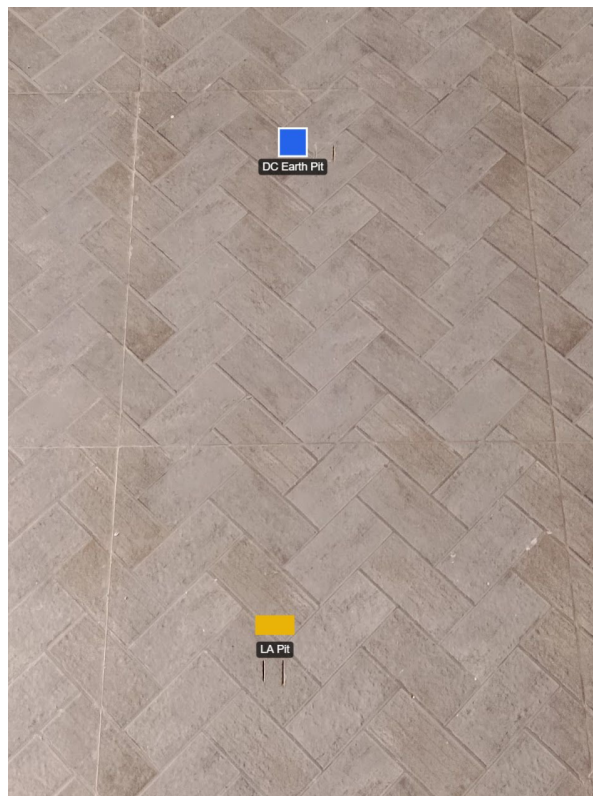


Client made two earthing pits for solar at the time of construction

Site Layout - Top View

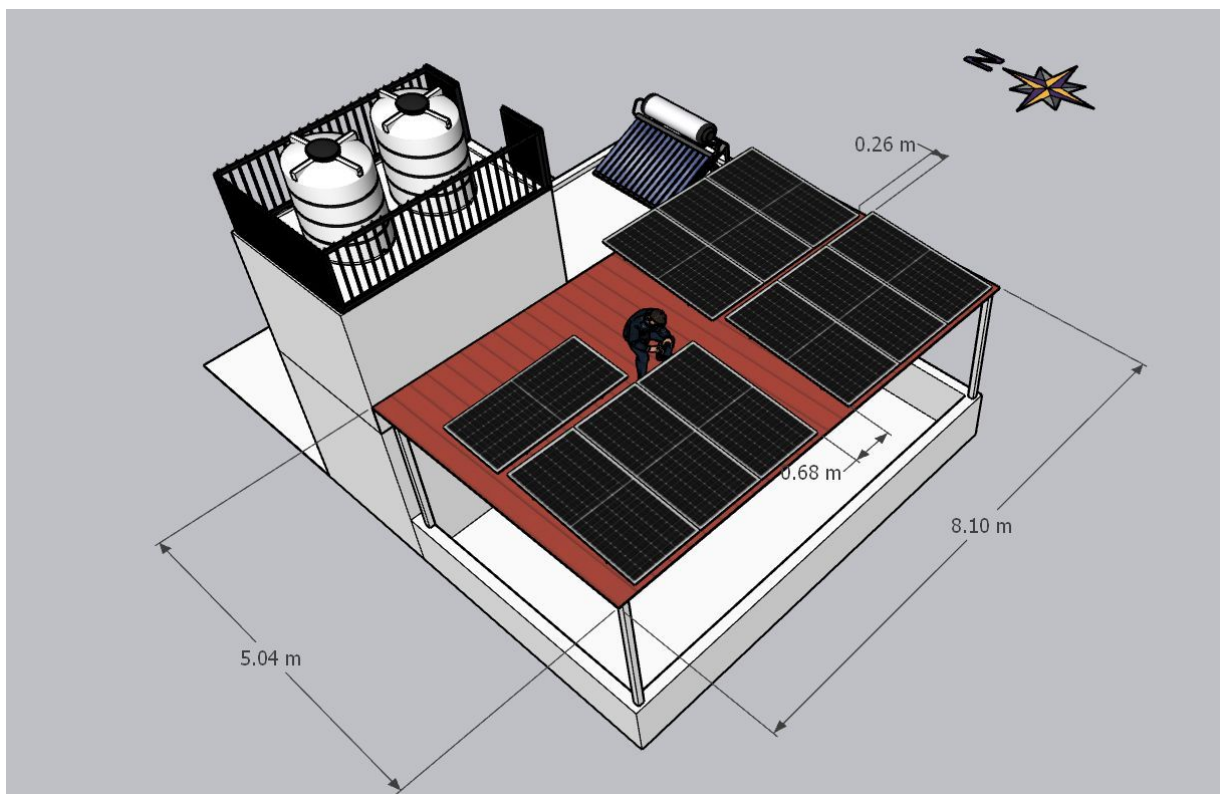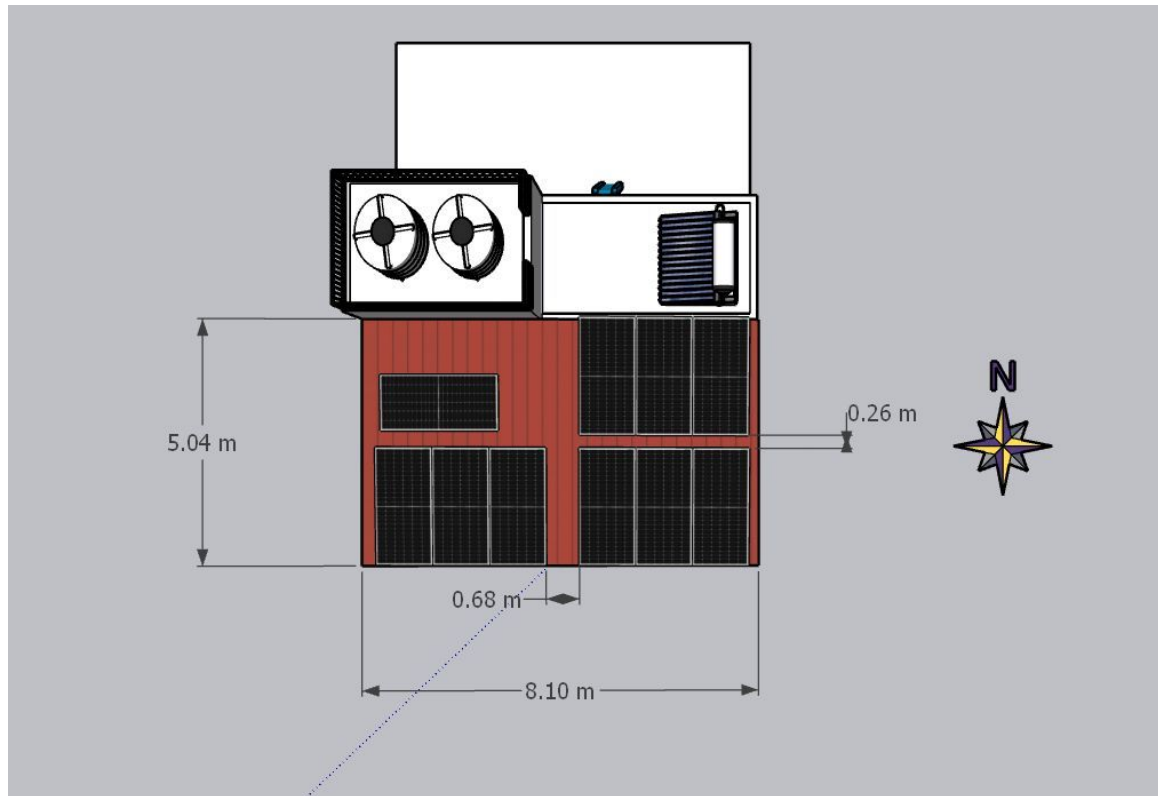

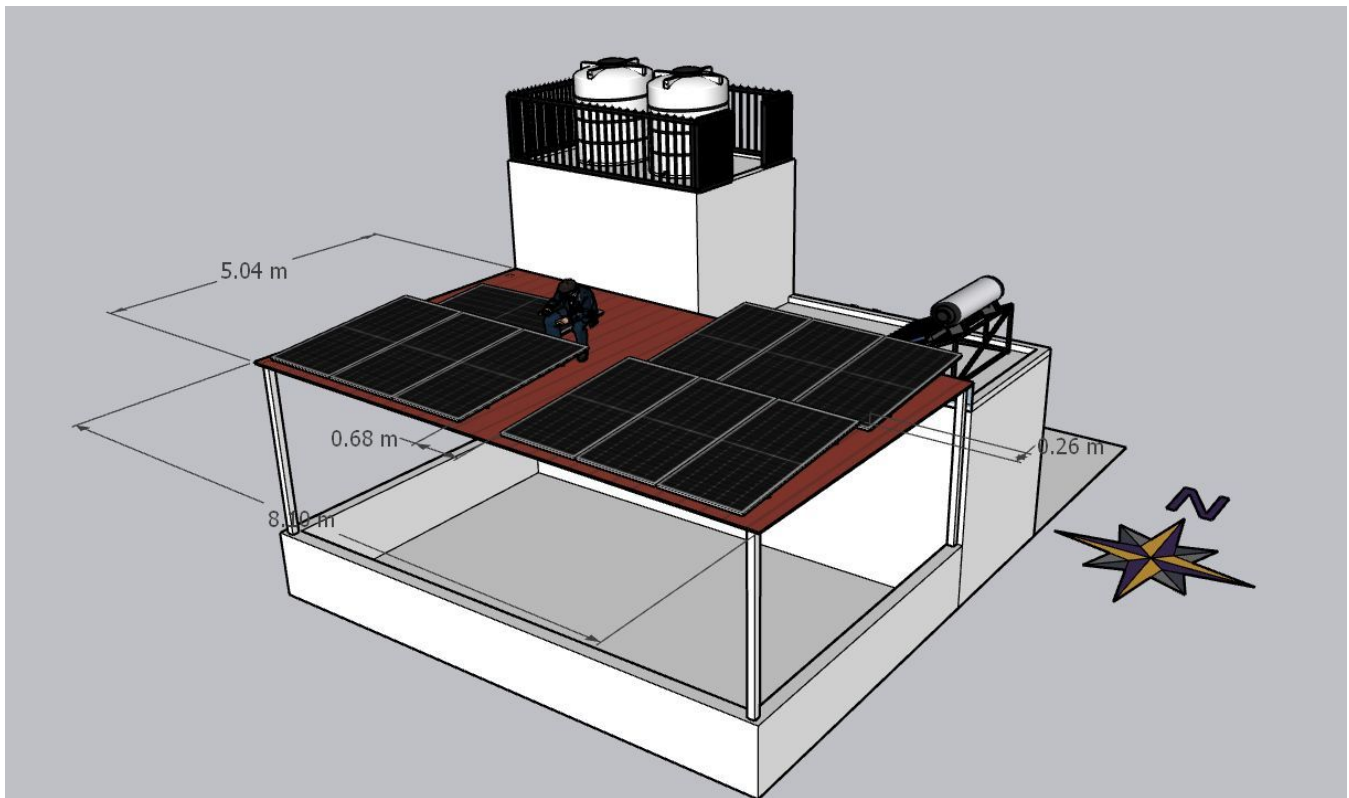

Shadow Analysis

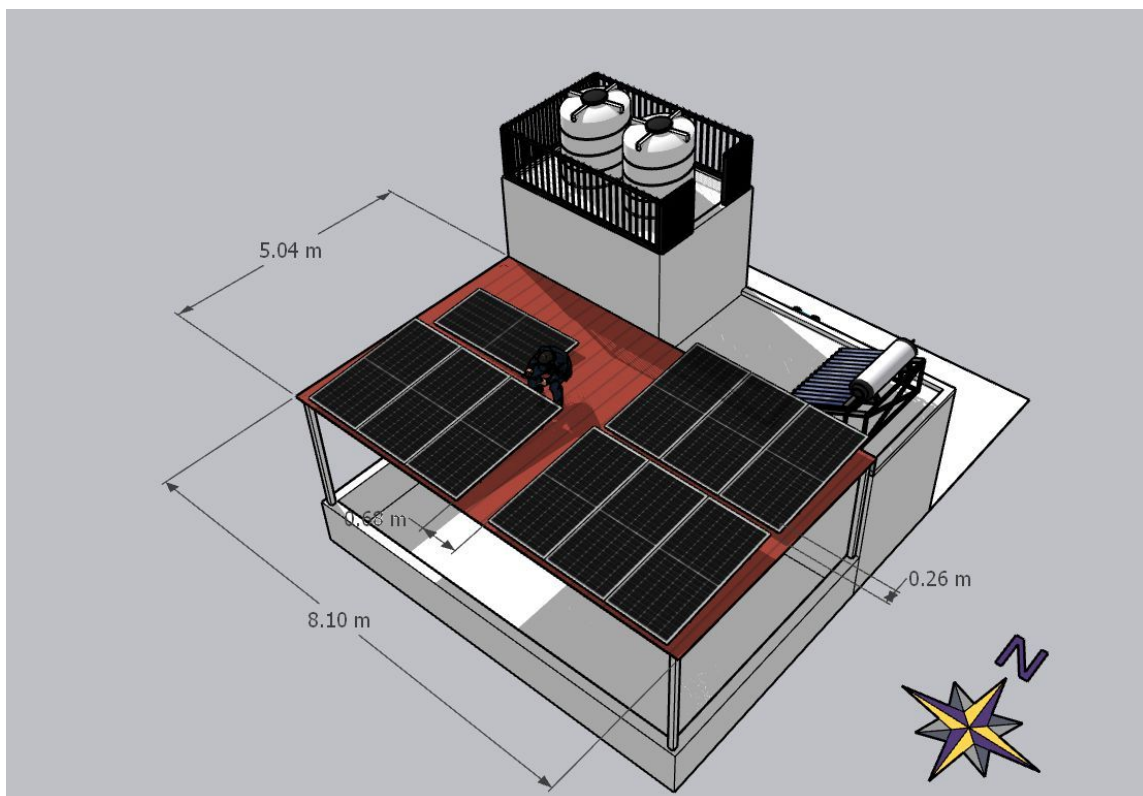

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	For installing the solar meter and associated accessories, we will utilize the available empty provisions in the existing meter panel board.
2	We will tap our DC and LA earthing to the existing earthing rods located in the main meter panel board.
3	The Material lifting has been lifted back side of the house
4	Made a hole to run the AC Cable and DC,LA earthing routing till the meter location

Customer Scope

#	Observation
1	Wi-Fi up to the solar meter location is under customer scope
2	Client made two available existing earth pits at the time of construction
3	The existing water tank will cast a shadow on the panels from May to August, between 3:30 PM and 4:30 PM.

THANK YOU

Dear JEEVANKUMAR VAKATI AND M SOHITHA,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
