

Technical Site Visit Report

Prepared for: Divik & Gunjan Saxena_JRC Palladio Non Subsidy_8.54kWp_Microinverter (IQ Series) - Villa 14

PROJECT INFORMATION

Report Number	ESV-2026-0183
Project ID	2B3CBF3A
Project Name	Divik & Gunjan Saxena_JRC Palladio Non Subsidy_8.54kWp_Microinverter (IQ Series)
Building Name	Villa 14
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju J S
Site Address	Villa # 14, Phase 2, JRC Palladio, Billapura, Cross, Sarjapura - Attibele Rd, Sarjapura, Bengaluru, Karnataka 562125.
GPS Coordinates	12.831415, 77.773988
Google Maps	https://www.google.com/maps?q=12.831415,77.773988
Visit Date	2026-08-08
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	Divik & Gunjan Saxena
Contact	9731777600

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	8.54
Sanction Load (kW)	10
Module Make & Capacity	Premier 610Wp Topcon Bi-Facial Non-DCR

Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	14
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	14
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Enphase accessories box, inbuilt with a solar meter provision can be installed near the existing main meter box located at the car porch on the front side of the building.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, discussed with the customer and finalised the location for earthing.	-
6	Where is the Internet Router located?	Not yet installed. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-

#	Question	Answer	Notes
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	<i>Elevated HDGI - 2m Front Leg (2 Rows, Portrait) with Drilling & Only Base Plate Cement Covering</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	<i>One can access the terrace floor via the inner staircase. But the roof proposed for installation can be accessed with the help of a ladder.</i>
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	10 Metres (G+2)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999)	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>The earthing can be done at the north side of the building. But with enough care, because the plumbing pipes are</i>



#	Question	Answer	Notes
			already laid underneath.
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	details: Enough care has to be given while digging the earthing pit, because the plumbing pipes are already laid underneath. No other location available for earthing pit.	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 2000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 5000, width: 300	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend



Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit

Site Layout - Top View

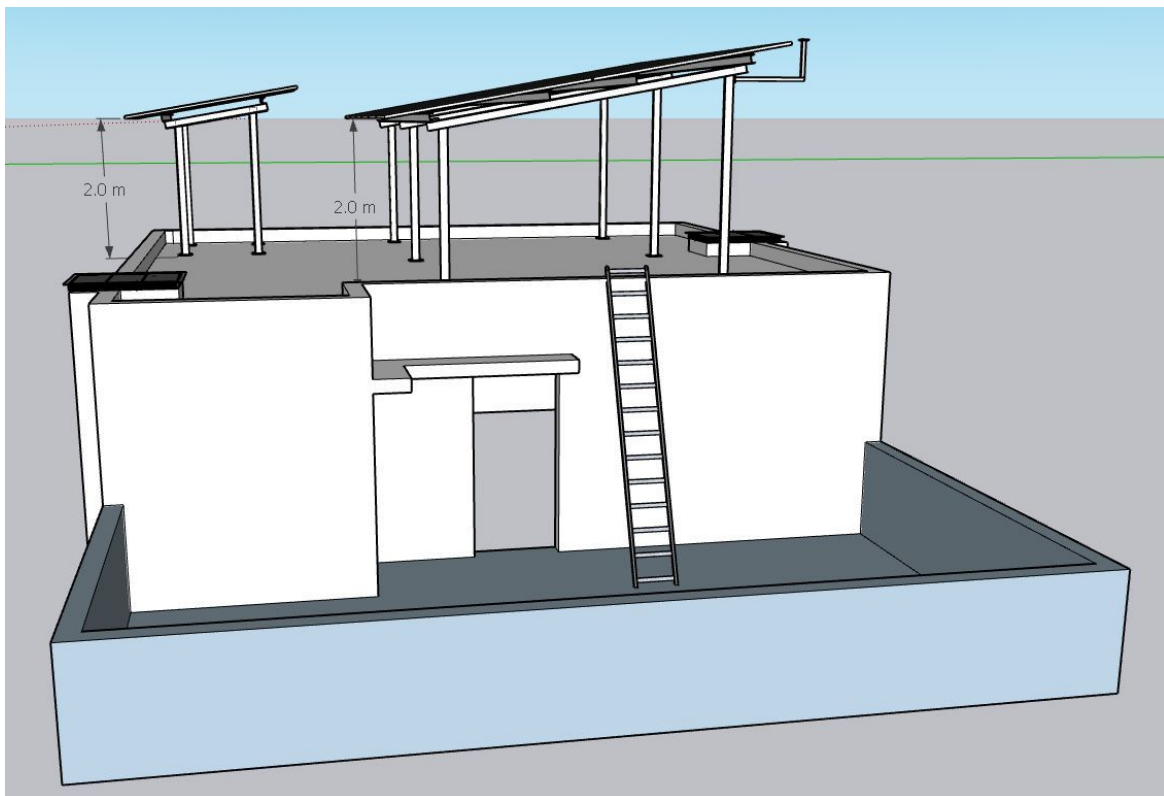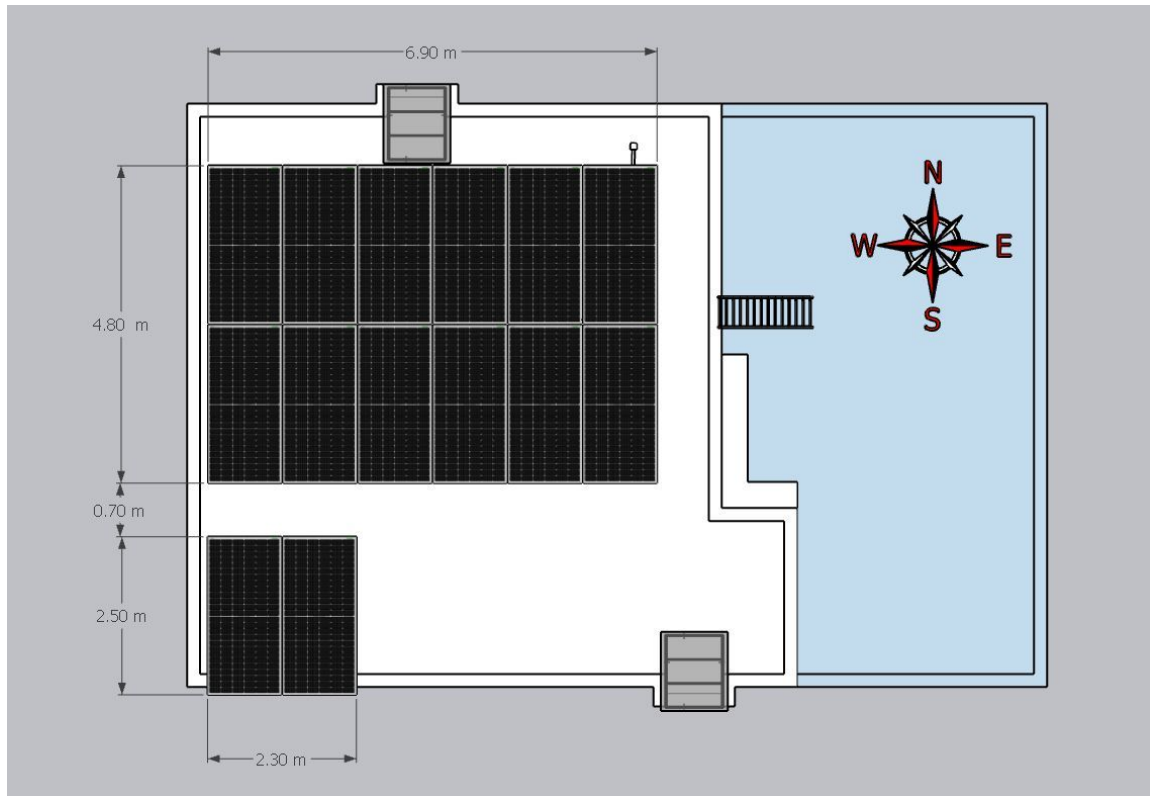

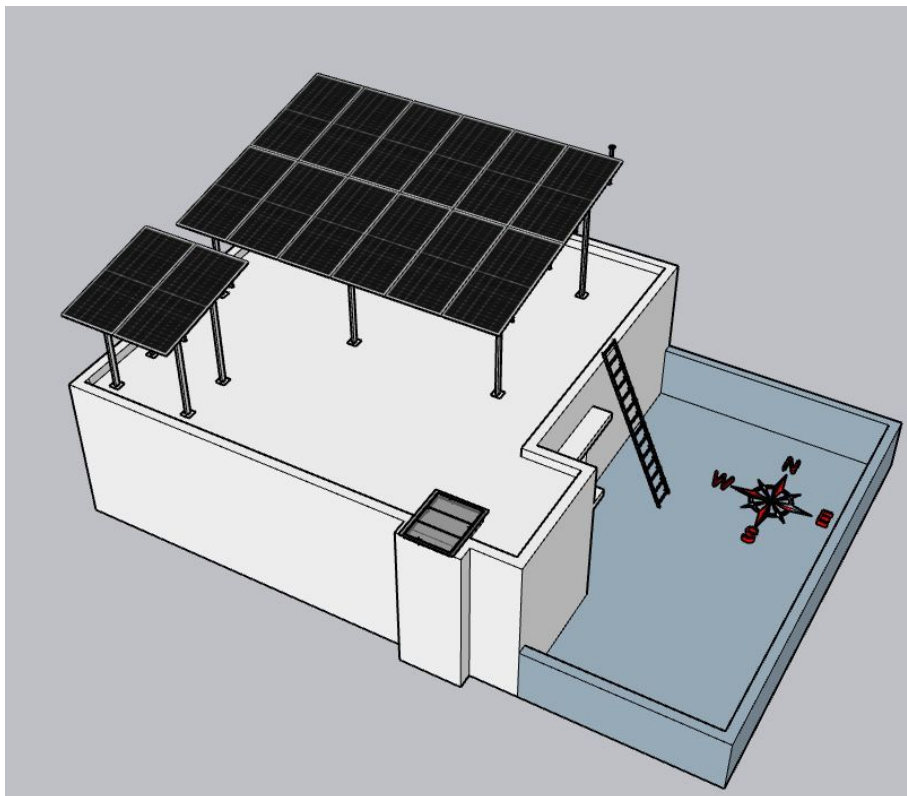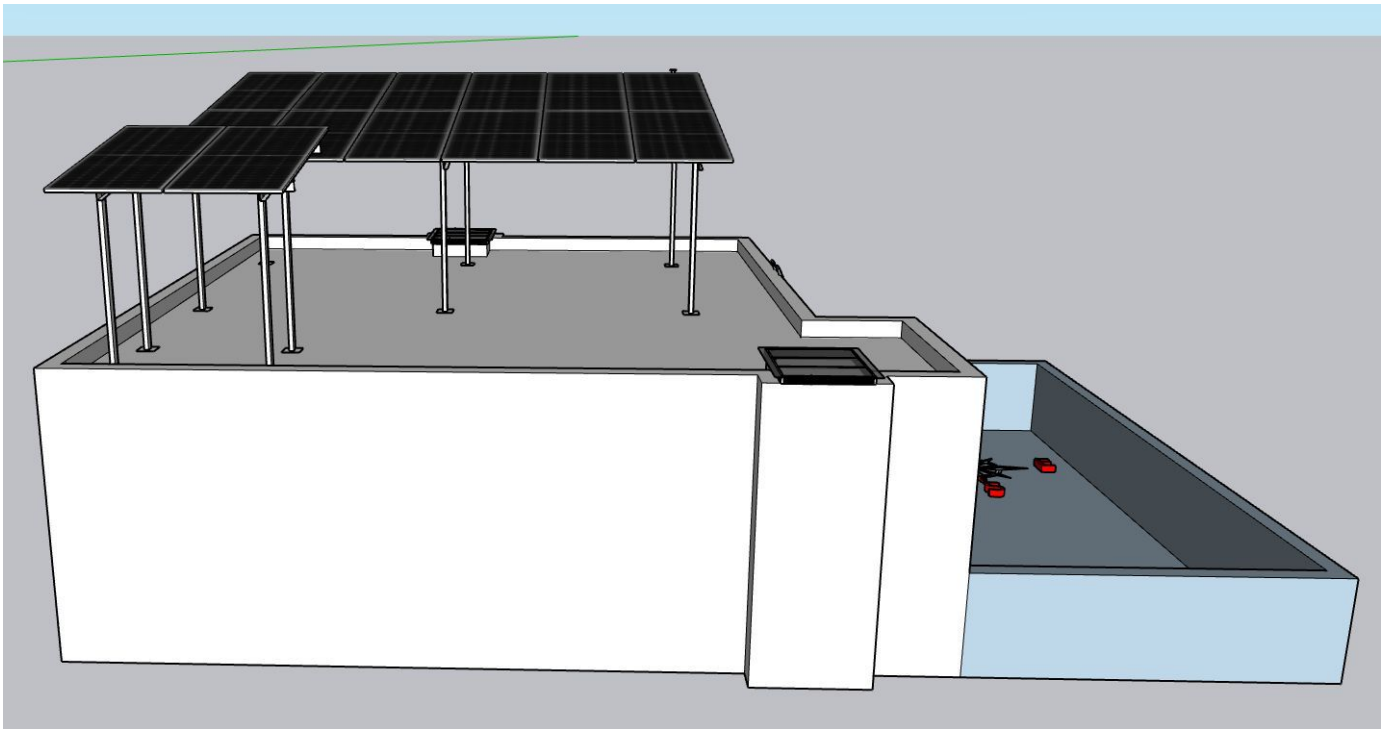

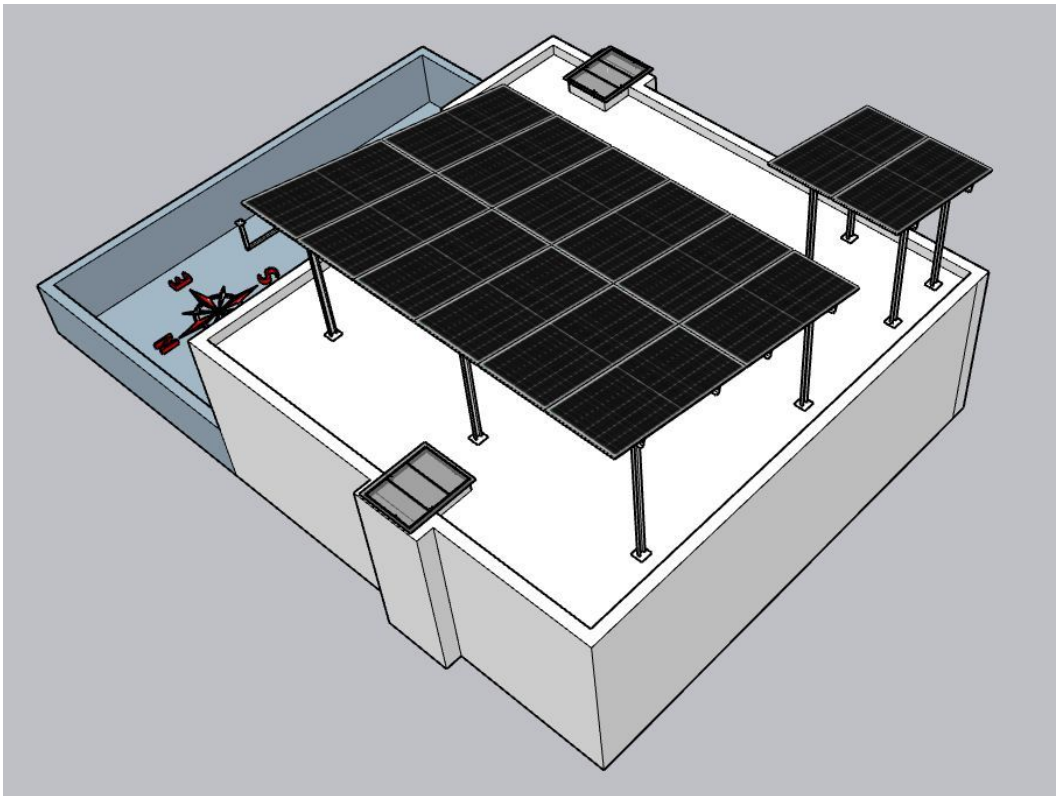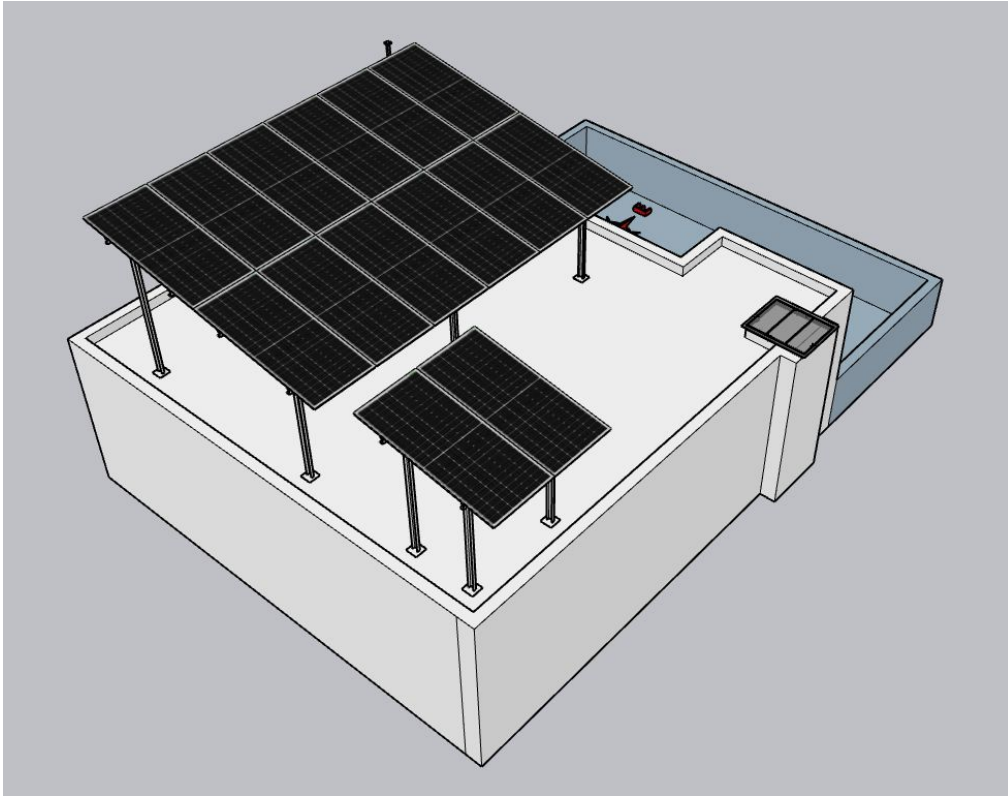

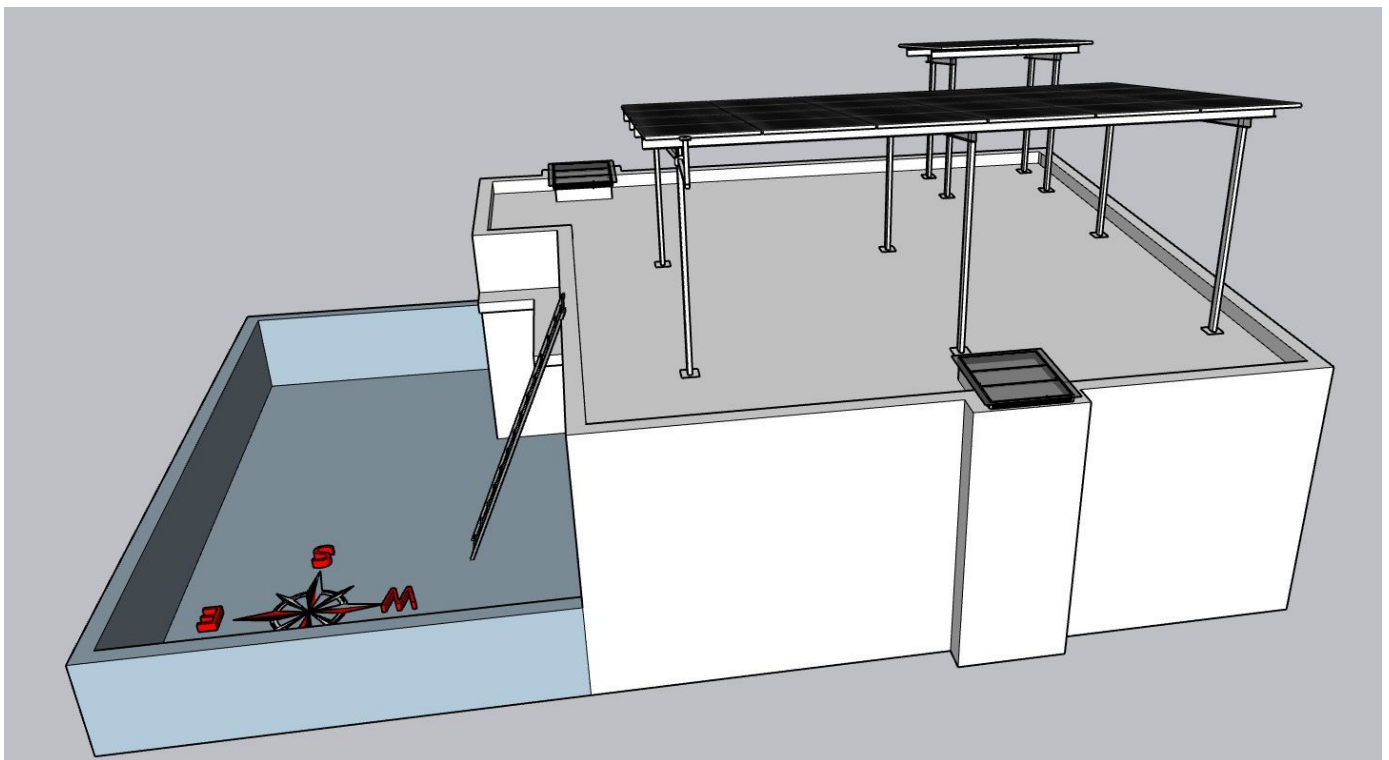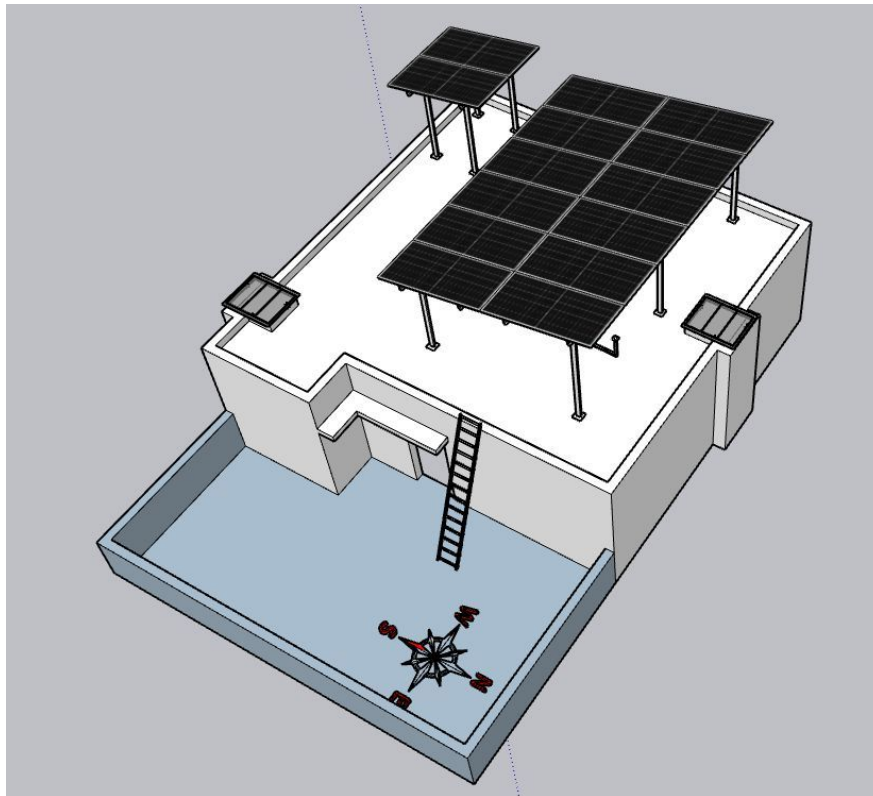

Building Exterior



Material Delivery Route



The materials can be shifted to the terrace via two options available at the site. Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



Materials moving towards the stairs.



The materials can follow the stairs until reaching the 2nd floor terrace.



The materials are reaching the 2nd floor.



The materials shifting outwards the balcony area can be stacked here before shifting to the upper terrace.

Staircase Details




Staircase width: 1000 mm

Proposed PV Area



Cable Routing

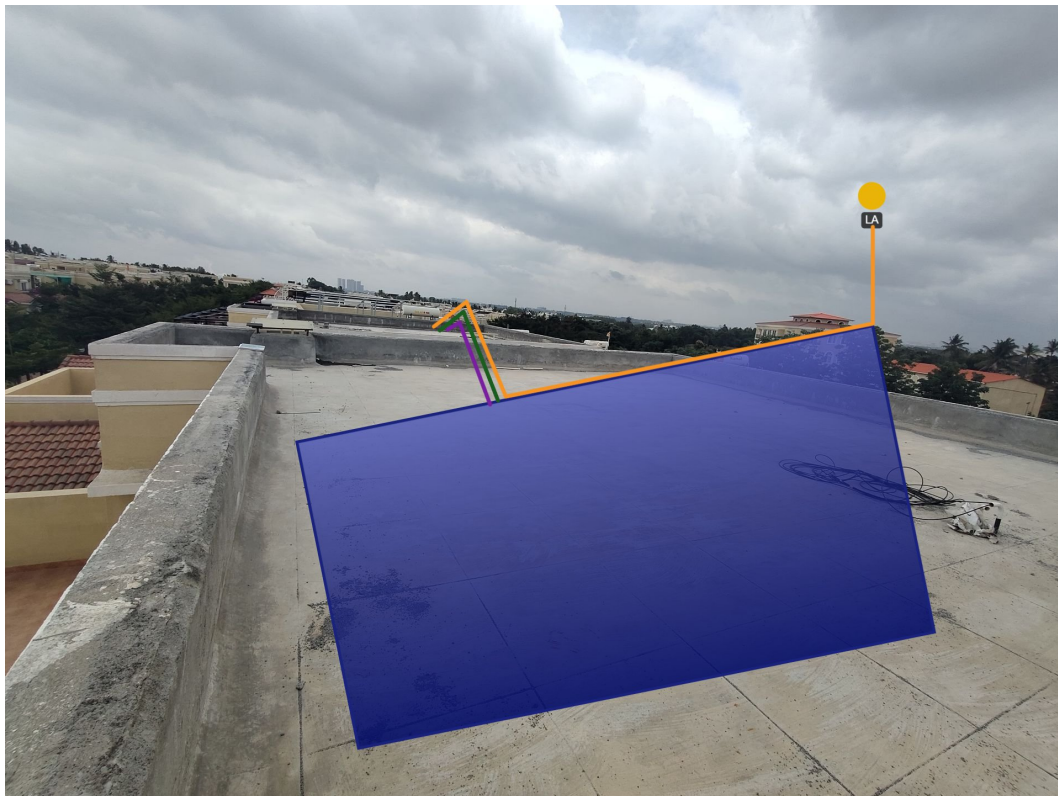






Meter Box



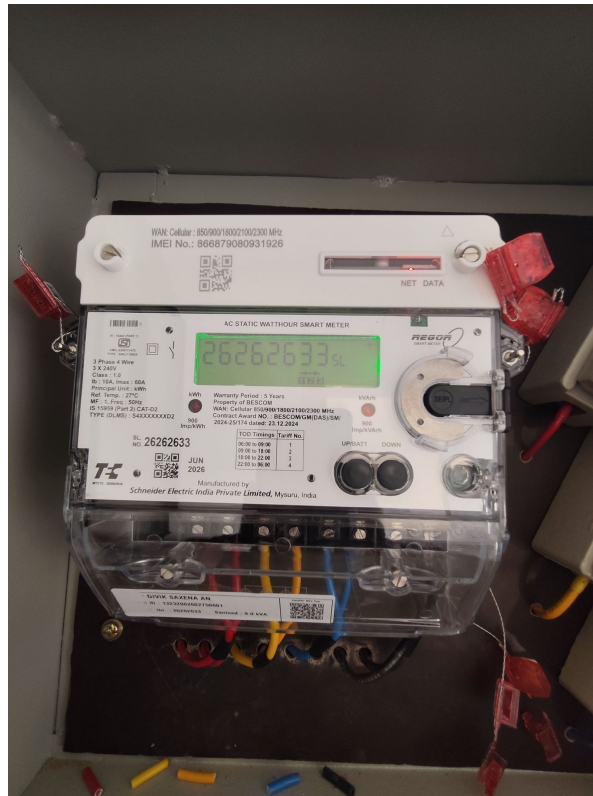

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 8.54kWp On-grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.
3	A base support provision for lightning arrester extension has to be provided at the rooftop.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.

THANK YOU

Dear Divik & Gunjan Saxena,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
