

Technical Site Visit Report

Prepared for: Sheshrao Eknath Shingote_Ramachandrapura Subsidy_4.3kWp_String

PROJECT INFORMATION

Report Number	ESV-2026-0143
Project ID	F216DA84
Project Name	Sheshrao Eknath Shingote_Ramachandrapura Subsidy_4.3kWp_String
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Govindaraju J S
Site Address	#42, Jyothi, 8th Cross, 2nd Main, Chamundeshwari Layout, Vidyaranyapura, Bangalore 560097
GPS Coordinates	13.066486, 77.554469
Google Maps	https://www.google.com/maps?q=13.066486,77.554469
Visit Date	2026-06-12
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	Sheshrao Eknath Shingote
Contact	9606212012

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	4.3
Sanction Load (kW)	4
Module Make & Capacity	Adani TOPCon Bi-facial DCR, 615 Wp
Module Length (mm)	2382

Module Width (mm)	1133
Number of Panels	7
Inverter Type	String
Inverter Brand	Deye (SUN-4K-G03) 4kW, 1ph
Number of Inverters	1
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	At the recessed space on the 1st floor, wall-mounted.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, Discussed with the customer and finalised the location for earthing.	-
6	Where is the Internet Router located?	Ground floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	The active WiFi / LAN cable connection will be provided to the inverter location by the customer.
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: An existing HDGI structure (with 2 PV modules): Will be removed or replaced by the customer. An existing solar water heater: Will be relocated by the customer from the proposed area of	-

#	Question	Answer	Notes
		new installation.	
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Ballast	-
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	<i>One can access the terrace floor via the inner staircase. But the roof proposed for installation can be accessed with the help of a ladder.</i>
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	10 Metres (G + 1 + head room)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-



#	Question	Answer	Notes
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall-mounted, At the recessed space on the 1st floor.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 300, width: 200	Space available inside the existing meter box for fixing the solar meter
21	Provide the dimension for earth pits location (L x W of available space).	length: 5000, width: 500	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION



Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout - Top View

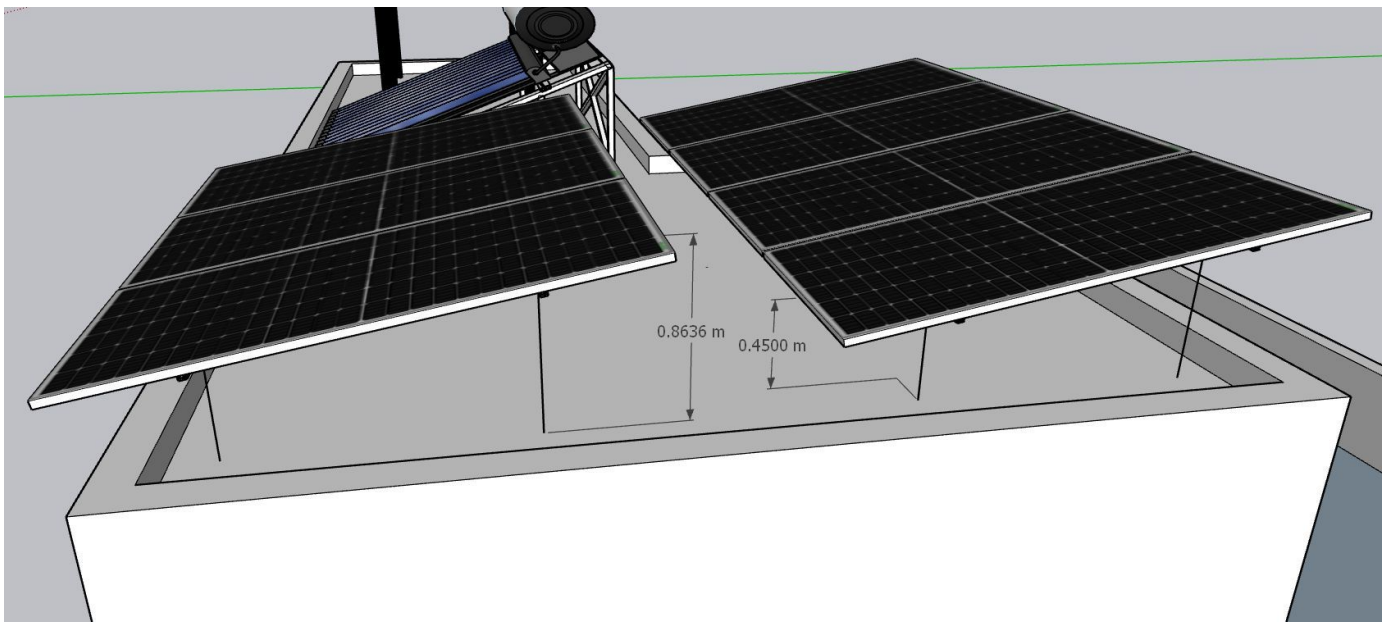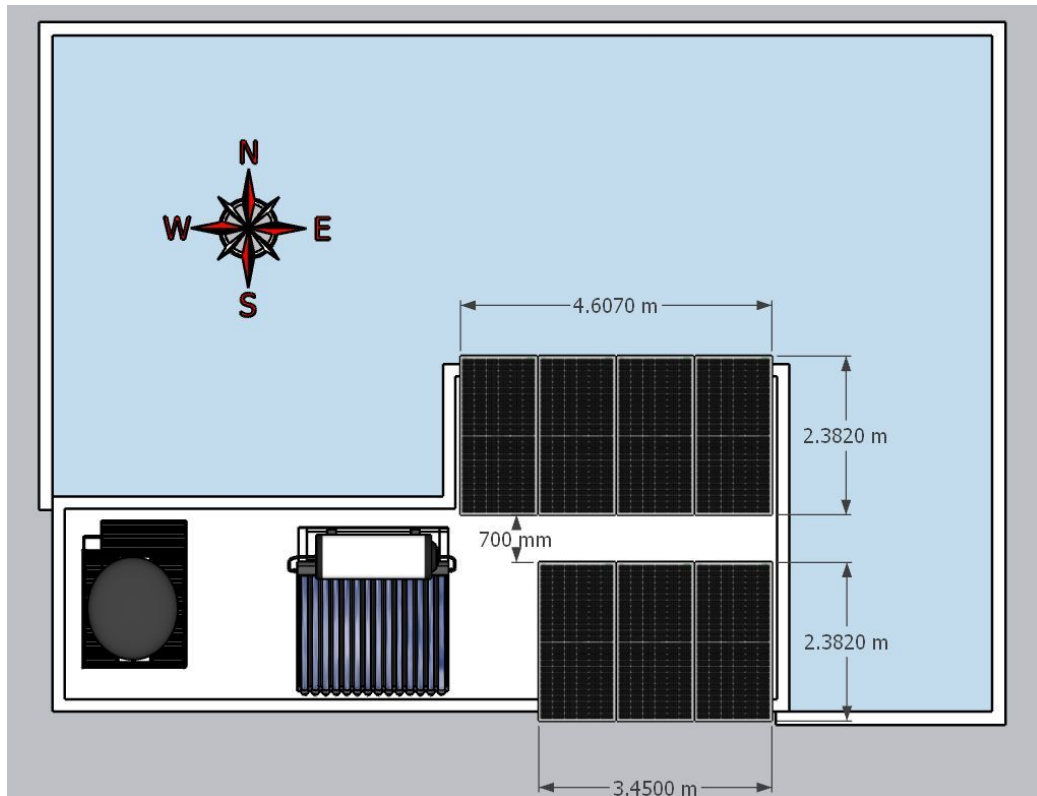

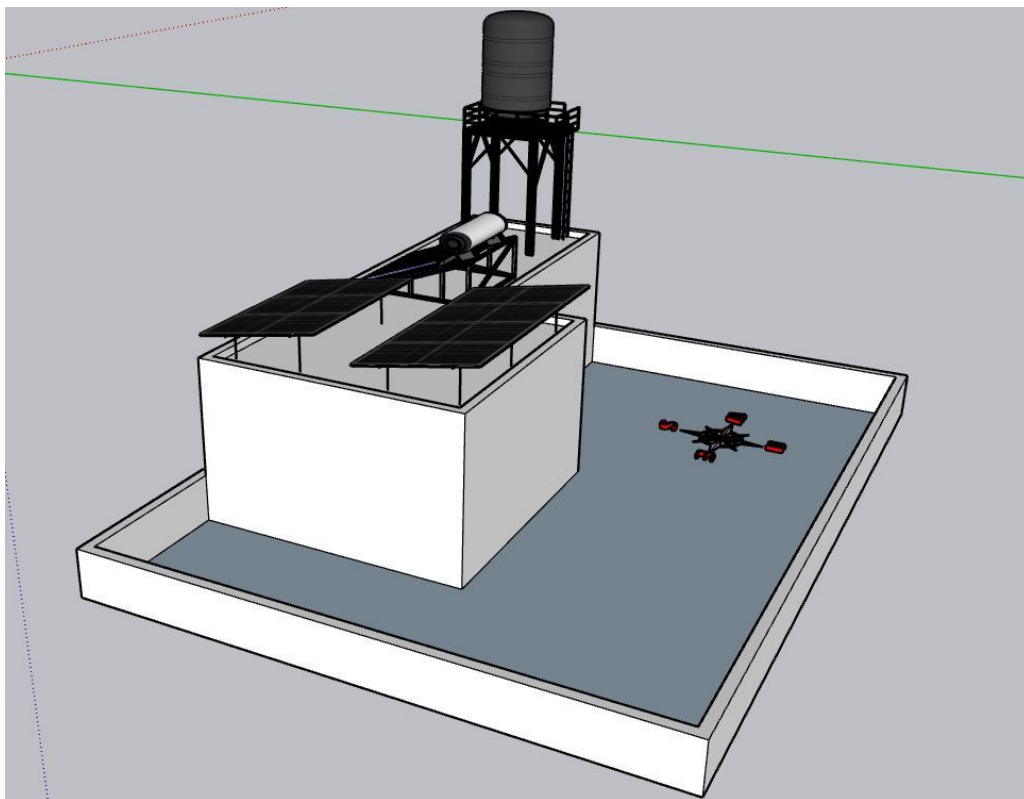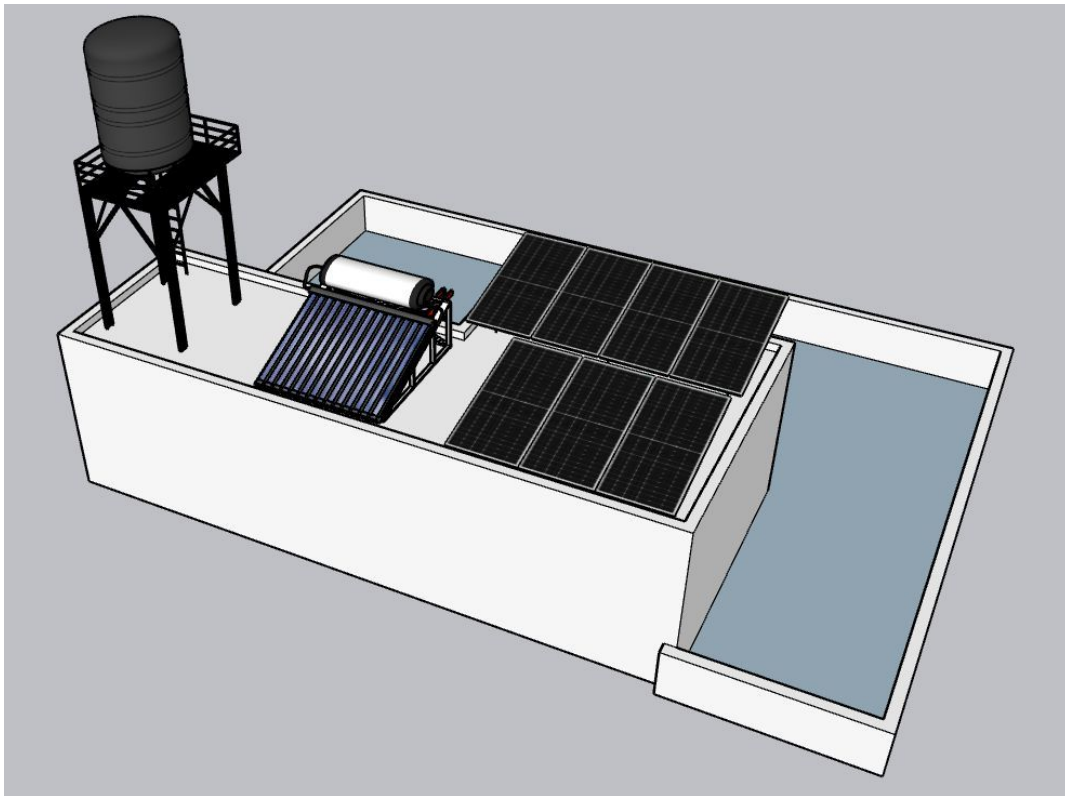

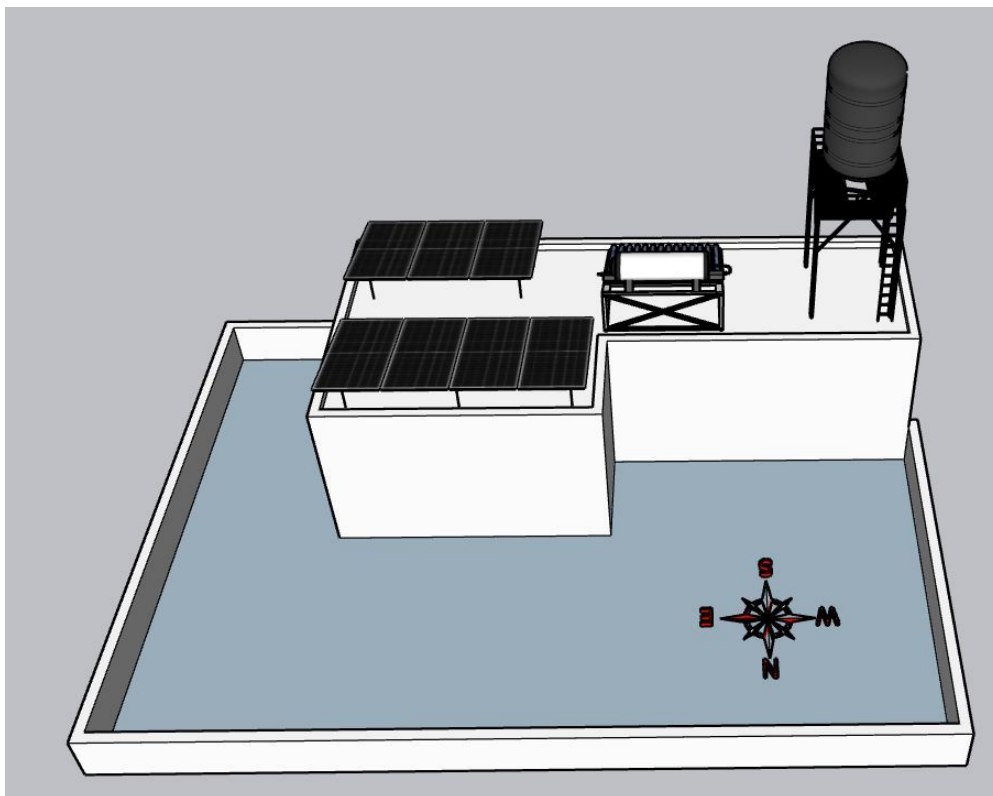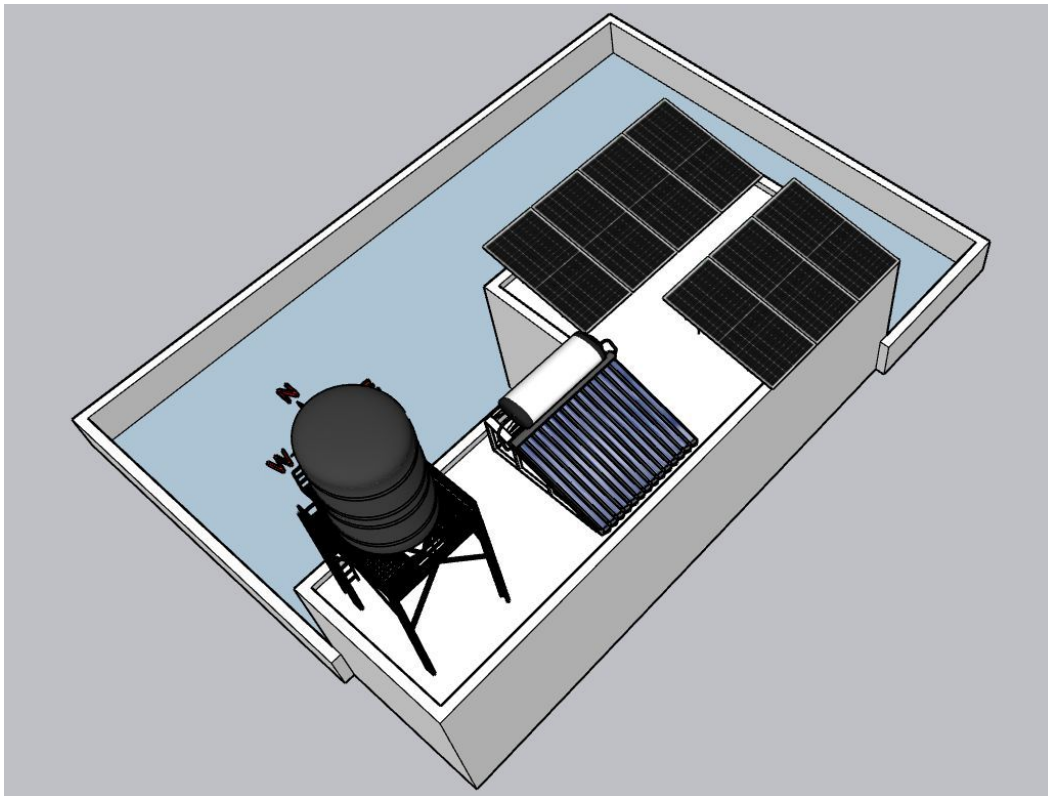

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



Follow the staircase until reaching the terrace floor.



The materials reaching the roof can be stacked here at the east side of the head room.

Staircase Details



Staircase width = 850mm

Material Storage




Proposed PV Area




Cable Routing



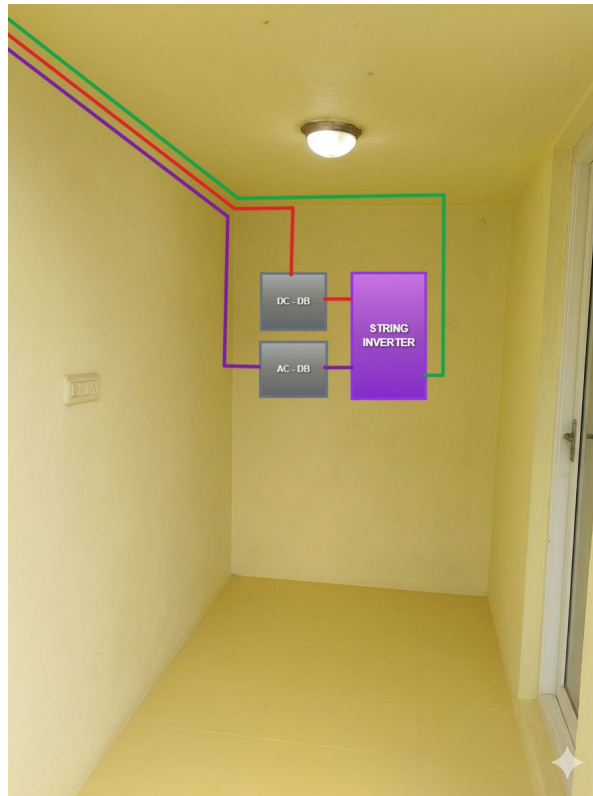





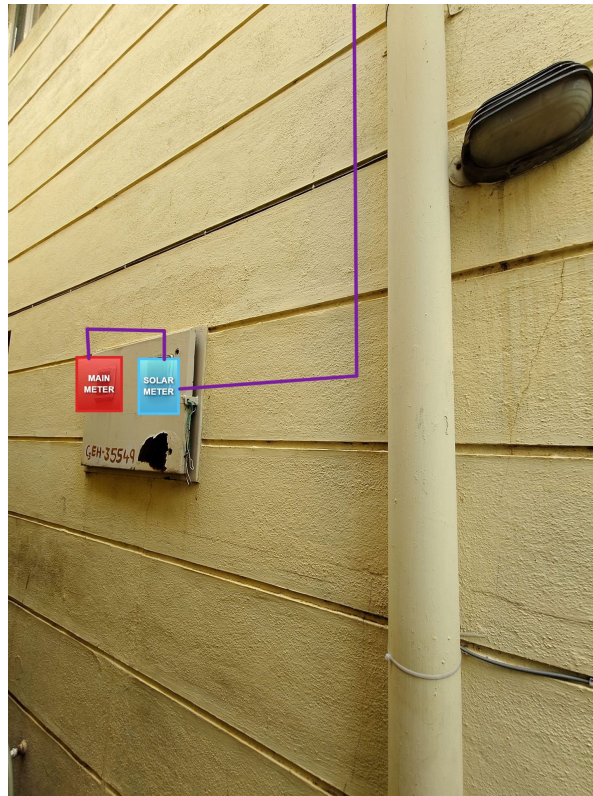

Meter Box





OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 4.3kWp, On-grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.
3	Removing/Relocating the HDGI structure (with 2 PV modules) that exists at the terrace, prior to the project's execution.
4	Relocating the solar water heater that exists at the terrace prior to the project's execution.

THANK YOU

Dear Sheshrao Eknath Shingote,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
