

Technical Site Visit Report

Prepared for: Adhesive specialities_Jigini, Chandapura_149.44kWp_Optimizer

PROJECT INFORMATION

Report Number	ESV-2026-0193
Project ID	83D63664
Project Name	Adhesive specialities_Jigini, Chandapura_149.44kWp_Optimizer
Project Sector	Industrial
Project Type	Without Subsidy
Sales Lead	Harsha Kuntur
Site Address	261/2, Vaddarapalya, Madapatna, Jigani Industrial Area 560105
GPS Coordinates	12.76795770748226, 77.64753776720406
Google Maps	https://www.google.com/maps?q=12.76795770748226,77.64753776720406
Visit Date	2026-08-27
Visited By	Charan P
Revision	Rev 1

CLIENT INFORMATION

Client Name	Adhesive Specialities
Contact	98450 29230

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	149.44
Sanction Load (kW)	288
Module Make & Capacity	Premier NON DCR Bi-facial and 615Wp
Module Length (mm)	2382
Module Width (mm)	1134

Number of Panels	243
Inverter Type	SolarEdge
Inverter Brand	SolarEdge 33.33kW - 3Ph with S1200 Optimizer
Number of Inverters	4
Number of Optimizers	122
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Near distribution panel	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, near the existing earth pits	-
6	Where is the Internet Router located?	Customer needs to provide	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	Puff sheet and plane sheet roof
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	-	Roof 1 with 6 degrees Roof 2 with 9 degrees
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	2	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Mini-rails	-
9	What is the orientation of the solar panels?	["South","North"]	-

#	Question	Answer	Notes
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	18m	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: HT	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Sealed	-
5	Is a Lightning Arrestor (LA) already available at the site?	Yes	-
6	Is space available for CT within Energy meter panel?	No	We have to provide additional box to mount Meter
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	20/1 A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	details: Extra care must be taken during installation, as the structure is a sheet roof at a height of 18 m.	-
15	Are there any safety risks associated with accessing the roof for installation?	Yes	-
16	Is space present in rooftop to store the panels?	No space	No space because it is a Sheet roof
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	No	-



#	Question	Answer	Notes
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 800	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 10000, width: 3000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout

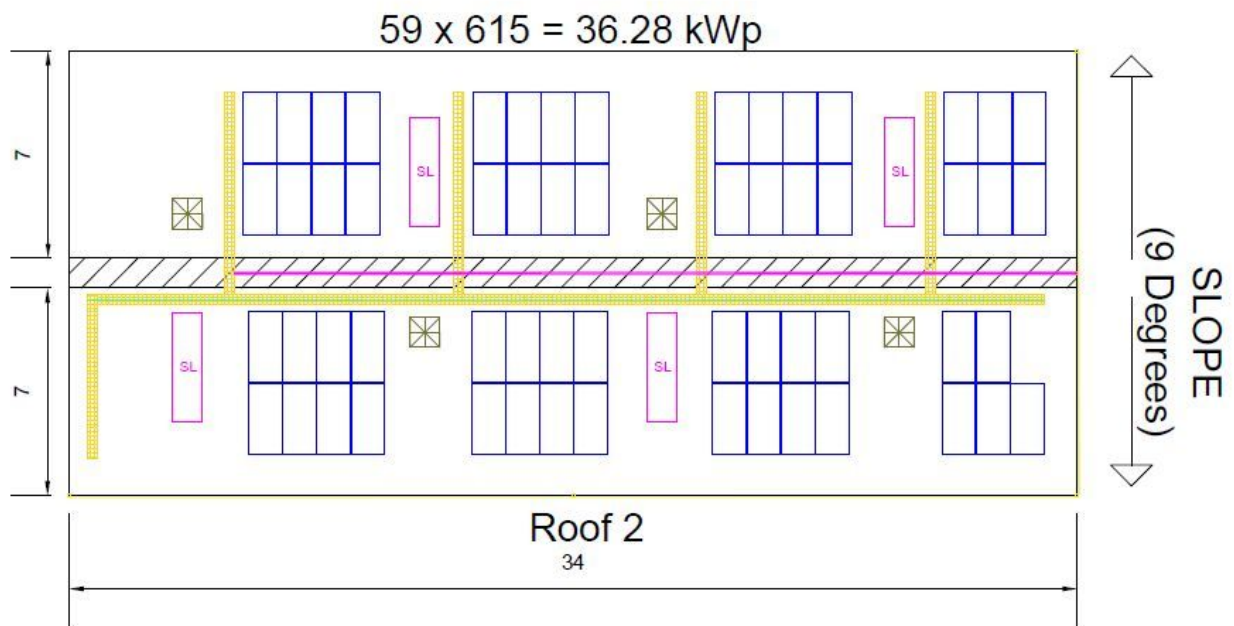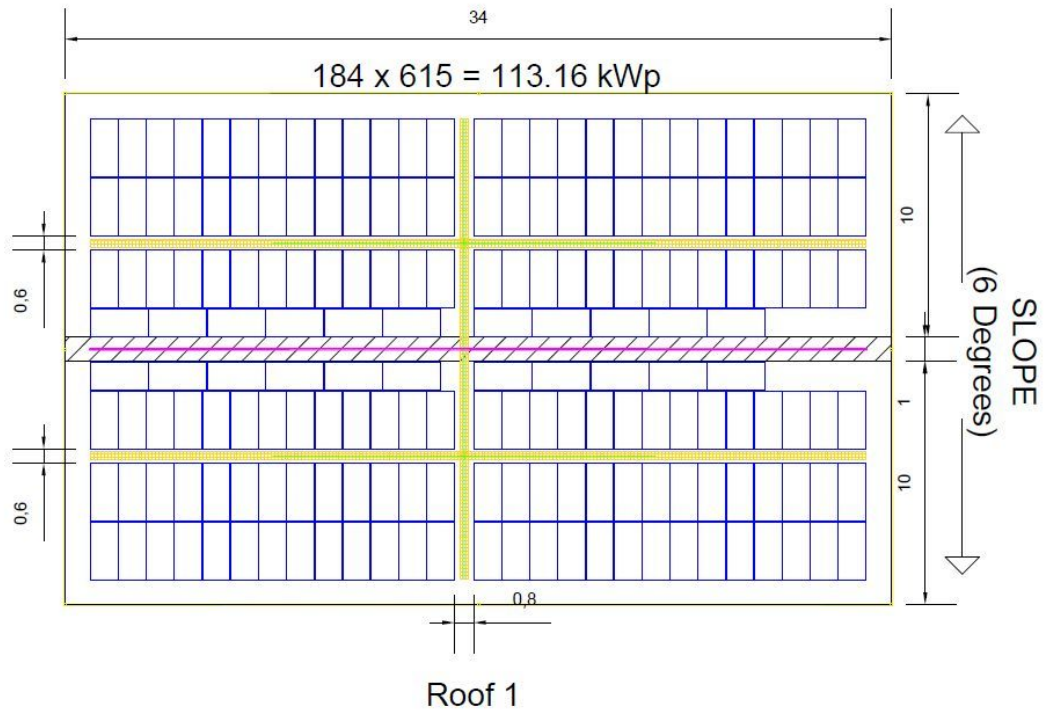

Building Exterior



Material Delivery Route





This route (using staircase) will be followed to carry small items.







This route (using side wall) will be followed to carry large items in Crane (like Panels) for roof 1.



This route (using side wall) will be followed to carry large items in Crane (like Panels) for roof 2.


Staircase Details





Material Storage



Proposed PV Area

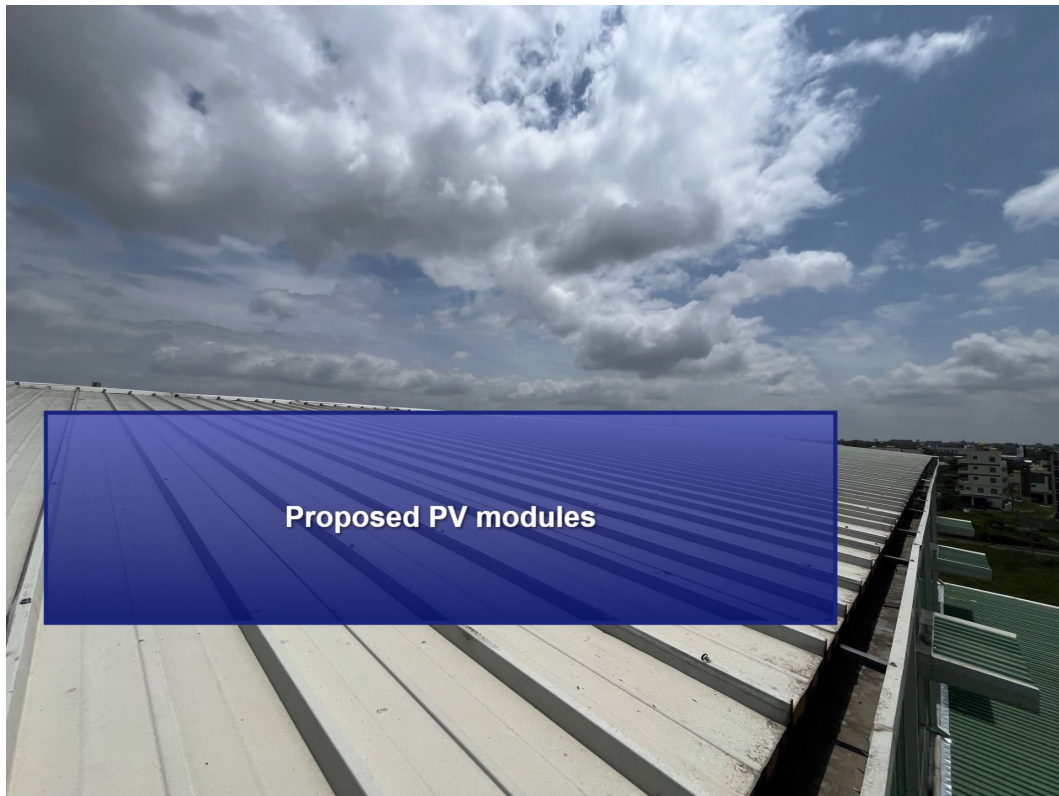


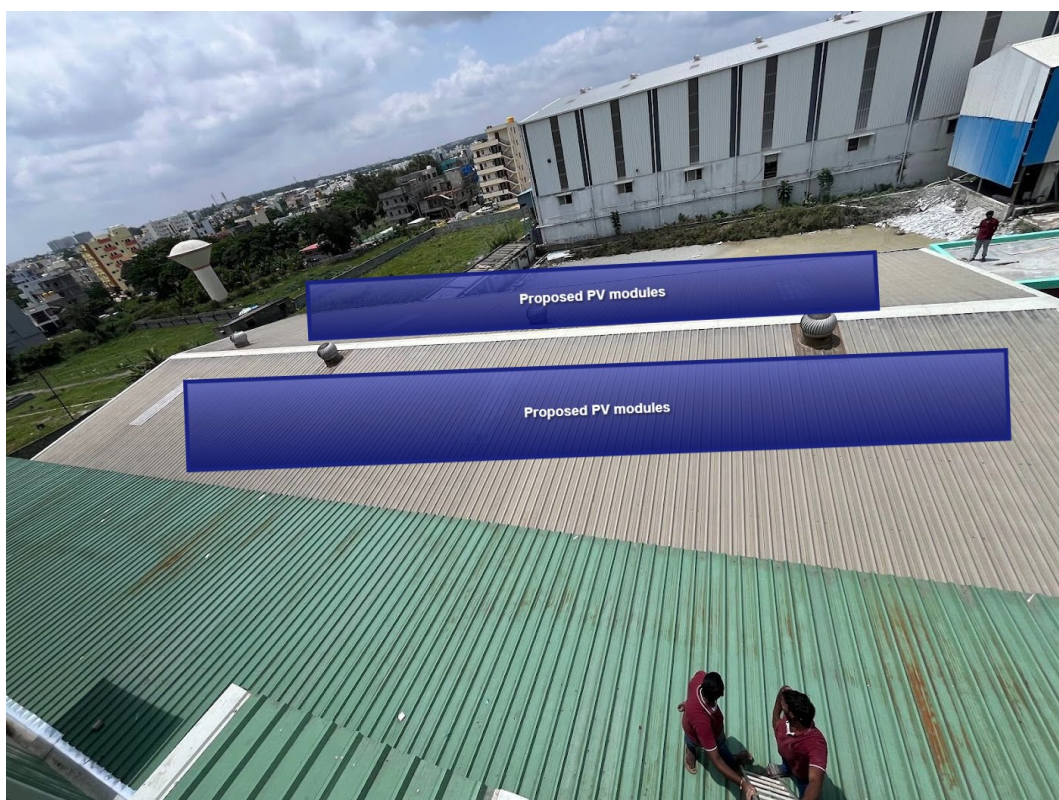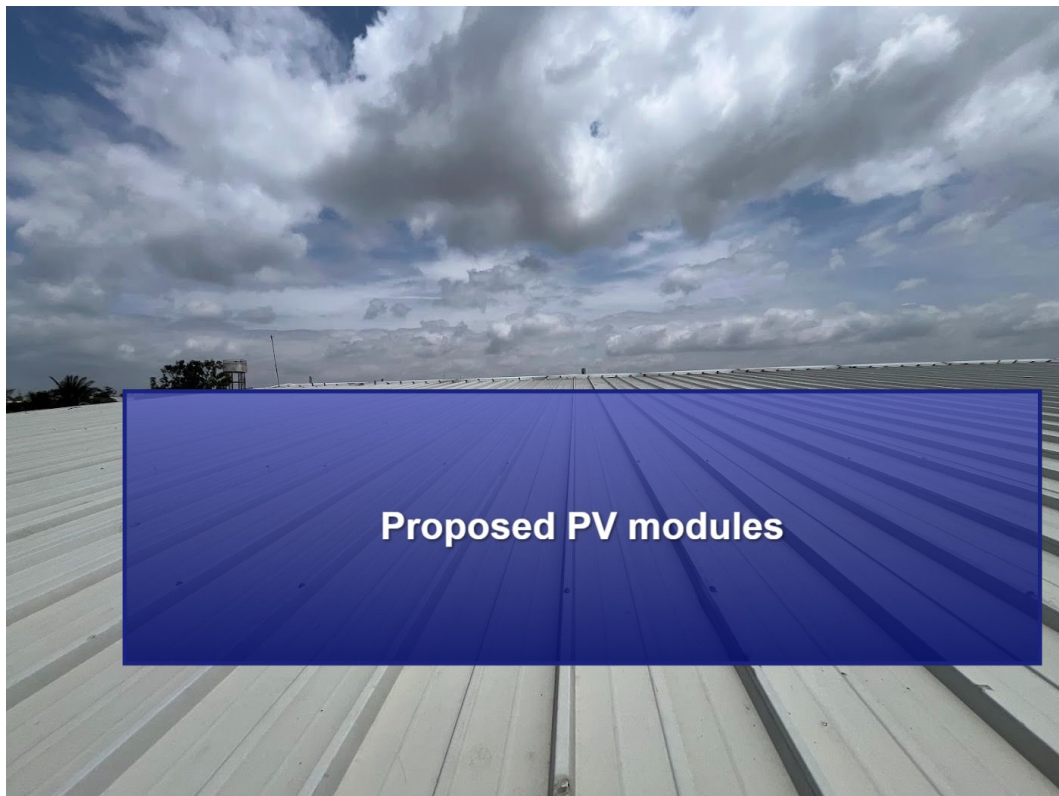


Cable Routing




We have to make 1 hole in the sheet to pass the DC cables

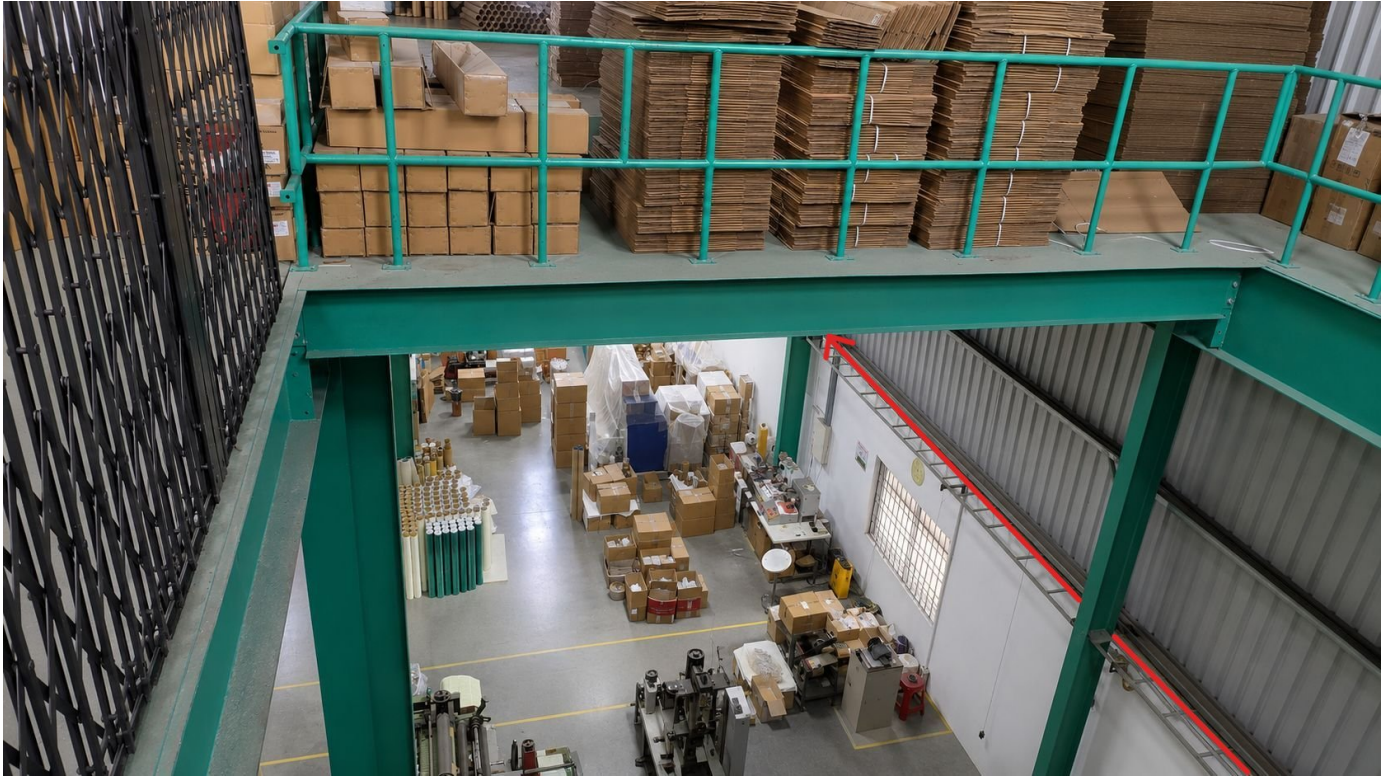



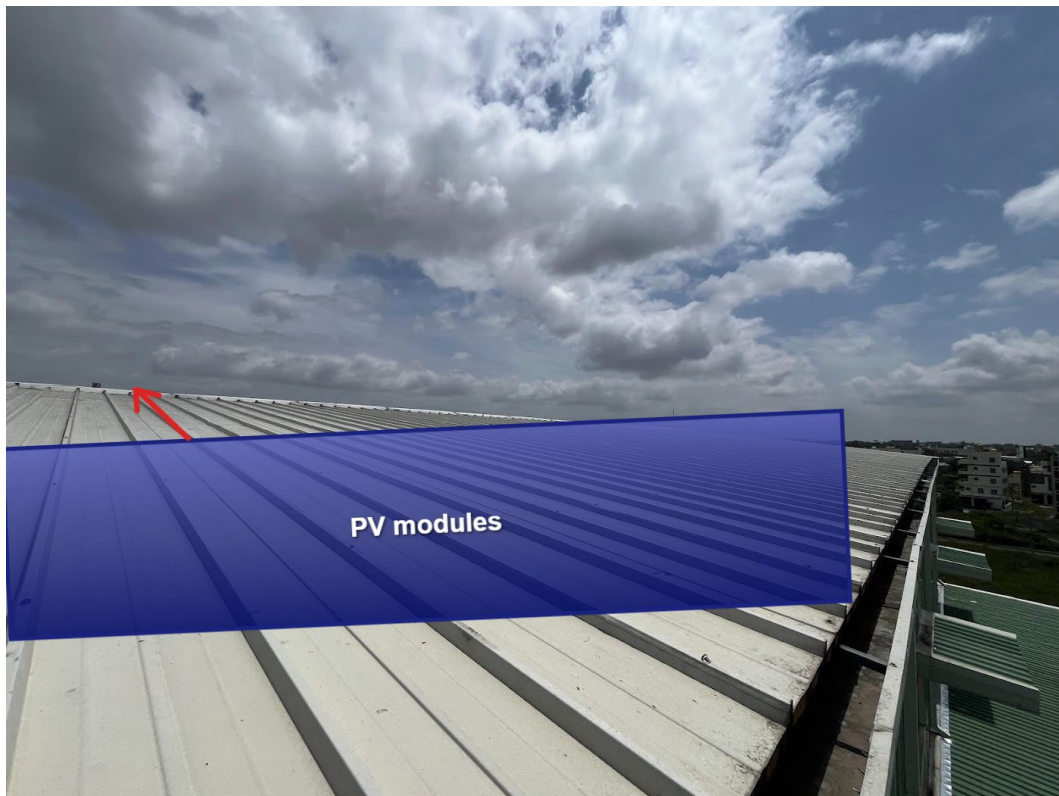

South slope

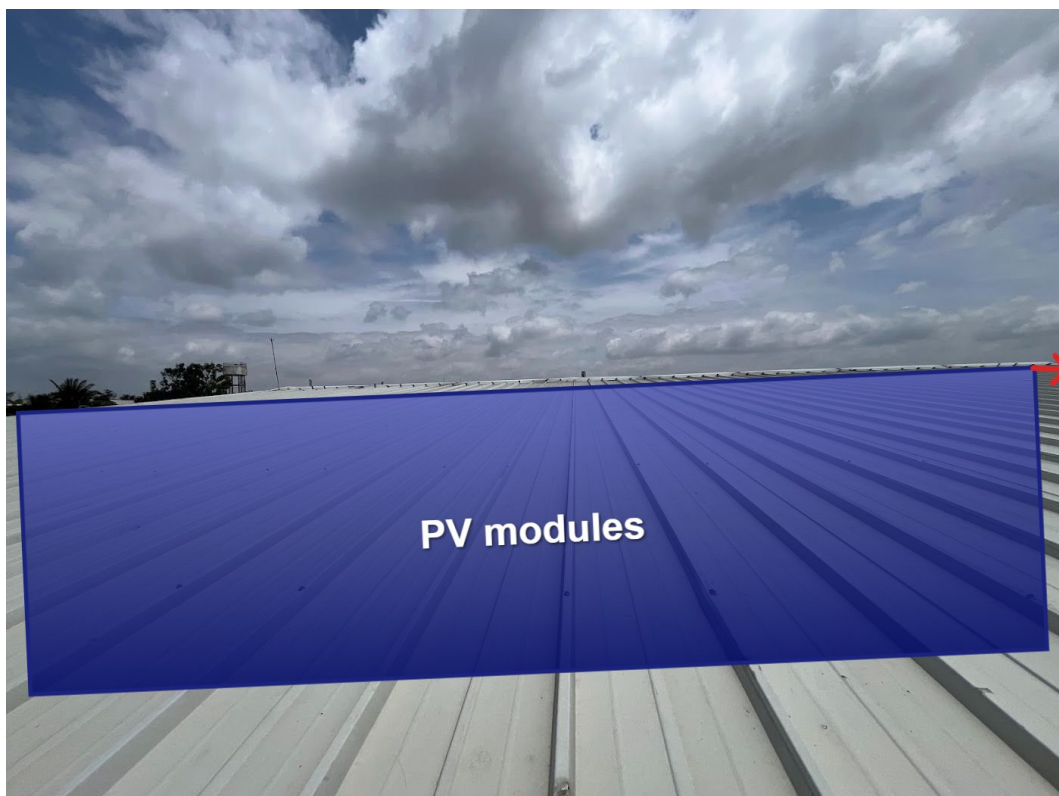

North slope







Cable will follow the trench.





We should takeout the cables from trench here.




LT Kiosk



Main meter



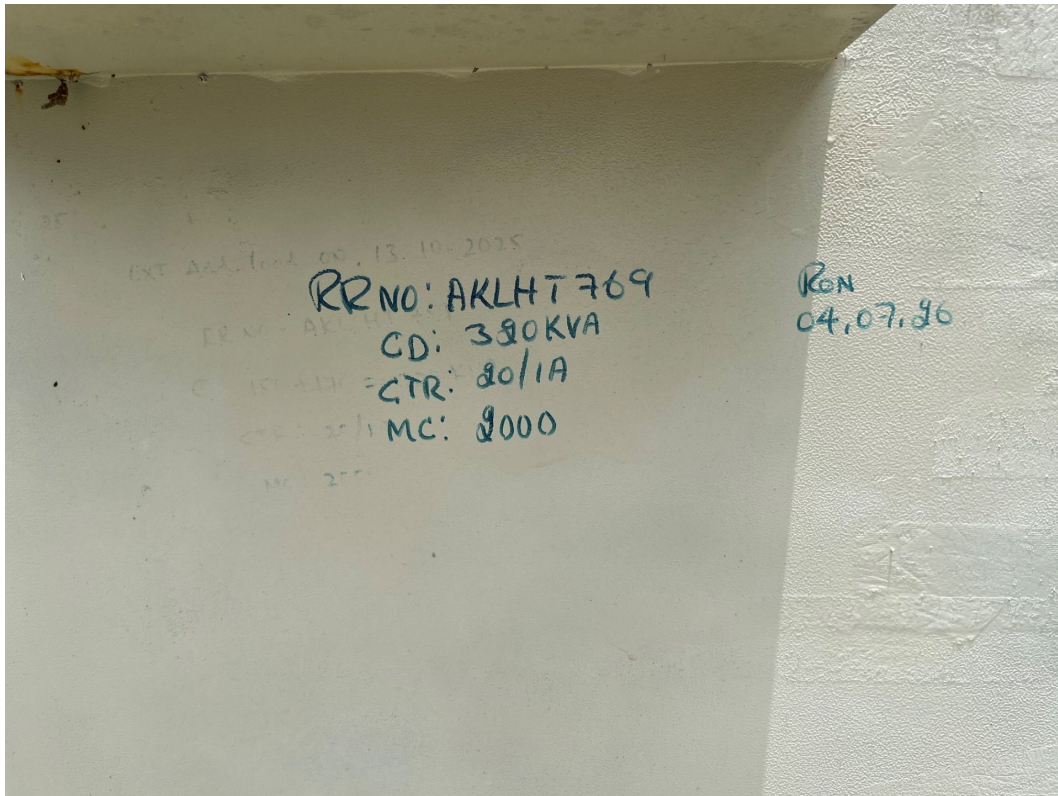



Earthing Routing







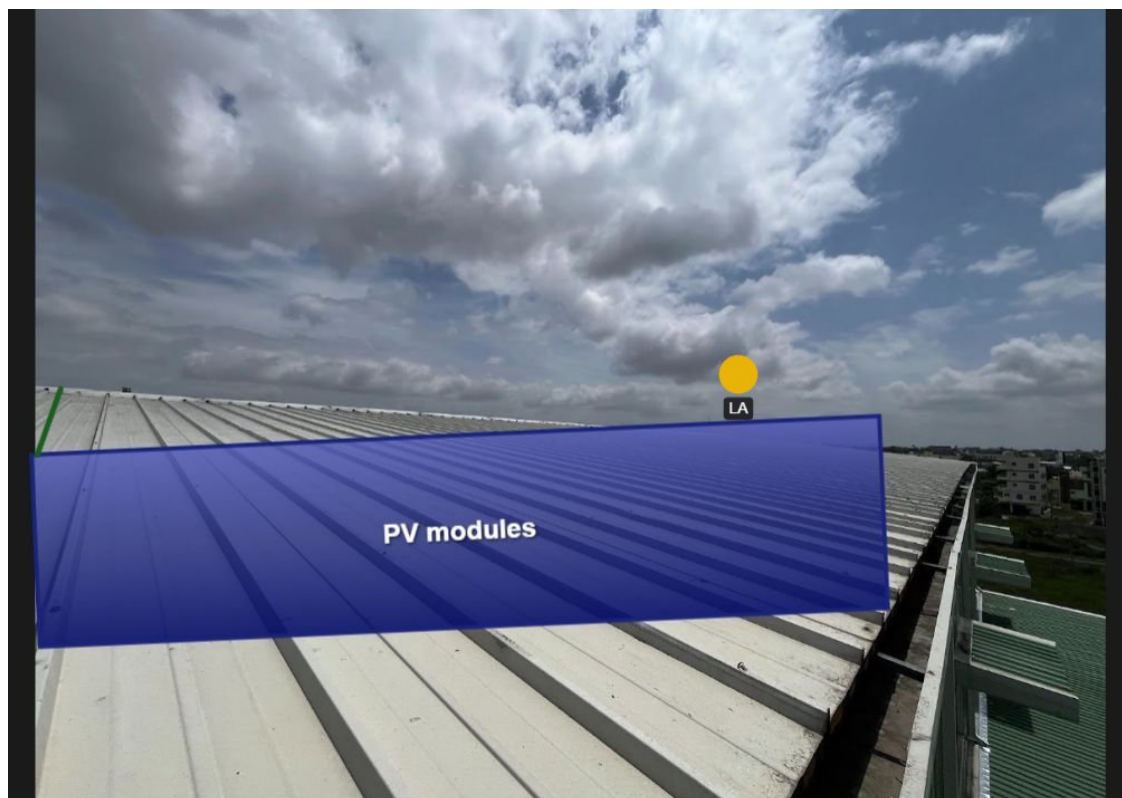

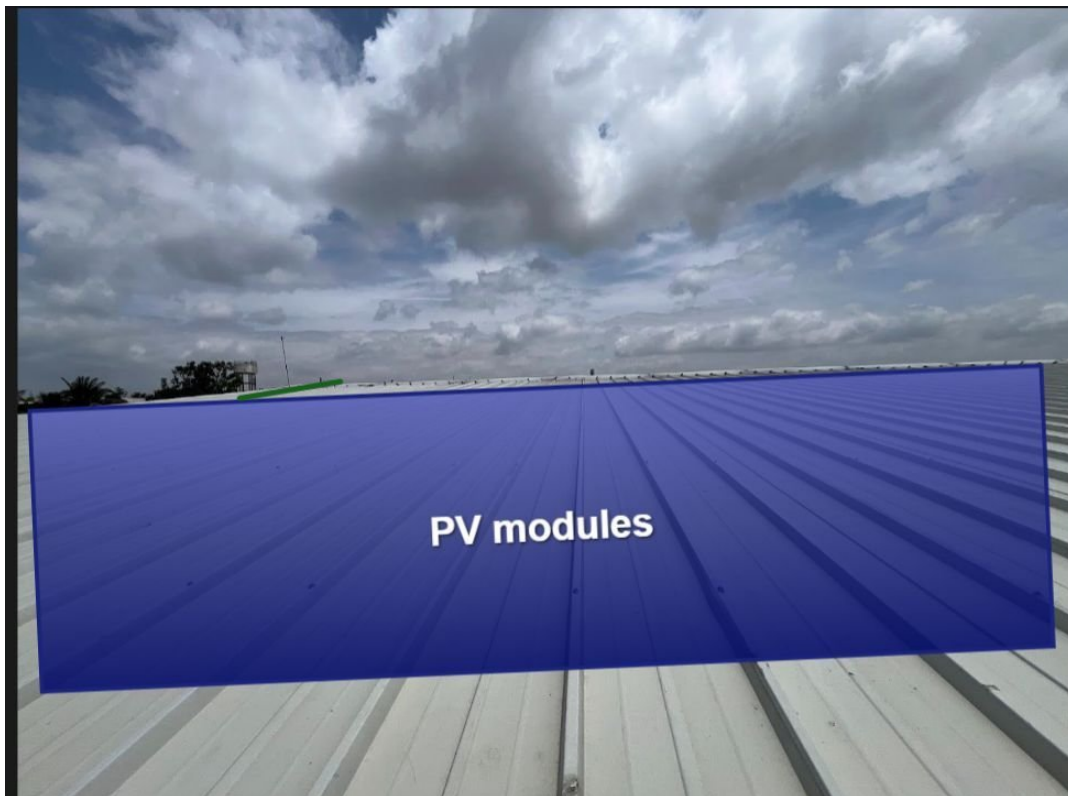



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Extra care must be taken during installation, as the structure is a sheet roof at a height of 18 m.
2	Roof 1 - 6 degrees with 330mm Pitch and Roof 2 - 9 degrees with 250mm Pitch

Customer Scope

#	Observation
1	Wi-Fi up to Inverter location.
2	Roof access is provided using the ladder.

THANK YOU

Dear Adhesive Specialities,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
