

Technical Site Visit Report

Prepared for: Prakash S M_Mango Acres_Subsidy_4.84kWp_Hybrid - #45, 13th Cross, Mango Acres

PROJECT INFORMATION

Report Number	ESV-2026-0176
Project ID	CE6DBA54
Project Name	Prakash S M_Mango Acres_Subsidy_4.84kWp_Hybrid
Building Name	#45, 13th Cross, Mango Acres
Billing Name	Prakash S M_Mango Acres_Subsidy_4.84kWp_Hybrid
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	#45, 13th Cross, Mango Acres S.Bingipura, Begur-Koppa Road Bengaluru – 560105, Karnataka.
GPS Coordinates	12.82235923813513, 77.62528958164499
Google Maps	https://www.google.com/maps?q=12.822359238135132,77.62528958164499
Visit Date	2026-07-20
Visited By	Sai
Revision	Rev 2

CLIENT INFORMATION

Client Name	Prakash S M
Contact	76761 34348

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	4.84
Sanction Load (kW)	5

Module Make & Capacity	Premier DCR bifacial 600 Wp
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	8
Inverter Type	Hybrid (String)
Inverter Brand	Feston 5kW 1 phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	5.12 kWh with 51.2V Lithium
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Inverter, DCDB, ACDB, Battery is located below the water tank	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Earth pits are located near the basement area.	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-

#	Question	Answer	Notes
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	MS Elevated structure
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	Height of the building is 13m; it has G+2+ Headroom	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	Building is under construction.
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	No	-
4	Is the Termination Point easily visible or sealed?	-	Building is under construction.
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	No	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	Building is under construction.
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	No	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-

#	Question	Answer	Notes
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Inverters/ACDB/DCDB be installed on a wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	-	<i>Building is under construction.</i>
21	Provide the dimension for earth pits location (L x W of available space).	length: 1000, width: 1000	<i>Building is under construction.</i>
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Building Exterior



Material Delivery Route





This route will carry the small items



This route will carry the large items (like panels)

Staircase Details




Meter Box




Material Storage




Site Layout - Top View

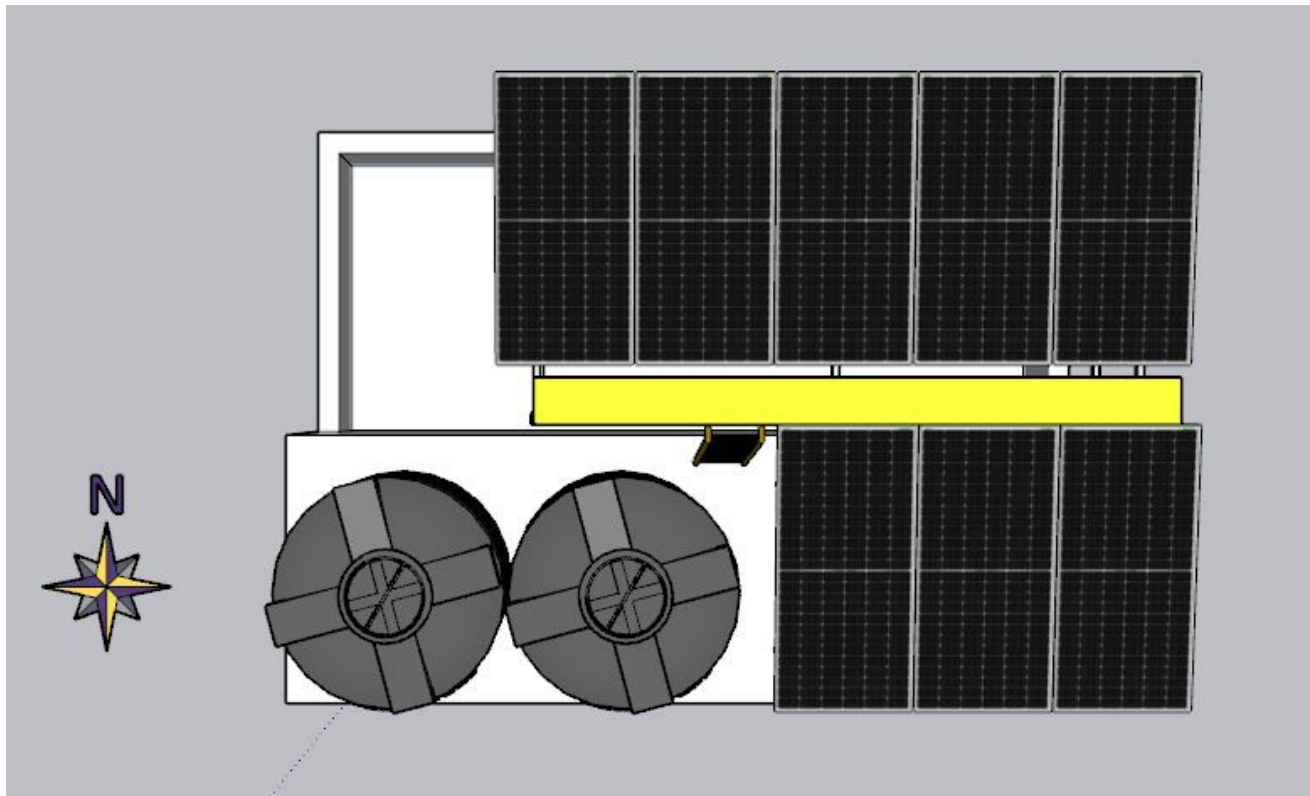

Top view

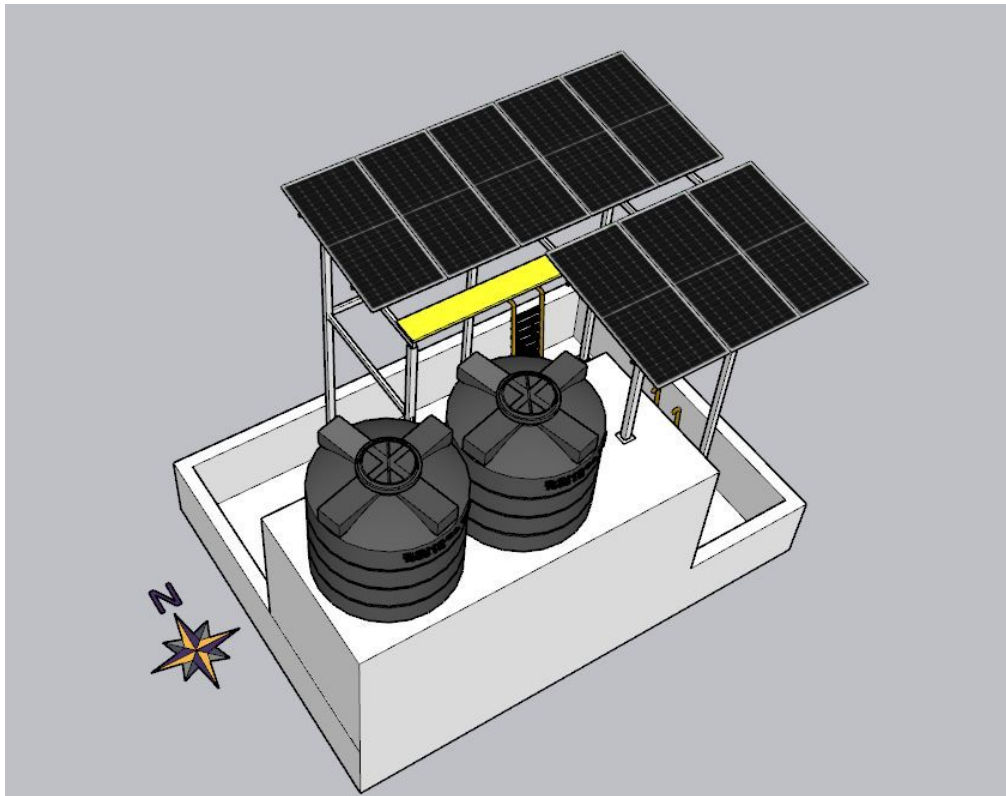

Side view (1)

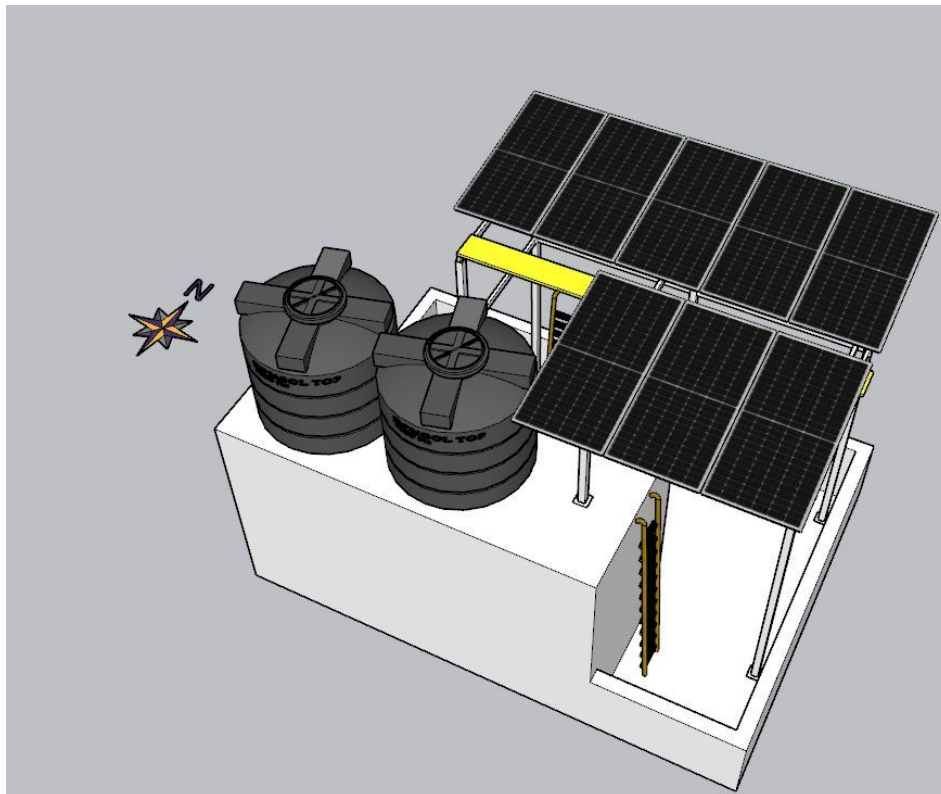

Side view (2)

Technical drawing of the 'Caja de la memoria' (Memory Box) showing its dimensions and components. The drawing includes a side elevation and a top-down view.


Side Elevation Dimensions:

- Total width: 5.74 m
- Total height: 4.31 m
- Top section height: 1.38 m
- Bottom section height: 1.50 m
- Top section segments (from left to right): 0.93 m, 1.01 m, 1.01 m, 1.01 m, 0.93 m
- Yellow rectangular panel width: 0.40 m


Top-down View Dimensions:

- Overall width: 3.44 m
- Two large circular components on the left.
- Smaller component on the right.


Page 10 of 18

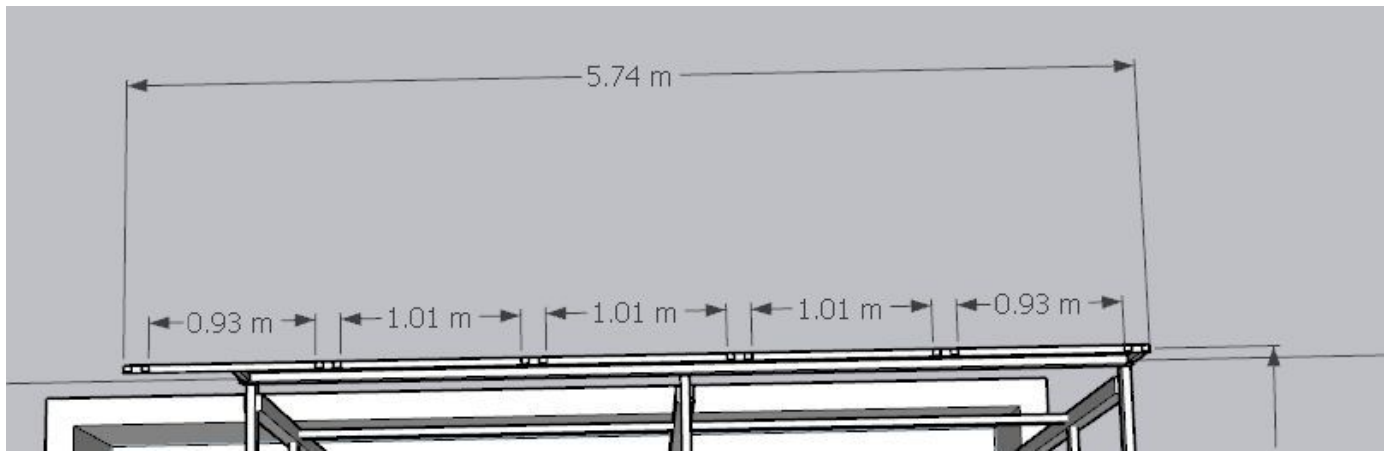


Structure details (3)




Structure details (4)

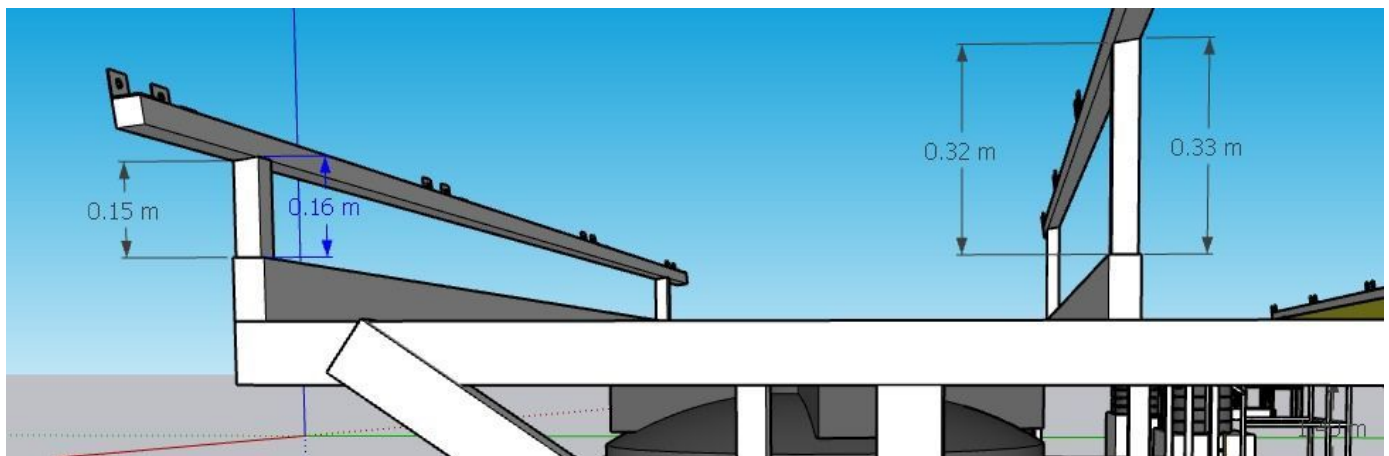

Structure details (5)

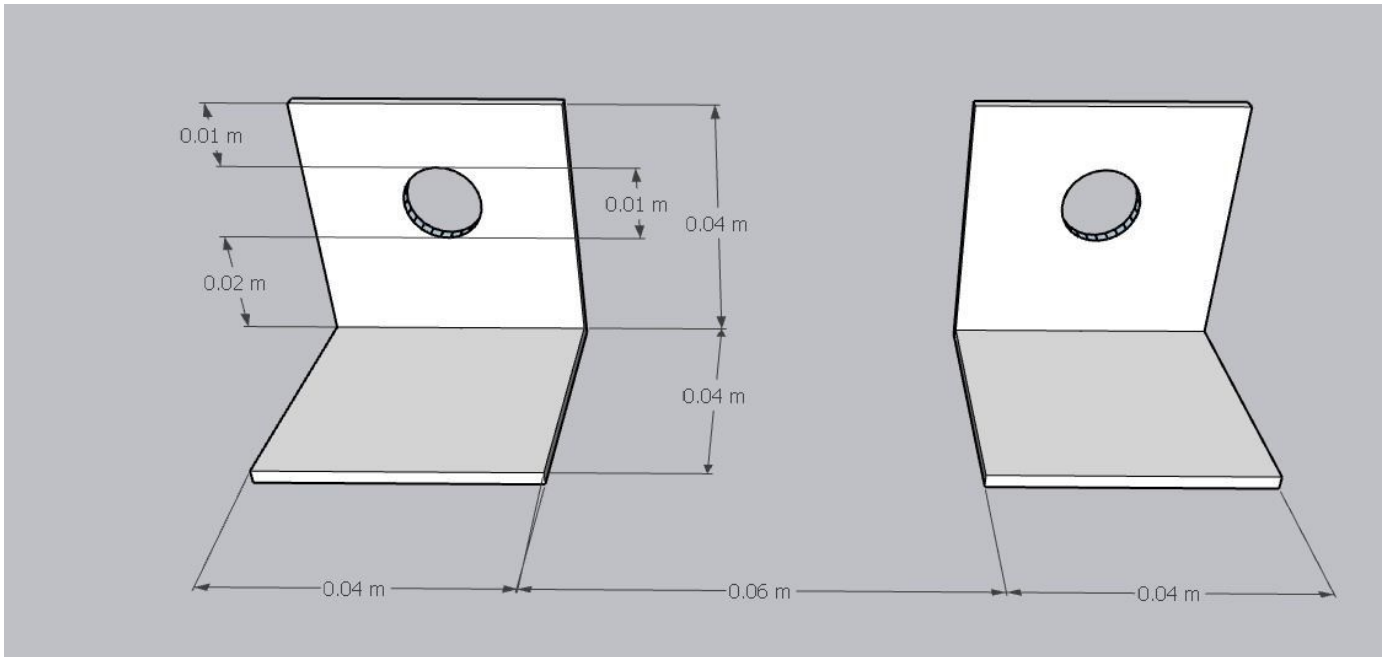


Structure details (6)

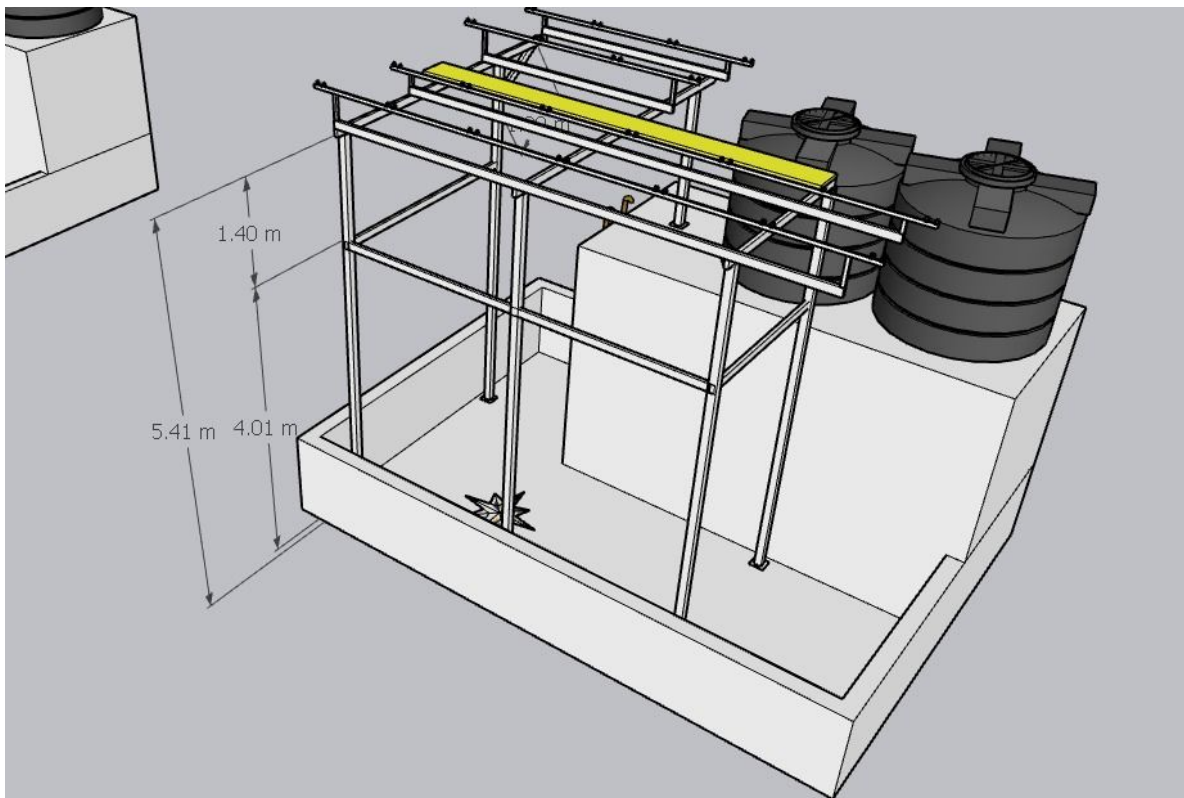


Structure details (7)




Structure details (8)

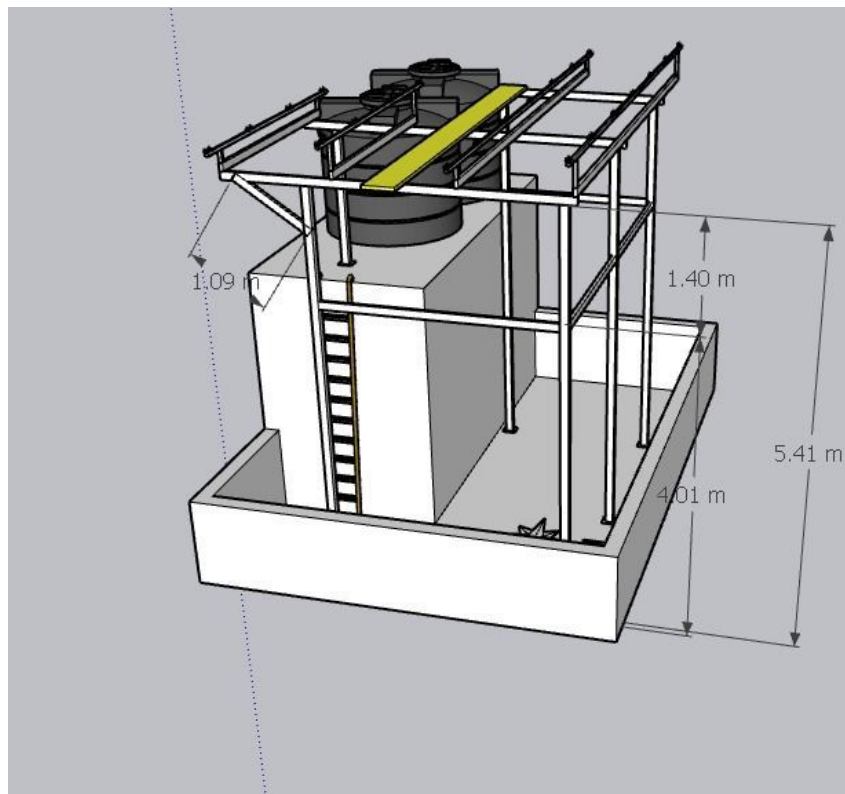

Structure details (9)

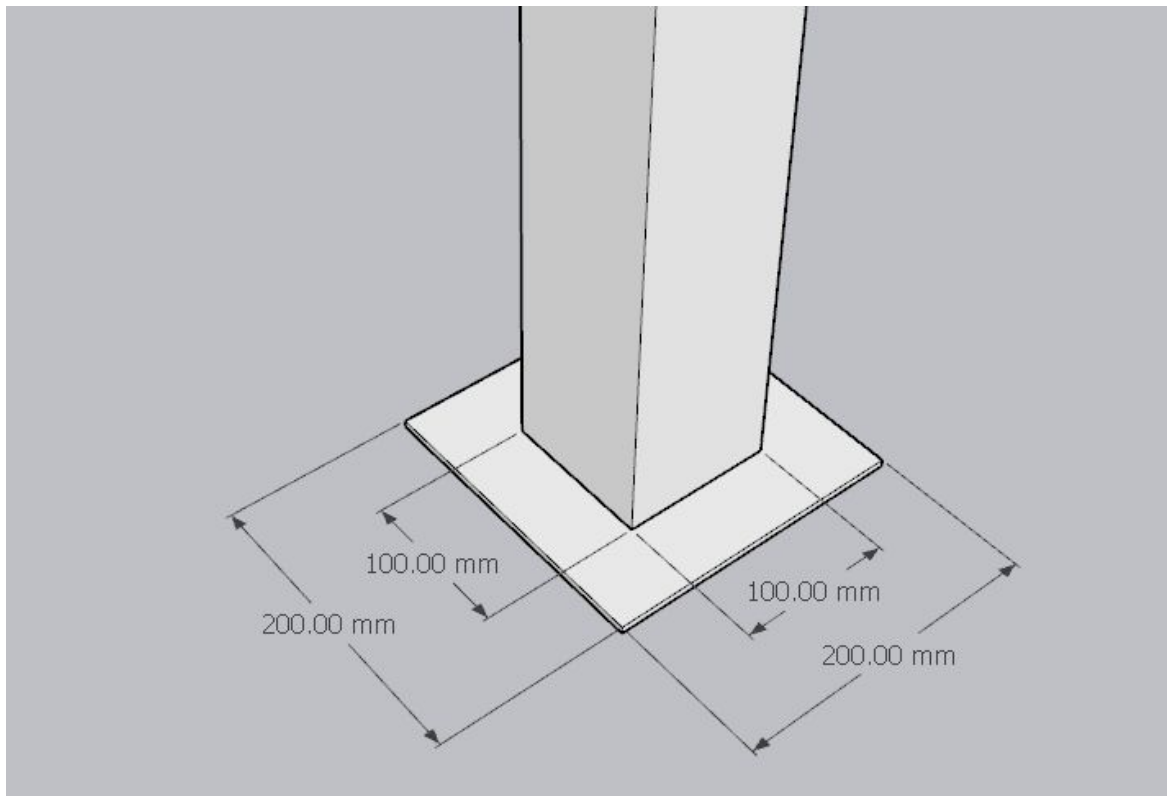

Structure details (10)

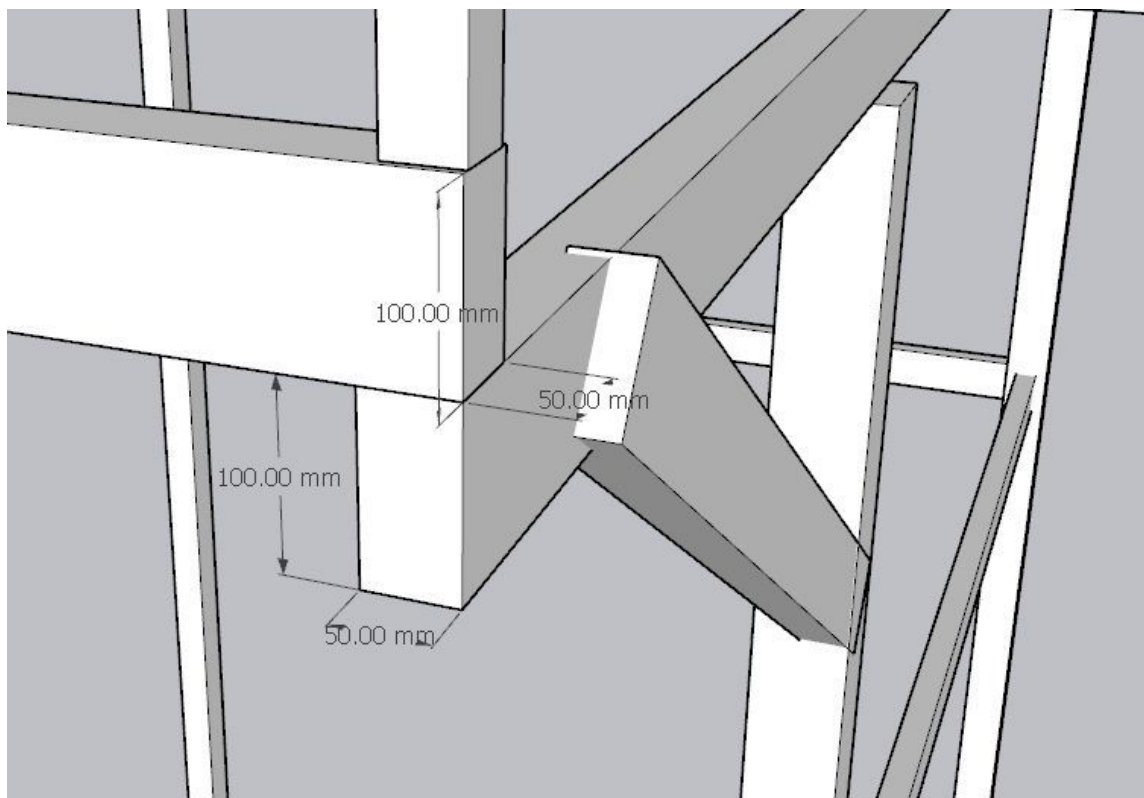

Structure details (11)

Proposed PV Area



Cable Routing



Equipment Location



Earth Pit Location





OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As per the Architect, civil engineer, electrician and also customer's suggestion, the routing, cable earthing, inverter location and also solar meter location have been considered.

Customer Scope

#	Observation
1	Wi-Fi is under customer scope
2	MS fabrication is under customer scope
3	UPS point is under customer scope

THANK YOU

Dear Prakash S M,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
