

## Technical Site Visit Report

Prepared for: Arun adoni\_#80, Prestige Ozone\_Subsidy\_3.60 kWp\_Microinverter (IQ Series) - Villa #80

### PROJECT INFORMATION

|                 |                                                                                                                       |
|-----------------|-----------------------------------------------------------------------------------------------------------------------|
| Report Number   | ESV-2026-0161                                                                                                         |
| Project ID      | 237FF55D                                                                                                              |
| Project Name    | Arun adoni_#80, Prestige Ozone_Subsidy_3.60 kWp_Microinverter (IQ Series)                                             |
| Building Name   | Villa #80                                                                                                             |
| Billing Name    | Arun adoni                                                                                                            |
| Project Sector  | Residential                                                                                                           |
| Project Type    | With Subsidy                                                                                                          |
| Sales Lead      | Mahantayya                                                                                                            |
| Site Address    | Arun adoni #80, Prestige Ozone Whitefiled main road Varturkodi, Banagluru- 560066                                     |
| GPS Coordinates | 12.9564335, 77.7487557                                                                                                |
| Google Maps     | <a href="https://www.google.com/maps?q=12.9564335,77.7487557">https://www.google.com/maps?q=12.9564335,77.7487557</a> |
| Visit Date      | 2026-07-28                                                                                                            |
| Visited By      | K Naveen                                                                                                              |
| Revision        | Rev 1                                                                                                                 |

### CLIENT INFORMATION

|             |             |
|-------------|-------------|
| Client Name | Arun adoni  |
| Contact     | 99860 46348 |

### PROJECT DETAILS

|                           |                          |
|---------------------------|--------------------------|
| Solar Rooftop System Type | On-Grid                  |
| System Capacity (kWp)     | 3.60                     |
| Sanction Load (kW)        | 6                        |
| Module Make & Capacity    | Premier DCR Bifacial 600 |

|                         |              |
|-------------------------|--------------|
| Module Length (mm)      | 2382         |
| Module Width (mm)       | 1133         |
| Number of Panels        | 6            |
| Inverter Type           | Micro        |
| Inverter Brand          | Enphase IQ8P |
| Number of Inverters     | 6            |
| Mounting Structure Type | Tiled Roof   |

## SITE INSPECTION CHECKLIST

### General

| # | Question                                                                   | Answer                                                                             | Notes                                                   |
|---|----------------------------------------------------------------------------|------------------------------------------------------------------------------------|---------------------------------------------------------|
| 1 | Can the delivery van/truck reach the material unloading point?             | Yes                                                                                | -                                                       |
| 2 | Are there any obstacles at the site that could hinder material lifting?    | details: Existing chajjas are the obstacles that could hinder the material lifting | -                                                       |
| 3 | Where will the Inverter, DCDB, ACDB, Battery, etc. be located?             | N/A                                                                                | -                                                       |
| 4 | Is a canopy required for protecting the Inverters/ACDB/DCDB?               | No                                                                                 | Canopy is required for protecting the Solar Accessories |
| 5 | Did you discuss the location of the earth pits with the customer?          | The earth pits are located rear side of the house which is near to the garden area | -                                                       |
| 6 | Where is the Internet Router located?                                      | Ground floor                                                                       | -                                                       |
| 7 | What's the Wi-Fi strength of the router near to the String inverter/Envoy? | 2 bars                                                                             | -                                                       |
| 8 | Did you pin the site location in your WhatsApp when you were at the site?  | Yes                                                                                | -                                                       |

### Roof Details

| # | Question                                                                         | Answer     | Notes                                          |
|---|----------------------------------------------------------------------------------|------------|------------------------------------------------|
| 1 | What type of roof is present at the site?                                        | Tiled Roof | -                                              |
| 2 | Are there any obstructions on the roof that could affect the solar installation? | No         | -                                              |
| 3 | What is the angle of the panels? (in degrees)                                    | 15         | -                                              |
| 4 | In case of sloped roof, what is the slope angle of the roof? (in degrees)        | 15         | -                                              |
| 5 | On how many roofs at the site are we installing solar?                           | 1          | Only one roof with existing multiple locations |
| 6 | If it is a Tiled roof, what is underneath the tiles?                             | RCC        | -                                              |

| #  | Question                                                                                                 | Answer                                                       | Notes                        |
|----|----------------------------------------------------------------------------------------------------------|--------------------------------------------------------------|------------------------------|
| 7  | If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?                     | N/A                                                          | -                            |
| 8  | What type of mounting structure is planned?                                                              | Other                                                        | Aluminum Full rail structure |
| 9  | What is the orientation of the solar panels?                                                             | ["East","West"]                                              | -                            |
| 10 | How can the roof be accessed?                                                                            | Ladder                                                       | -                            |
| 11 | Is the building currently under construction?                                                            | No                                                           | -                            |
| 12 | In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing? | N/A                                                          | -                            |
| 13 | What is the height of the building and how many floors does it have?                                     | The Height of the building is G+1 is approximately 10 meters | -                            |
| 14 | Is the site photo matching with the building description?                                                | Yes                                                          | -                            |
| 15 | Is there an overhead HT line passing within a 10-meter radius of the site?                               | No                                                           | -                            |

## Residential / Electrical

| #  | Question                                                                                                | Answer                                                                              | Notes                                          |
|----|---------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|------------------------------------------------|
| 1  | What type of energy meter is currently installed?                                                       | Phase: Three Phase, Type: Digital                                                   | -                                              |
| 2  | Is the Meter cubicle photo matching with the previous answer?                                           | Yes                                                                                 | -                                              |
| 3  | Has the termination point in the Main meter panel been identified?                                      | Yes                                                                                 | -                                              |
| 4  | Is the Termination Point easily visible or sealed?                                                      | Visible                                                                             | -                                              |
| 5  | Is a Lightning Arrestor (LA) already available at the site?                                             | No                                                                                  | -                                              |
| 6  | Is space available for CT within Energy meter panel?                                                    | No                                                                                  | -                                              |
| 7  | In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m? | Less than 50m                                                                       | -                                              |
| 8  | Provide details of the existing CT ratings (if applicable).                                             | N/A                                                                                 | -                                              |
| 9  | In Main meter panel, is empty space available for solar meter?                                          | No                                                                                  | -                                              |
| 10 | In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?      | No                                                                                  | -                                              |
| 11 | Is there space available to dig DC, AC and LA earth pits?                                               | Yes                                                                                 | Space is available to dig the DC,LA earth pits |
| 12 | In case of elevated structures, is an LA extension provided at the far end?                             | Yes                                                                                 | -                                              |
| 13 | In case of elevated structures, is it with or without grouting?                                         | N/A                                                                                 | -                                              |
| 14 | Are there any challenges with respect to Installation and Maintenance activities?                       | details: The existing roof is nearly about 15 degree slope to installing the panels | -                                              |
| 15 | Are there any safety risks associated with accessing the roof for installation?                         | details: There is a conjusted space to accessing the roof                           | -                                              |

| #  | Question                                                                                          | Answer                       | Notes |
|----|---------------------------------------------------------------------------------------------------|------------------------------|-------|
| 16 | Is space present in rooftop to store the panels?                                                  | No space                     | -     |
| 17 | In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin. | N/A                          | -     |
| 18 | Is ventilation available in the battery location?                                                 | N/A                          | -     |
| 19 | Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?                       | N/A                          | -     |
| 20 | Provide the dimensions for solar meter cubicle placement (L x W of wall).                         | length: 1500,<br>width: 1500 | -     |
| 21 | Provide the dimension for earth pits location (L x W of available space).                         | length: 500,<br>width: 1500  | -     |
| 22 | Is LAN cable under customer scope?                                                                | No                           | -     |
| 23 | Is there any shadow that affects the solar installation?                                          | No                           | -     |
| 24 | Is there any trench work to be done to carry the AC cable to the meter location?                  | No                           | -     |

## PHOTO DOCUMENTATION

### Cable Routing Legend

| Legend                                                                              | Description              |
|-------------------------------------------------------------------------------------|--------------------------|
|  | Proposed PV Module Array |
|  | Main Meter Location      |
|  | Solar Meter              |
|  | Battery                  |
|  | Inverter                 |
|  | Other Equipment          |
|  | DC Cable                 |
|  | AC Cable                 |
|  | Material Shifting        |
|  | DC Earthing Cable        |
|  | AC Earthing Cable        |
|  | LA Cable                 |
|  | DC Earth Pit             |
|  | AC Earth Pit             |
|  | LA Pit                   |
|  | LA                       |

### Material Delivery Route





*This route (using lifting) will be followed to carry large items (like Panels). and small items*










## Staircase Details



### Meter Box

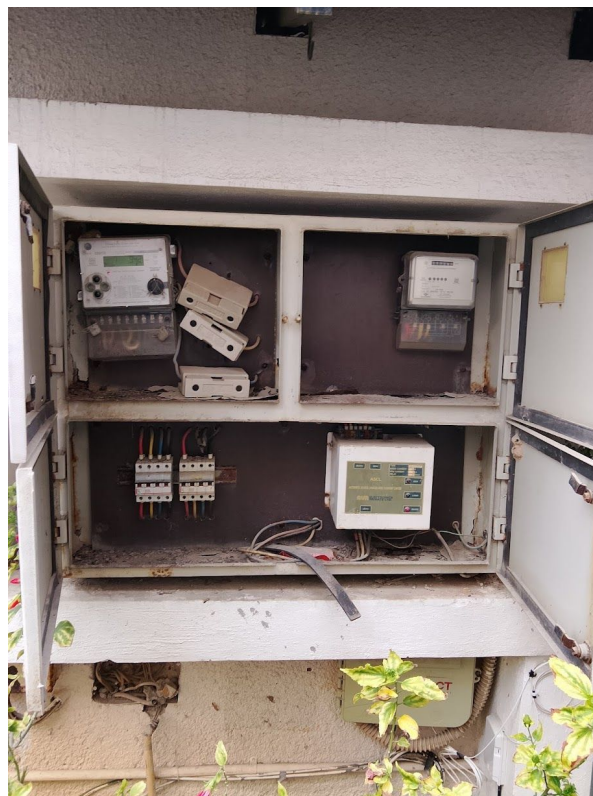



## Material Storage



## Proposed PV Area







## Cable Routing












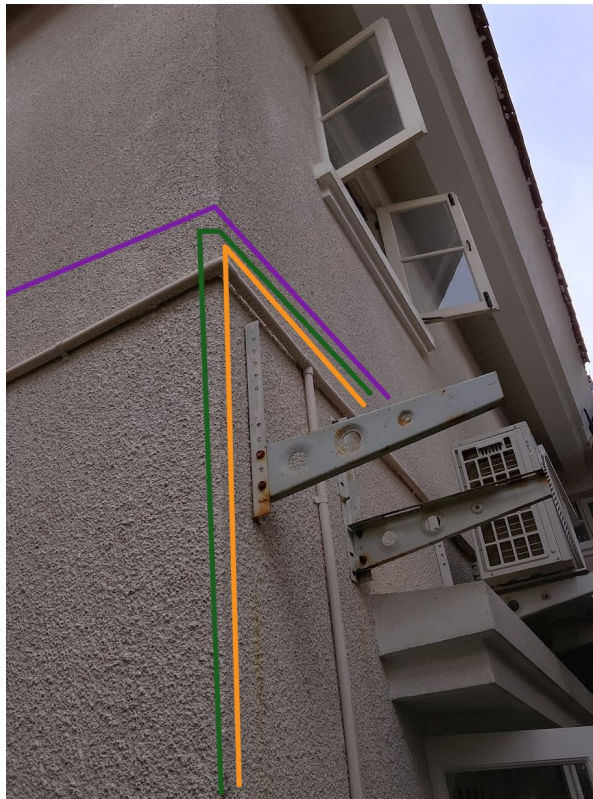



*Make a hole to run the AC cable till the meter location.*












## Equipment Location

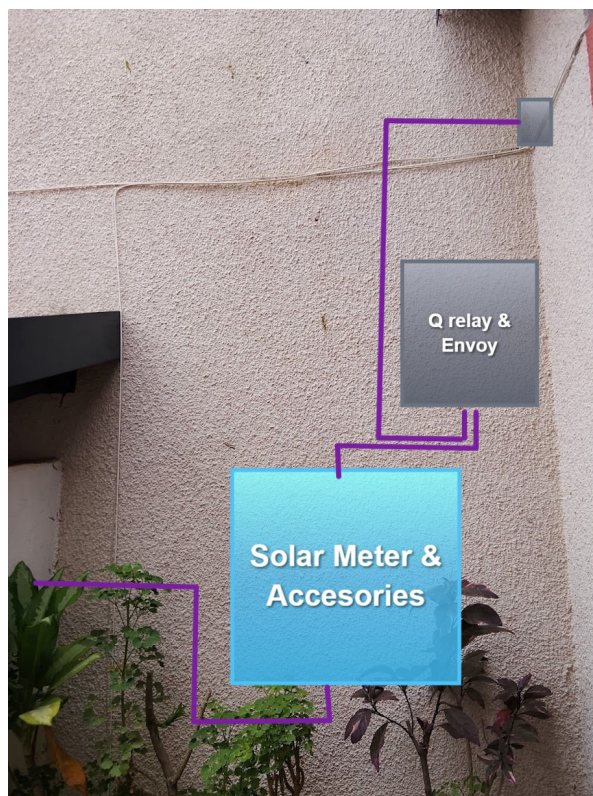


*Canopy is required for protecting solar meter*




#### Earth Pit Location







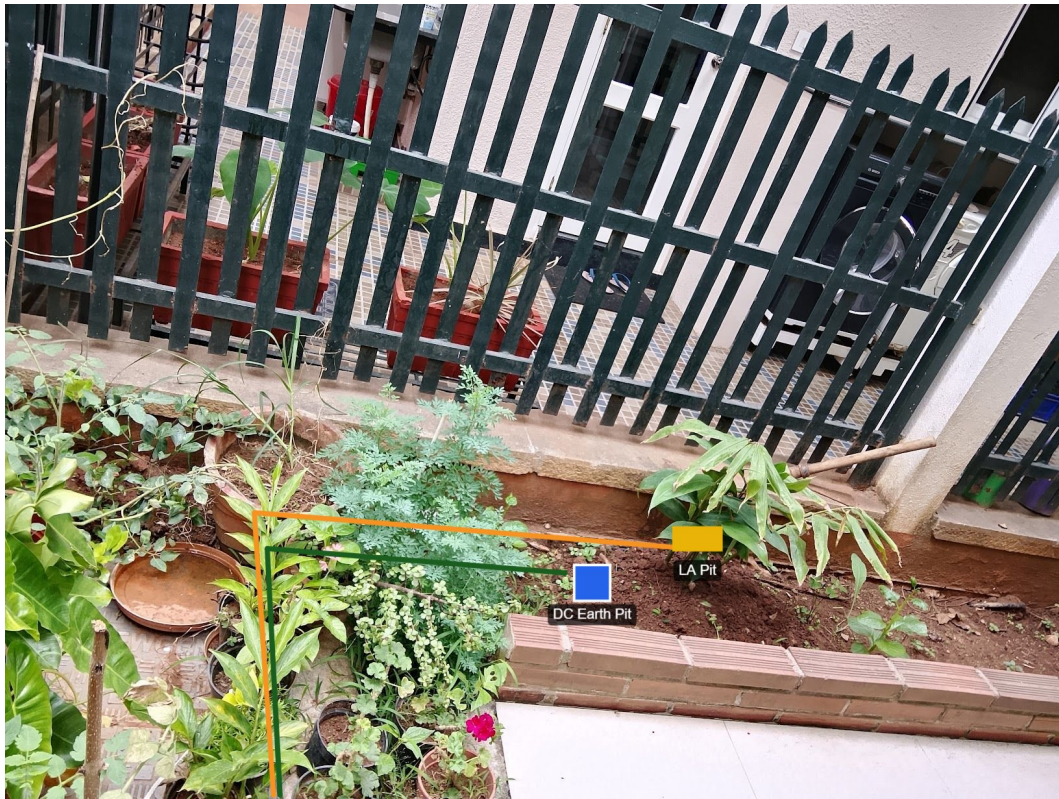

### Site Layout - Top View

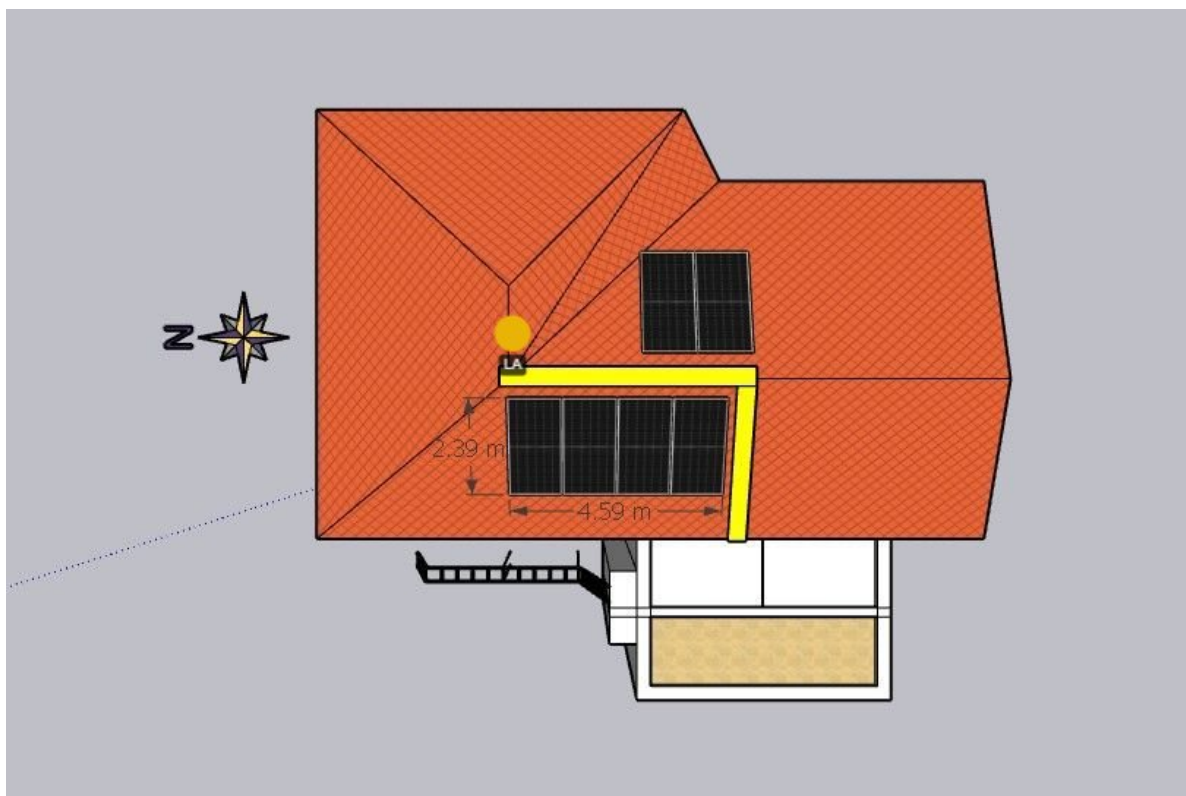

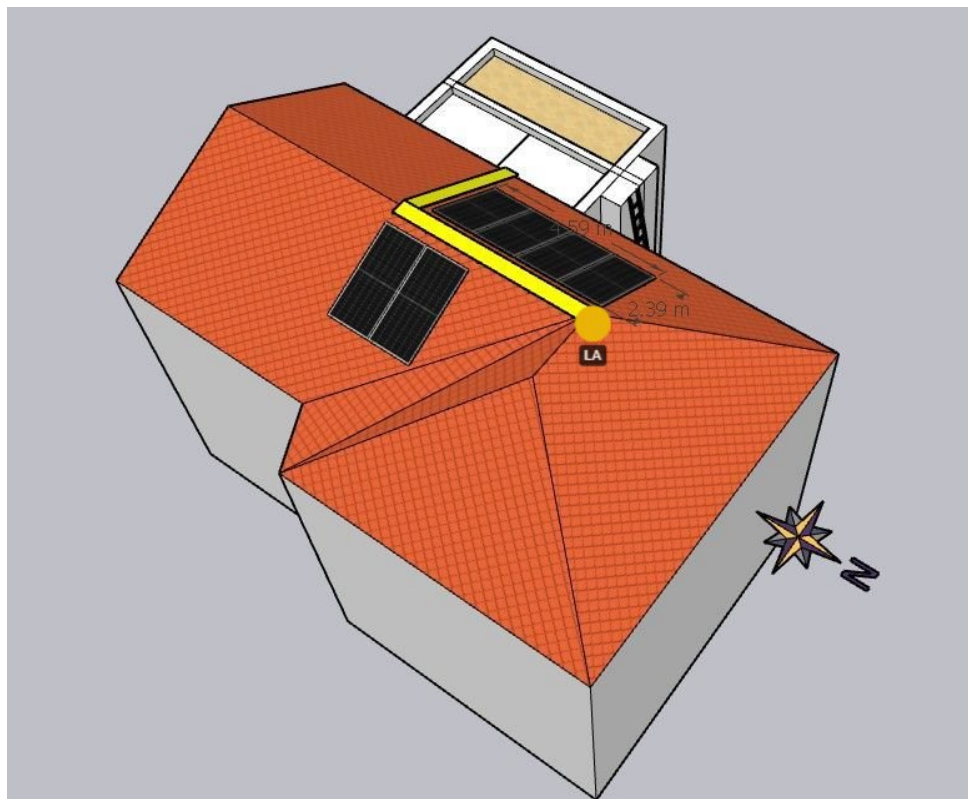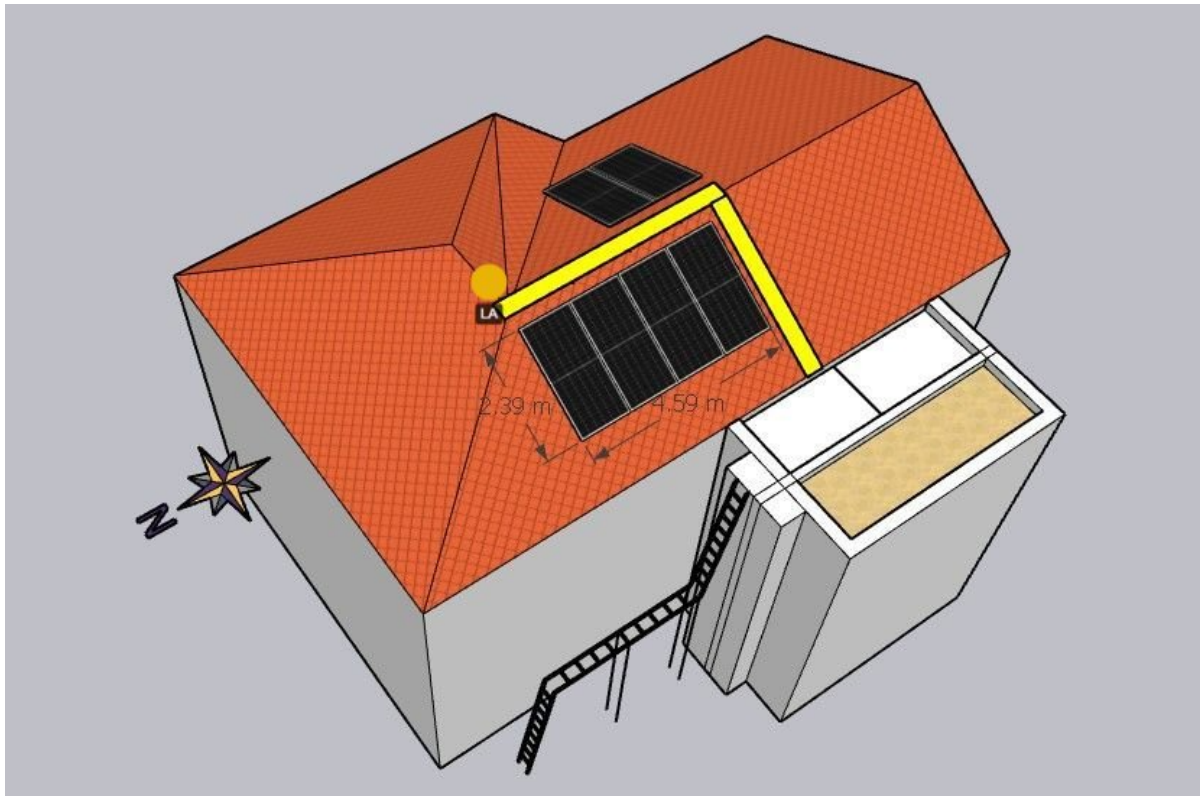

## Building Exterior





## OBSERVATIONS & RECOMMENDATIONS

### Customer Scope

| # | Observation                                                                                                        |
|---|--------------------------------------------------------------------------------------------------------------------|
| 1 | Wi-Fi up to the solar meter location is under customer scope.                                                      |
| 2 | MS walkway is under customer scope.                                                                                |
| 3 | Canopy is required for protecting the solar meter is under customer scope.                                         |
| 4 | Remove flower pots near the solar meter location is under customer scope, to avoid the installation disturbances.. |
| 5 | As per the customer suggestions only the panel layout,earthing,cable routing has been considered.                  |

## THANK YOU

Dear Arun adoni,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,  
**Team EcoSoch**

### & Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

**EcoSoch Solar Pvt. Ltd.**

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

[www.ecosoch.com](http://www.ecosoch.com) | [info@ecosoch.com](mailto:info@ecosoch.com)
