

Technical Site Visit Report

Prepared for: Dr.Sharad Nadig (rekha)_HSR_3.72kWp_Optimizer

PROJECT INFORMATION

Report Number	ESV-2026-0117
Project ID	FAAC2C41
Project Name	Dr.Sharad Nadig (rekha)_HSR_3.72kWp_Optimizer
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Hariom
Site Address	392, First Floor , 28 th main HSR layout Bangalore 560102
GPS Coordinates	12.918613, 77.652191
Google Maps	https://www.google.com/maps?q=12.918613,77.652191
Visit Date	2026-05-14
Visited By	ABILASH N K
Revision	Rev 1

CLIENT INFORMATION

Client Name	Dr.Sharad Nadig (rekha)
Contact	8431013653

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	3.72
Sanction Load (kW)	4
Module Make & Capacity	Adani DCR Bi-facial, 620 Wp
Module Length (mm)	2382
Module Width (mm)	1133

Number of Panels	6
Inverter Type	SolarEdge
Inverter Brand	SolarEdge 4kW-1 phase Optimizer
Number of Inverters	1
Number of Optimizers	6
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Ground floor, Wall mounted (Near the existing EB meter)	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	Yes	-
5	Did you discuss the location of the earth pits with the customer?	Yes. Discussed and finalized.	-
6	Where is the Internet Router located?	Ground floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	2 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: Terrace have uneven heights. Skylights available in the terrace floor. It might obstruct when positioning the structure lug base.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-

#	Question	Answer	Notes
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	<i>An elevated MS structure is mandatory for this site.</i>
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	12 metres (G + 3)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital, If 3-phase: N/A	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>The thick base floor has to be core cut</i>
12	In case of elevated structures, is an LA extension provided at the far end?	Not Applicable	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	details: Due to the limited space of the staircase, lifting the PV modules and structural materials requires careful attention from skilled labor.	-
15	Are there any safety risks associated with accessing the roof for installation?	details: Due to the limited space of the staircase, lifting the PV	-



#	Question	Answer	Notes
		modules and structural materials requires careful attention from skilled labor.	
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 800	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 500	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-



PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout - Top View

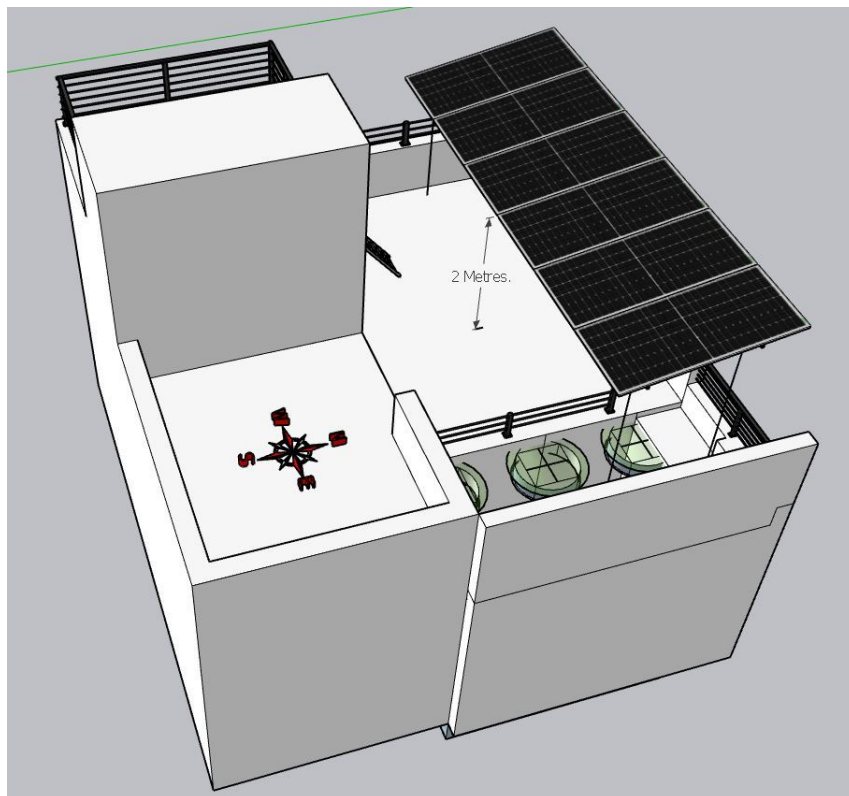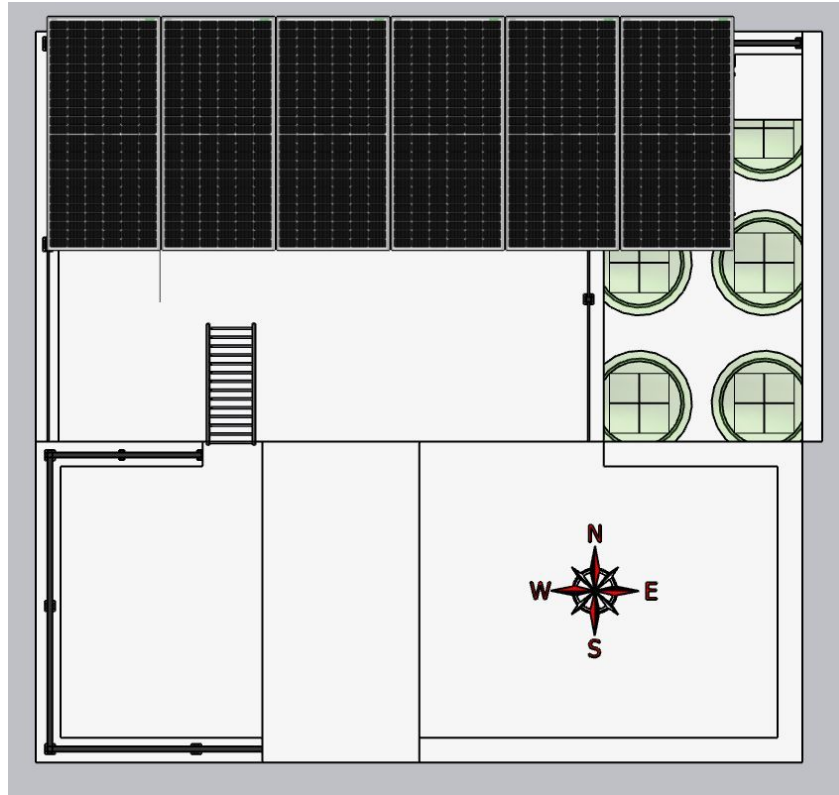

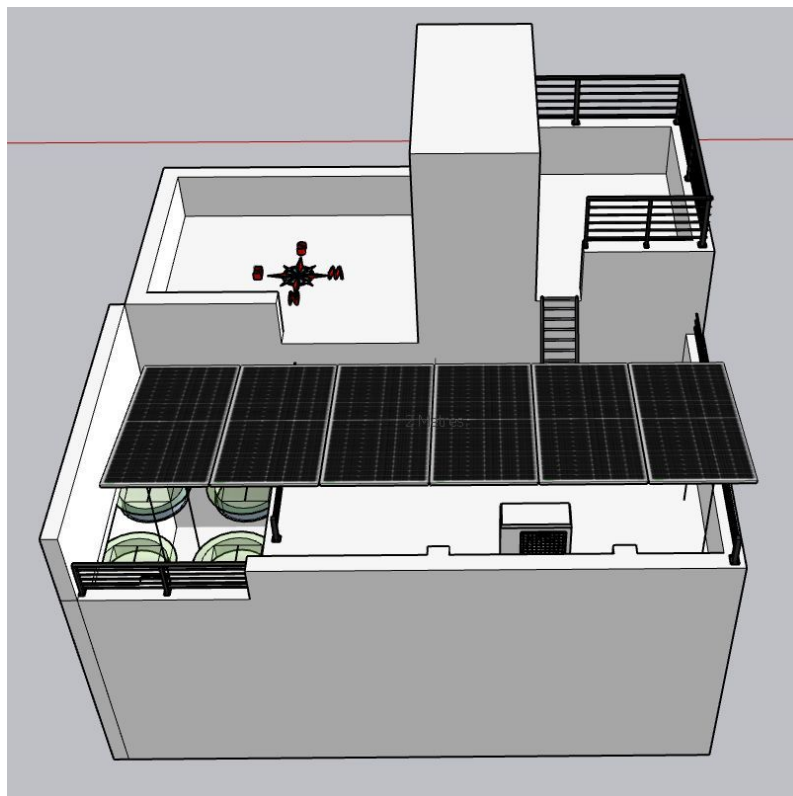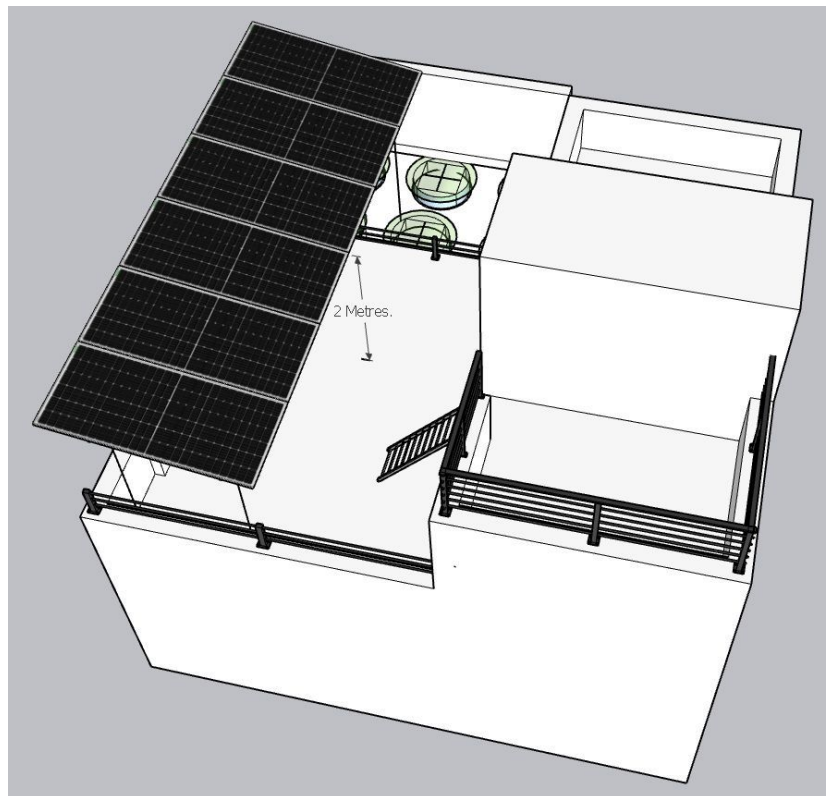

Building Exterior



Material Delivery Route



All the materials can be shifted from ground through the staircase-ladder of the neighbour house.



Materials including PV modules can be shifted through this way.



Once the materials reach the terrace of the neighbour house, it can be shifted to the customer's terrace over the side railings.

Staircase Details




Staircase width: 700mm

Material Storage





Proposed PV Area

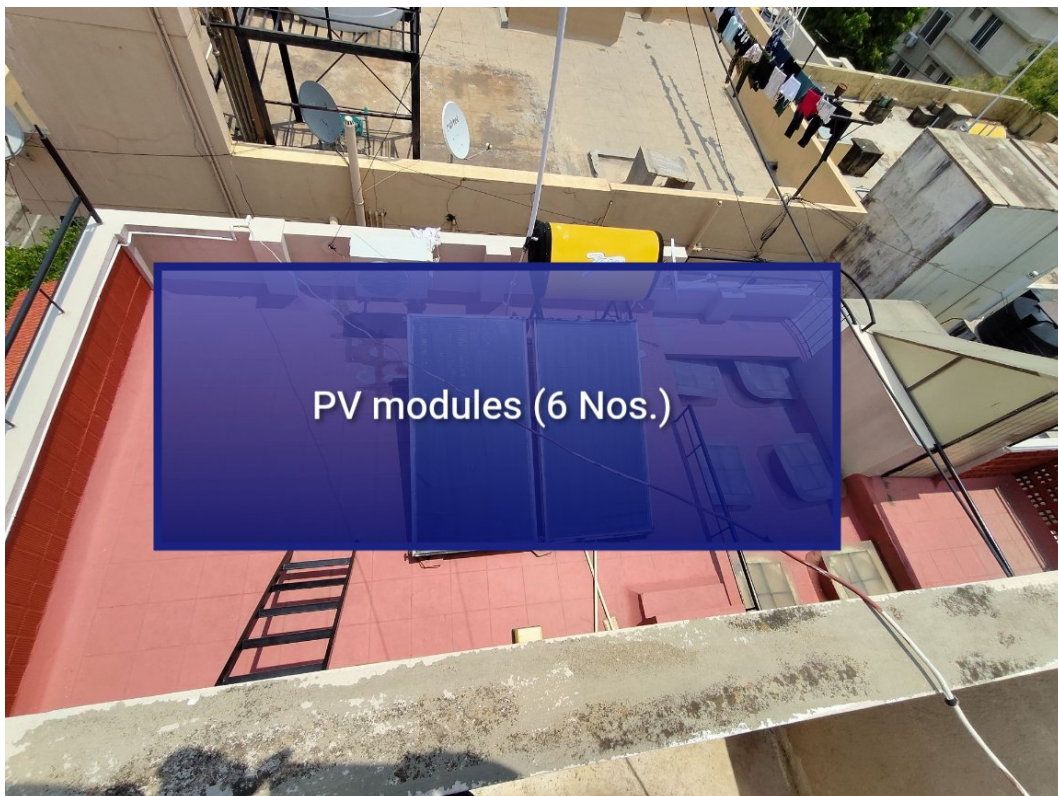

Cable Routing



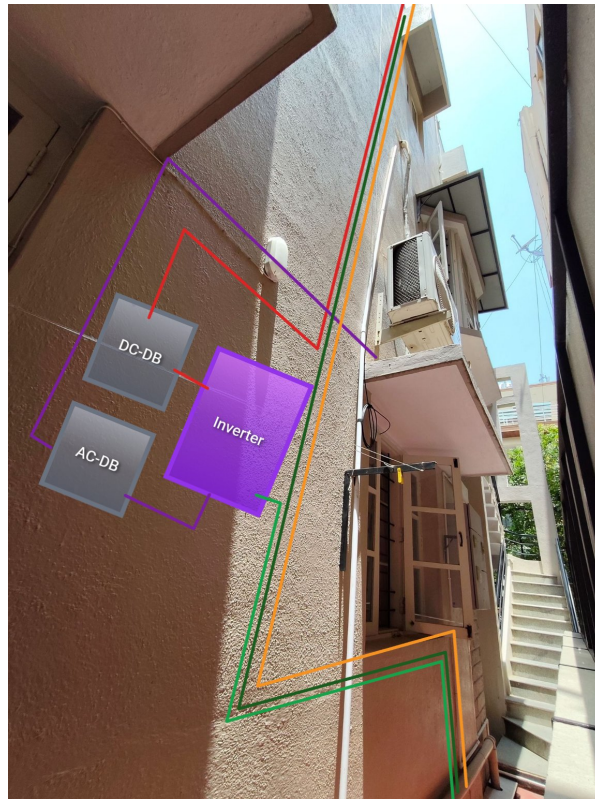

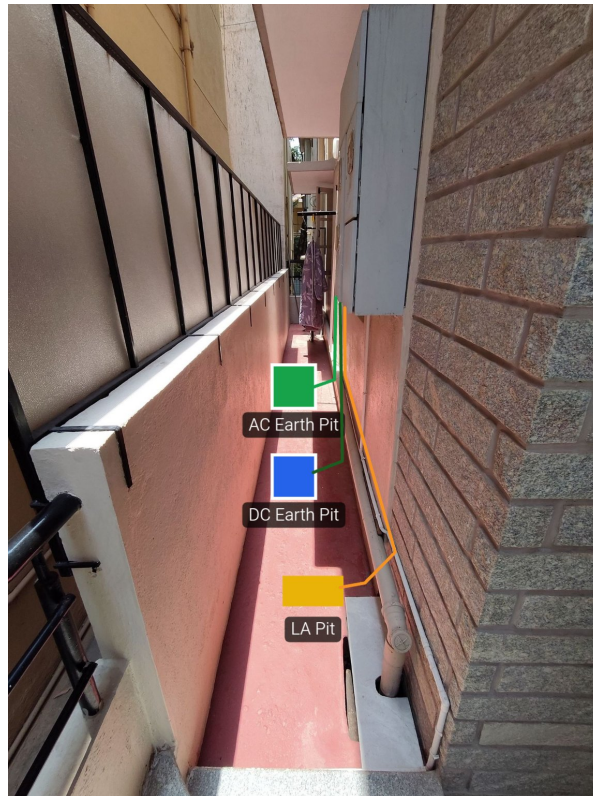


Earth pit have to be dug by core cutting the base slab of 400mm thick



Meter Box






Shadow Analysis

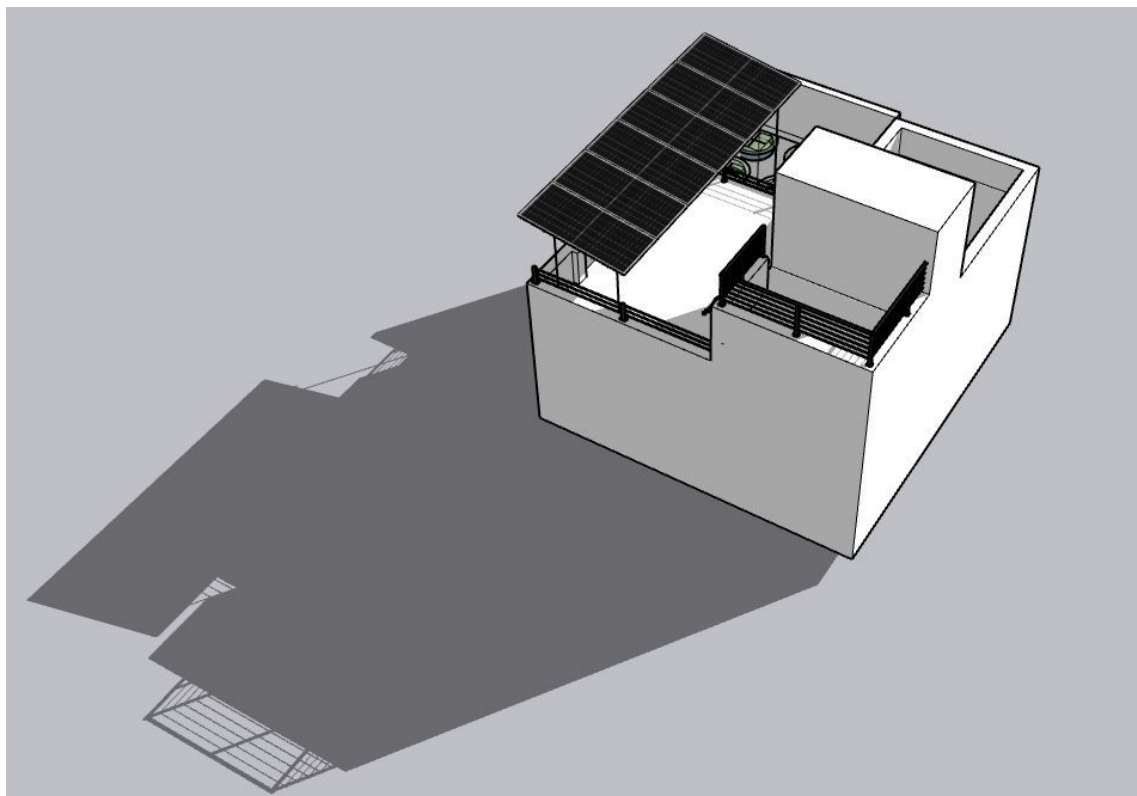

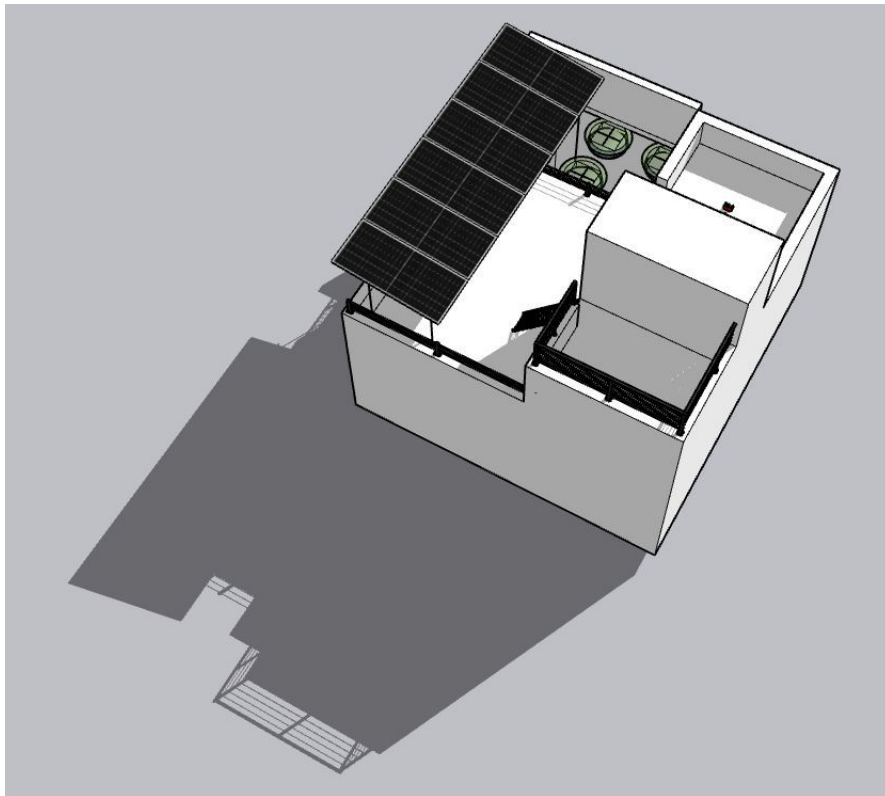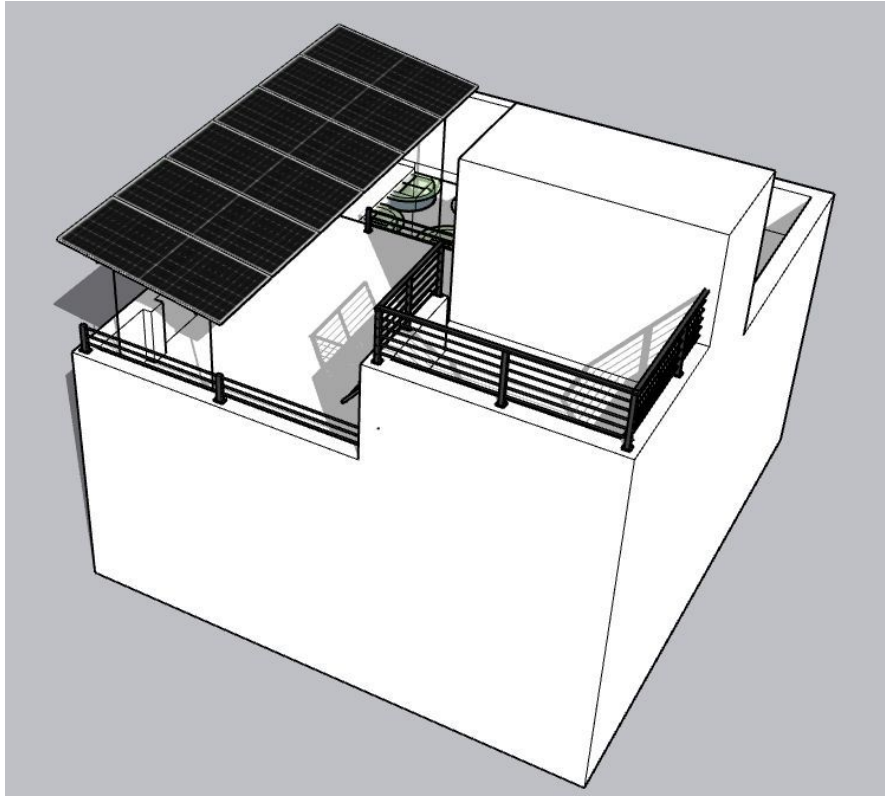

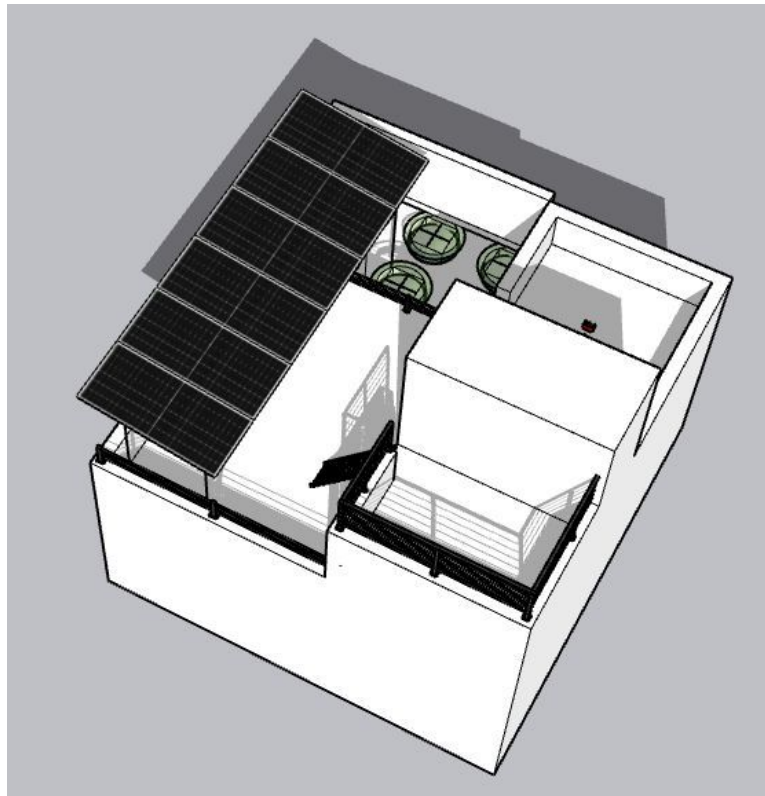

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 3.72kWp, On-grid solar power plant at the proposed premises.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	Fabricating a canopy to protect the inverter, DC-DB and AC-DB

THANK YOU

Dear Dr.Sharad Nadig (rekha),

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
