

Technical Site Visit Report

Prepared for: K. Arun Kumar_NGEF Layout_Subsidy_8.68kWp_String - 25, 4th , Sadanada nagar

PROJECT INFORMATION

Report Number	ESV-2026-0211
Project ID	LZ7FGMJ6
Project Name	K. Arun Kumar_NGEF Layout_Subsidy_8.68kWp_String
Building Name	25, 4th , Sadanada nagar
Billing Name	K. Arun Kumar_NGEF Layout_Subsidy_8.68kWp_String
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	K. Arun Kumar25, 4th , Sadanada nagar NGEF Layout, Bangalore- 560038
GPS Coordinates	12.99660777044941, 77.65717404134463
Google Maps	https://www.google.com/maps?q=12.99660777044941,77.65717404134463
Visit Date	2026-09-23
Visited By	Sai
Revision	Rev 1

CLIENT INFORMATION

Client Name	K. Arun Kumar
Contact	9632044335

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	8.68
Sanction Load (kW)	8.8
Module Make & Capacity	Premier DCR bifacial 620 Wp

Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	14
Inverter Type	String
Inverter Brand	Deye 8kW 3 phase String
Number of Inverters	1
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Inverter, DCDB, ACDB located below the syntex water area.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Earth pits are located near the basement area.	-
6	Where is the Internet Router located?	Customer scope	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	5	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	5	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Mini-rails	Aluminium short rails is planned for this project.

#	Question	Answer	Notes
9	What is the orientation of the solar panels?	["East"]	<i>corrugated Sheet roof slope is towards the east direction.</i>
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	Height of the building is 20m; it has G+3+Headroom.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-
16	What is the profile pitch of the corrugated sheet roof	N/A	-
17	What is the profile pitch of the corrugated sheet roof	240mm	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: N/A	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	<i>Earth pits need to dig between the compound wall area.</i>
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	No	-
15	Are there any safety risks associated with accessing the roof for installation?	No	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-

#	Question	Answer	Notes
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Inverters/ACDB/DCDB be installed on a wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 600, width: 400	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Building Exterior



Material Delivery Route





This route will carry the small items



This route will carry the large items (like panels)

Staircase Details




Meter Box




Material Storage




Site Layout - Top View

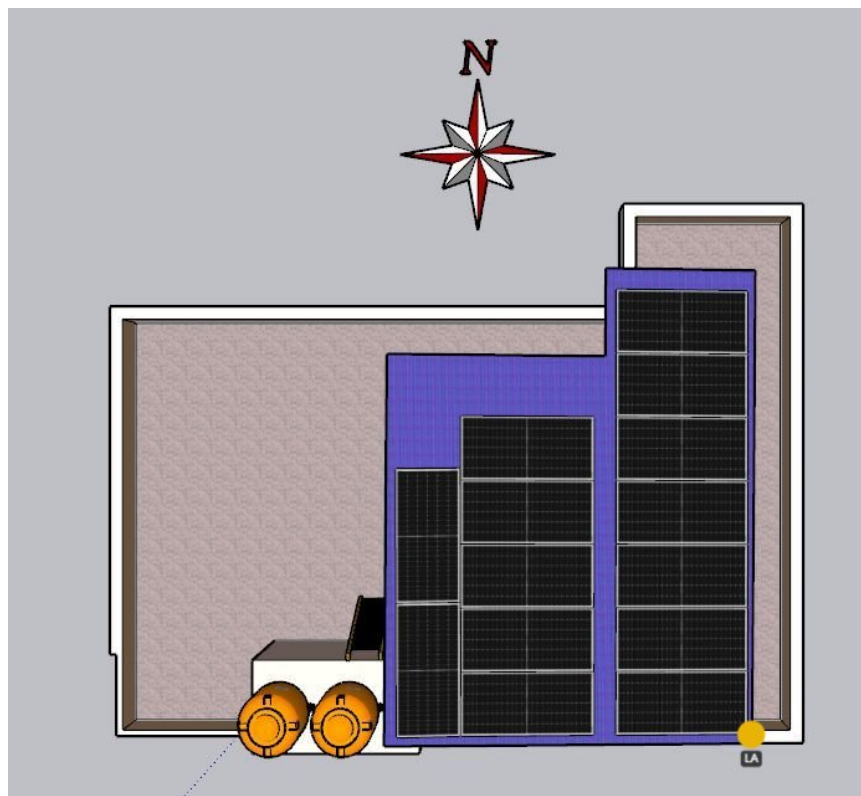


Top view

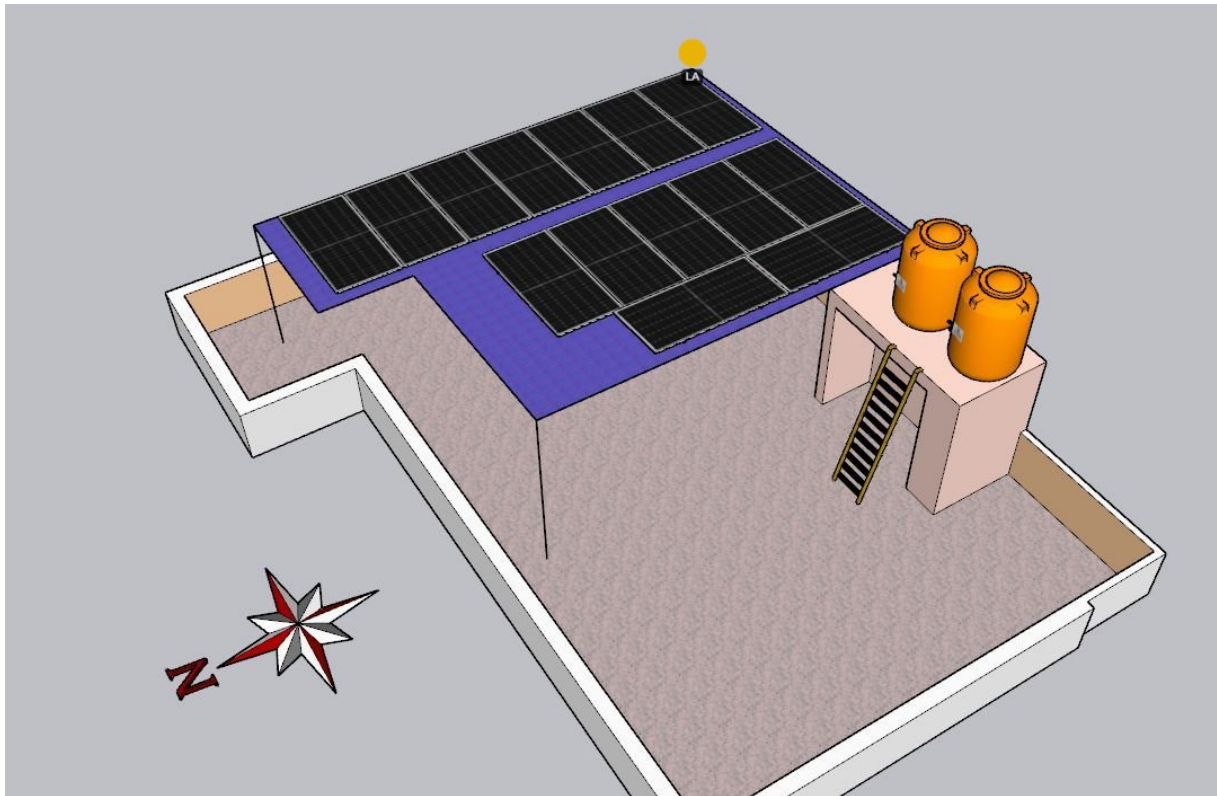


Side view (1)

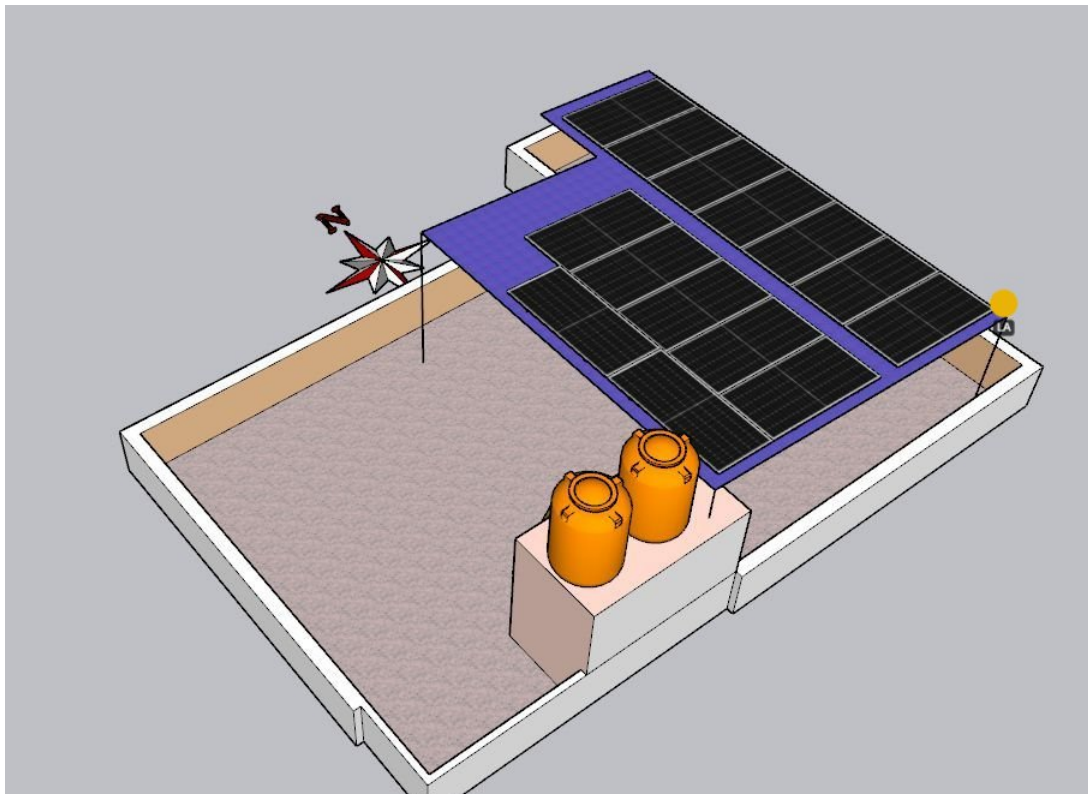

Side view (2)

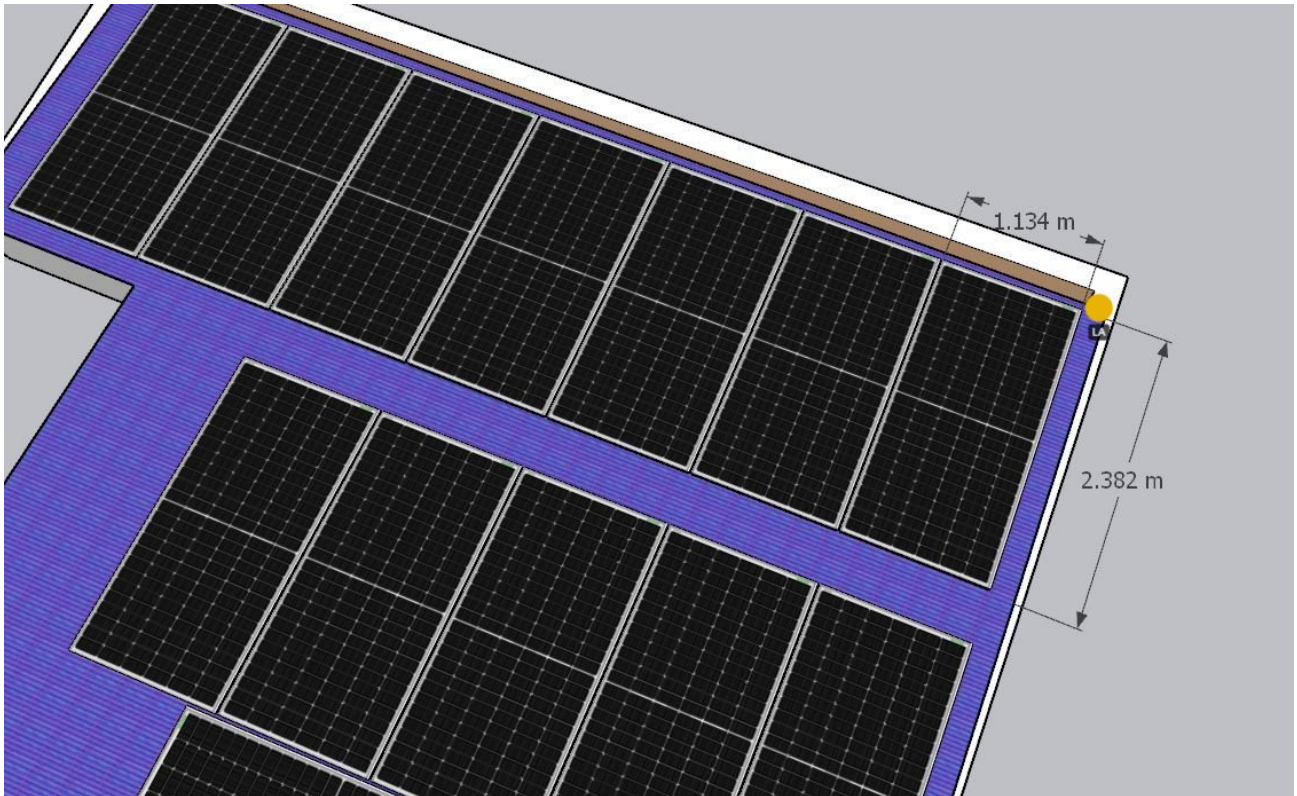

Panel dimensions (1)

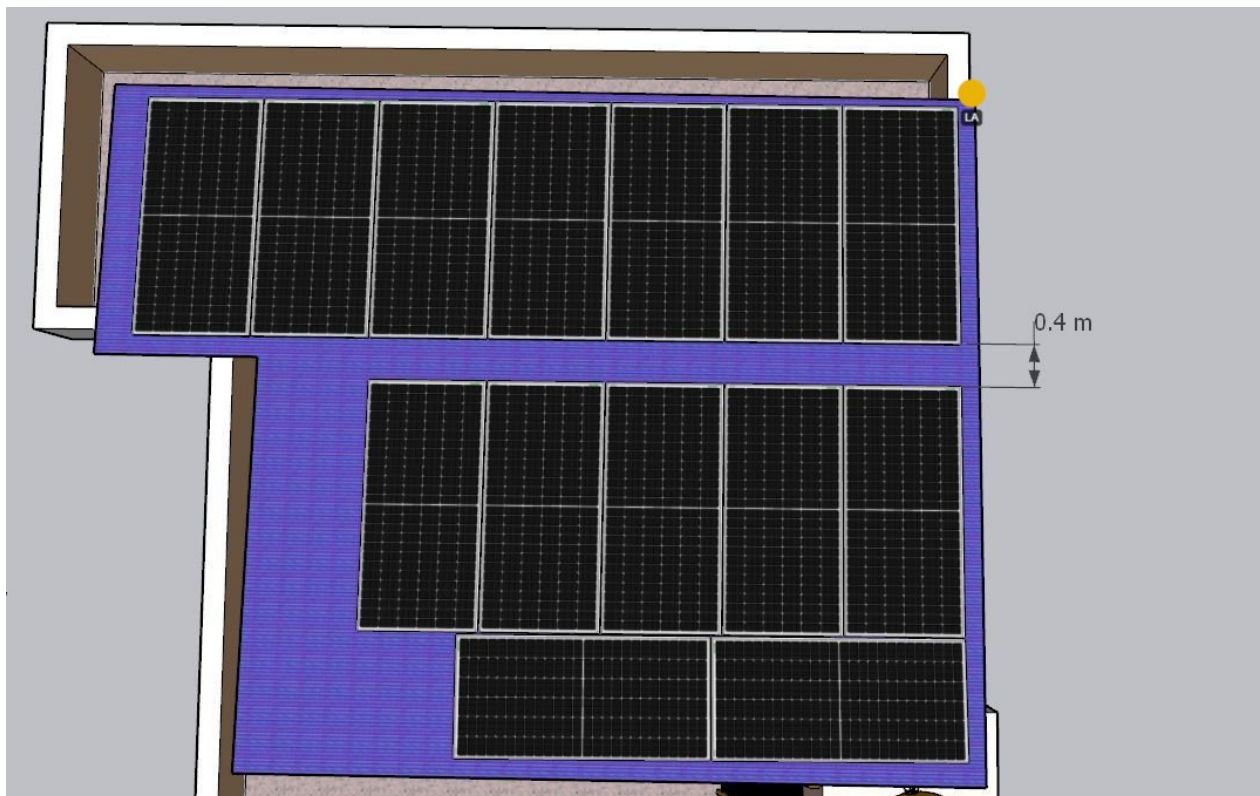


Panel to panel distance


Proposed PV Area



Cable Routing



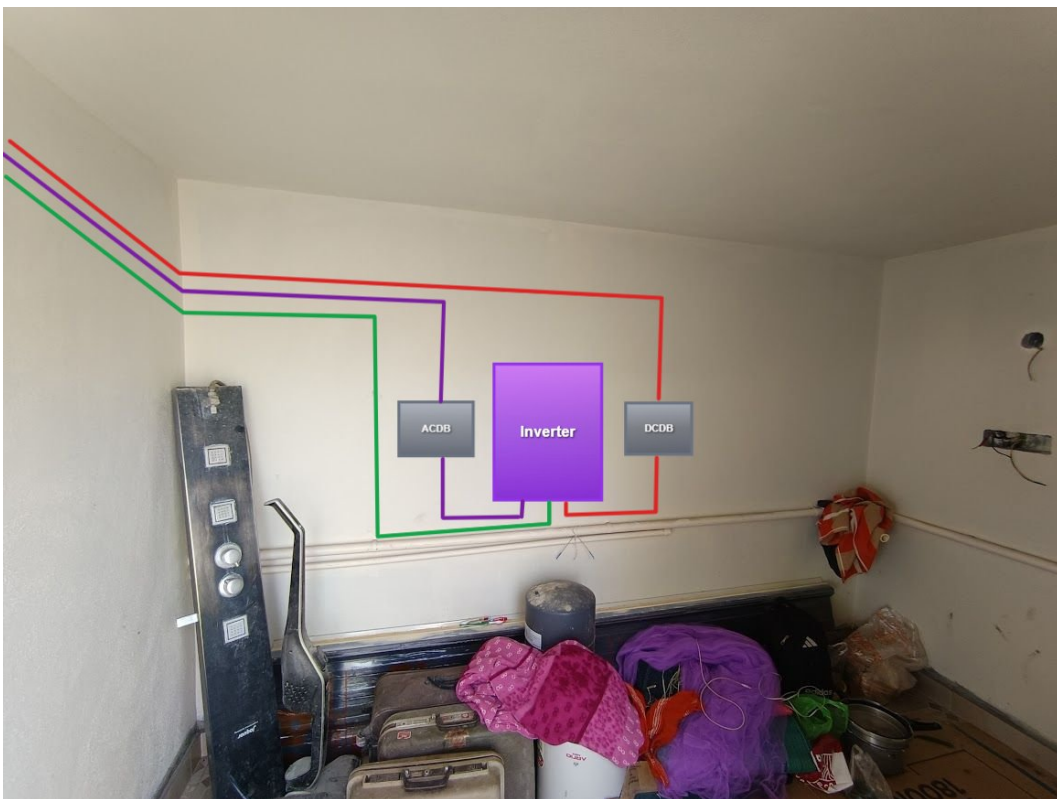


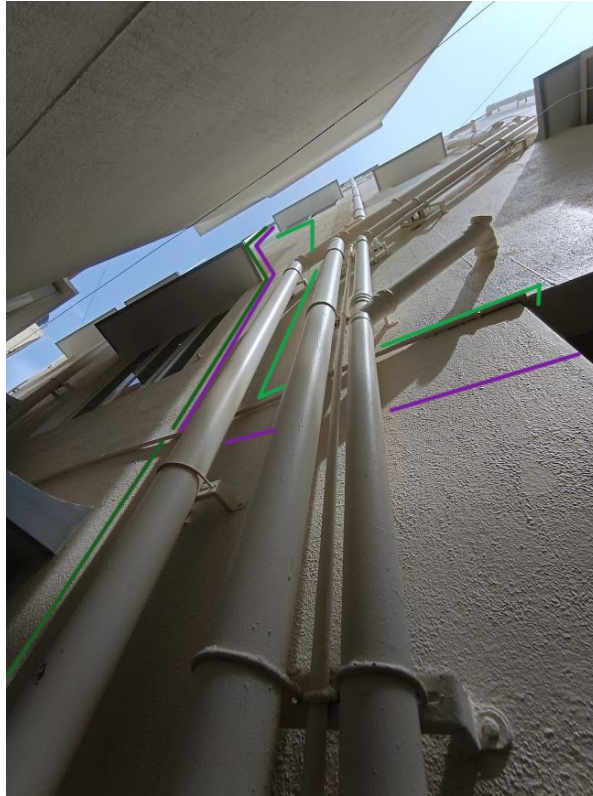






Equipment Location



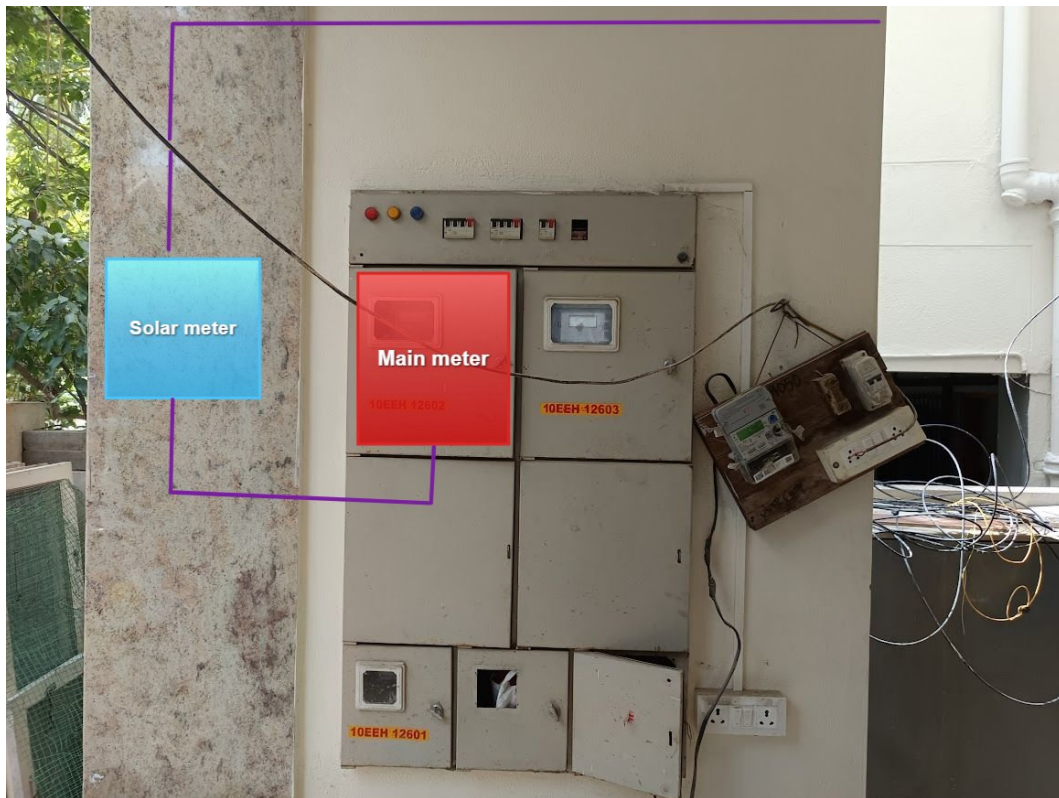

Earth Pit Location

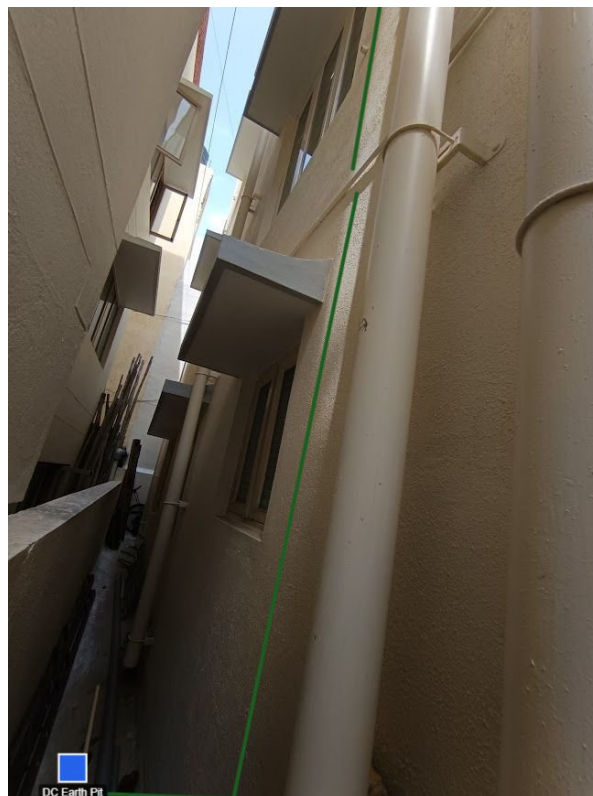

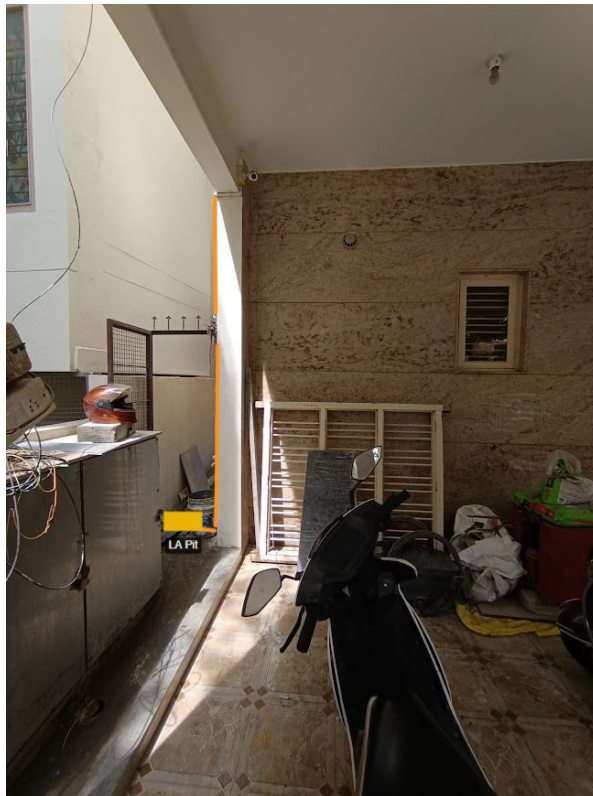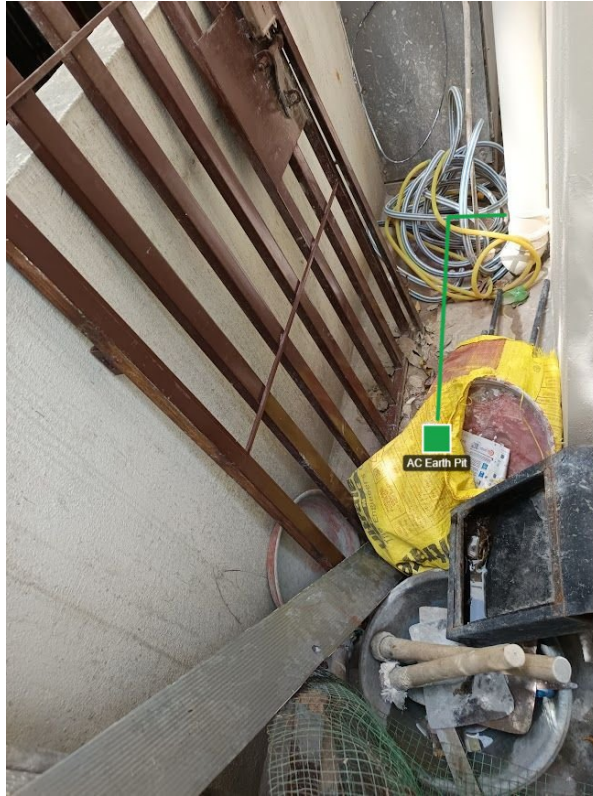

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As per the customer's suggestion, the routing, cable earthing, inverter location and also solar meter location have been considered.

Customer Scope

#	Observation
1	Wi-Fi upto solar meter is under customer scope

THANK YOU

Dear K. Arun Kumar,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
