Technical Site Visit Report

Prepared for: George_Pavilion Villas Brigade Orchards Non Subsidy_8.68kWp_Microinverter (IQ Series) - Villa M03

PROJECT INFORMATION

Report Number	ESV-2026-0229
Project ID	2VQZNSK4
Project Name	George_Pavilion Villas Brigade Orchards Non Subsidy_8.68kWp_Microinverter (IQ Series)
Building Name	Villa M03
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Govindaraju J S
Site Address	Villa M03, Pavilion Villas, Brigade Orchards, Devanahalli, Bangalore Rural, Karnataka 562110.
GPS Coordinates	13.227556, 77.720215
Google Maps	https://www.google.com/maps?q=13.227556,77.720215
Visit Date	2026-10-01
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	George
Contact	+91 8655496152

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	8.68
Sanction Load (kW)	10
Module Make & Capacity	Waaree 620Wp Topcon Bi-Facial Non-DCR

Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	14
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	14
Mounting Structure Type	Tiled Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	**No**	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Enphase accessories box, inbuilt with a solar meter provision, can be installed near the existing main meter box located on the ground floor (east side of the building)	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	Yes, the space for earthing is planned in the northwest courtyard of the building on the ground floor.	-
6	Where is the Internet Router located?	Not available at the moment. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Tiled Roof	*Type of roof tile material: Mineral-granule-coated*

#	Question	Answer	Notes
			bitumen shingles (the asphalt roofing shingles). Base of the roof: RCC
2	Are there any obstructions on the roof that could affect the solar installation?	**No**	-
3	What is the angle of the panels? (in degrees)	26	*The PV modules have to be installed to the existing tiled roof as flash-mounted.*
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	26	*The PV modules have to be installed to the existing tiled roof as flash-mounted.*
5	On how many roofs at the site are we installing solar?	3	*The roofs are on the same terrace level, but 3 different sides of the roof have been considered for the installation of PV modules*
6	If it is a Tiled roof, what is underneath the tiles?	RCC	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Long rails with L clamps	*Alu. Long Rails with L Clamps (Portrait Orientation on Metal Sheet with Trapezoidal Profile)*
9	What is the orientation of the solar panels?	-	*As the panels are flush mounted, we follow the orientation of the existing roofs for the panels too.* *Roof 1: North-facing (6 Nos. of PV modules)* *Roof 2: West-facing (4 Nos. of PV modules)* *Roof 3: East-facing (4 Nos. of PV modules)*
10	How can the roof be accessed?	Staircase	*One can access the terrace floor via the inner staircase. But the roof proposed for installation can be accessed with the help of a metal ladder through which only people can enter; not any bulky materials.*
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	**No**	-
13	What is the height of the building and how many floors does it have?	12 (G + 2 + Head room)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If	-

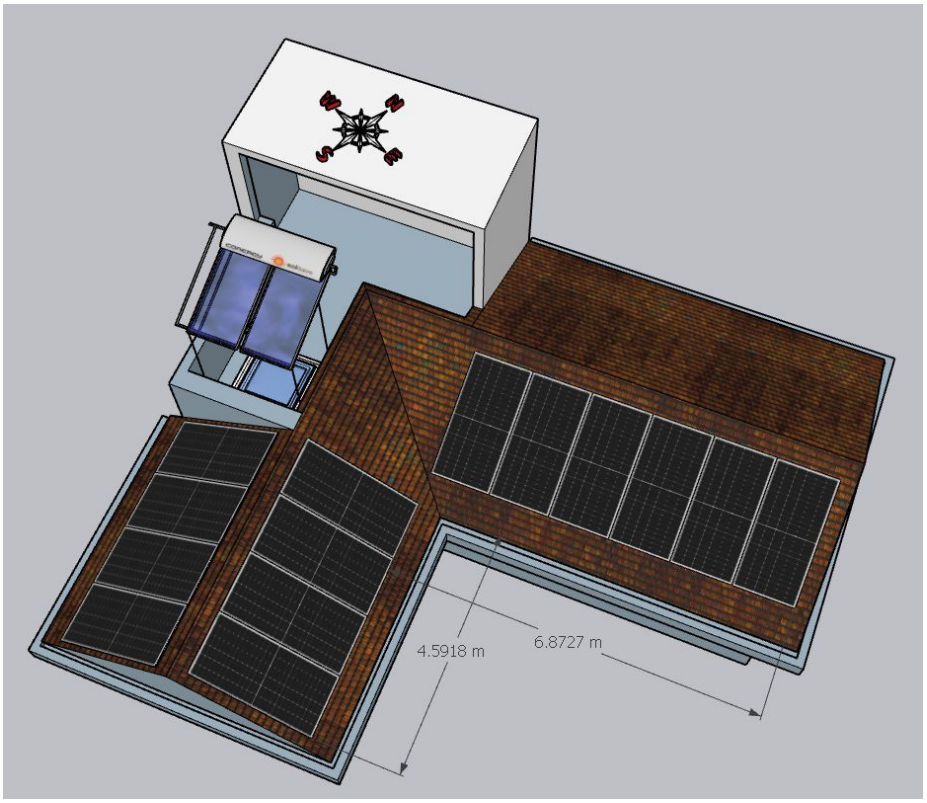
#	Question	Answer	Notes
		3-phase: LT w/o CT (5 - 34.999)	
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	**No**	*A separate box has to be provided to house the solar meter and the Enphase accessories.*
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	**No**	*A separate box has to be provided to house the solar meter and the Enphase accessories.*
11	Is there space available to dig DC, AC and LA earth pits?	Yes	*The space for earthing is planned in the northwest courtyard of the building on the ground floor.*
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	**No**	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1500, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 3000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	**No**	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-


PHOTO DOCUMENTATION


Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA


Site Layout - Top View



4.5918 m
6.8727 m

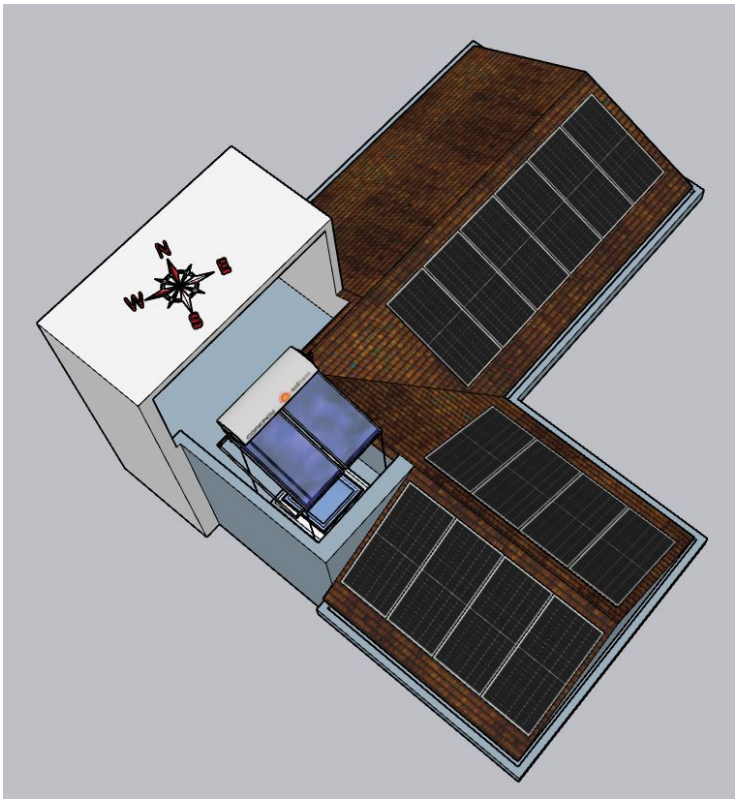


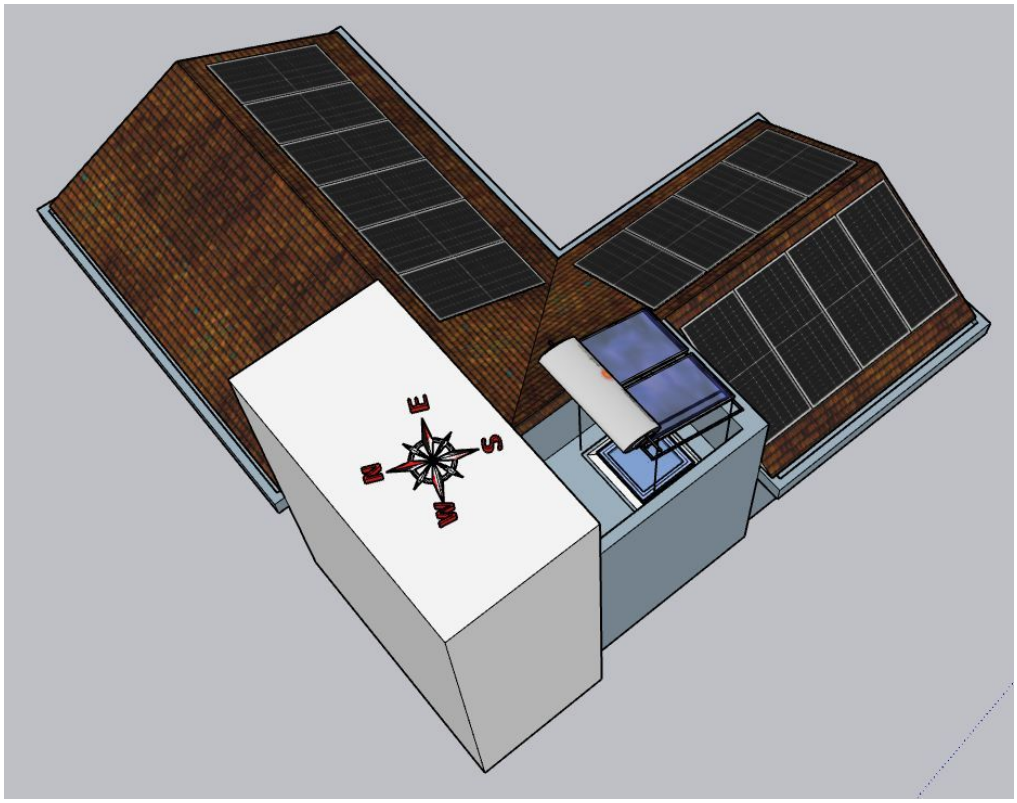
E
S
W
N

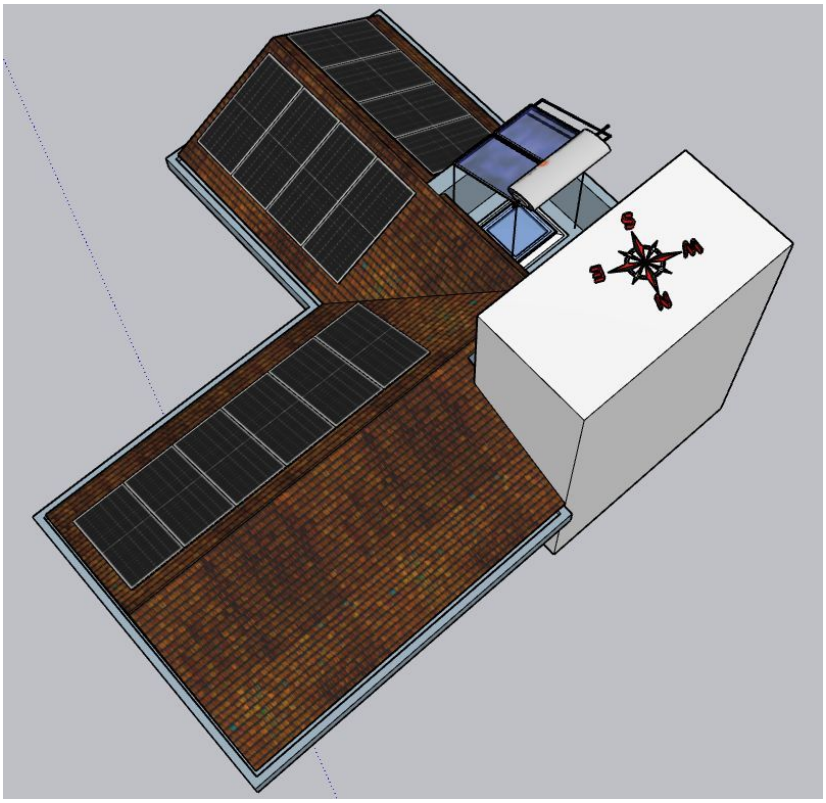
S
W
E
N

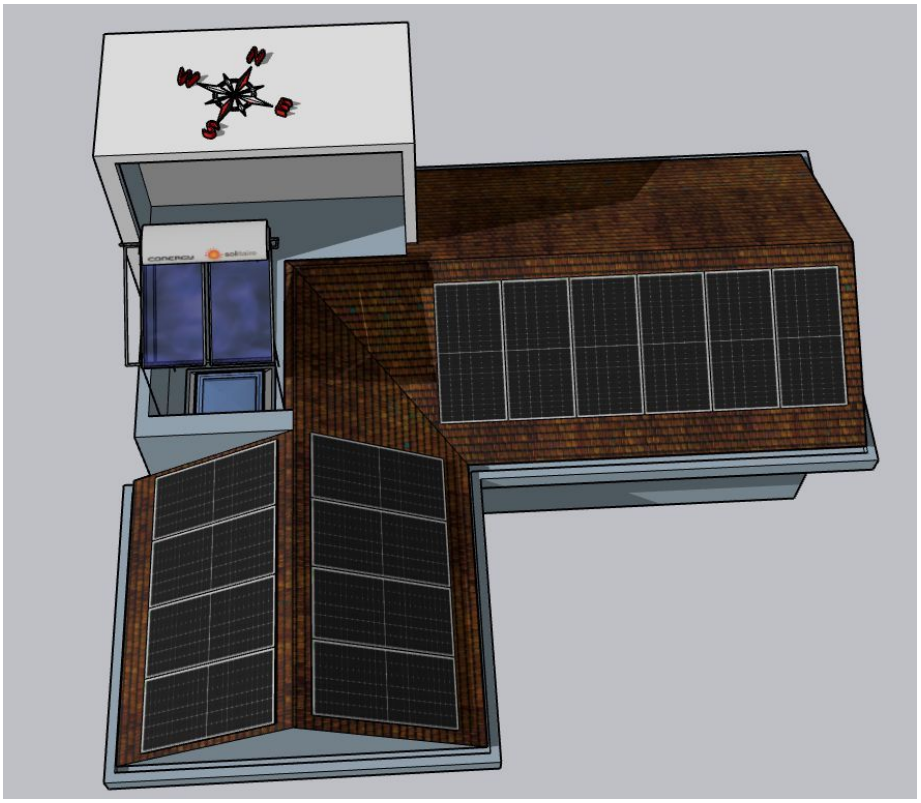

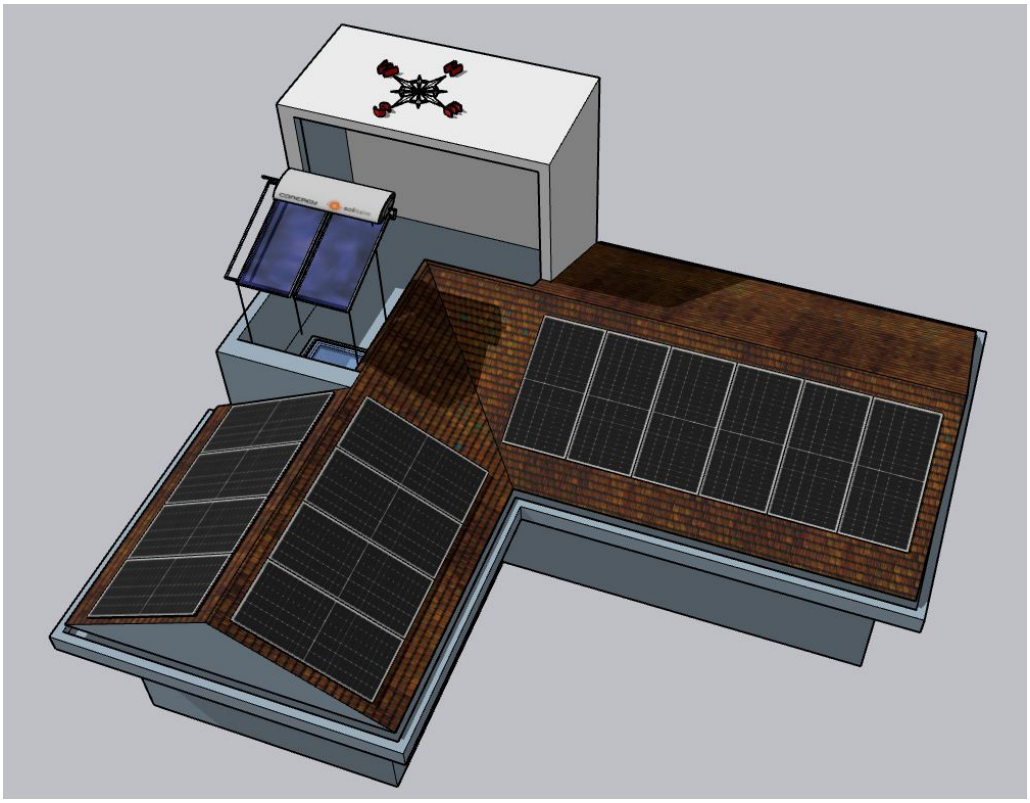

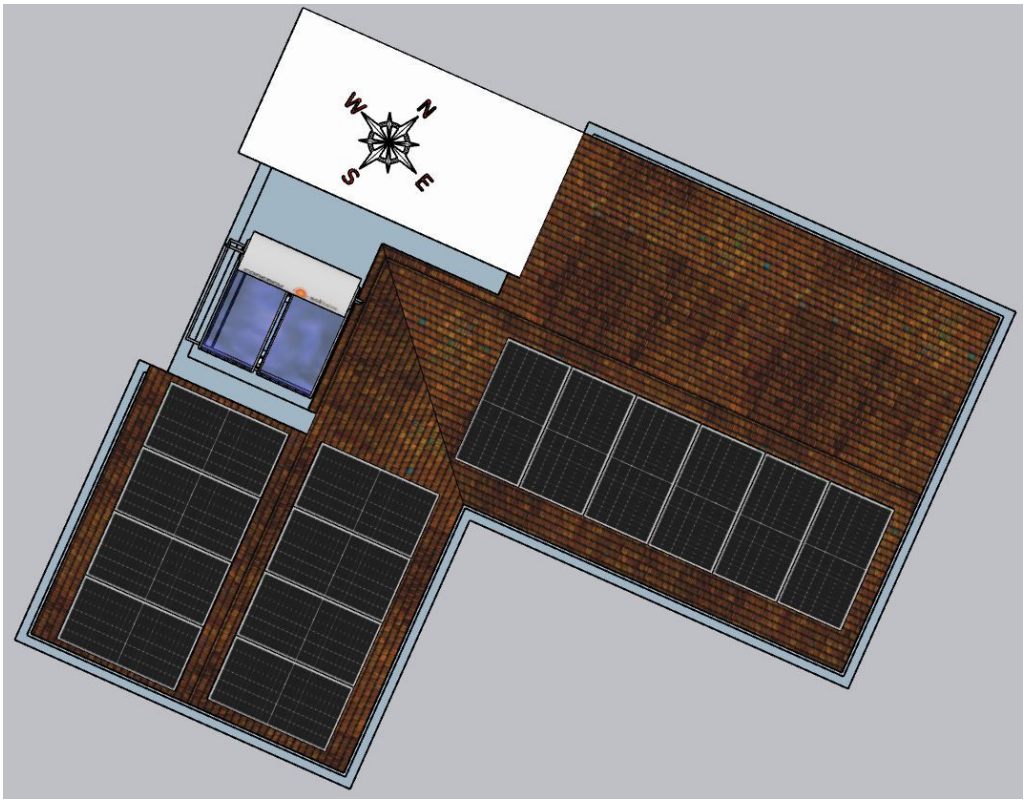

Building Exterior



Material Delivery Route



The materials can follow the way on the right side of the building to reach the outer courtyard.



The materials can follow the way on the right side of the building to reach the outer courtyard.



Once reaches the ground courtyard, All the materials including the PV modules can be shifted to the upper balcony and then the top terrace over the side wall of the building.

Staircase Details



Staircase width: 1000 mm


Material Storage



Proposed PV Area



Cable Routing

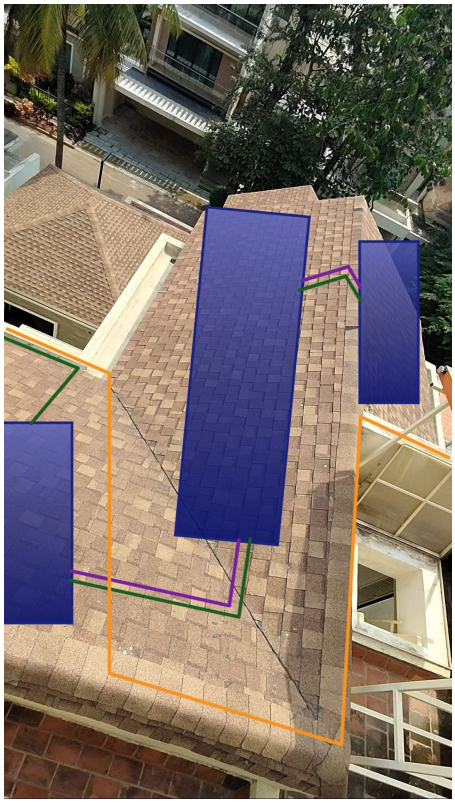


The AC power cable should run from the tiled roofs to the meter location on the north-east side of the building. But the LA earthing cable and the DC earthing cable have to run towards the north-west courtyard of the building.



The lightning arrester can be installed on the tank tower and the cable should be run along the side walls and follow the parapet wall in the terrrace level.



The AC cable will run vertically inside the vertical shaft available near the meter location. The AC power cables initially enter into the Enphase accessories box and then to the solar meter inbuilt in it.

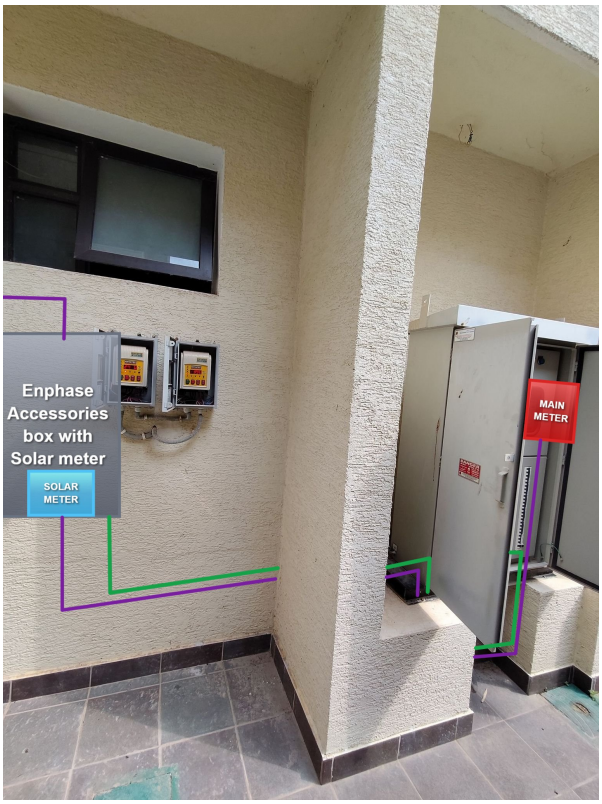

AC cable from the Enphase accessories box then run towards the main meter. The AC cable should enter into the client meter box from underneath entry provision. The AC earthing from the Enphase box can be terminated at the existing meter box.



The LA and DC earthing cables have to run vertically from the upper gutter to the ground via the existing cable drain pipe shaft shown.

Meter Box





OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 8.68 kWp On-grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the Enphase Accessories box location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.

THANK YOU

Dear George,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
