Technical Site Visit Report

Prepared for: Shobha Patil_Prestige Oasis Subsidy_4.96kWp_Microinverter (IQ Series) - #Villa 43

PROJECT INFORMATION

Report Number	ESV-2026-0218
Project ID	XQIK87W3
Project Name	Shobha Patil_Prestige Oasis Subsidy_4.96kWp_Microinverter (IQ Series)
Building Name	#Villa 43
Billing Name	Shobha Patil
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Govindaraju
Site Address	Villa 43, Prestige Oasis, Adde Vishwanathapura Rd, Vaishnavi Layout, Adde Vishwanathapura, Adde Viswanathapura, Karnataka 560119
GPS Coordinates	13.17980040528198, 77.55468989662691
Google Maps	https://www.google.com/maps?q=13.179800405281979,77.55468989662691
Visit Date	2026-09-10
Visited By	K Naveen
Revision	Rev 0

CLIENT INFORMATION

Client Name	Shobha Patil
Contact	'+91 9742353608

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	4.96
Sanction Load (kW)	12

Module Make & Capacity	Premier DCR Bifacial 620
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	8
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	8
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	**No**	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the corridor which is near south side garden area.	-
6	Where is the Internet Router located?	Not Available	*Under construction*
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	*PUF sheet roof with 0.25 m profile pitch*
2	Are there any obstructions on the roof that could affect the solar installation?	**No**	-
3	What is the angle of the panels? (in degrees)	5	*During the site visit the existing PUF sheet roof slope is 2 degree.*
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	2	-
5	On how many roofs at the site are we installing solar?	1	-

#	Question	Answer	Notes
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Other	*Aluminum Short Rail structure with L Bracket - Sheet Roof*
9	What is the orientation of the solar panels?	["West"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Not Applicable	*Not available*
13	What is the height of the building and how many floors does it have?	The height of the building is G+1+headroom is approximately 12meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	**No**	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Not Applicable	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	**No**	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin	Rafter to Rafter is	-

#	Question	Answer	Notes
	to purlin.	approximately 1.2 m and purlin to purlin is approximately 0.8 m.	
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1200, width: 1200	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1000, width: 1000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	N/A	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-

PHOTO DOCUMENTATION


Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using Staircase) will be followed to carry large items, small items.

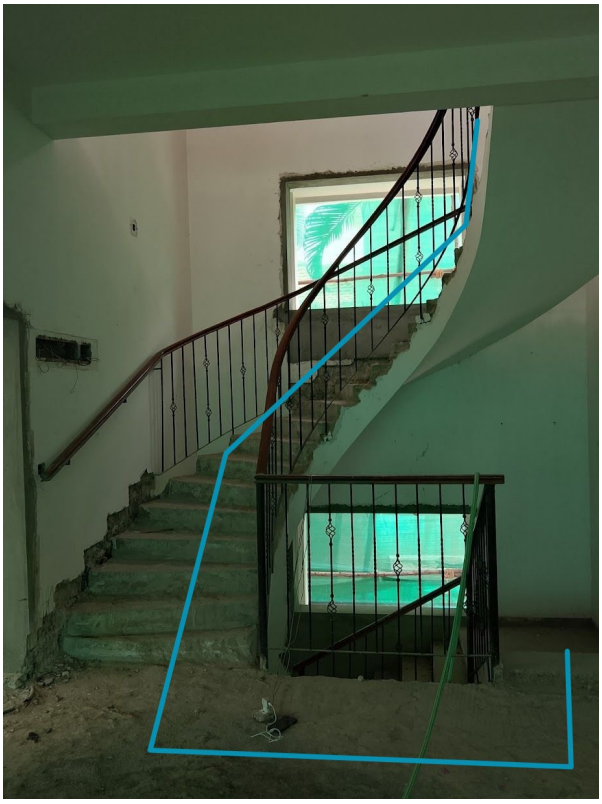










Staircase Details


0.95 M


Meter Box


Electronic Trivector Meter ER300P
11259186
LARSEN & TOUBRO LIMITED, MYSORE, INDIA
RS232

Material Storage

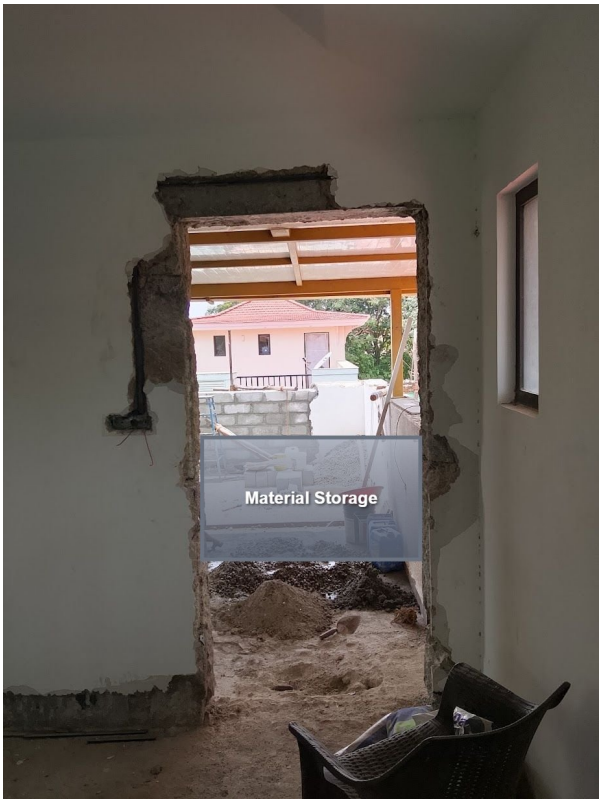

Proposed PV Area

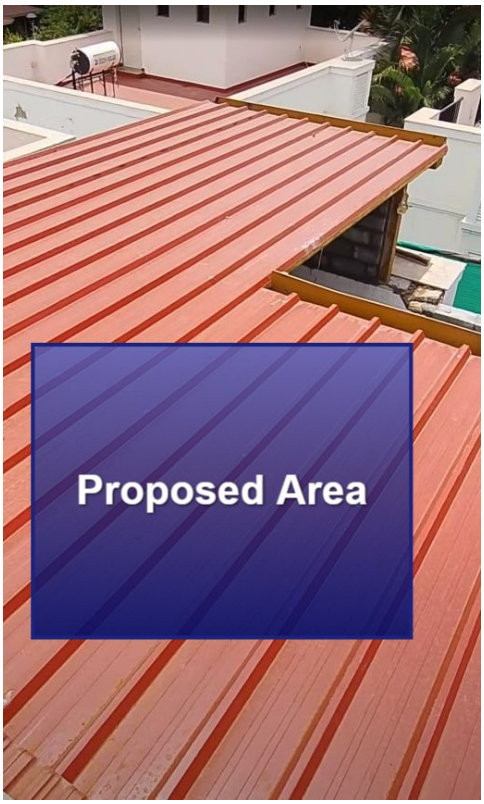

Cable Routing












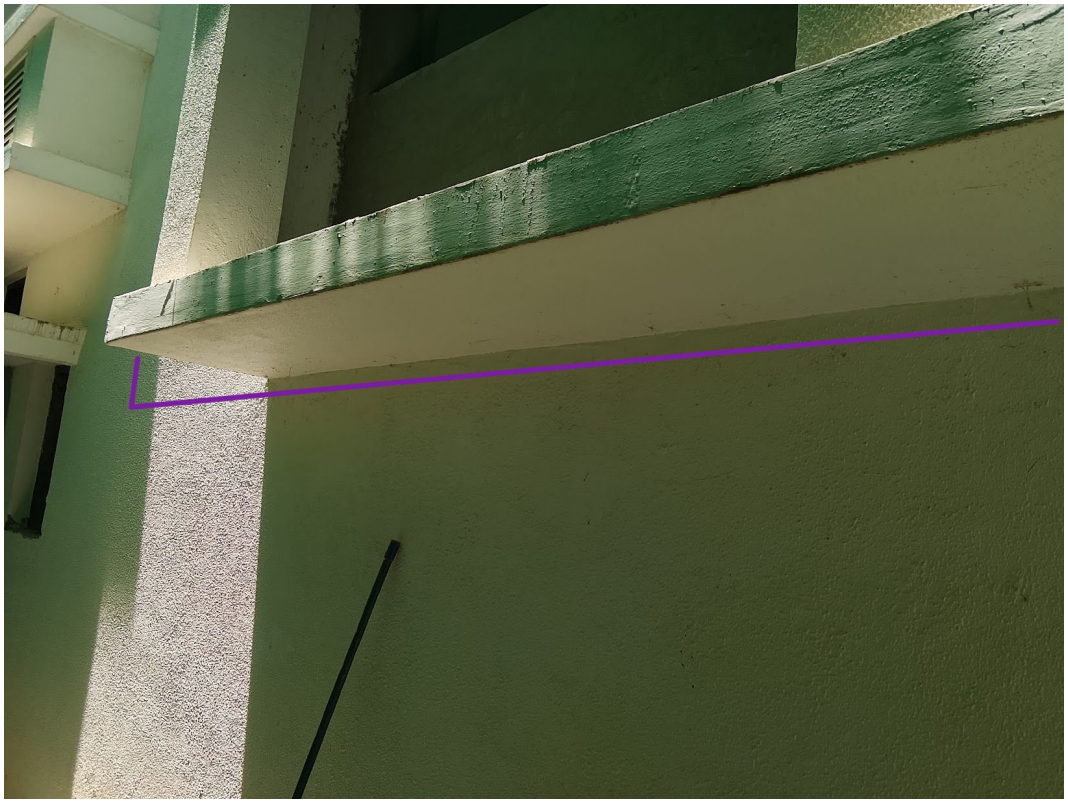








Make a hole to run the AC Cable up to the meter location



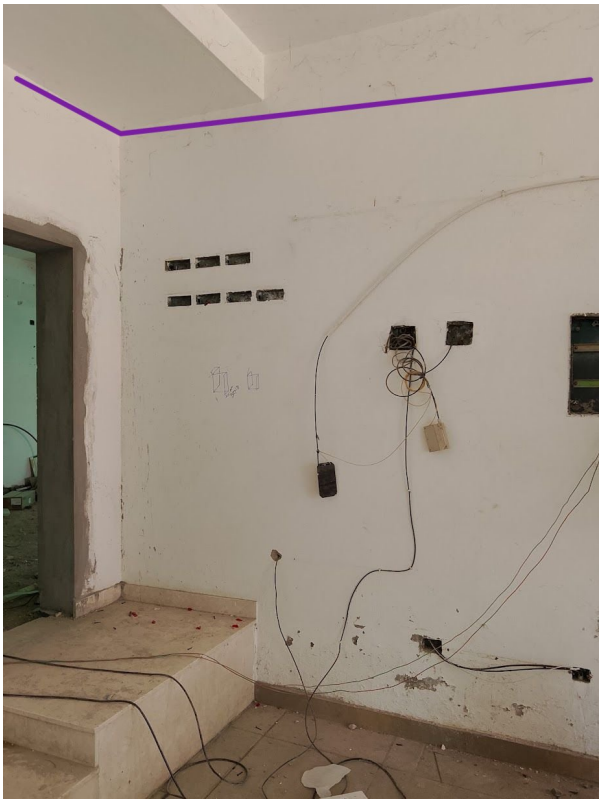

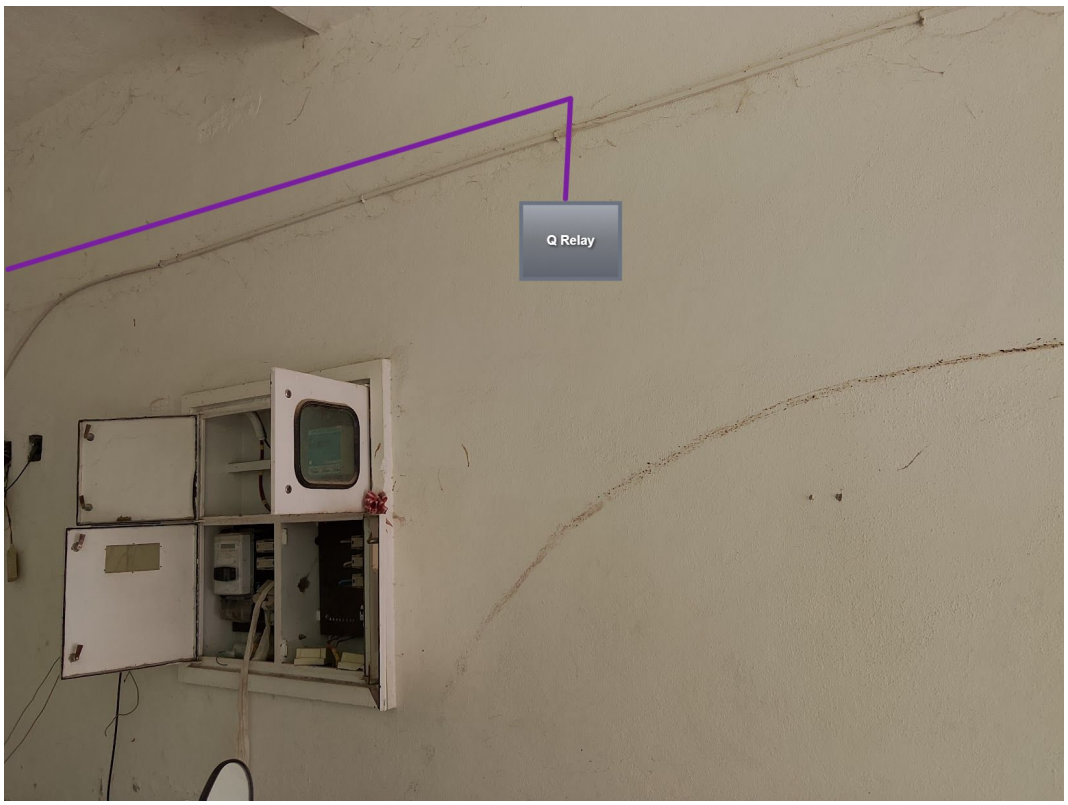


Equipment Location

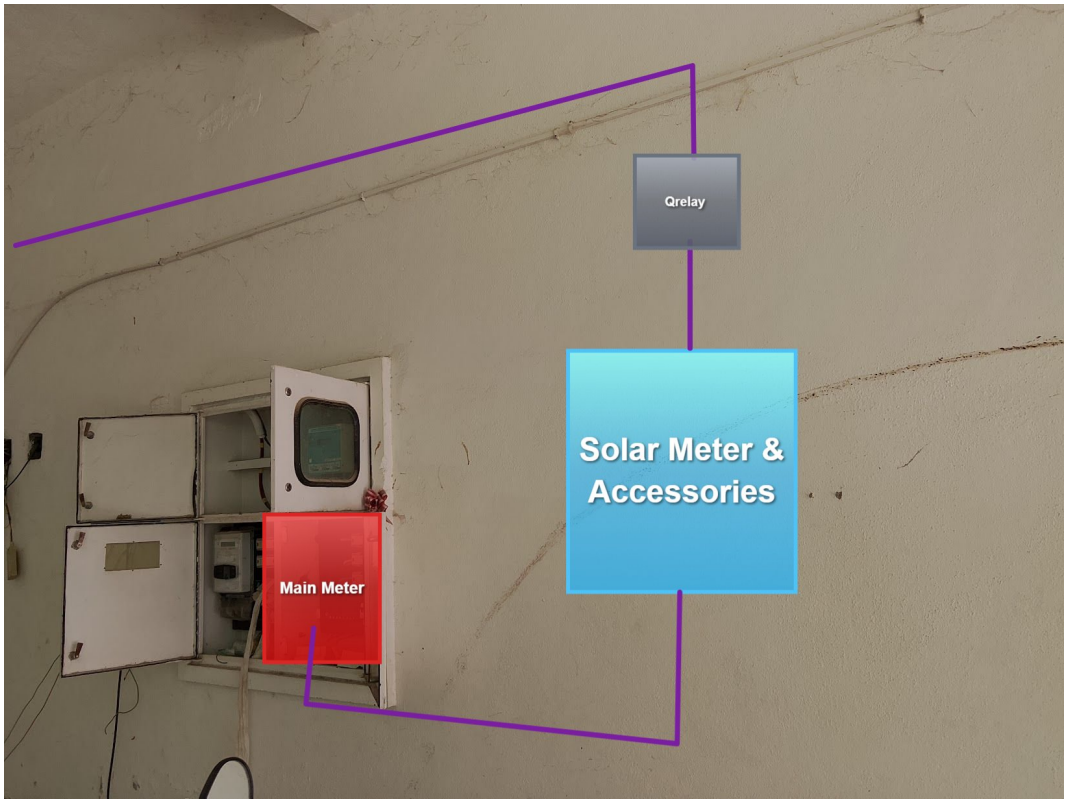



Earth Pit Location



Site Layout - Top View

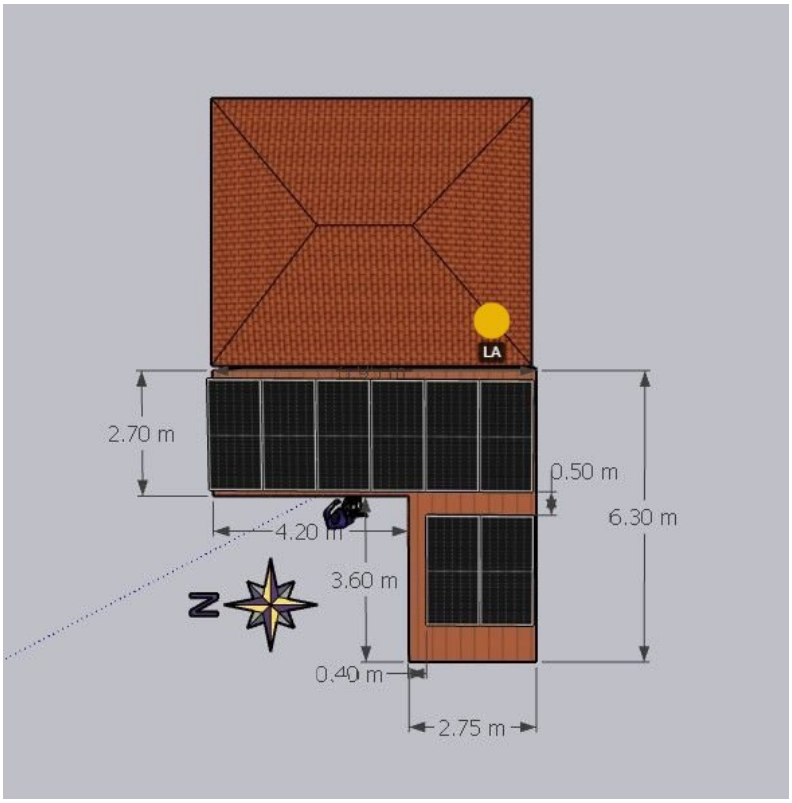

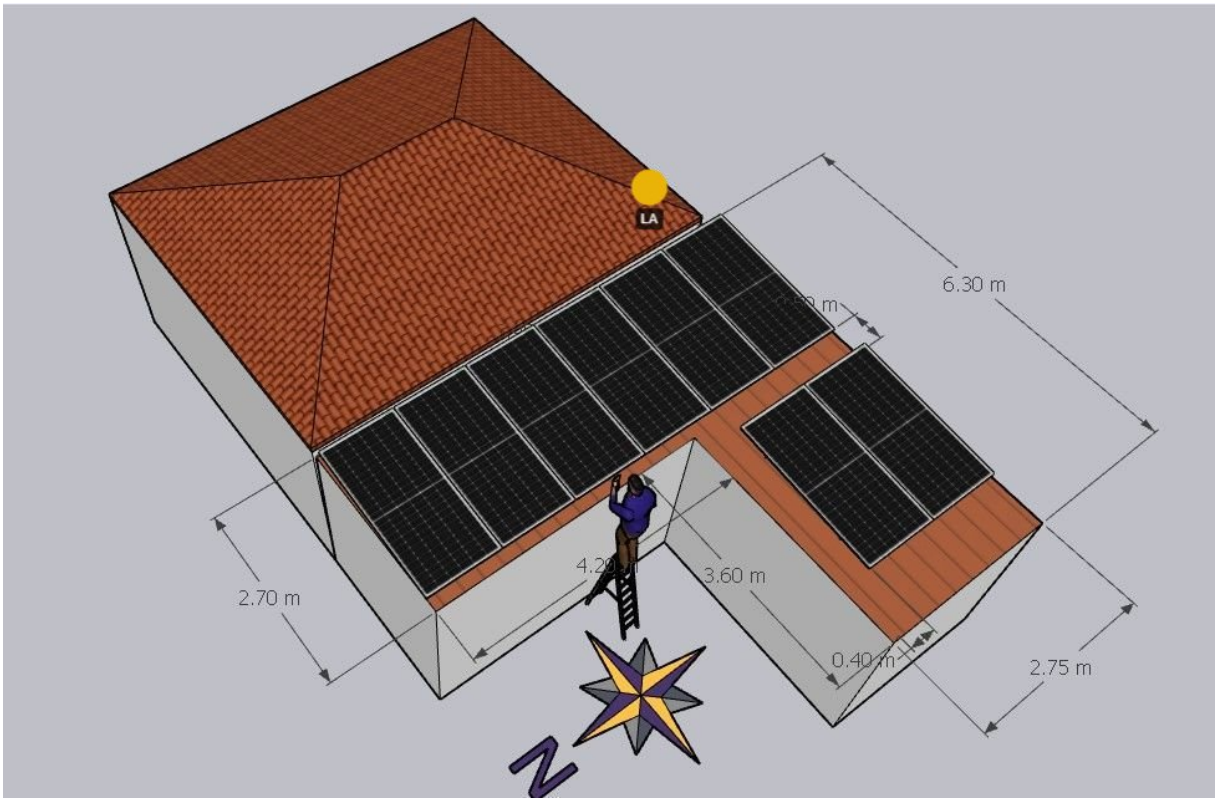

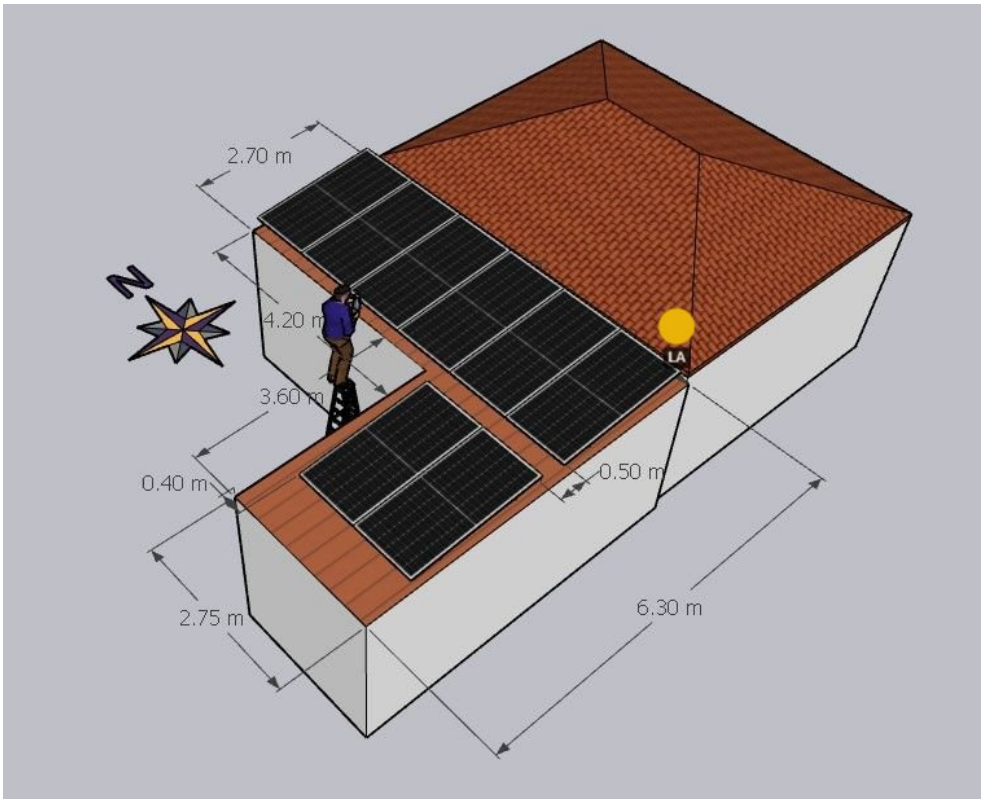

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As discussed with Govindaraju the panel layout has been finalised.
2	The profile pitch of existing PUF sheet roof is 0.25 m.
3	During the site visit existing PUF sheet roof slope is 2 degree.

Customer Scope

#	Observation
1	Wi-Fi up to the solar meter is under customer scope.
2	As discussed with the site engineer and fabricator the slope of the PUF sheet roof is confirmed by 2 degree.
3	Based on the site conditions the (Aluminum Short Rail structure with L Bracket) structure has been considered.

THANK YOU

Dear Shobha Patil,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
