Technical Site Visit Report

Prepared for: Manju M_JP Nagar_Subsidy_4.96kWp_Hybrid - Site No #8

PROJECT INFORMATION

Report Number	ESV-2026-0227
Project ID	AQ3K1J22
Project Name	Manju M_JP Nagar_Subsidy_4.96kWp_Hybrid
Building Name	Site No #8
Billing Name	Manju M
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	Manju M NO 8 ,7TH MAIN 14TH CROSS THIPPASANDRA NARAYANA NAGAR 2ND BLOCK NEAR NATURE KICKS THIPPASANDRA Bangalore, 560108
GPS Coordinates	12.8699725, 77.5540651
Google Maps	https://www.google.com/maps?q=12.8699725,77.5540651
Visit Date	2026-10-13
Visited By	K Naveen
Revision	Rev 1

CLIENT INFORMATION

Client Name	Manju M
Contact	+91 9886208976

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	4.96
Sanction Load (kW)	8

Module Make & Capacity	Premier DCR Bifacial 620
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	8
Inverter Type	Hybrid (String)
Inverter Brand	Deye 5 kW 1phase String
Number of Inverters	1
Battery	Needed
Number of Batteries	1
Capacity of each Battery (kWh)	5.1
Battery Model No.	Deye Battery: SE-F5plus - 1
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The existing chajja are the obstacles that could affect the solar material lifting.	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter, ACDB, DCDB, Battery will be installed in the basement which is near to the meter location.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located front side of the house which is near to the meter location.	-
6	Where is the Internet Router located?	Not available	*Under construction*
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The water tanks, solar water heaters, are the obstructions that could affect the solar installation.	-
3	What is the angle of the panels? (in degrees)	7	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*AL Short Rail - Elevated Structure (Fabricated MS elevated Structure)*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	-
13	What is the height of the building and how many floors does it have?	The height of the building is G+3+headroom is approximately 15 meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital	*Temporary existing single phase meter.*
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	*As discussed with the*

#	Question	Answer	Notes
			client and site engineer they will give the provision for solar meter in the panel board.
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	**No**	-
16	Is space present in rooftop to store the panels?	Horizontally sleeping	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1200, width: 1400	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 350, width: 850	-
22	Is LAN cable under customer scope?	**No**	-
23	Is there any shadow that affects the solar installation?	**No**	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	**No**	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).





This route (using Staircase) will be followed to carry Small items.










Staircase Details




Meter Box

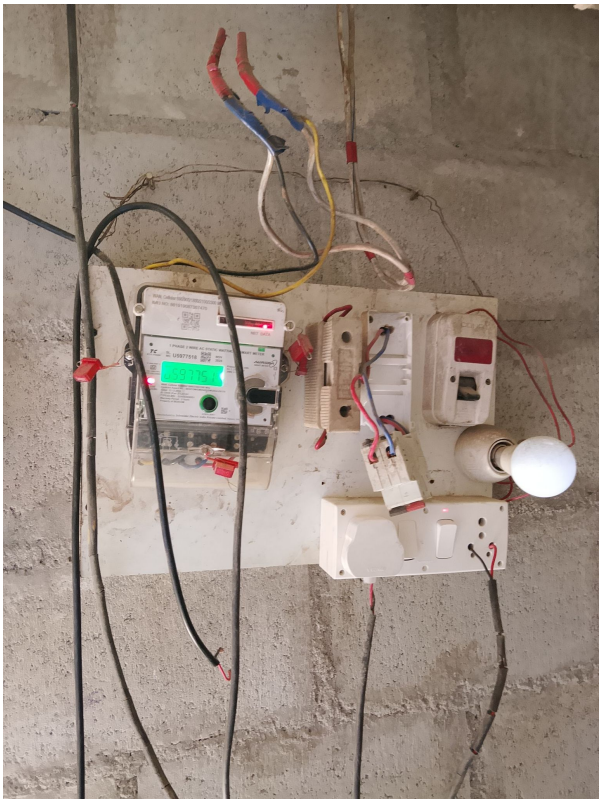

Material Storage



Proposed PV Area

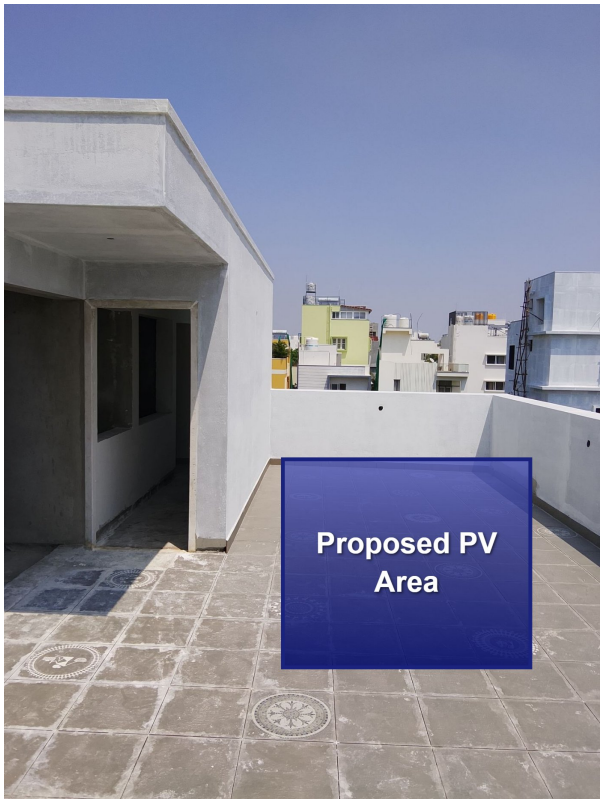

Cable Routing







The DC Cable will run through the existing 1 inch conduit pipe












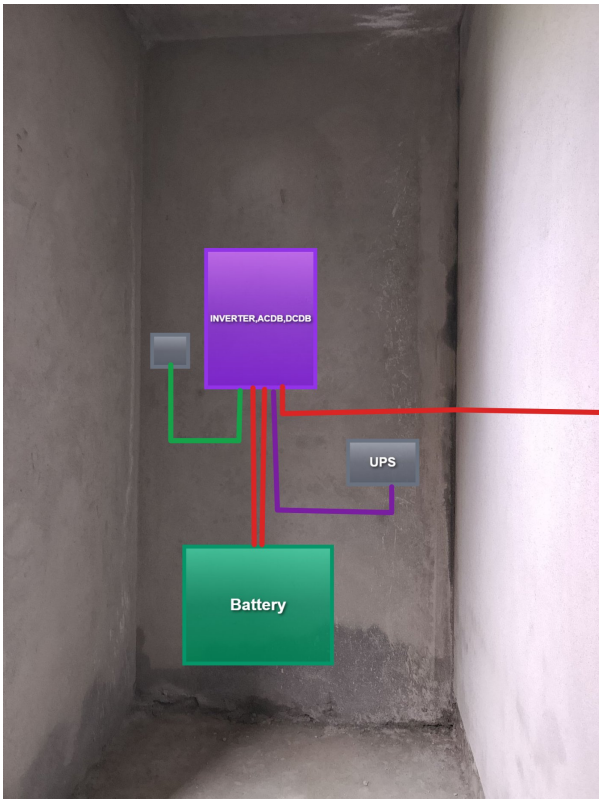

Make a hole to run the AC earthing cable till the earth pit location










Equipment Location

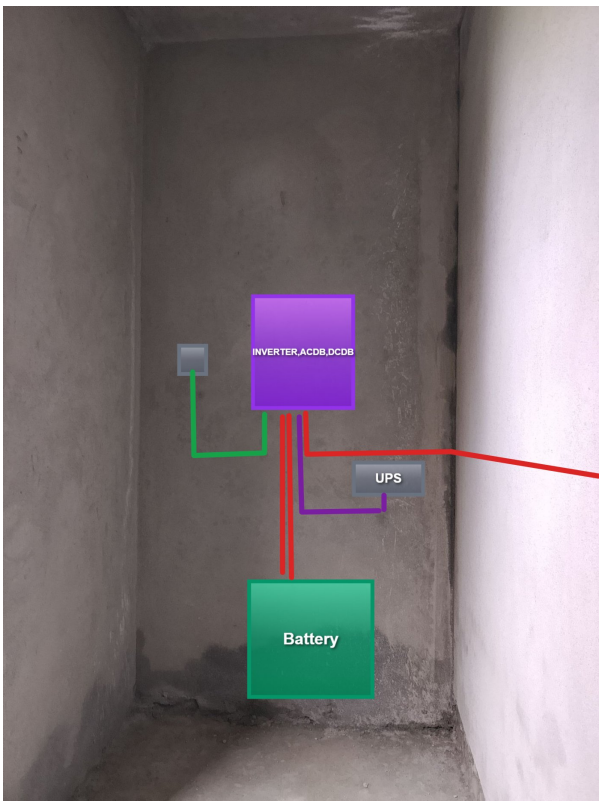





Earth Pit Location







Site Layout - Top View

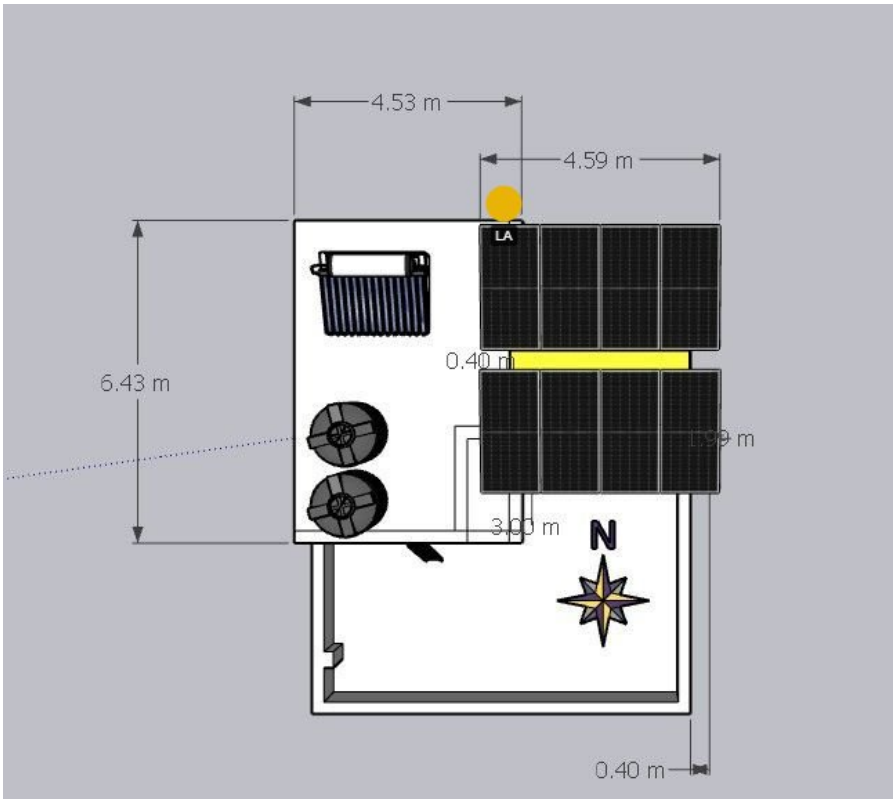
4.53 m
4.59 m
LA
6.43 m
0.40 m
3.00 m
N
0.40 m

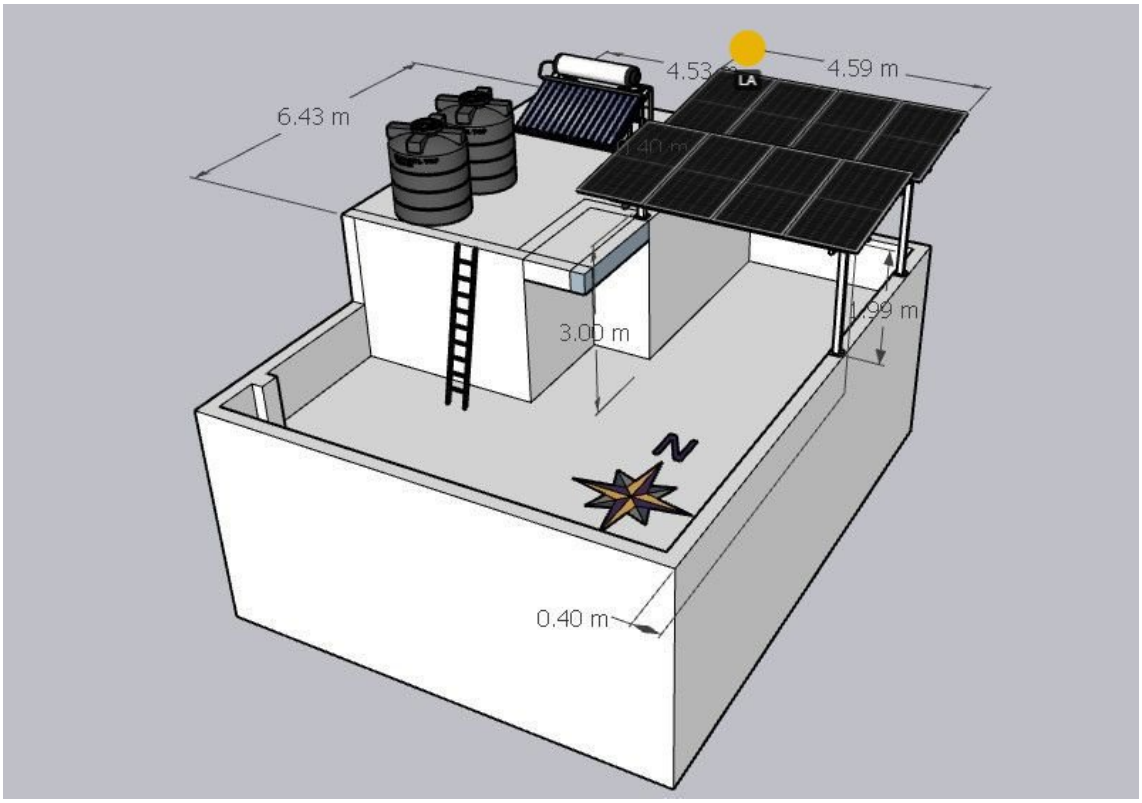
4.59 m
LA
6.43 m
3.00 m
N
0.40 m

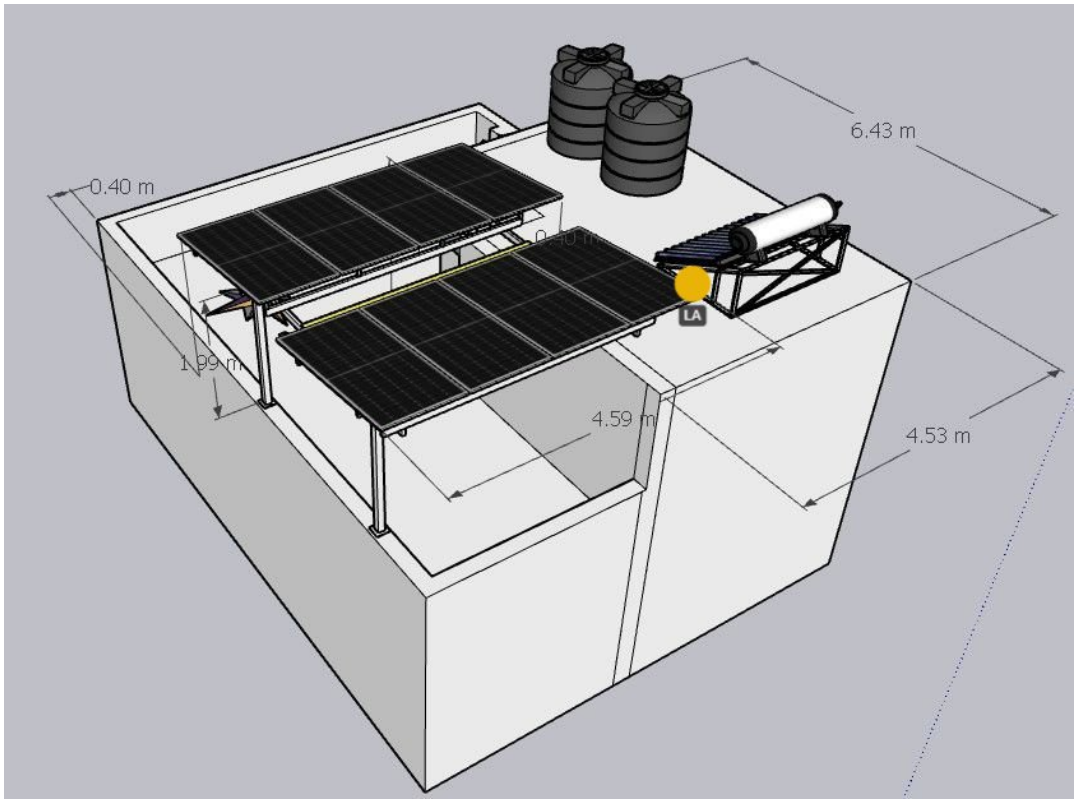

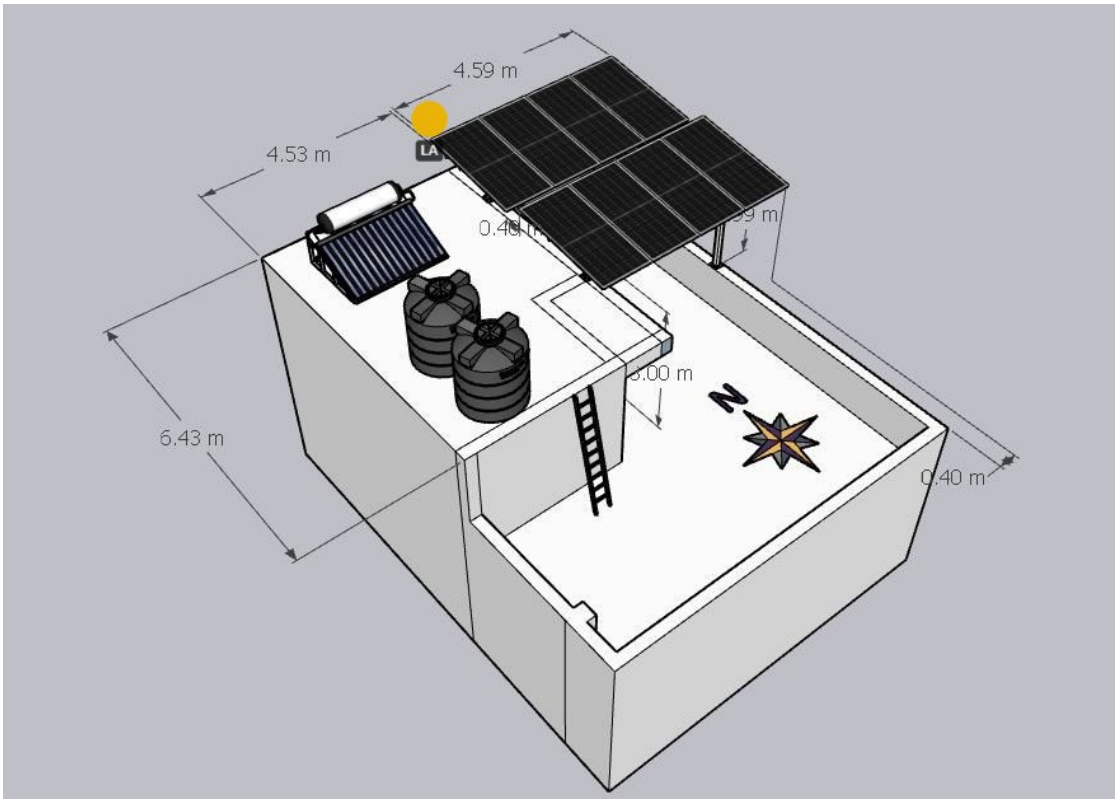

Building Exterior





OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	At the time of material lifting the existing scaffolding will be removed ,if not try to lift another route.

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	As per the client, site engineer suggestions only, the panel layout, cable, earthing routing has been considered.
3	UPS point near the inverter location is under customer scope.
4	MS fabrication is under customer scope.

THANK YOU

Dear Manju M,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
