Technical Site Visit Report

Prepared for: Sridevi MA_Tindlu_Subsidy_3.1kWp_String

PROJECT INFORMATION

Report Number	ESV-2026-0228
Project ID	05PJ5KJO
Project Name	Sridevi MA_Tindlu_Subsidy_3.1kWp_String
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Govindaraju JS
Site Address	17, 1st Cross Bank Colony, Thindlu Main Road, Vidyaranyapura, Bengaluru 560097.
GPS Coordinates	13.070573, 77.565781
Google Maps	https://www.google.com/maps?q=13.070573,77.565781
Visit Date	2026-10-13
Visited By	ABILASH N K
Revision	Rev 2

CLIENT INFORMATION

Client Name	Sridevi MA
Contact	+91 8892343889

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	3.10
Sanction Load (kW)	3
Module Make & Capacity	Premier 620Wp Topcon Bi-Facial DCR
Module Length (mm)	2382
Module Width (mm)	1134

Number of Panels	5
Inverter Type	String
Inverter Brand	Inverter Deye (SUN-3K-G04) 3kW 1 Ph
Number of Inverters	1
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	**No**	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The inverter, DCDB and ACDB can be mounted on the wall, near to the existing meter box in the ground-floor car porch.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	Yes, discussed with the customer and finalised the location for earthing at the car porch area after removing the tile of required size.	-
6	Where is the Internet Router located?	Currently available in the 1st floor.	*The customer will provide a reliable Wi-Fi router near to the inverter location during the installation.*
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	**No**	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-

#	Question	Answer	Notes
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*Elevated HDGI - 2m Front Leg (2 Rows, Portrait) with Drilling & Only Base Plate Cement Covering*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	*The upper headroom can be accessed via a metal staircase provided.*
11	Is the building currently under construction?	**No**	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	16 Metres. (G + 3 + Headroom)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital, If 3-phase: N/A	*It is a smart meter.*
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	*The location for earthing is available at the car porch area by removing the tile of the required size.*
12	In case of elevated structures, is an LA extension provided at the far end?	Yes	*The LA extension has to be considered.*
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	**No**	-
16	Is space present in rooftop to store the panels?	Vertically leaning	-

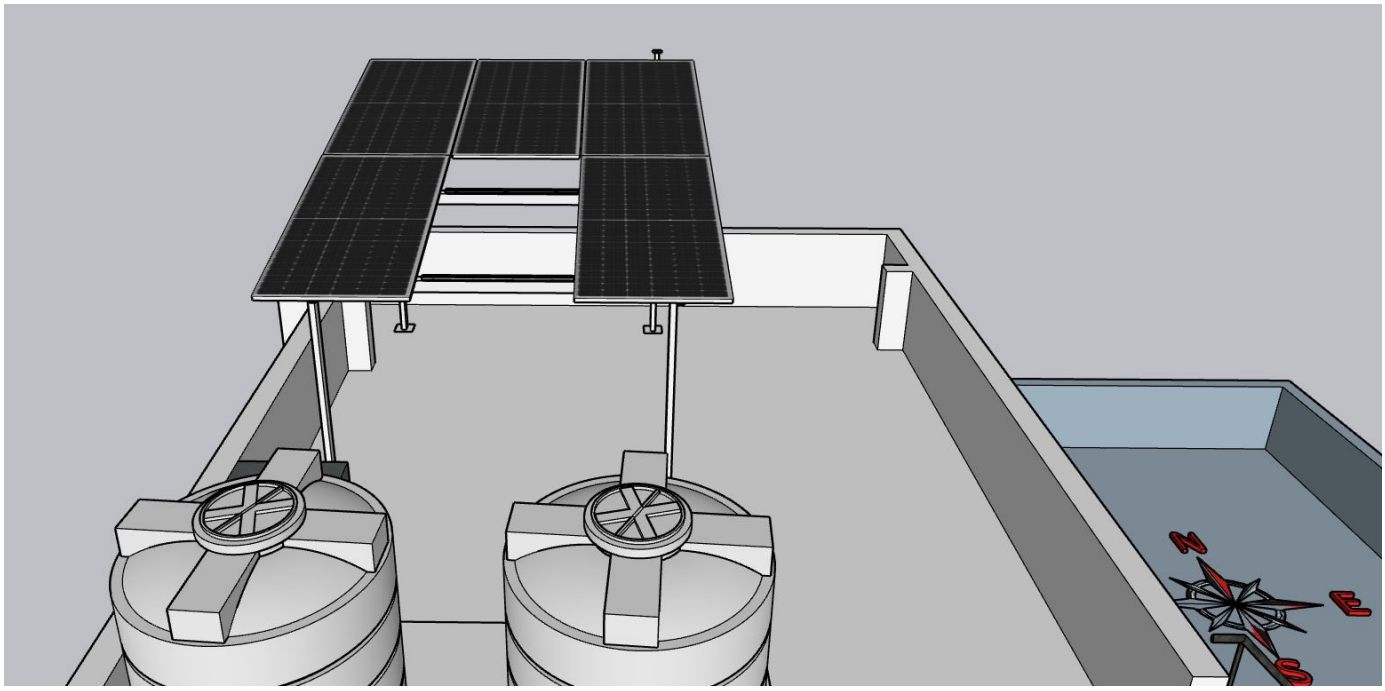
#	Question	Answer	Notes
		against the wall	
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	All are wall mounted.	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 300, width: 300	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 2000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-


PHOTO DOCUMENTATION


Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA


Site Layout - Top View



N
E
S

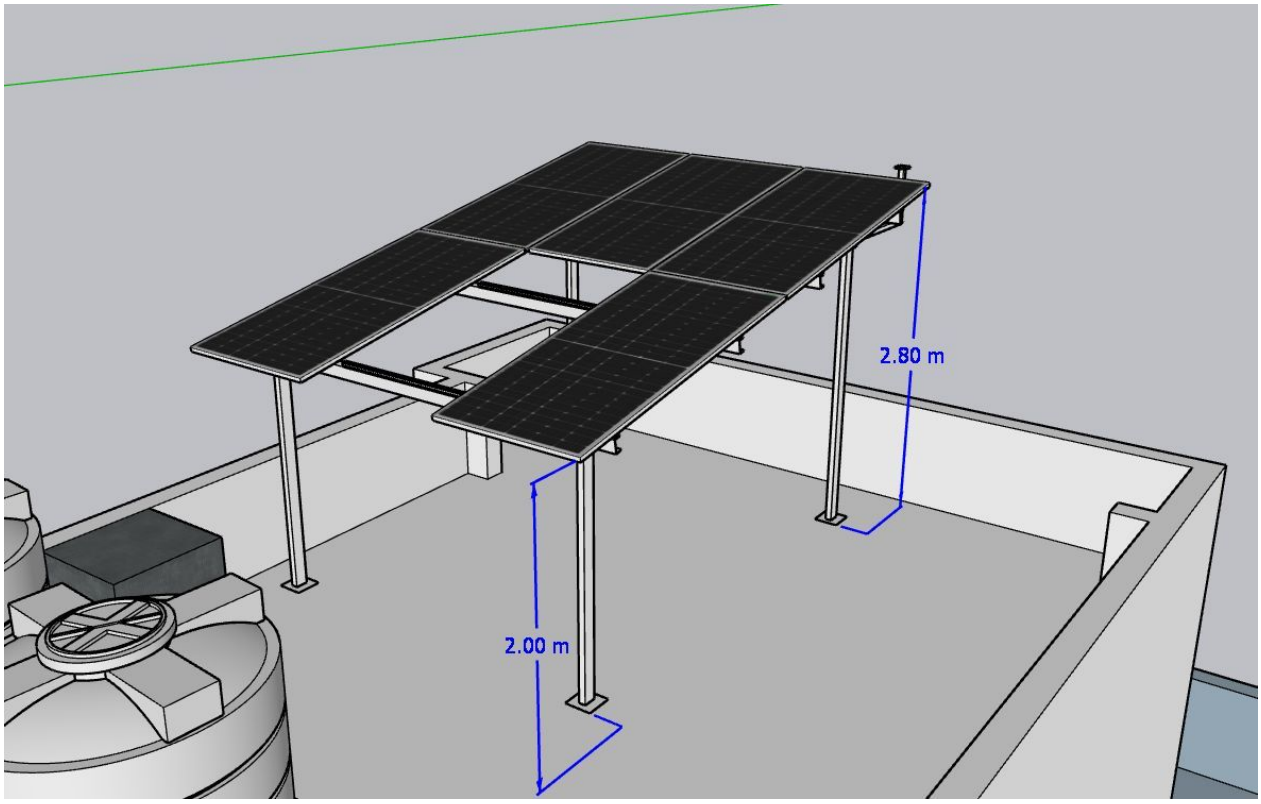

2.80 m
2.00 m

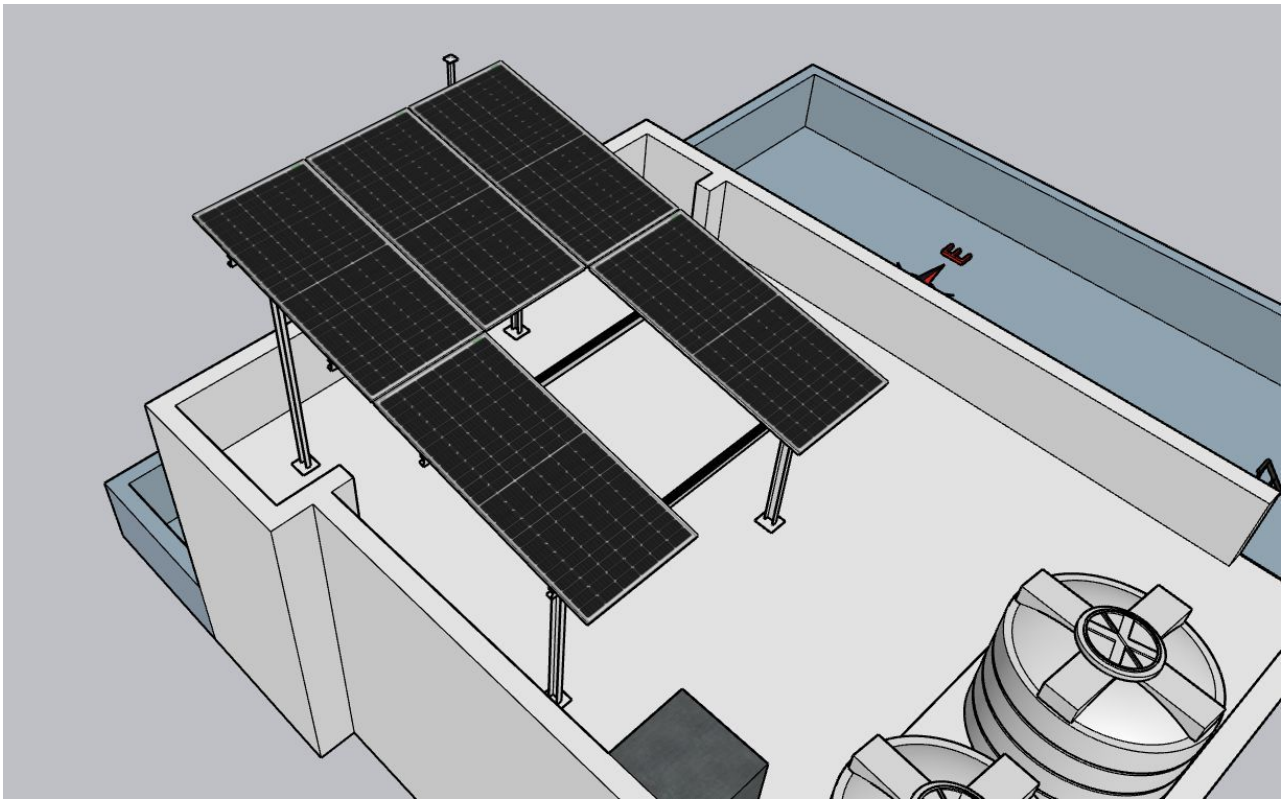

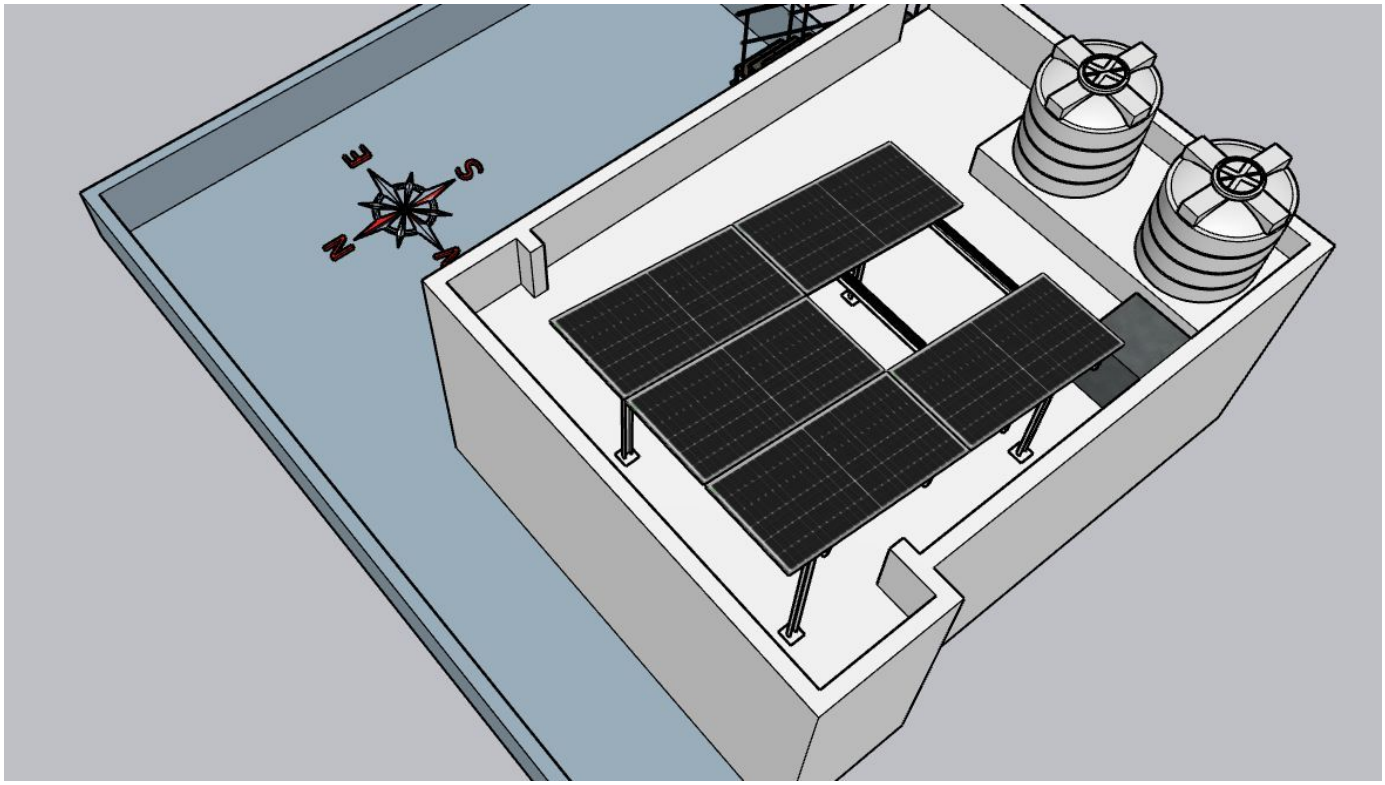
E
S
W
N

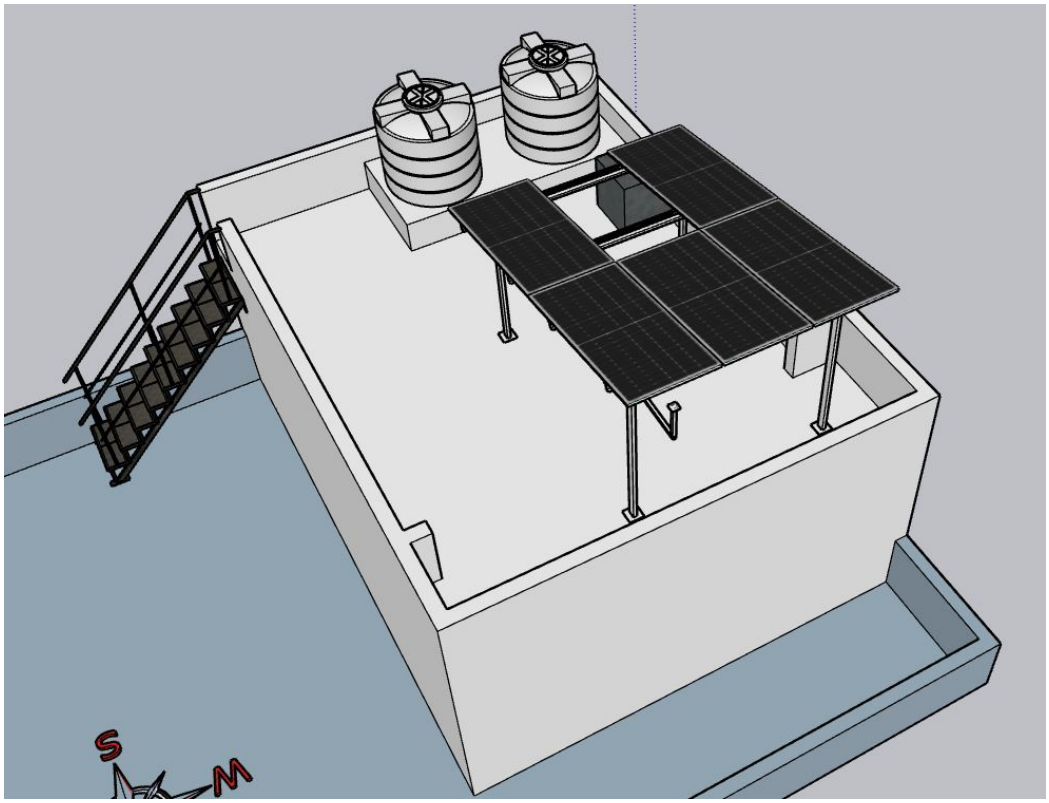
S
M

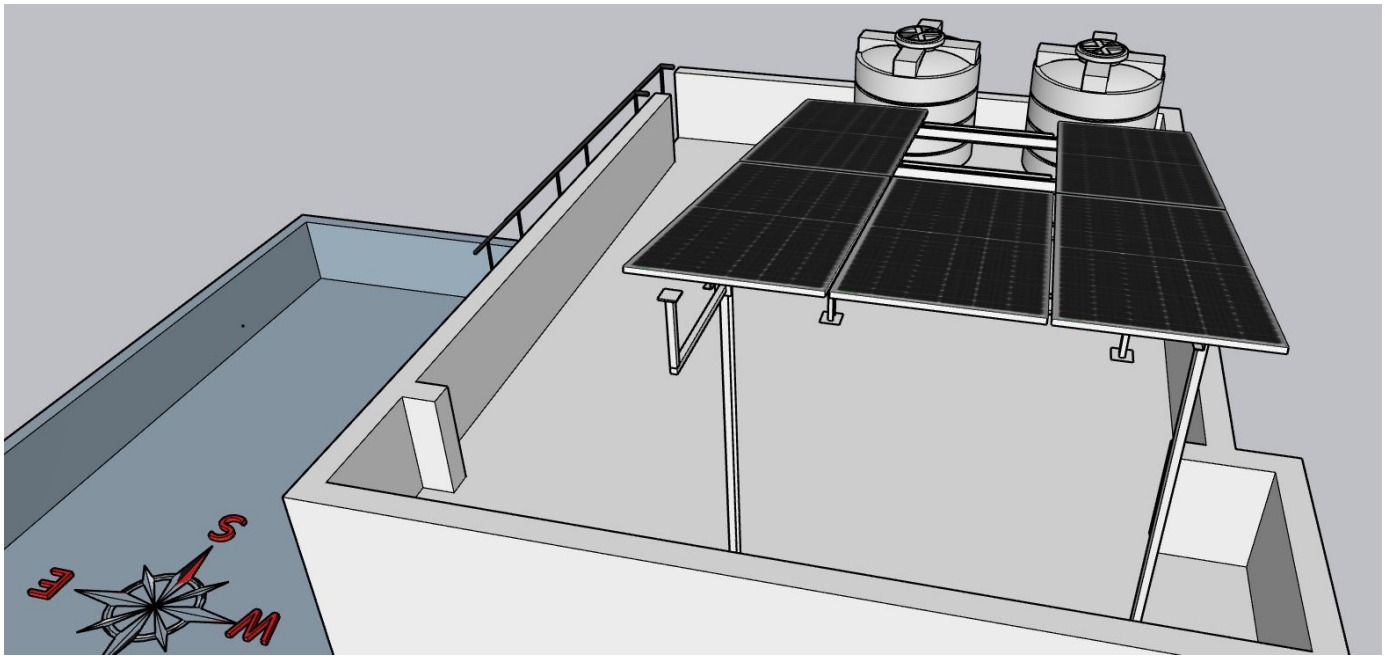
S
E
M

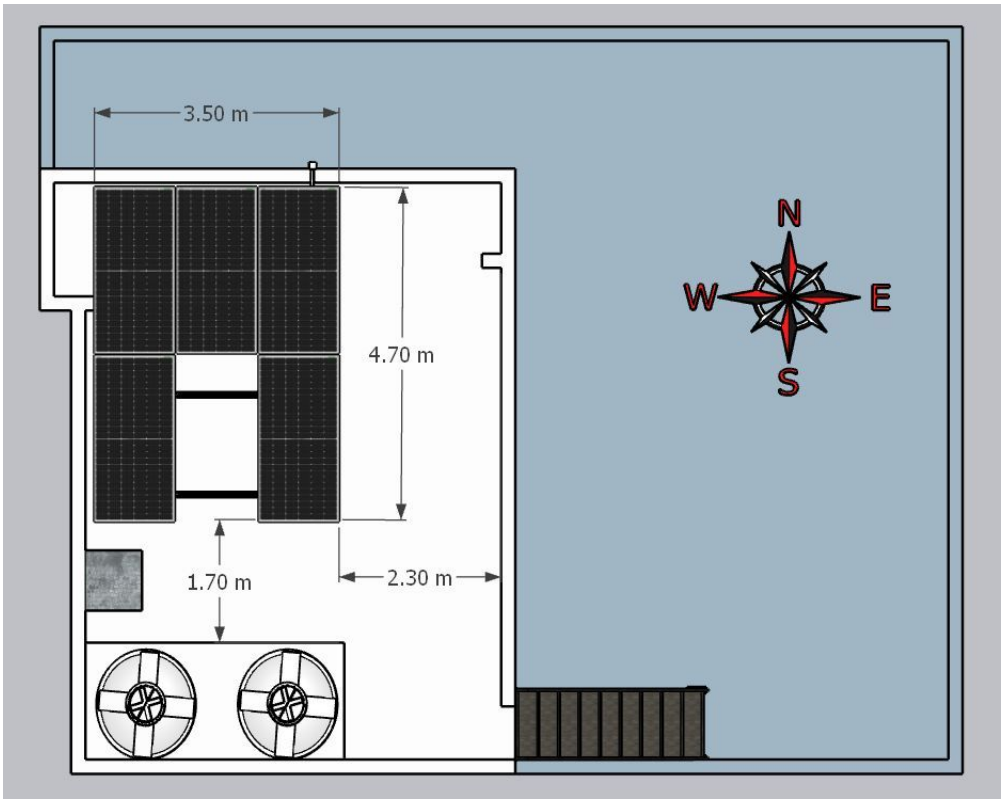

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



The materials can follow the stairs until reaching the terrace.



The materials can follow the stairs until reaching the terrace.



The materials can follow the stairs until reaching the terrace.



The materials can follow the stairs until reaching the terrace.



The materials can follow the metal stairs to access the upper terrace.

Staircase Details



Staircase width: 900 mm

Material Storage




The materials can be stored here in the lower terracce before shifting to the upper terrace for installation.

Proposed PV Area




Cable Routing

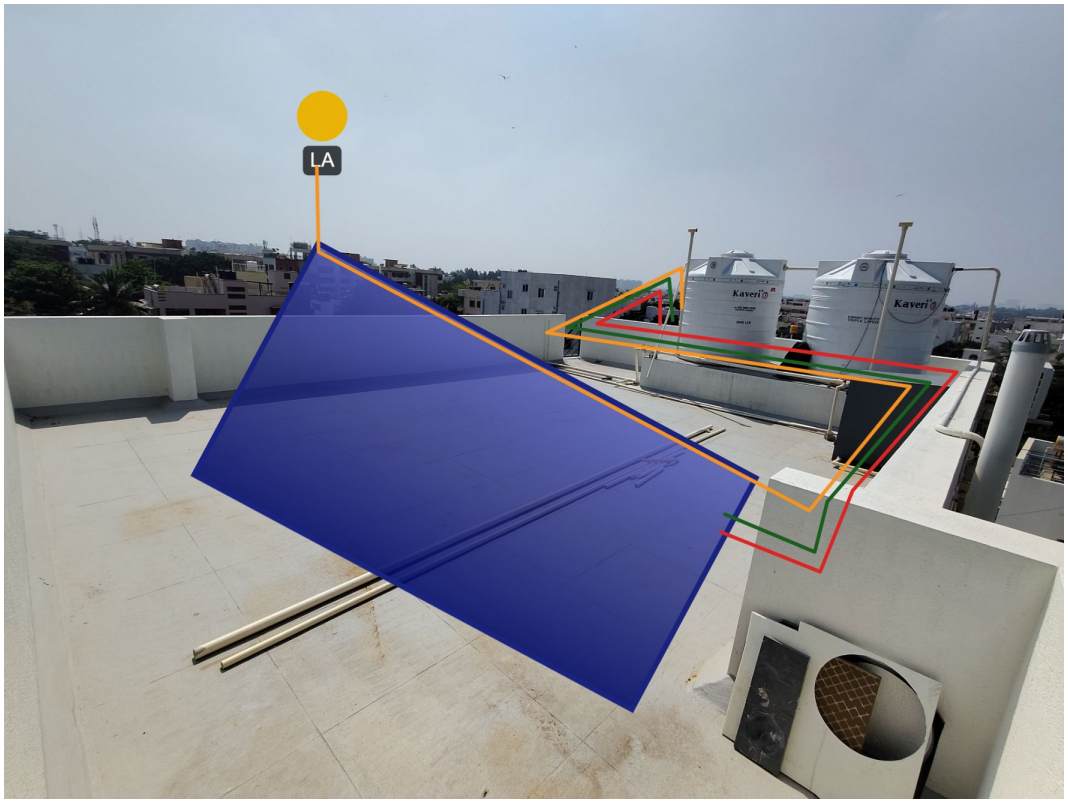







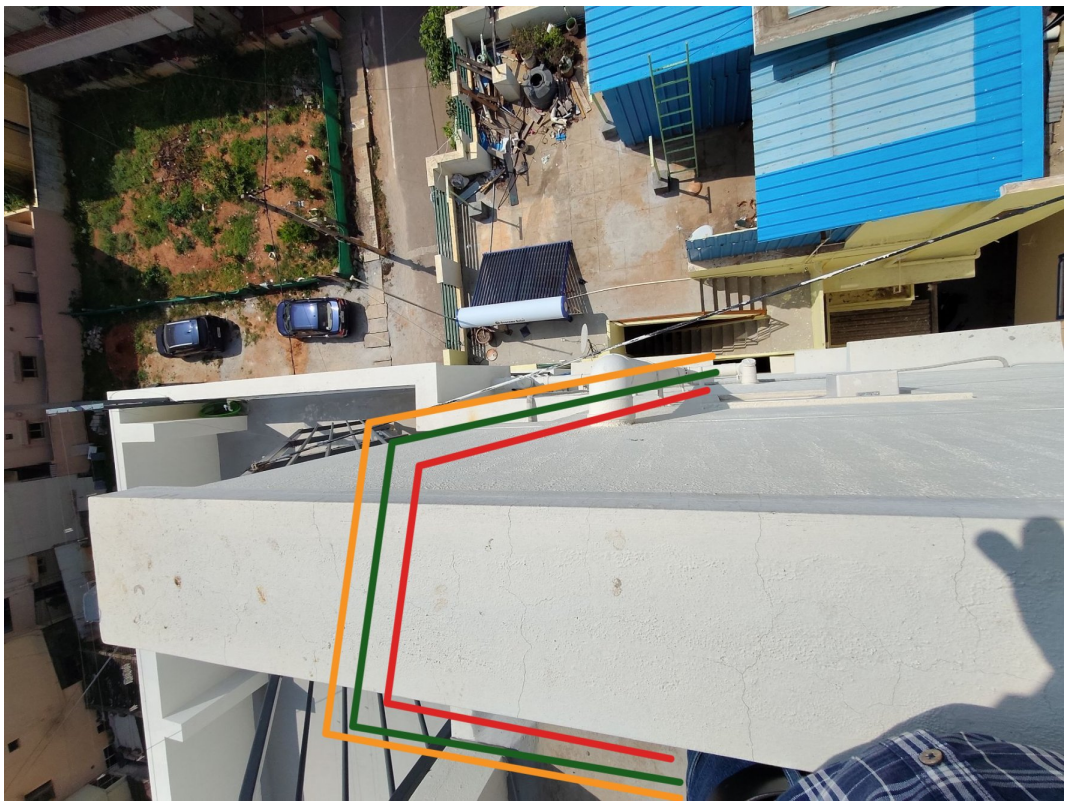




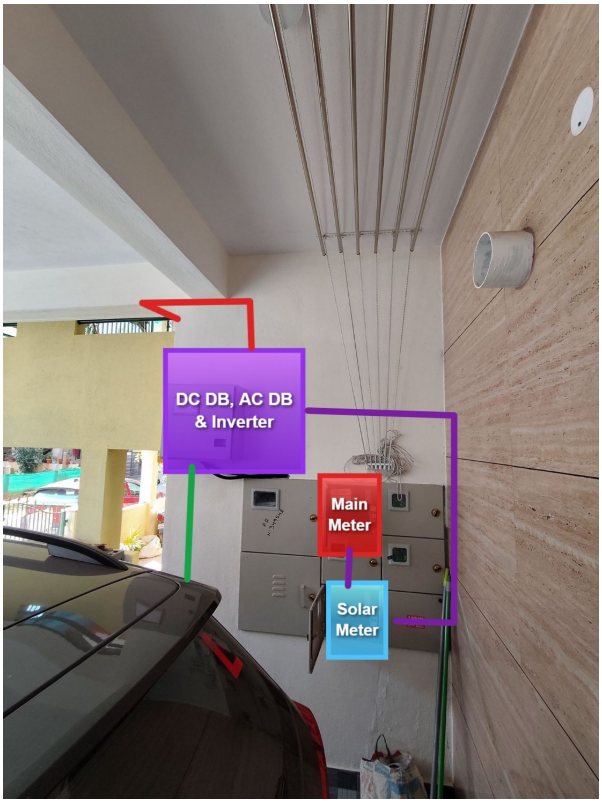


DC DB, AC DB
& Inverter
Main
Meter
Solar
Meter

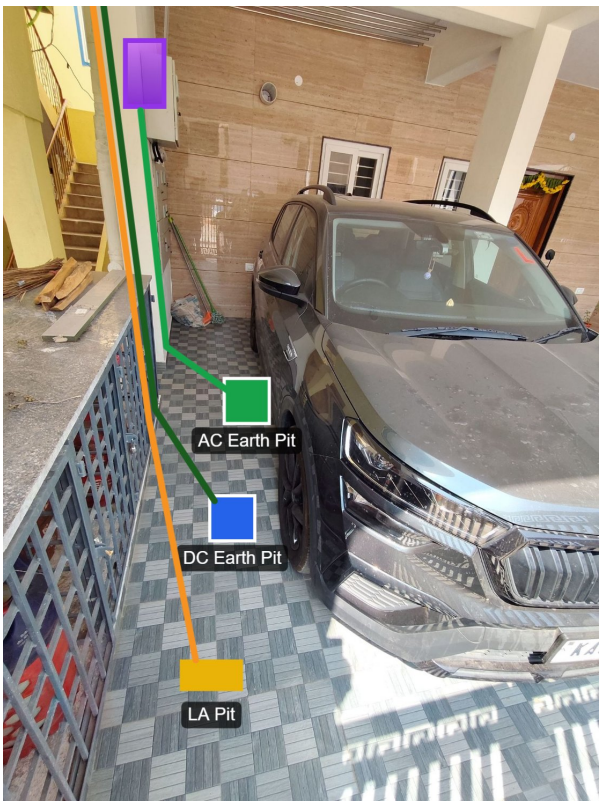

Meter Box

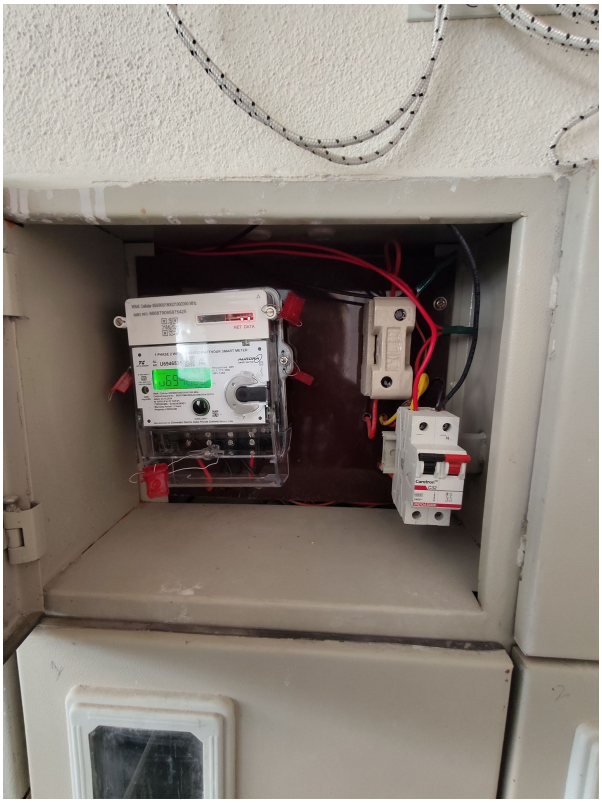



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 3.1 kWp On-Grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.

THANK YOU

Dear Sridevi MA,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
