Technical Site Visit Report

Prepared for: Kothamasu Dinesh(ram teja)_Myhna medows_4.96kWp_On Grid. - Villa #49

PROJECT INFORMATION

Report Number	ESV-2026-0140
Project ID	050DED20
Project Name	Kothamasu Dinesh(ram teja)_Myhna medows_4.96kWp_On Grid.
Building Name	Villa #49
Billing Name	Kothamasu Dinesh(ram teja)
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Hariom
Site Address	Myhna Meadows, Villa 49, Gunjur, 560087
GPS Coordinates	12.923051, 77.7353799
Google Maps	https://www.google.com/maps?q=12.923051,77.7353799
Visit Date	2026-06-11
Visited By	K Naveen
Revision	Rev 2

CLIENT INFORMATION

Client Name	Kothamasu Dinesh(ram teja)
Contact	+91 80192 69762

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	4.96
Sanction Load (kW)	5

Module Make & Capacity	Adani DCR bifacial 620 Wp
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	8
Inverter Type	SolarEdge
Inverter Brand	5 kW 3 phase On-Grid
Number of Inverters	1
Number of Optimizers	8
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	**No**	*The existing chajjas are the obstacles that could hinder the material lifting*
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter, DCDB, ACDB will be installed near the headroom.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	The location of the earth pits are near the meter location which is north side corriodor	-
6	Where is the Internet Router located?	Ground floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	2 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	*PUF Sheet roof*
2	Are there any obstructions on the roof that could affect the solar installation?	**No**	-
3	What is the angle of the panels? (in degrees)	5	-

#	Question	Answer	Notes
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	0	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Other	*Aluminum short rail structure.*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Not Applicable	-
13	What is the height of the building and how many floors does it have?	The height of the building is G+2+headroom is approximately 12 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	**No**	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	**No**	*Not Available*
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	Not Applicable	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	N/A	-
15	Are there any safety risks associated with accessing the roof for installation?	N/A	-
16	Is space present in rooftop to store the panels?	Horizontally	-

#	Question	Answer	Notes
		sleeping	
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	No	*During the site visit not yet constructed*
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Under construction	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1500, width: 1500	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1500, width: 800	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).





This route (using Staircase) will be followed to carry Small items.






Staircase Details



Meter Box



Material Storage

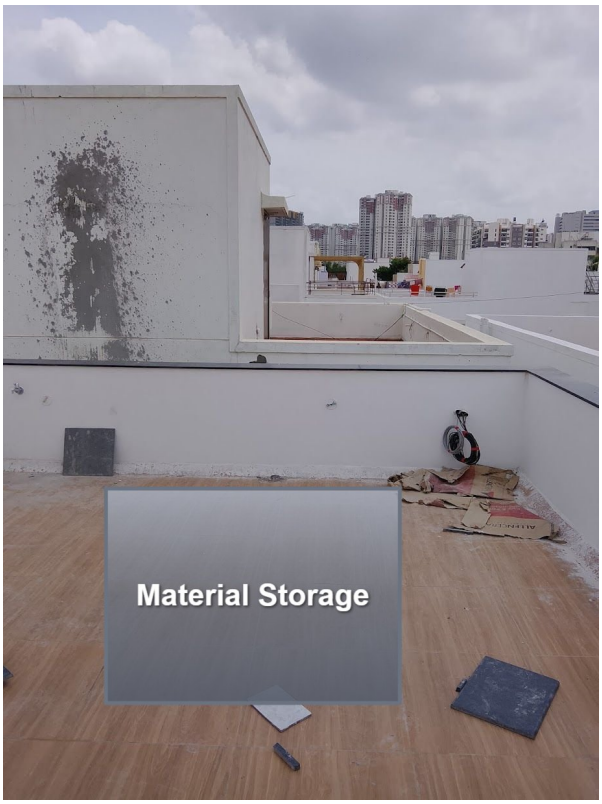

Proposed PV Area





Cable Routing





Asian Paints
Apex
Ultima
Protek
Exterior
Emulsion


LA






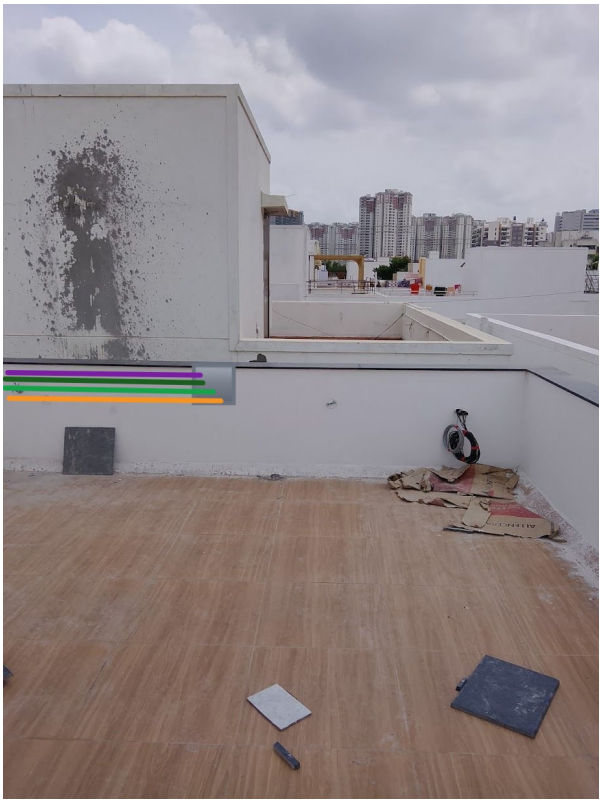

Make a hole to run the AC cable, AC,DC,LA earthing, till the meter and earth pit location



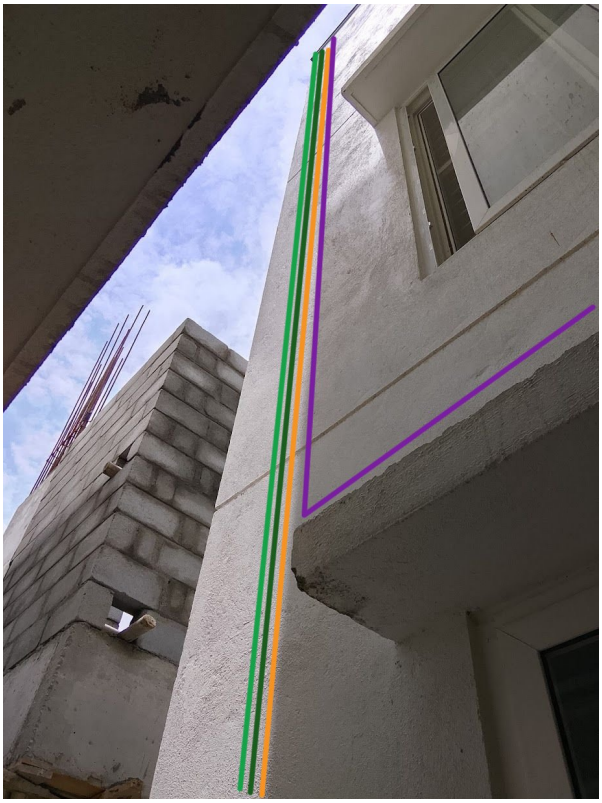




Equipment Location





Earth Pit Location





Site Layout - Top View

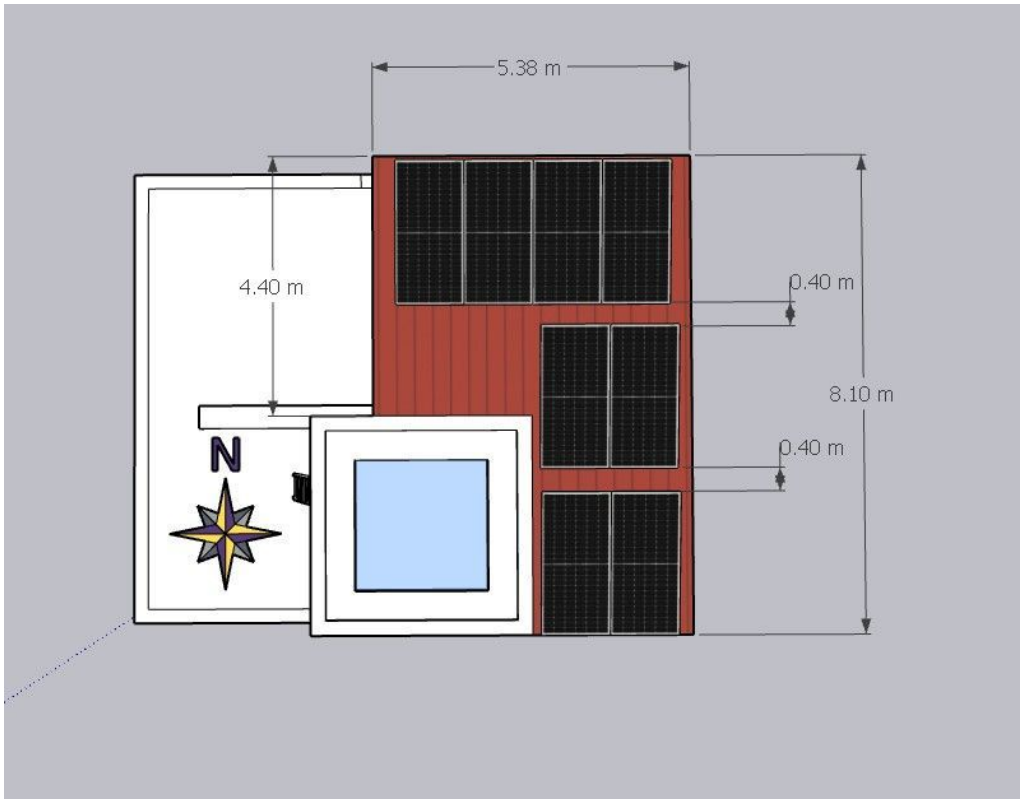

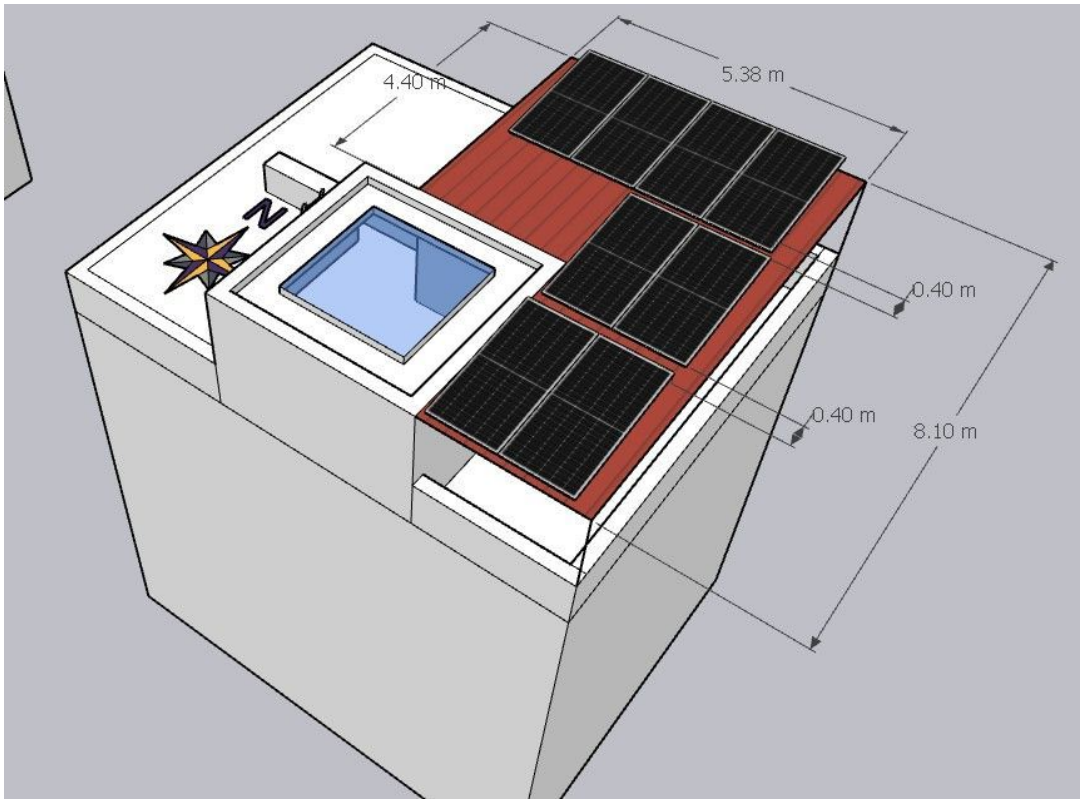
4.40 m
5.38 m
0.40 m
0.40 m
8.10 m

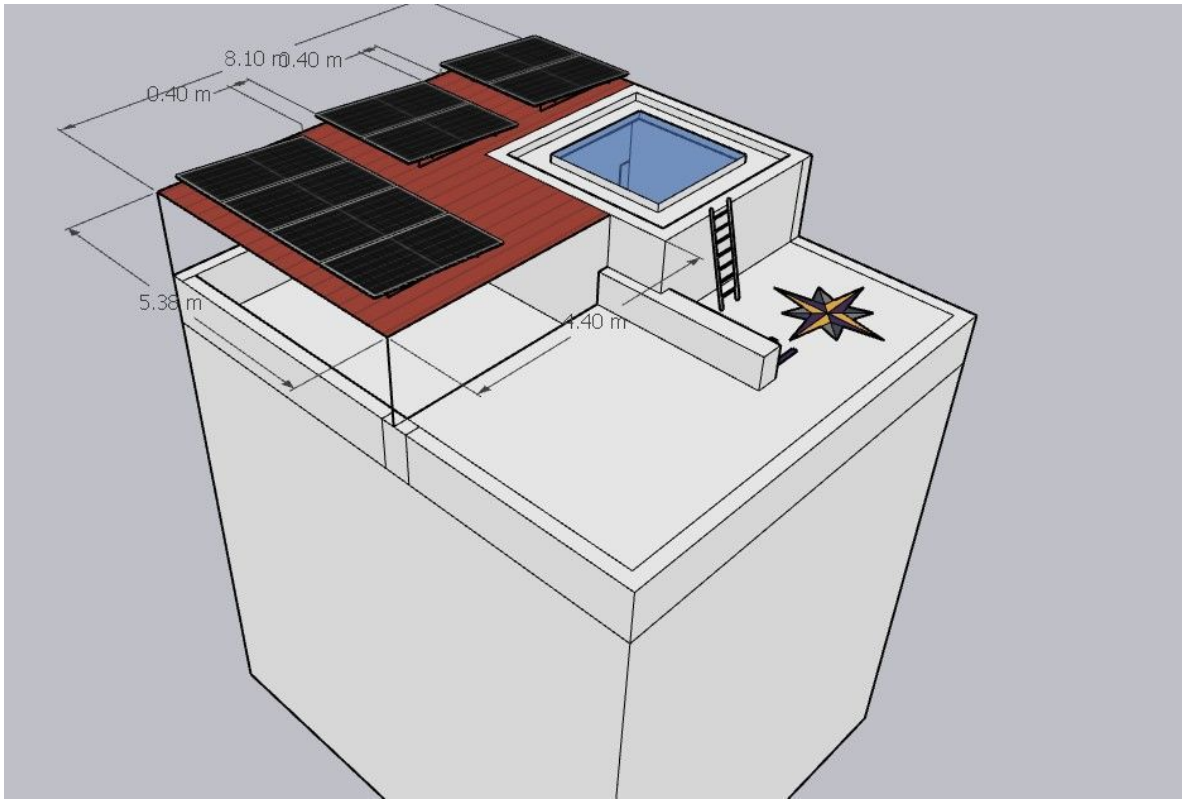
8.10 m
0.40 m
0.40 m
5.38 m
4.40 m

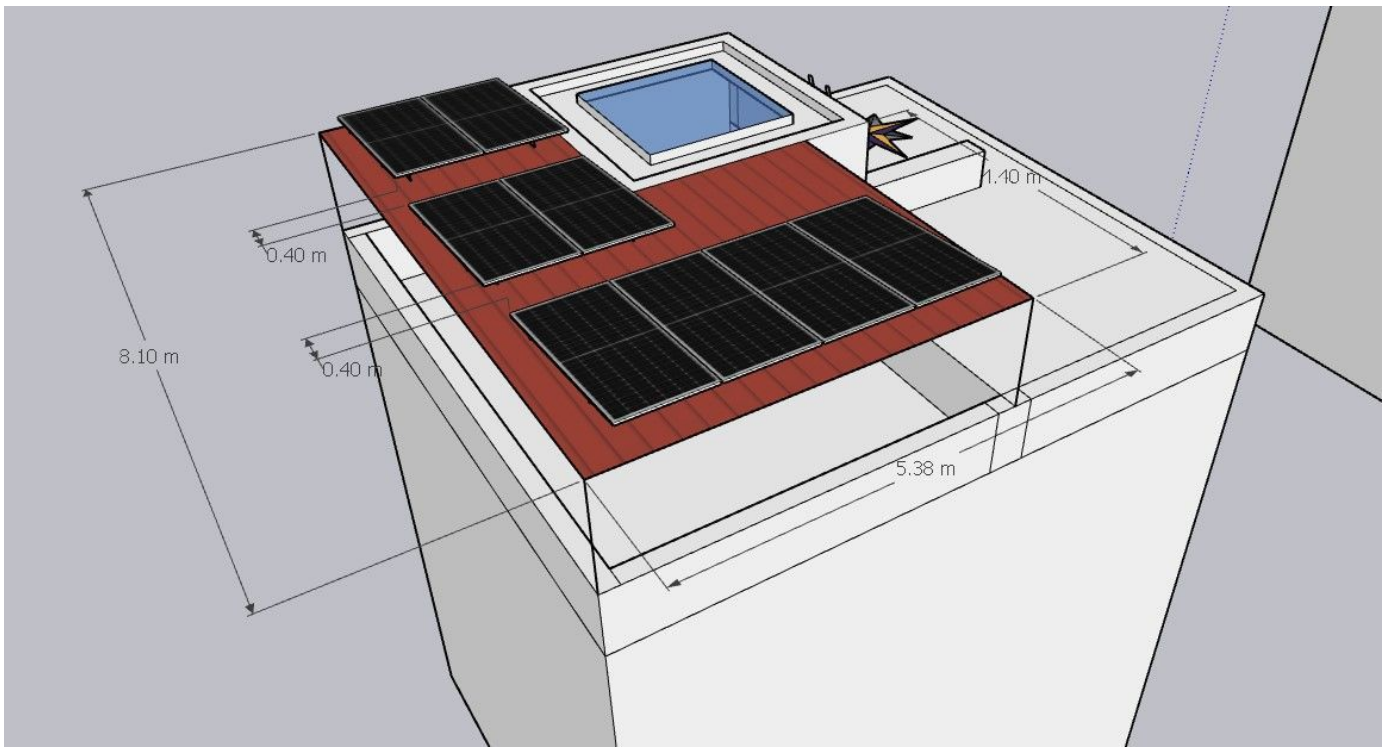
1.40 m
0.40 m
8.10 m
0.40 m
5.38 m

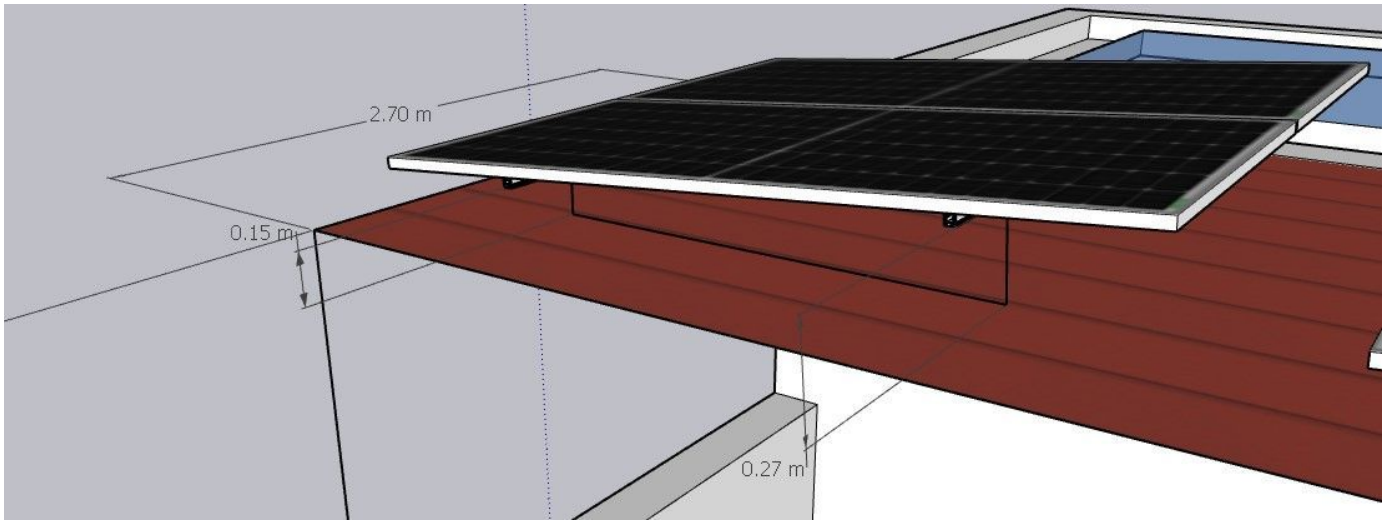
2.70 m
0.15 m
0.27 m



Profile pitch of the sheet roof

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	As per the customer suggestions only the earthing, cable routing has been considered
3	Due to space consistence the AC,DC,LA earthing has to be installed by the north west corner
4	During the site visit there is no puf sheet based on the building outline dimensions only the sheet has bee designed

THANK YOU

Dear Kothamasu Dinesh(ram teja),

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
