Technical Site Visit Report

Prepared for: Ms. Kirti Prabhu & Ms. Lata Prabhu_Embassy Springs_Plot no 22-22_9.92kWp_Hybrid

PROJECT INFORMATION

Report Number	ESV-2026-0233
Project ID	SE9DGN0F
Project Name	Ms. Kirti Prabhu & Ms. Lata Prabhu_Embassy Springs_Plot no 22-22_9.92kWp_Hybrid
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	Plot No. 22-22, By the Lake, Embassy Springs, Nagamangala Village, Kundana Hobli Devanahalli Taluk - 562110.
GPS Coordinates	13.211665, 77.613966
Google Maps	https://www.google.com/maps?q=13.211665,77.613966
Visit Date	2026-10-07
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	Ms. Kirti Prabhu & Ms. Lata Prabhu
Contact	+91 9886070002

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	9.92
Sanction Load (kW)	15
Module Make & Capacity	Premier bifacial DCR, 620 Wp
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	16
Inverter Type	Hybrid (String)
Inverter Brand	Deye: 15KW - 48V - LV - Three Phase
Number of Inverters	1
Battery	Needed
Number of Batteries	2
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye SE-F5plus
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	**No**	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The carport wall is available on the ground floor to house the ACDB, DCDB, INVERTER & BATTERIES.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	Yes. 3 nos of earth pits can be dug near the carport area. (The soil available at the building setback space on the south side)	-
6	Where is the Internet Router located?	Not provided yet. Building under construction.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	*Elevated (HDGI) - Penetrative*
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*Mounting Structures: HDGI - 2m Front Leg with Grouting (16 panels)*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	12 (G + 2 + Headroom)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	No Meter	*Building under construction. A 3-phase LT panel is ready at the premises. Awaiting to be installed on the wall at the proposed location.*
2	Is the Meter cubicle photo matching with the previous answer?	No	*Building under construction.*
3	Has the termination point in the Main meter panel been identified?	No	*Building under construction.*
4	Is the Termination Point easily visible or sealed?	-	*Building under construction.*
5	Is a Lightning Arrestor (LA) already available at the site?	No	*The LA extension has to be provided with the HDGI structure.*
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-


#	Question	Answer	Notes
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	*3 nos of earth pits can be dug near the car port area. (The soil available at the building setback space on the south side)*
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	PVC chamber	-
13	In case of elevated structures, is an LA extension provided at the far end?	Yes	*The LA extension has to be provided with the HDGI structure.*
14	In case of elevated structures, is it with or without grouting?	With Grouting	-
15	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
16	Are there any safety risks associated with accessing the roof for installation?	**No**	-
17	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
19	Is ventilation available in the battery location?	Yes	-
20	Is Battery wall mounted or stand mounted?	Wall mounted	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	All accessories are wall mounted.	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 400, width: 400	*The solar meter cabin is available in the client's LT panel.*
23	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 500	-
24	Is LAN cable under customer scope?	Yes	-
25	Is there any shadow that affects the solar installation?	**No**	-
26	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-


PHOTO DOCUMENTATION


Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable


Site Layout - Top View

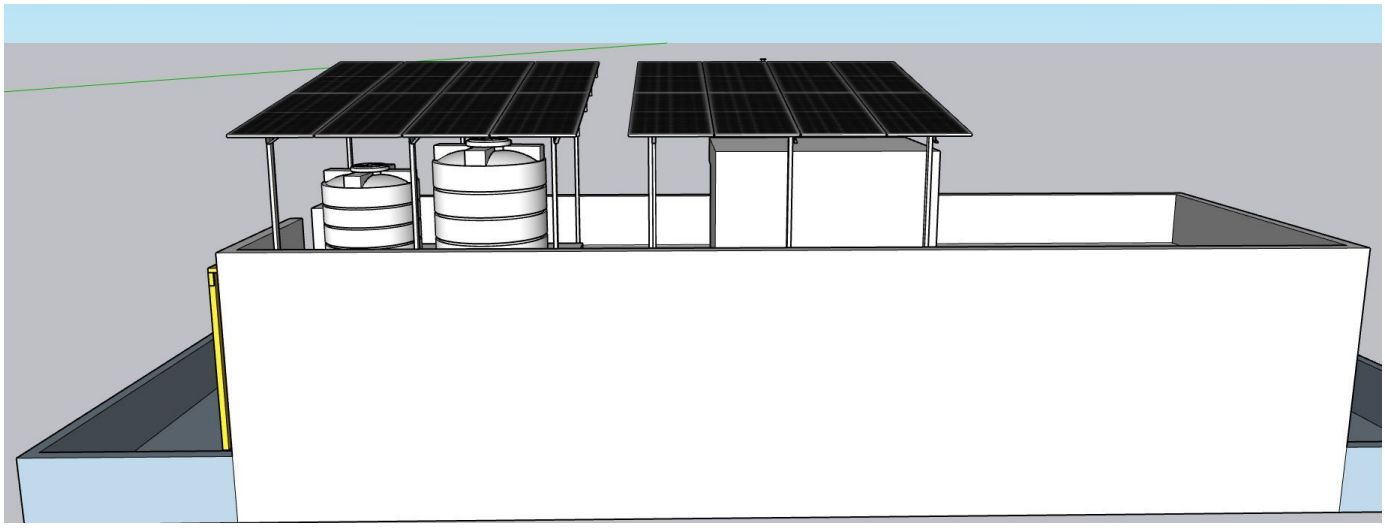


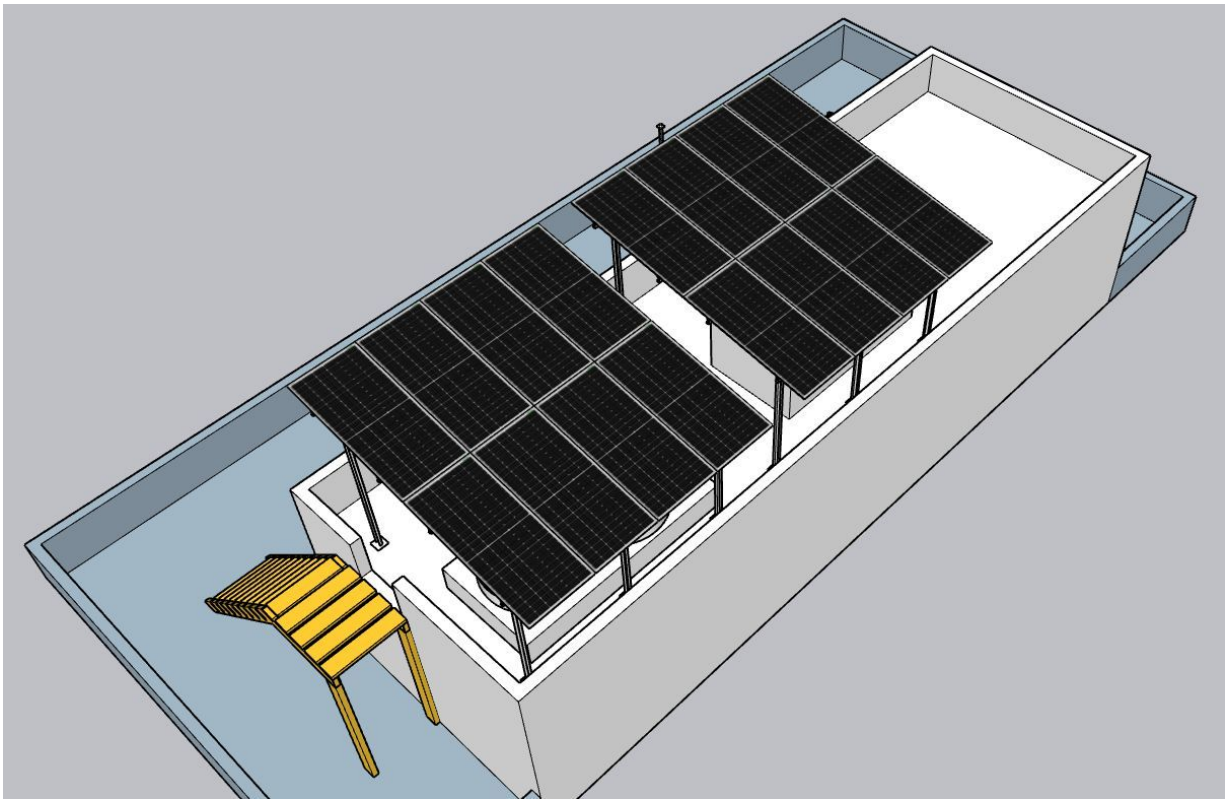


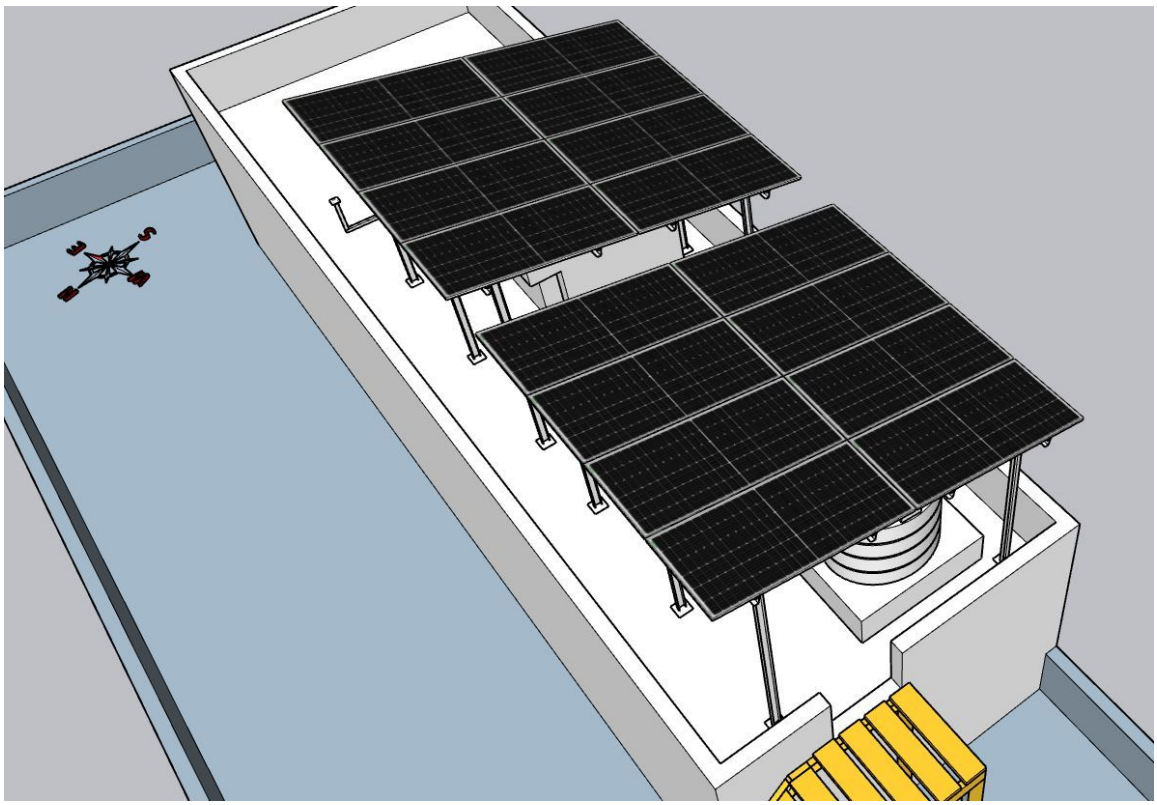


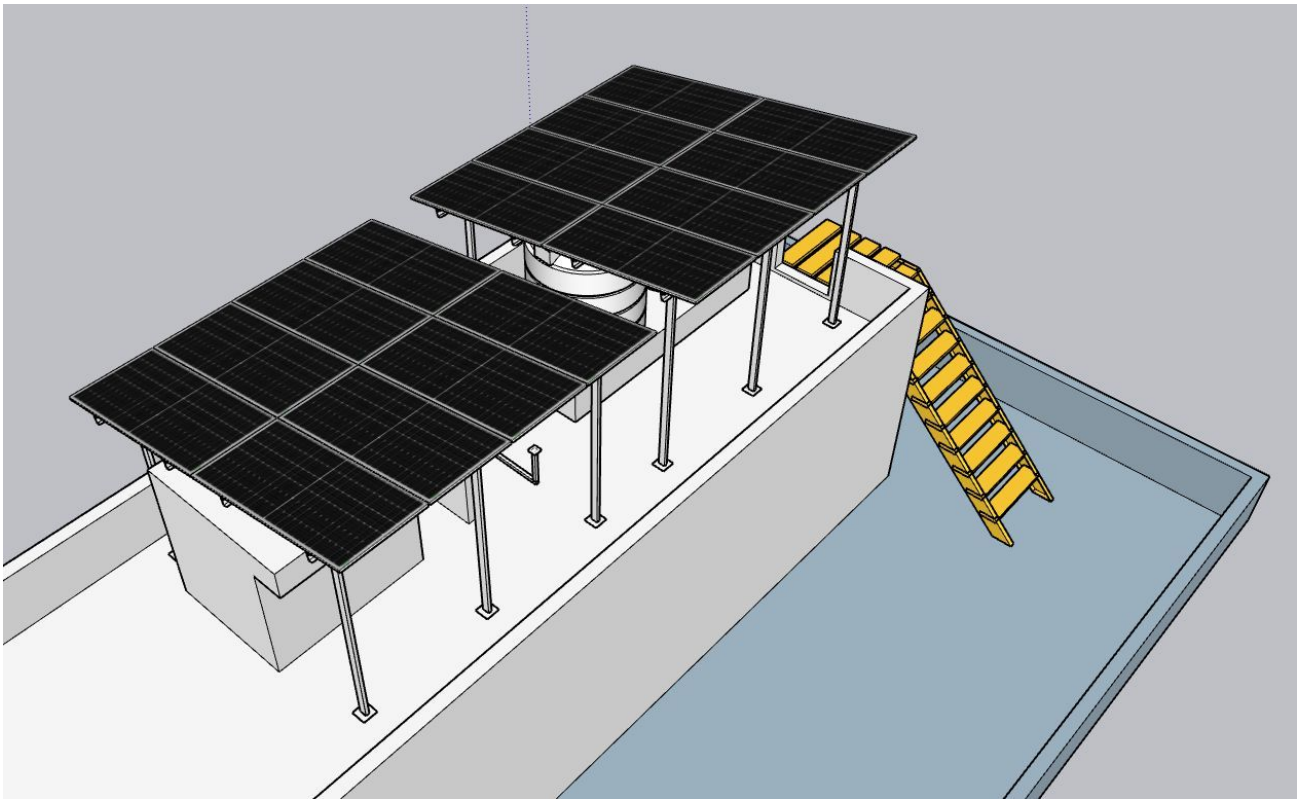


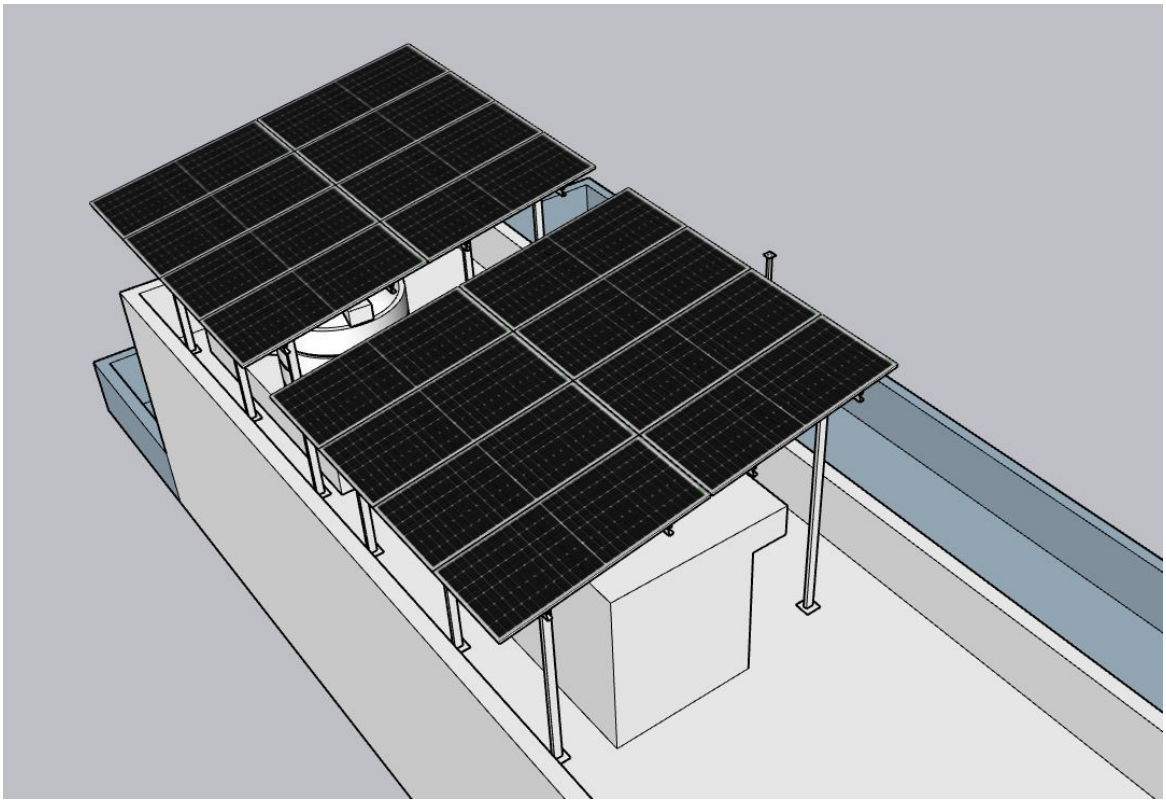


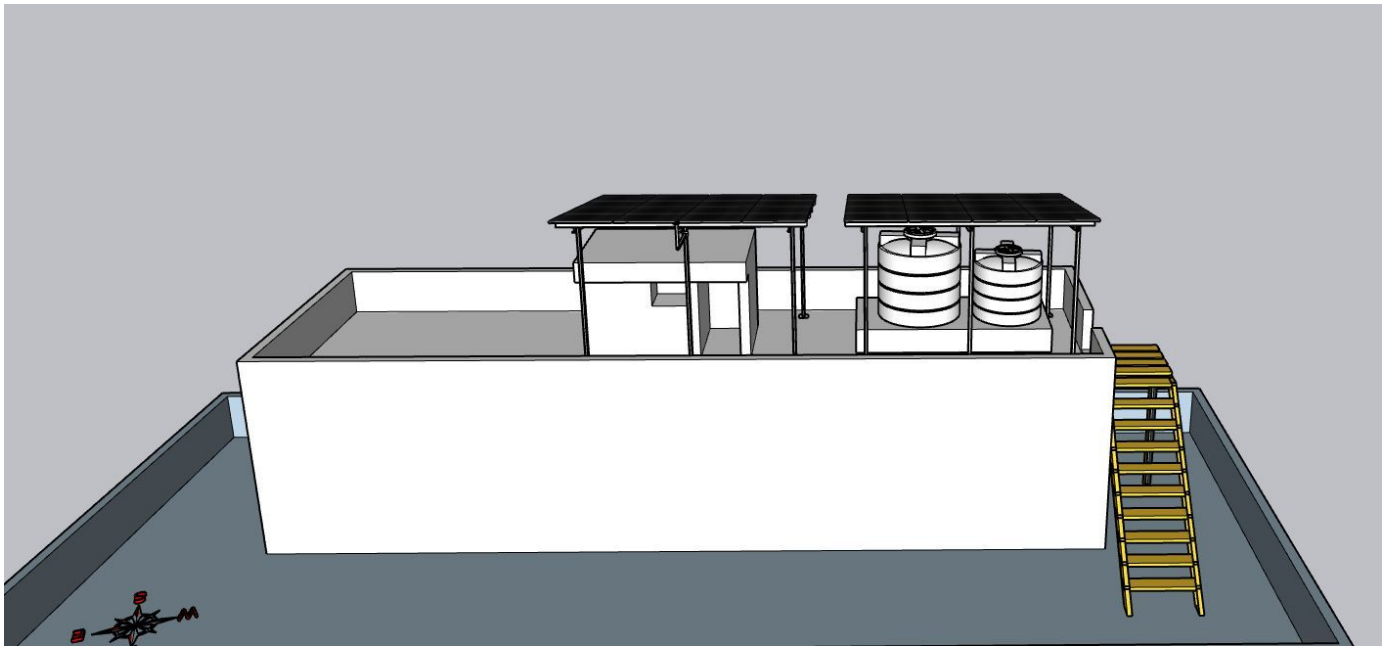


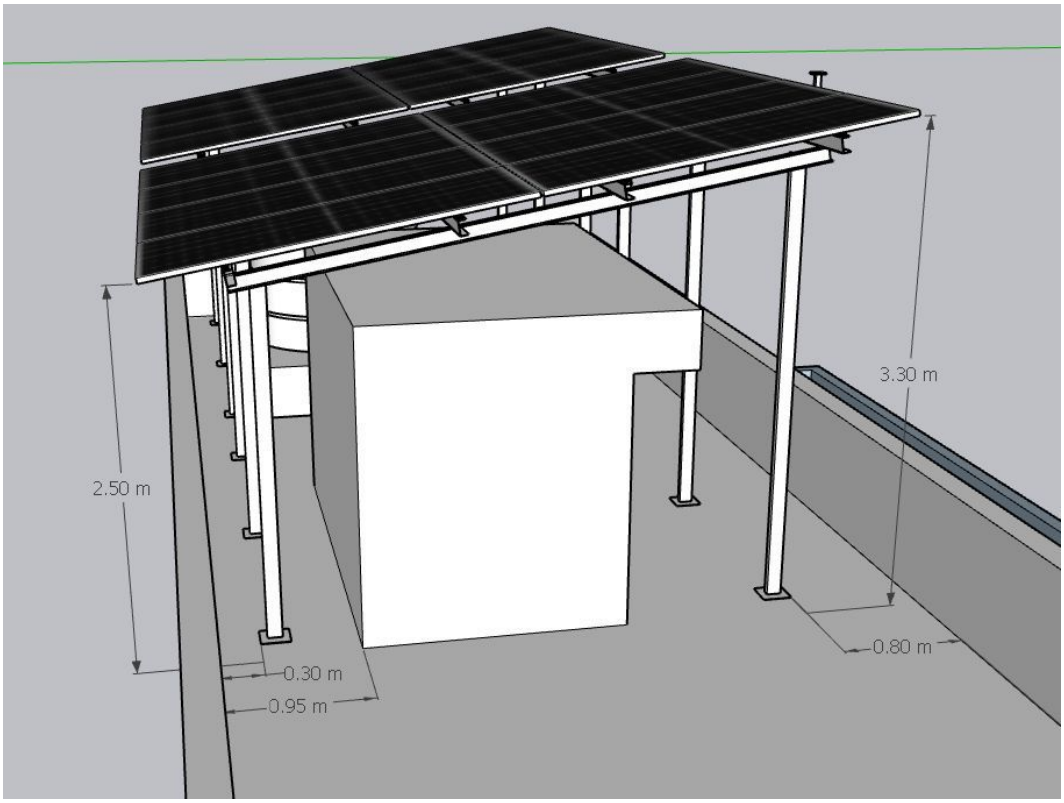
2.50 m
3.30 m
0.30 m
0.95 m
0.80 m

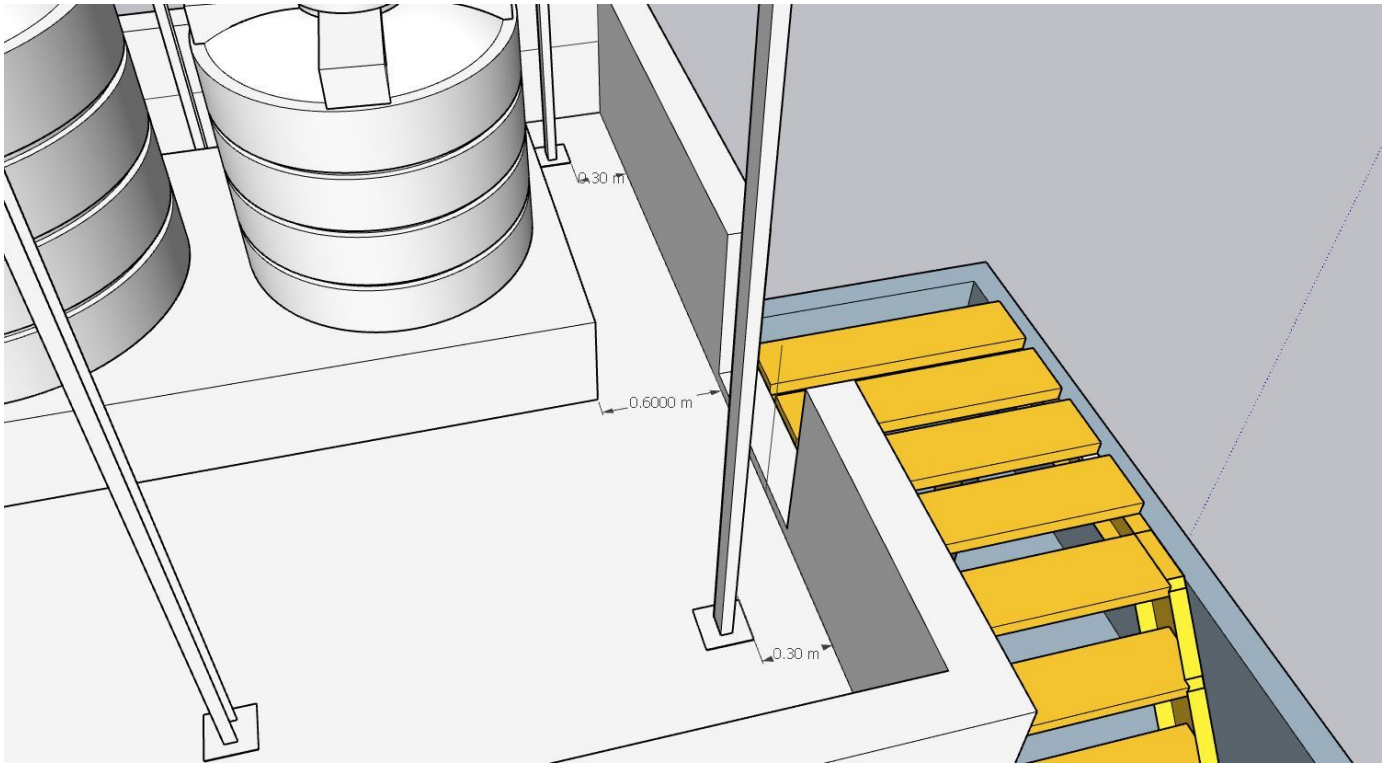
0.30 m
0.6000 m
0.30 m

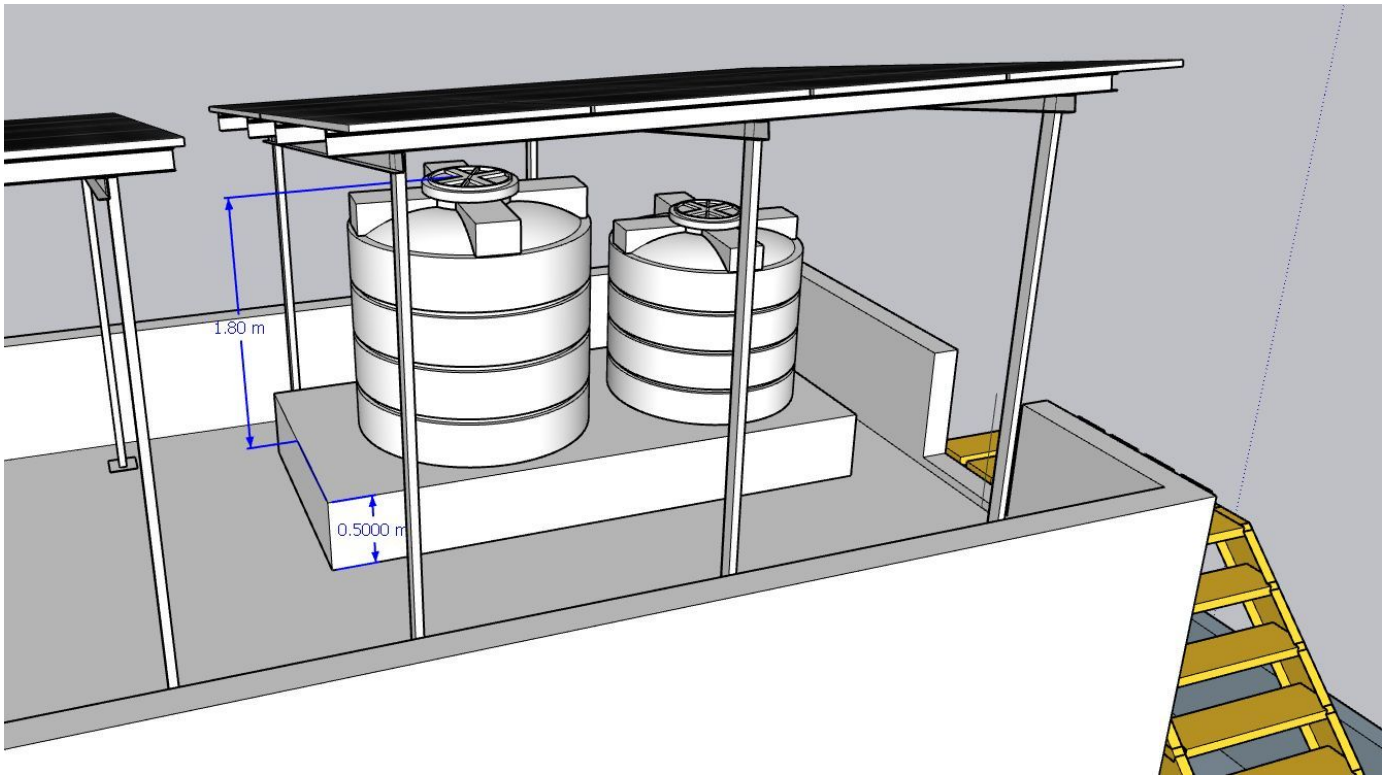
1.80 m
0.5000 m

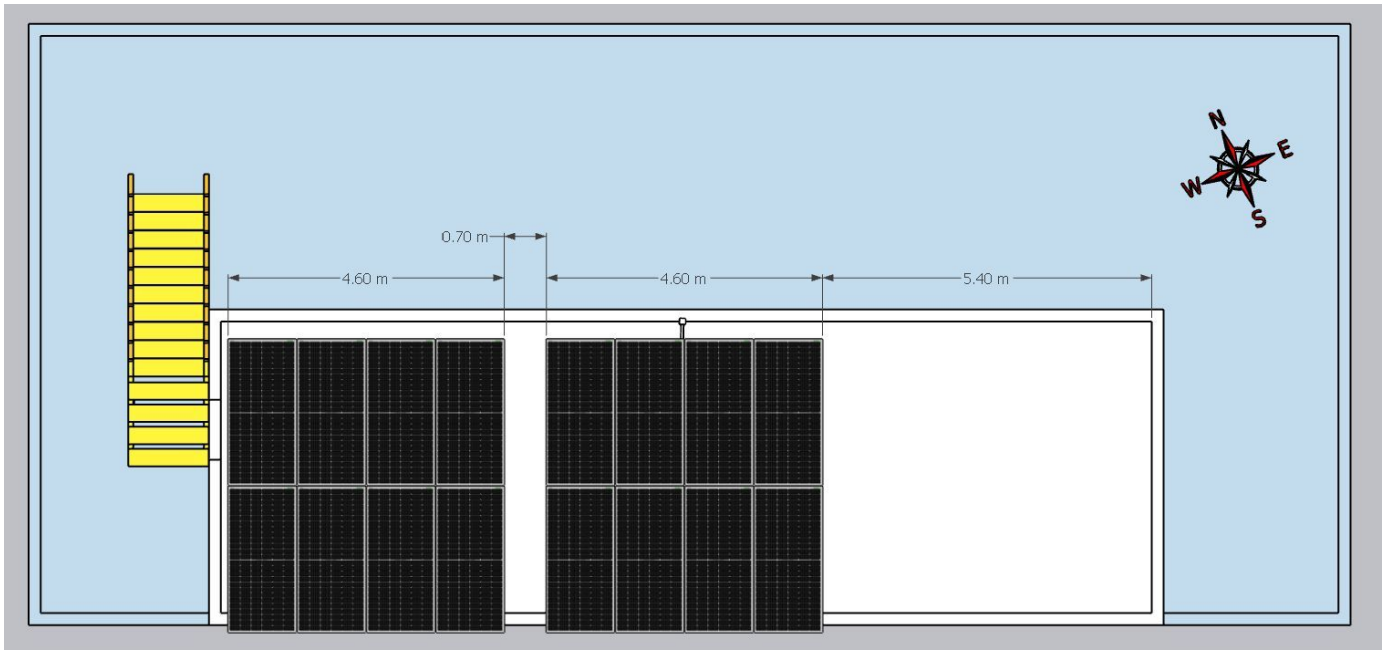
N
E
W
S
0.70 m
4.60 m
4.60 m
5.40 m

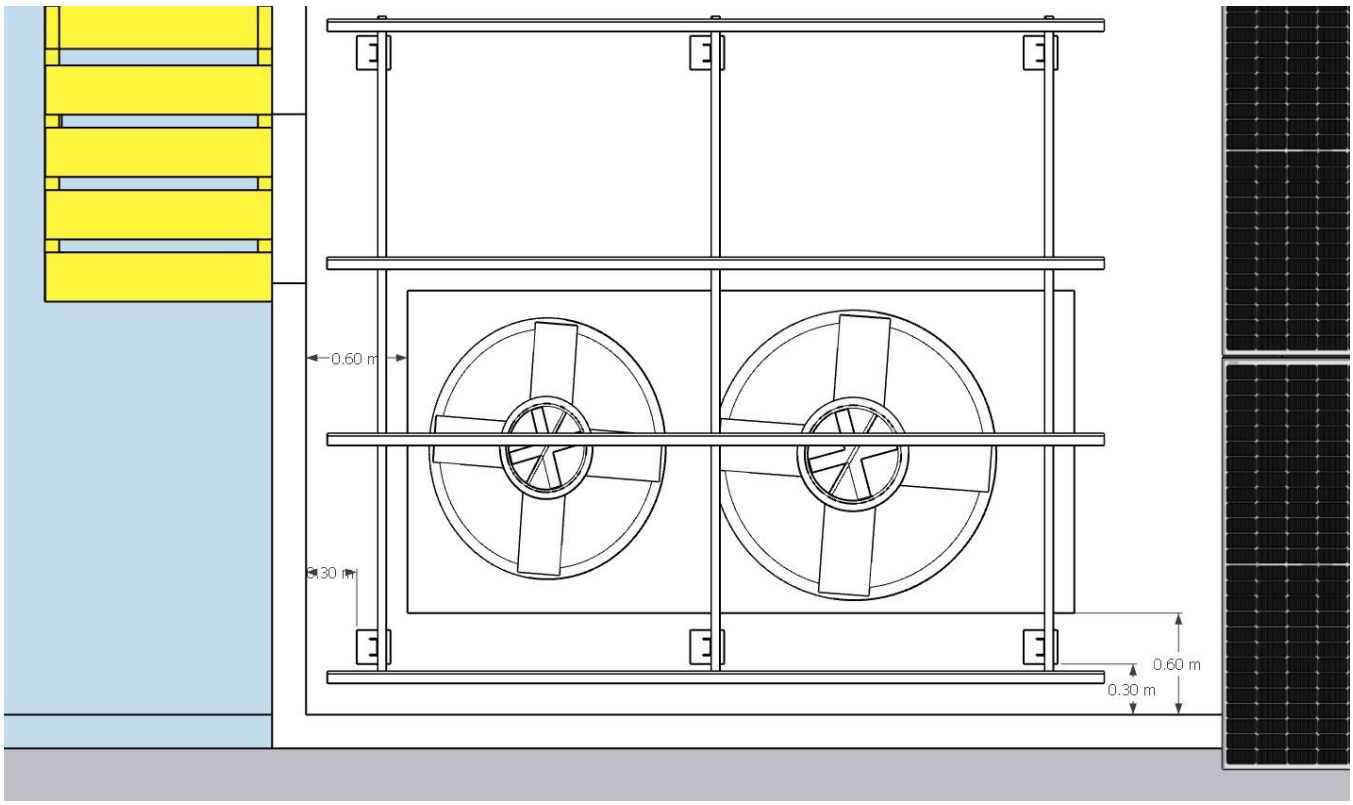

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



The materials can follow the stairs.



The materials can follow the stairs.



The materials can follow the stairs.



The materials can follow the METAL stairs.



The materials can follow the METAL stairs.



The materials reaching the upper headroom terrace can be moved to the East side of the terrace for safe storage.




The materials reaching the upper headroom terrace can be moved to the East side of the terrace for safe storage.

Staircase Details




Inner RCC staircase width: 800 mm

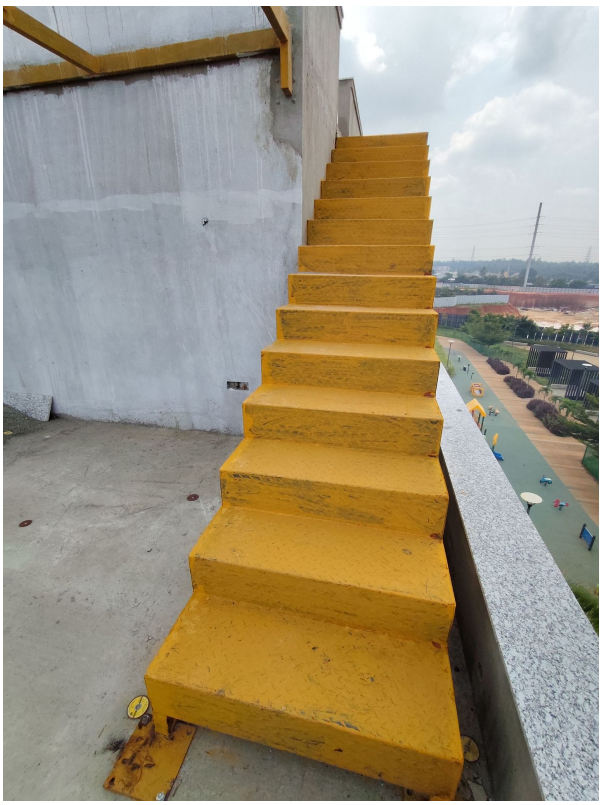


Upper terrace METAL staircase width: 800 mm

Proposed PV Area

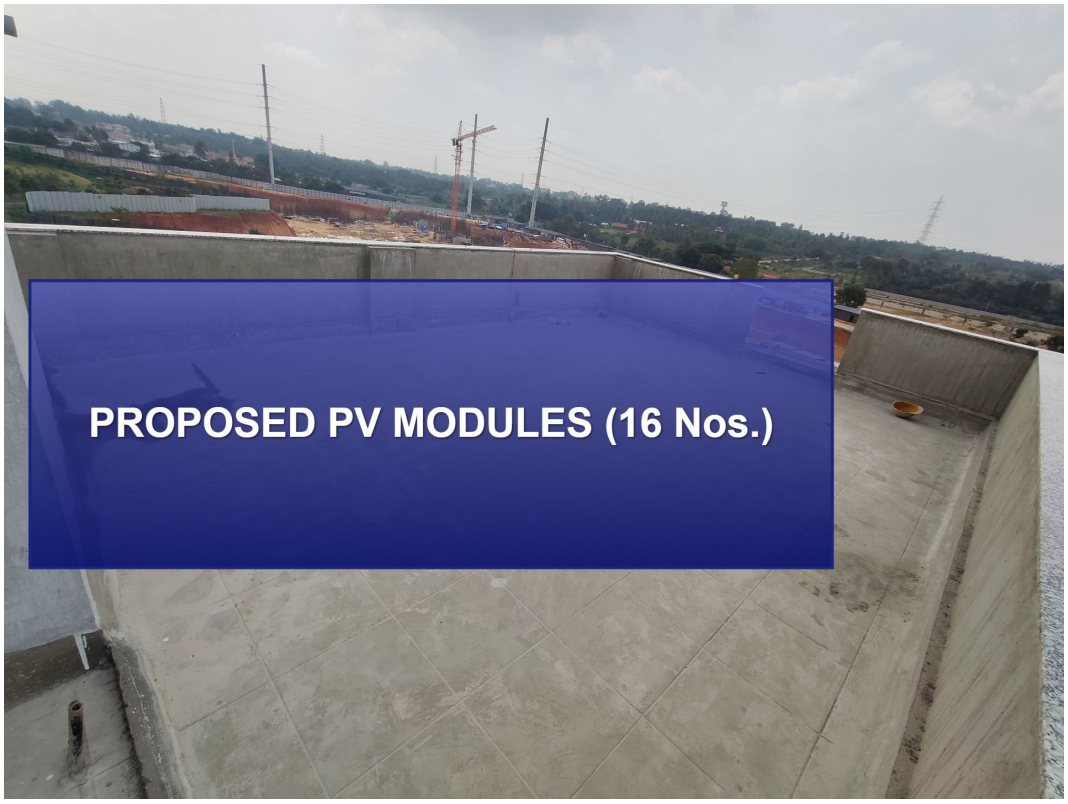


Cable Routing

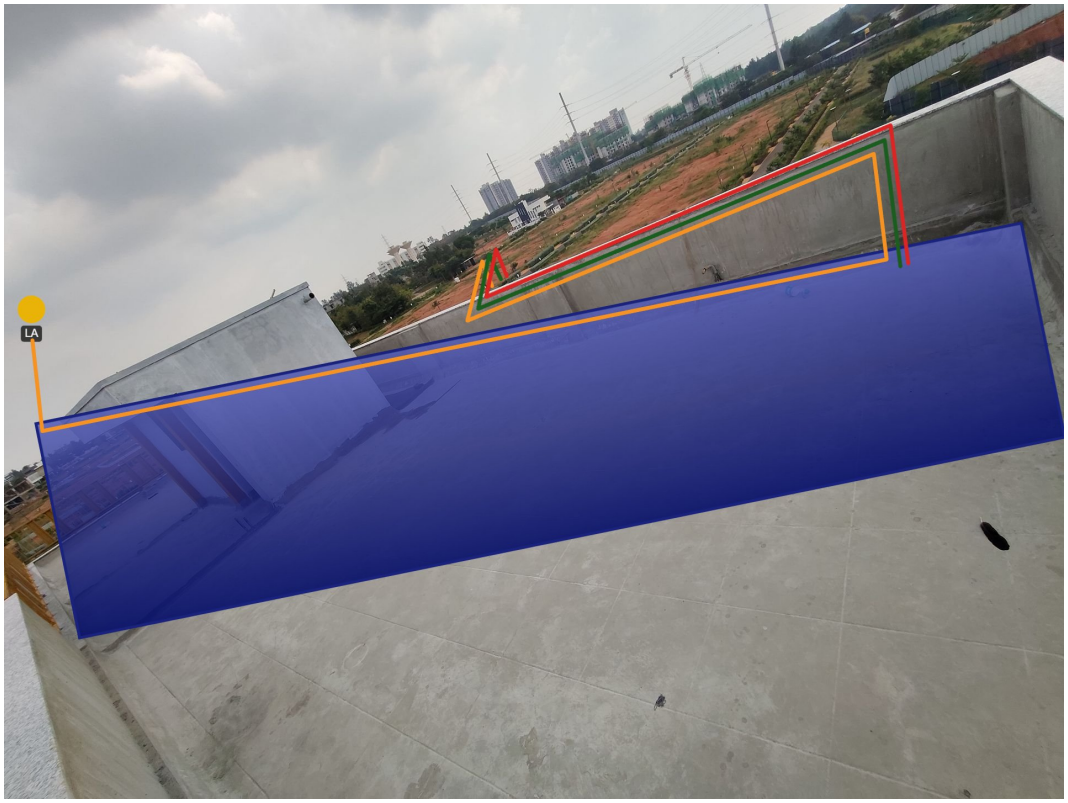




DC-DB,
Inverter &
AC-DB

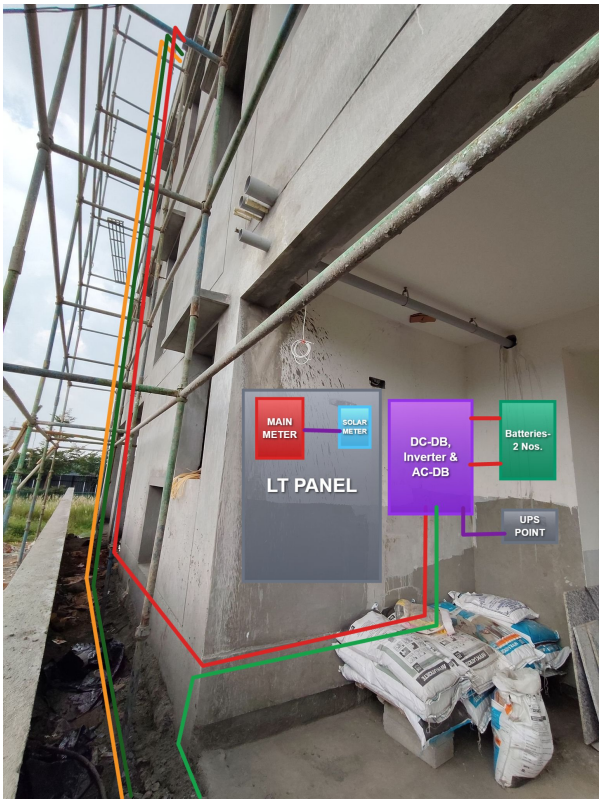
MAIN
METER
SOLAR
METER
LT PANEL
DC-DB,
Inverter &
AC-DB
Batteries-
2 Nos.
UPS
POINT



Meter Box



The LT panel is ready at the premises. Awaiting to be installed on the wall at the proposed location.

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 9.92 kWp Hybrid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the inverter location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.

THANK YOU

Dear Ms. Kirti Prabhu & Ms. Lata Prabhu,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
