Technical Site Visit Report

Prepared for: INDRANIL AICH_Subsidy_Bukkasagara_Bannerghatta_3.1kWp_Microinverter (IQ Series) - Site No #233

PROJECT INFORMATION

Report Number	ESV-2026-0241
Project ID	PZSYVHVX
Project Name	INDRANIL AICH_Subsidy_Bukkasagara_Bannerghatta_3.1kWp_Microinverter (IQ Series)
Building Name	Site No #233
Billing Name	INDRANIL AICH
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	INDRANIL AICH 233, 11th Cross, Pride Green Meadows Layout Phase II, Bukkasagara Bannerghatta. Bangalore- 560083
GPS Coordinates	12.7712268, 77.6058441
Google Maps	https://www.google.com/maps?q=12.7712268,77.6058441
Visit Date	2026-11-05
Visited By	K Naveen
Revision	Rev 1

CLIENT INFORMATION

Client Name	INDRANIL AICH
Contact	+91 9980619836

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	3.1
Sanction Load (kW)	3.3

Module Make & Capacity	Premier DCR Bifacial 620
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	5
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	5
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The building Chajja are the obstacles that could affect the material lifting.	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located west side of the corridor which is near to garden area.	-
6	Where is the Internet Router located?	Ground floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	3 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	8	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	8	-
5	On how many roofs at the site are we installing solar?	1	-

#	Question	Answer	Notes
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Mini-rails	*Short Rail - Sheet Roof*
9	What is the orientation of the solar panels?	["South","North"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	N/A	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	The height of the building is G+2+headroom is approximately 12 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Single, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	**No**	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	**No**	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	**No**	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	PVC chamber	-
13	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
14	In case of elevated structures, is it with or without grouting?	N/A	-
15	Are there any challenges with respect to Installation and Maintenance activities?	N/A	-
16	Are there any safety risks associated with accessing the roof for installation?	**No**	-
17	Is space present in rooftop to store the panels?	Horizontally sleeping	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin	Dimensions of	-

#	Question	Answer	Notes
	to purlin.	Purlin to Purlin is 0.90 ,0.95, 0.90 and rafter to rafter is 1m	
19	Is ventilation available in the battery location?	N/A	-
20	Is Battery wall mounted or stand mounted?	N/A	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 700, width: 700	-
23	Provide the dimension for earth pits location (L x W of available space).	length: 750, width: 15000	-
24	Is LAN cable under customer scope?	**No**	-
25	Is there any shadow that affects the solar installation?	**No**	-
26	Is there any trench work to be done to carry the AC cable to the meter location?	**No**	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).





This route (using Staircase) will be followed to carry Small items.










Staircase Details



Meter Box

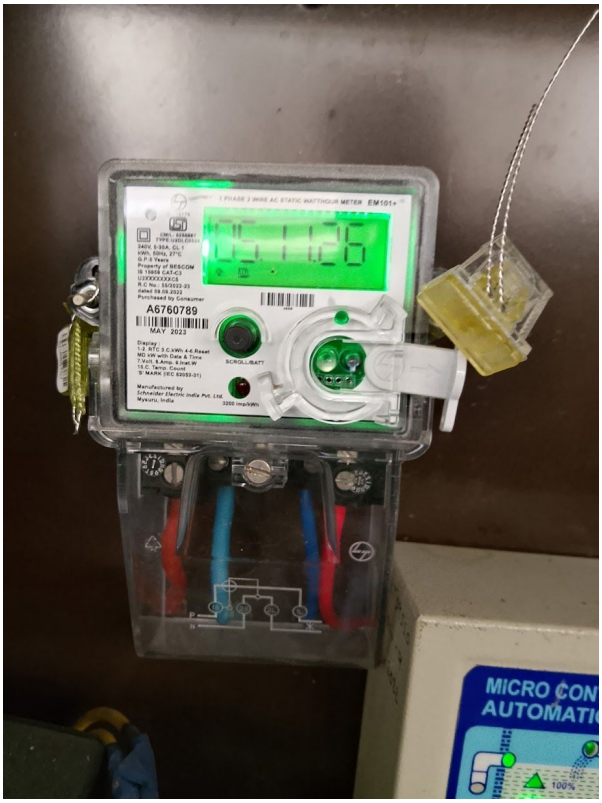

Material Storage




Proposed PV Area




Cable Routing





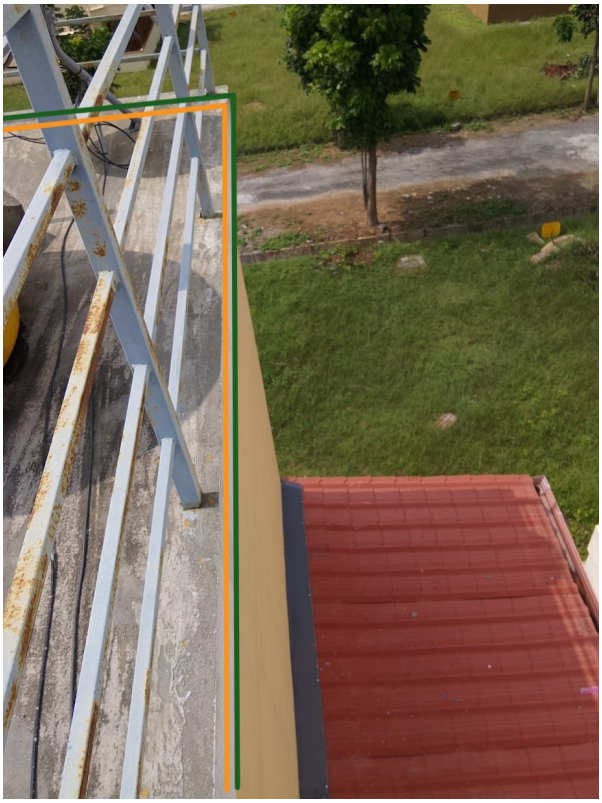



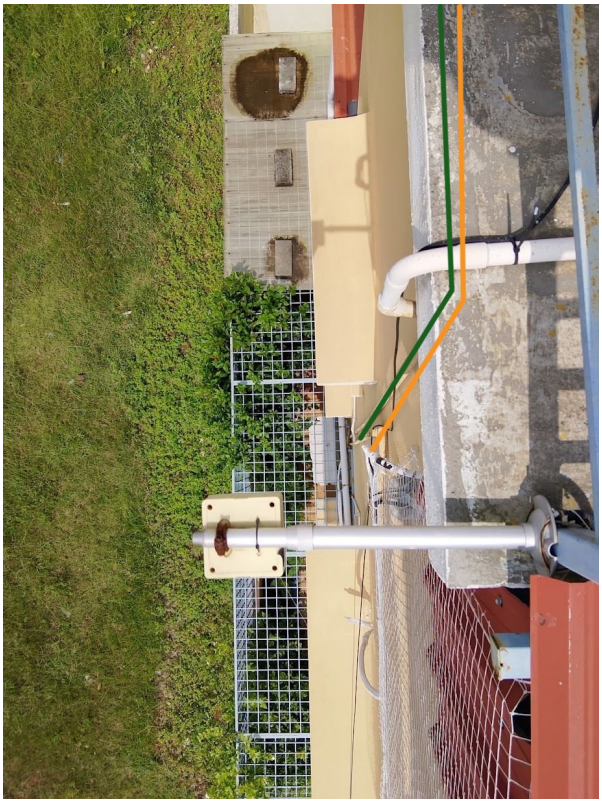









Make a hole to run the AC cable up to the meter location.





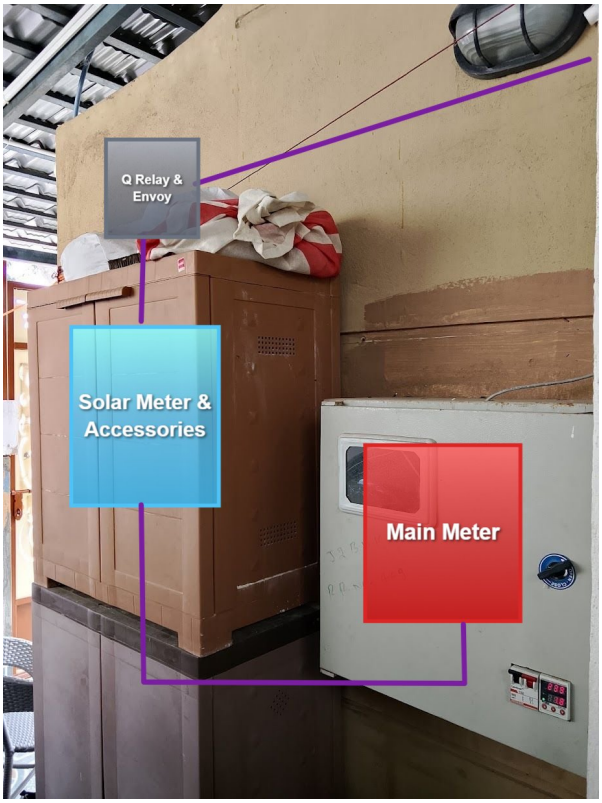


Equipment Location

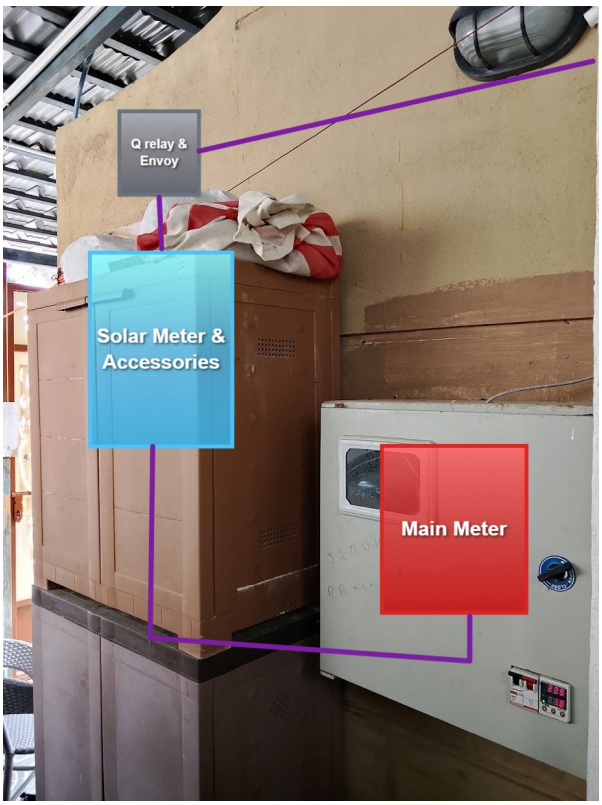



To remove the obstacle to place the solar meter and accessories is under customer scope.


Earth Pit Location

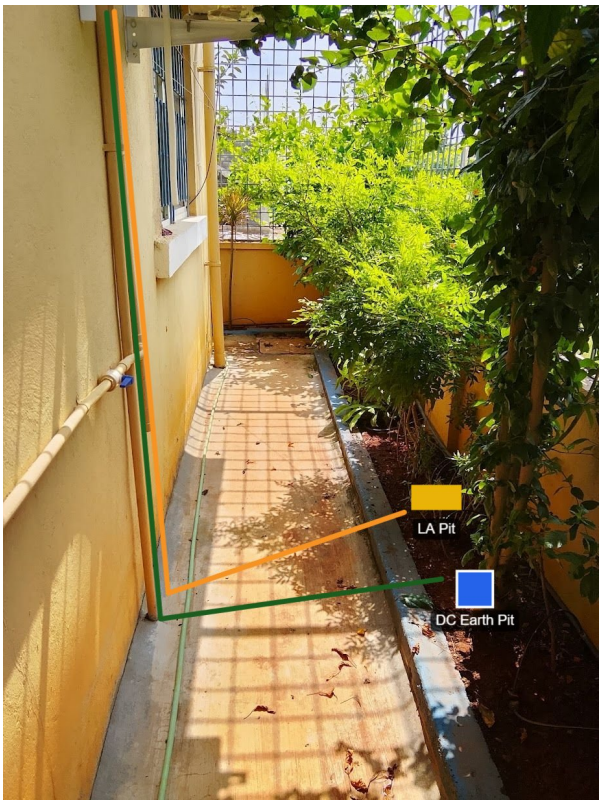


Site Layout - Top View

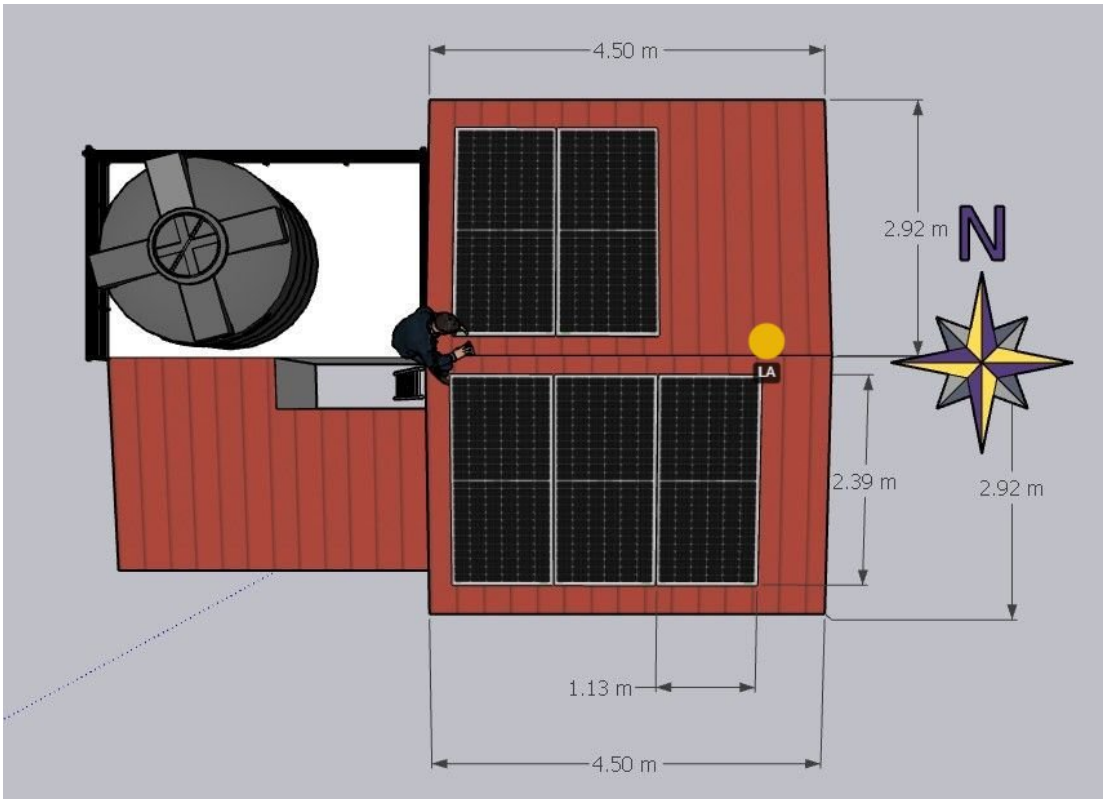

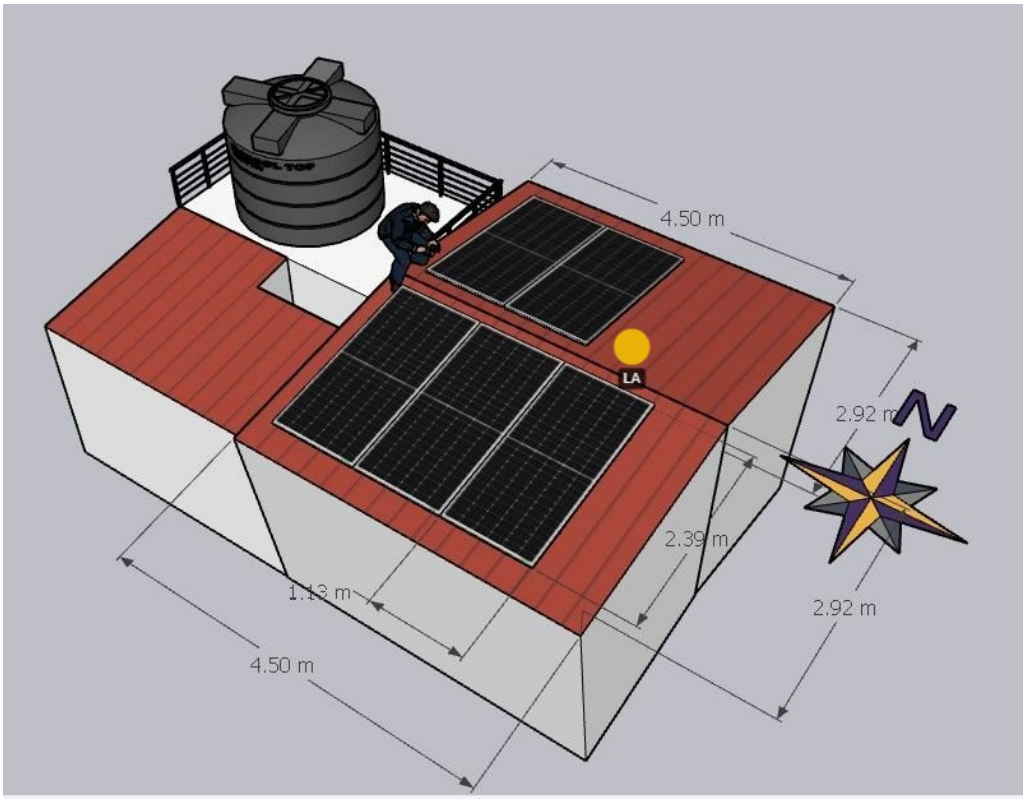

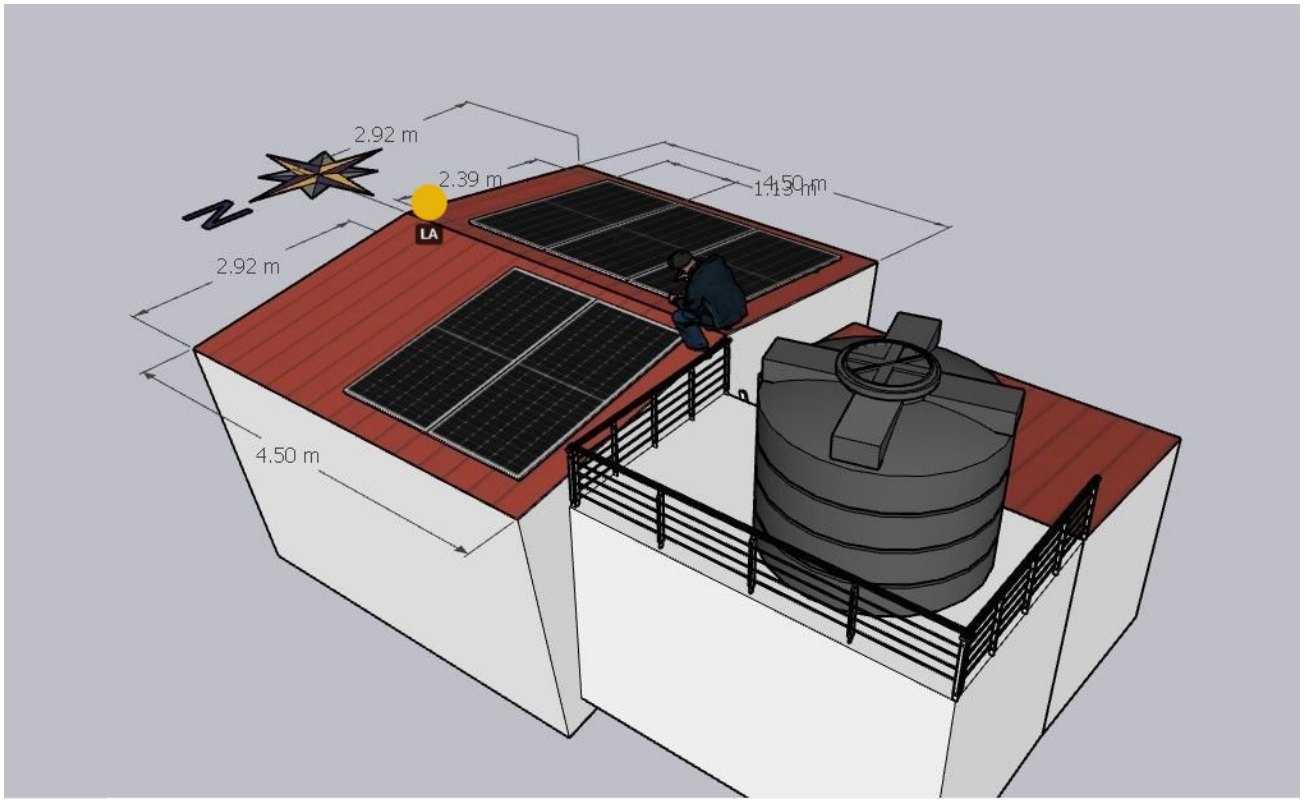
2.92 m
2.39 m
4.50 m
1.13 m
LA
2.92 m
4.50 m
N

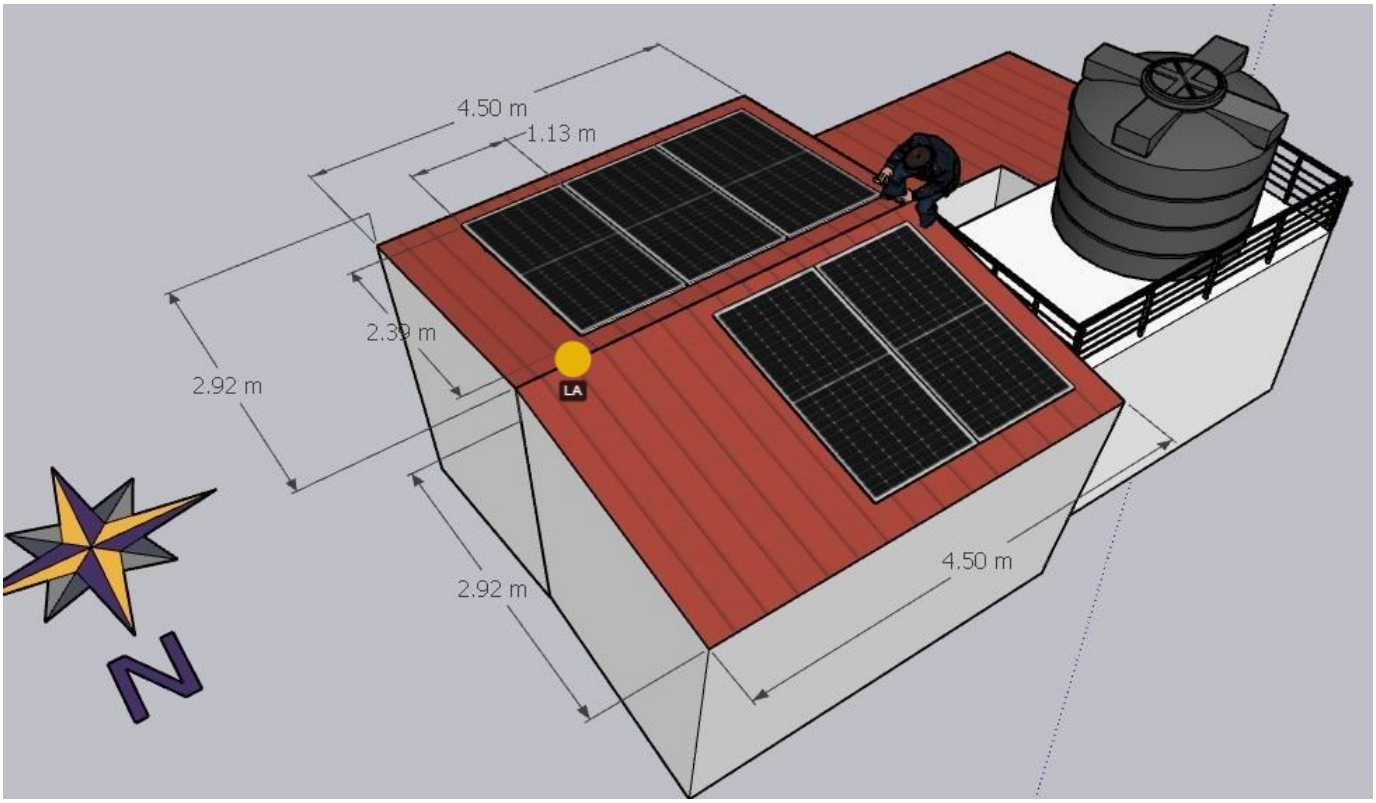
4.50 m
1.13 m
2.39 m
2.92 m
LA
4.50 m
2.92 m
N



Profile pitch of sheet roof 0.20 M

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Power and water source to be provided by the client
2	Wi-Fi up to the solar meter location is under customer scope.
3	As per the customer suggestions only the panel layout, earthing, cable routing has been considered.
4	The profile pitch of existing sheet roof is 0.20 M.
5	To remove the obstacle to place the solar meter and accessories is under customer scope.

THANK YOU

Dear INDRANIL AICH,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
