Technical Site Visit Report

Prepared for: Sowmya D_Subsidy_MEI Layout_6.2kWp_Microinverter (IQ Series) - #454,Ananda Bairava

PROJECT INFORMATION

Report Number	ESV-2026-0101
Project ID	17E46B9F
Project Name	Sowmya D_Subsidy_MEI Layout_6.2kWp_Microinverter (IQ Series)
Building Name	#454,Ananda Bairava
Billing Name	Sowmya D_Subsidy_MEI Layout_6.2kWp_Microinverter (IQ Series)
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	MEI Layout, Bagalagunte, Bengaluru North City Corporation, Bengaluru, Bangalore North, Bengaluru Urban, Karnataka, 560073, India
GPS Coordinates	13.0587945, 77.5030726
Google Maps	https://www.google.com/maps?q=13.0587945,77.5030726
Visit Date	2026-04-29
Visited By	-
Revision	Rev 0

CLIENT INFORMATION

Client Name	Soumya D
Contact	96632 21033

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	6.2
Sanction Load (kW)	6.6

Module Make & Capacity	Adani DCR bifacial 620 Wp
Module Length (mm)	2382
Module Width (mm)	1133
Number of Panels	10
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	10
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	**No**	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	N/A	-
5	Did you discuss the location of the earth pits with the customer?	Earth pits are located in the ground floor towards east direction.	-
6	Where is the Internet Router located?	Customer scope.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	N/A	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: Skylight on the roof that could affect the solar installation.	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	01	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-

#	Question	Answer	Notes
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*HDGI with 2.5m front height.*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	**No**	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	Height of the building is 12m.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999)	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	**No**	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	**No**	-
11	Is there space available to dig DC, AC and LA earth pits?	**No**	-
12	In case of elevated structures, is an LA extension provided at the far end?	**No**	-
13	In case of elevated structures, is it with or without grouting?	With Grouting	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	**No**	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-

#	Question	Answer	Notes
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 800, width: 499	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 450, width: 450	-
22	Is LAN cable under customer scope?	**No**	-
23	Is there any shadow that affects the solar installation?	Yes	*A small amount of shadow will fall on the panels.*
24	Is there any trench work to be done to carry the AC cable to the meter location?	**No**	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Building Exterior

Material Delivery Route

This route will carry the small items

This route will carry the large items (like panels)

Material Storage

Staircase Details

Meter Box

Cable Routing

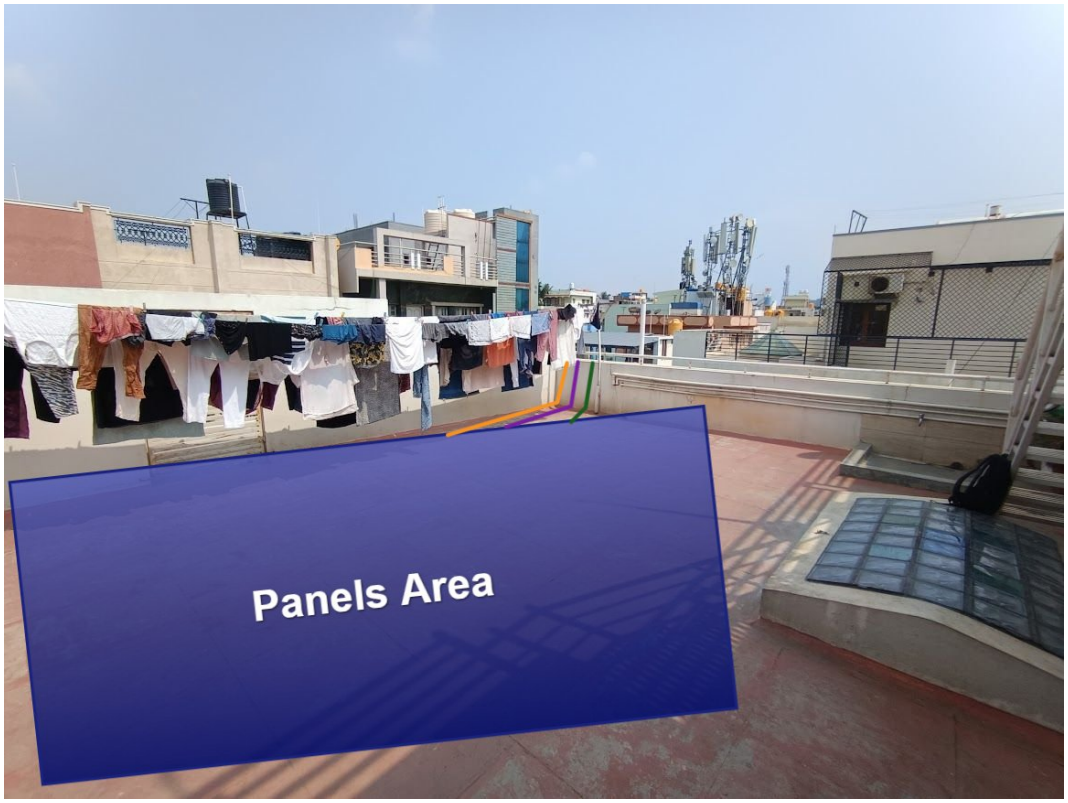

Proposed PV Area

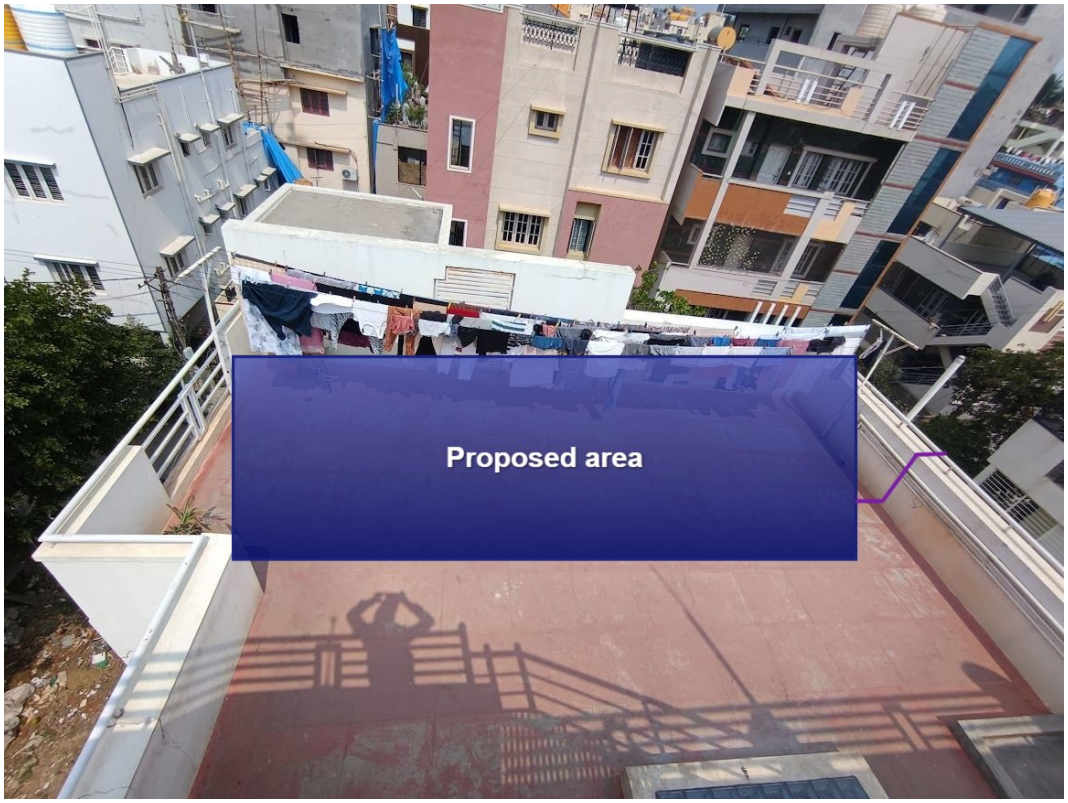

Site Layout - Top View

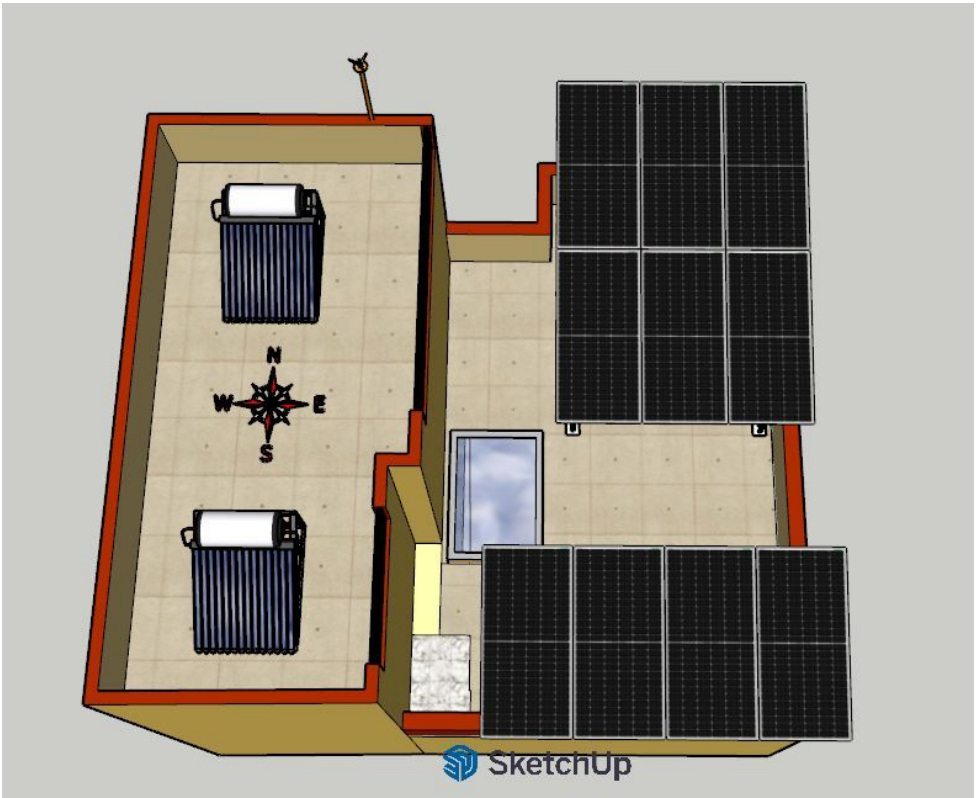

Top view

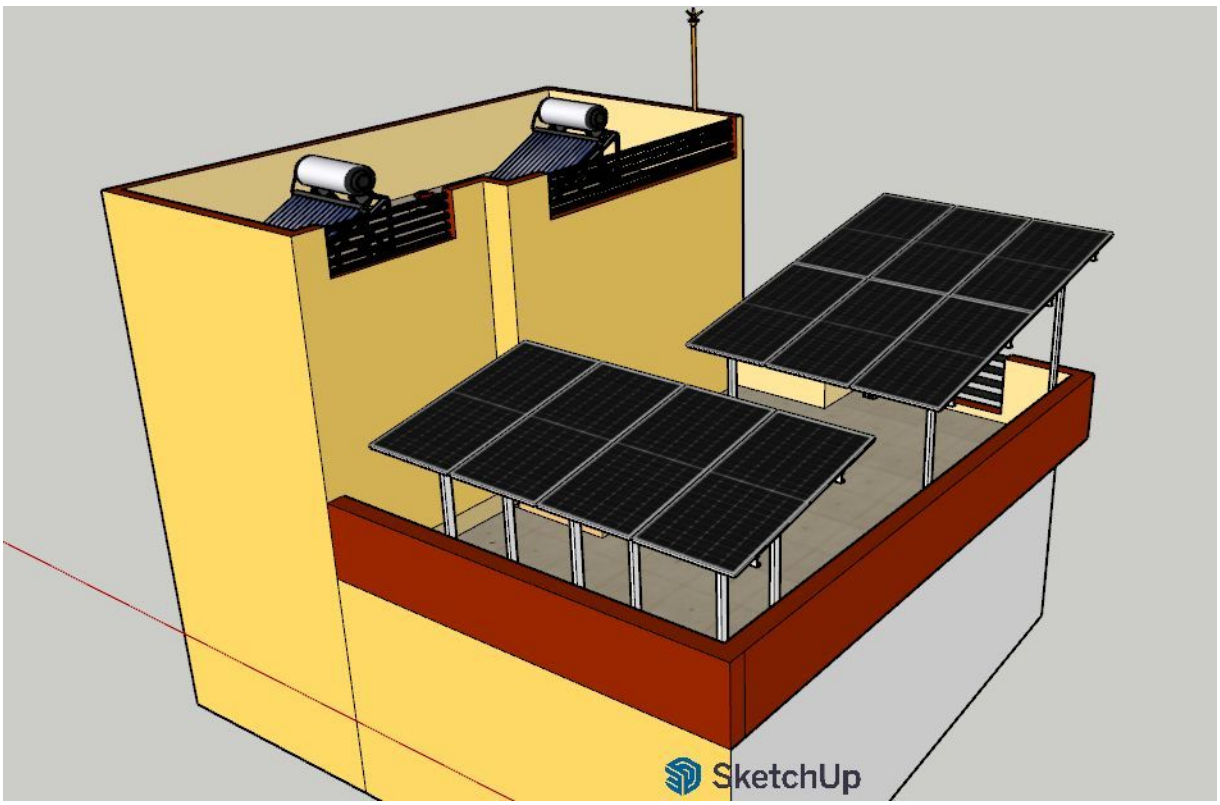

Side view

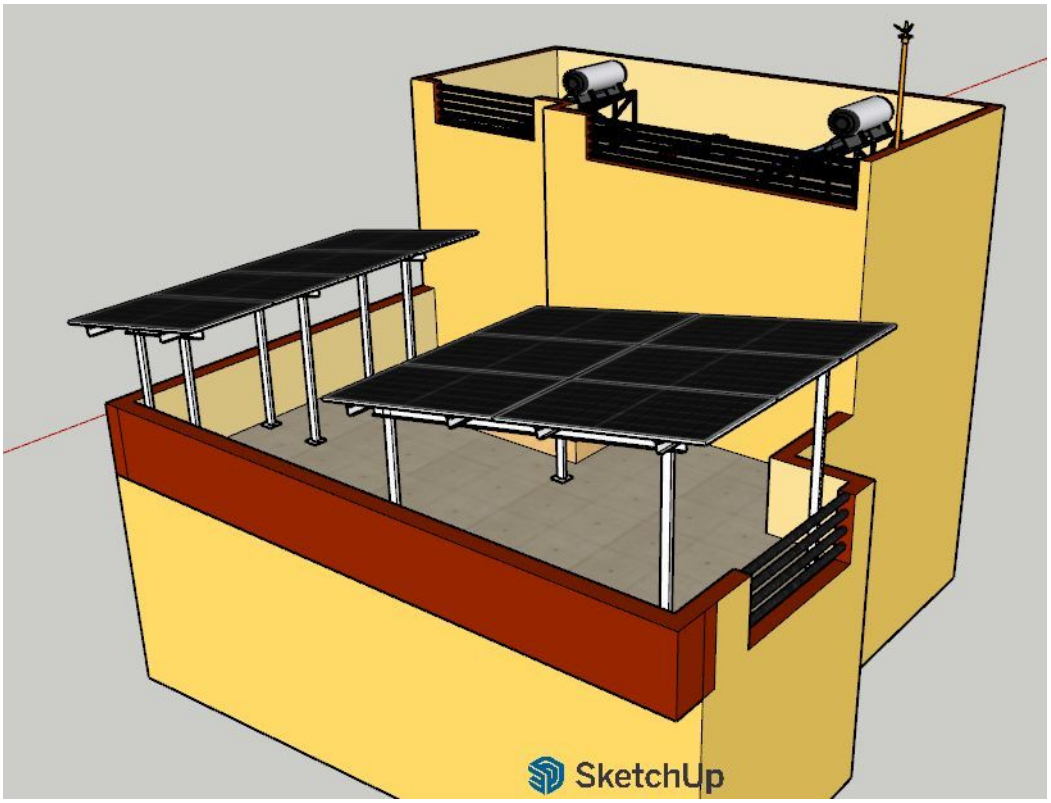

Side view

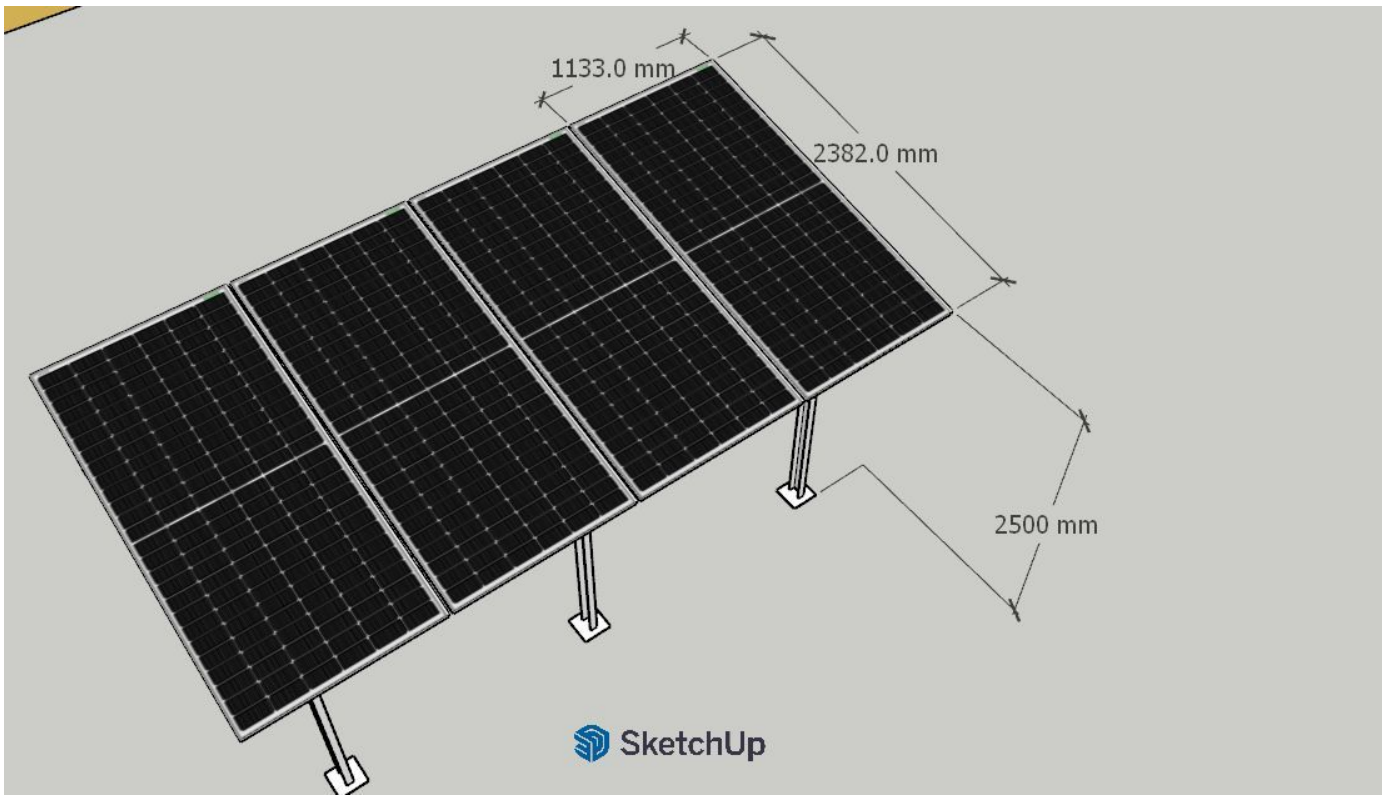

Structure details (1)

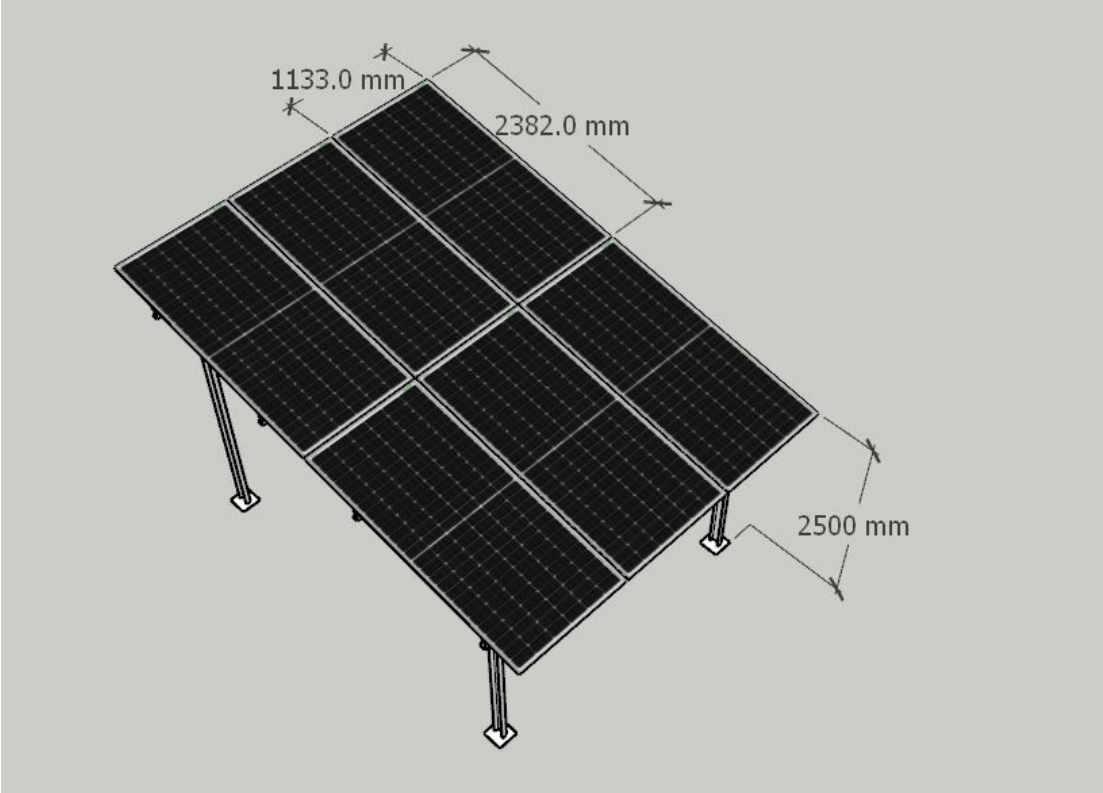

Structure details (1)

Equipment Location

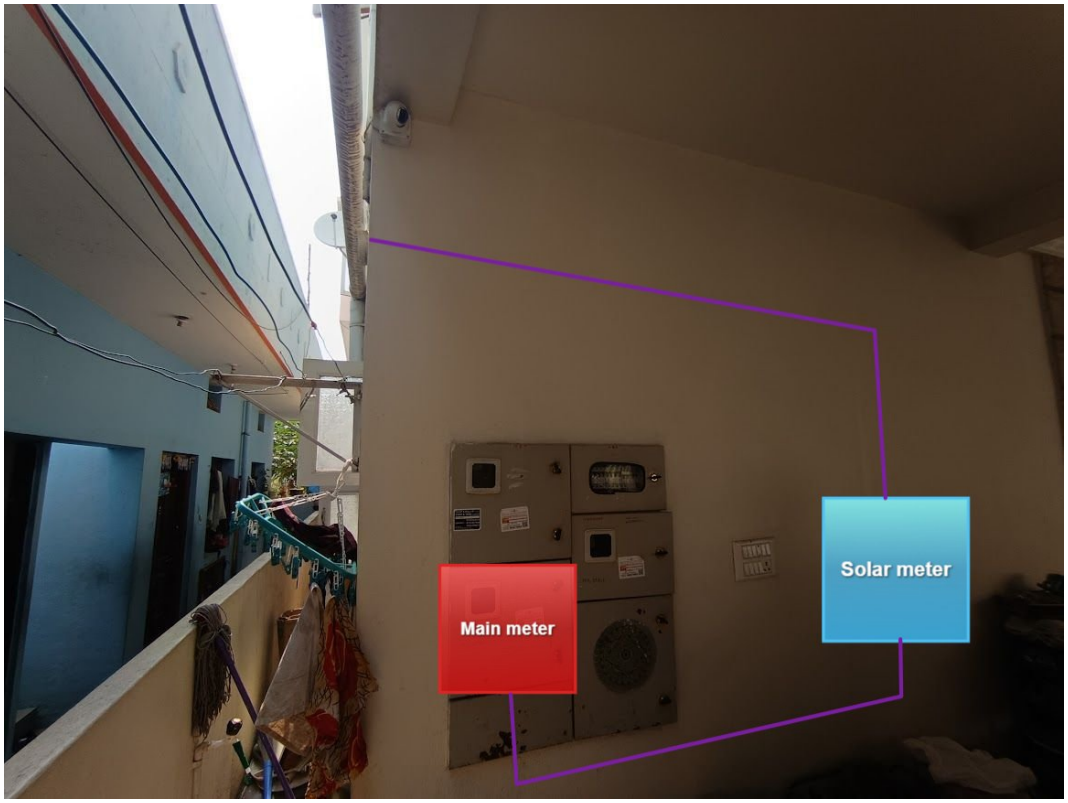

Shadow Analysis

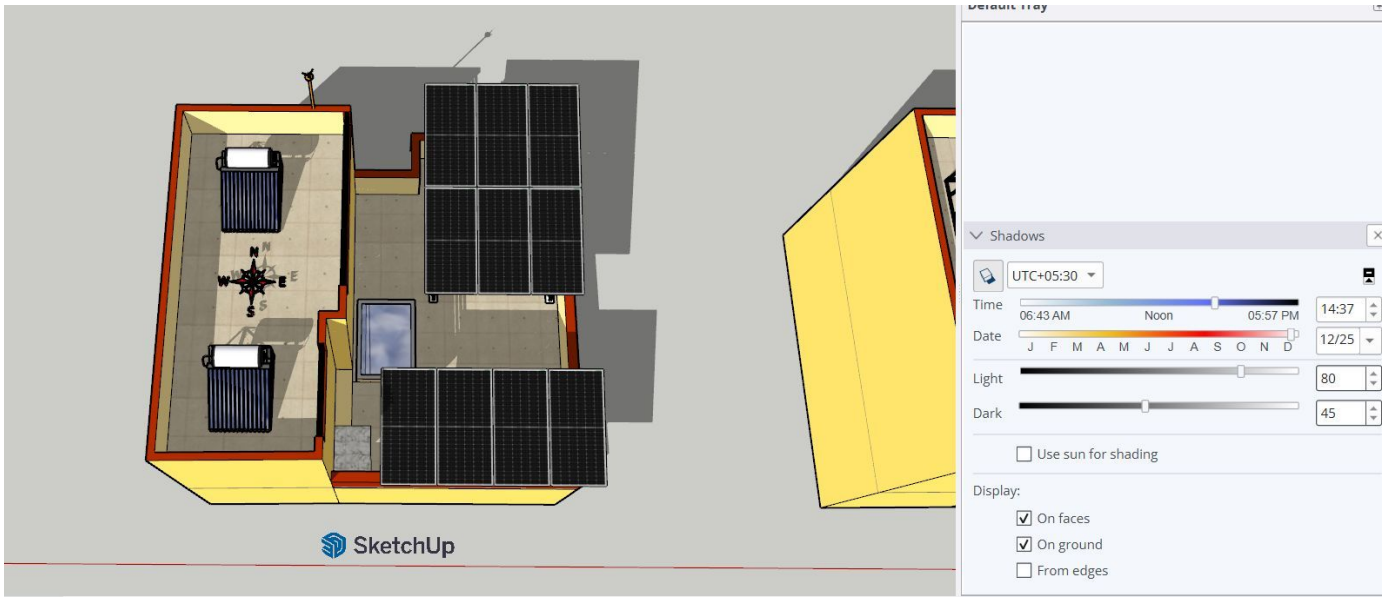

A small amount of Shadow will cast on the panels in the month of November and december

Earth Pit Location

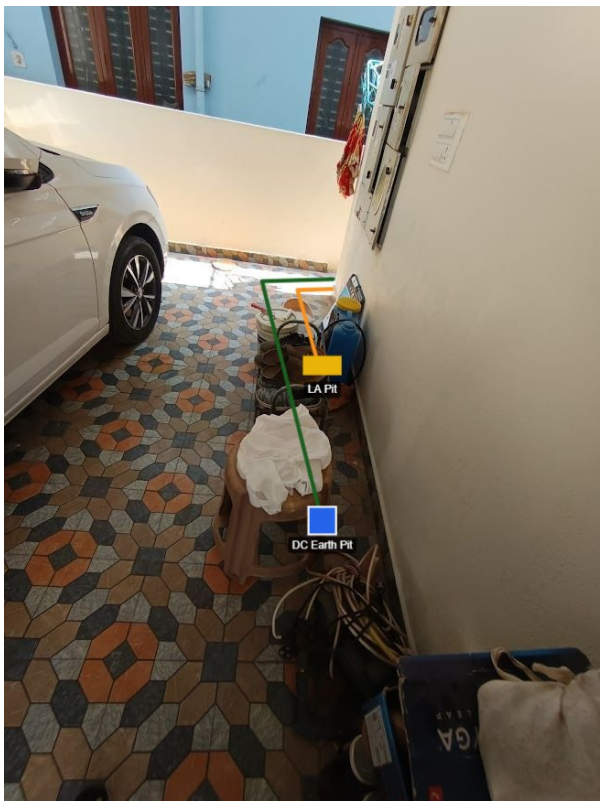

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	As per the customer suggestion, routing, cable earthing, inverter location and also solar meter have been considered.

Customer Scope

#	Observation
1	Wi-Fi upto solar meter is under customer scope

THANK YOU

Dear Soumya D,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
