Technical Site Visit Report

Prepared for: Ganesh Krishnamurthy C28_Chaitanya Samarth_6.765kWp_Microinverter (IQ Series) - C28

PROJECT INFORMATION

Report Number	ESV-2026-0248
Project ID	VLS3K1IK
Project Name	Ganesh Krishnamurthy C28_Chaitanya Samarth_6.765kWp_Microinverter (IQ Series)
Building Name	C28
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Harsha Kuntur
Site Address	C28, Chaitanya Samarth, Mandur Village, Bidarahalli Hobli, Bengaluru East Taluk, Bengaluru Urban, Karnataka 560049.
GPS Coordinates	13.070998, 77.734234
Google Maps	https://www.google.com/maps?q=13.070998,77.734234
Visit Date	2026-11-06
Visited By	ABILASH N K
Revision	Rev 0

CLIENT INFORMATION

Client Name	Ganesh Krishnamurthy
Contact	+91 9886046624

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	6.765
Sanction Load (kW)	10
Module Make & Capacity	Waaree Non DCR Topcon, 615 Wp

Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	11
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	11
Mounting Structure Type	Tiled Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The client's main meter box consists of the existing Enphase accessories as well as the solar meter.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes. One no. of earth pit needs to be dug in the garden area near the existing BESCOM meter for the newly installed LA. The DC earthing has already been done for the existing structure.	-
6	Where is the Internet Router located?	1st floor.	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	3 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Tiled Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	15	-

#	Question	Answer	Notes
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	15	-
5	On how many roofs at the site are we installing solar?	2	*Roof 1 (South-facing): 7 Nos.* *Roof 2 (North-facing): 4 Nos.*
6	If it is a Tiled roof, what is underneath the tiles?	RCC	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Long rails with L clamps	-
9	What is the orientation of the solar panels?	-	*Roof 1 (South-facing): 7 Nos.* *Roof 2 (North-facing): 4 Nos.*
10	How can the roof be accessed?	Ladder	*There is no ladder provision available at the site to get access to the tiled roof terrace. A temporary ladder will be arranged by the customer during the installation.*
11	Is the building currently under construction?	**No**	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	*The existing conduits can be used to bring the connection from the rooftop to the Enphase accessories box located on the ground floor near the BESCOM meter. The same cable route can be used to pull the LA earthing cable from the rooftop to the ground.*
13	What is the height of the building and how many floors does it have?	8 metres. (G + 1 + Tiled roof)	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: LT w/o CT (5 - 34.999)	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	*LA is not available for the existing system. An LA with a pedestal for the sloped roof needs to be considered.*
6	Is space available for CT within Energy meter panel?	Yes	*LA is not available for the existing system. An LA with a pedestal for the sloped roof needs to be considered.*

#	Question	Answer	Notes
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	**No**	*The client's main meter box consists of the existing Enphase accessories as well as the solar meter.*
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	Yes	*The client's main meter box consists of the existing Enphase accessories as well as the solar meter.*
11	Is there space available to dig DC, AC and LA earth pits?	Yes	*One earthing pit needs to be dug in the garden area near the existing BESCOM meter for the newly installed LA. The DC earthing has already been done for the existing structure.*
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	PVC chamber	-
13	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
14	In case of elevated structures, is it with or without grouting?	N/A	-
15	Are there any challenges with respect to Installation and Maintenance activities?	details: There is no ladder provision available at the site to get access to the tiled roof terrace. A temporary ladder will be arranged by the customer during the installation.	-
16	Are there any safety risks associated with accessing the roof for installation?	details: There is no ladder provision available at the site to get access to the tiled roof terrace. A temporary ladder will be arranged by the customer during the installation.	-
17	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
19	Is ventilation available in the battery location?	N/A	-
20	Is Battery wall mounted or stand mounted?	N/A	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mounted.	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 1000	-
23	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 1000	-

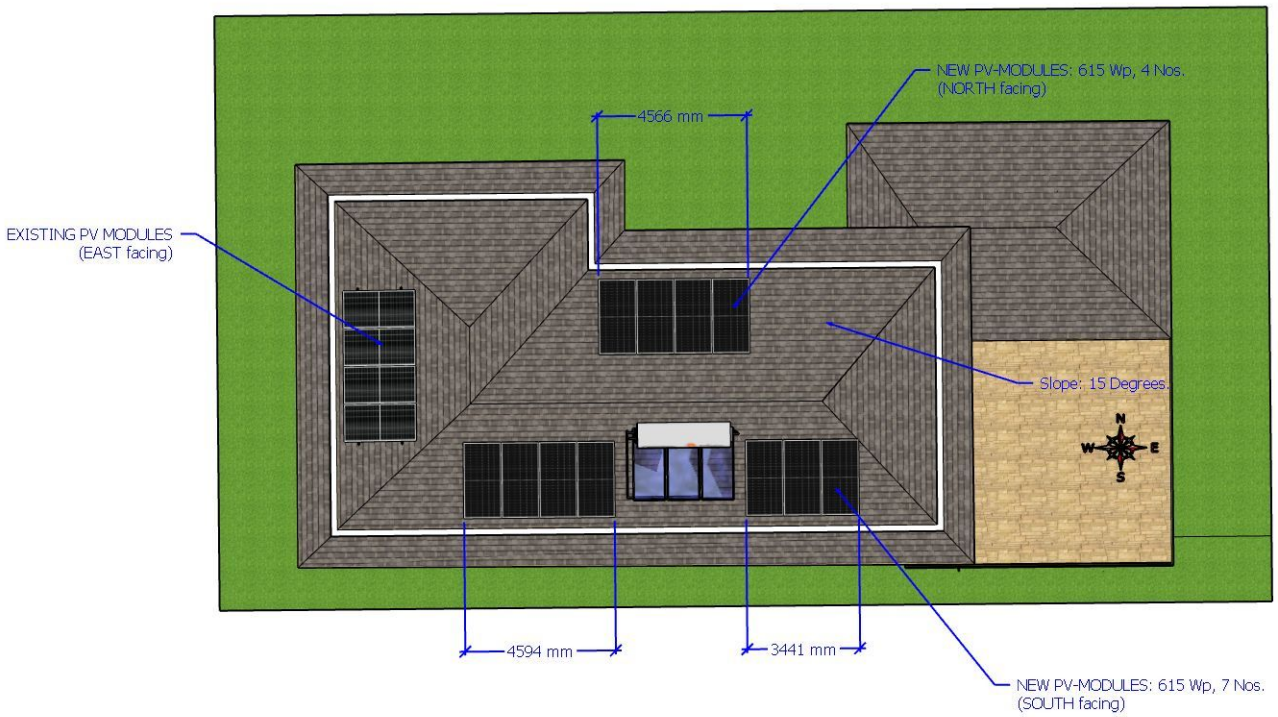
#	Question	Answer	Notes
24	Is LAN cable under customer scope?	Yes	-
25	Is there any shadow that affects the solar installation?	No	-
26	Is there any trench work to be done to carry the AC cable to the meter location?	N/A	-


PHOTO DOCUMENTATION


Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout - Top View


NEW PV-MODULES: 615 Wp, 4 Nos.
(NORTH facing)
4566 mm
EXISTING PV MODULES
(EAST facing)
Slope: 15 Degrees.
N
W
E
S
4594 mm
3441 mm
NEW PV-MODULES: 615 Wp, 7 Nos.
(SOUTH facing)

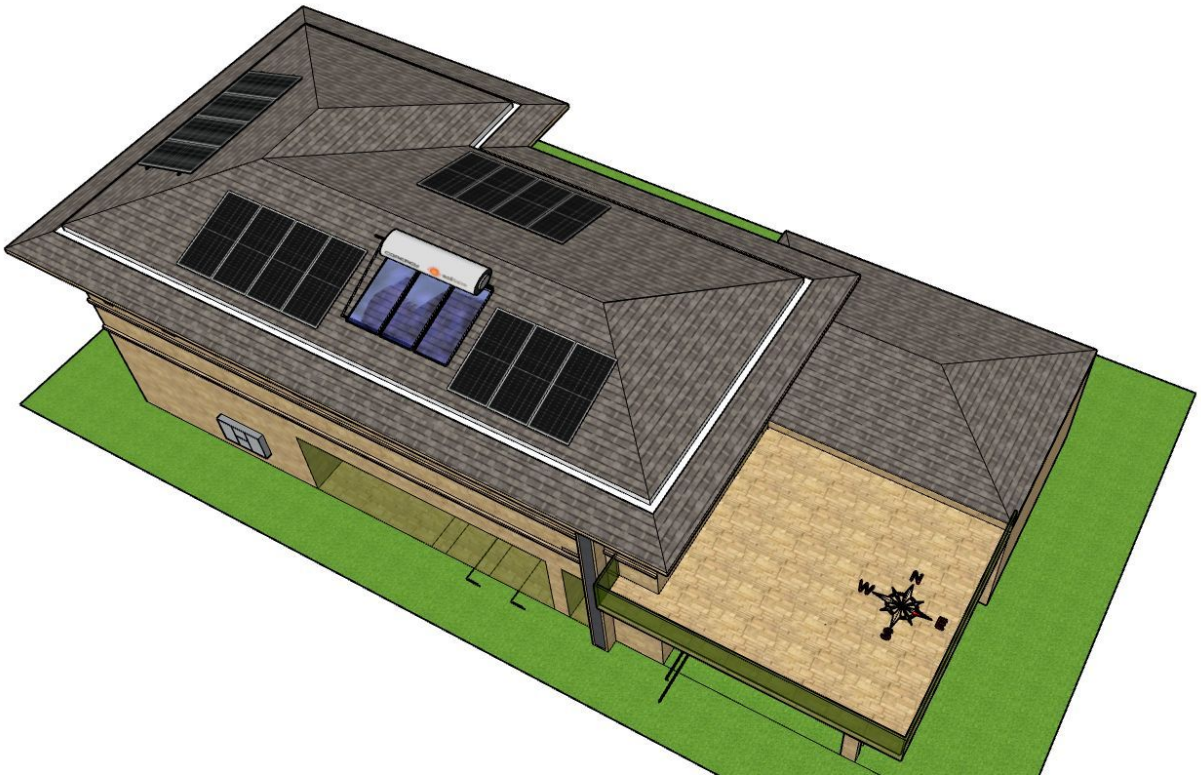
N
W
E
S

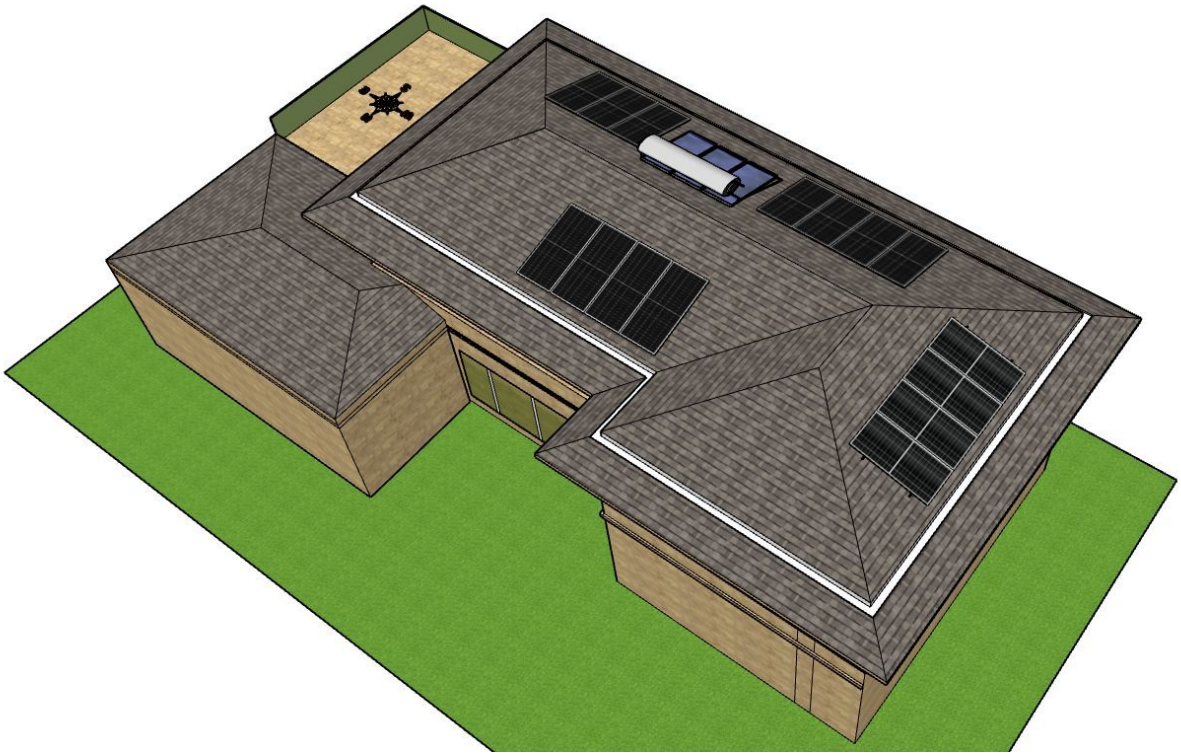

Building Exterior



Material Delivery Route



Heavy materials such as PV modules can be shifted over the side wall of the building.



Light weight materials can be shifted to the terrace via the inner staircase.



The materials reaching the balcony can be shifted to the upper terrace over the side roof.

Staircase Details



Inner staircase width: 1000 mm

Proposed PV Area



Cable Routing



The DC earthing cable must be connected between the existing structure and the new structure.



The LA earthing cable can follow the existing cable route to reach the ground.




The AC power cable too can follow the same route to reach the Enphase accessories box.




Finally, the LA earthing cable can be terminated at the earthing pit. And the AC cable can get into the meter box.

Meter Box

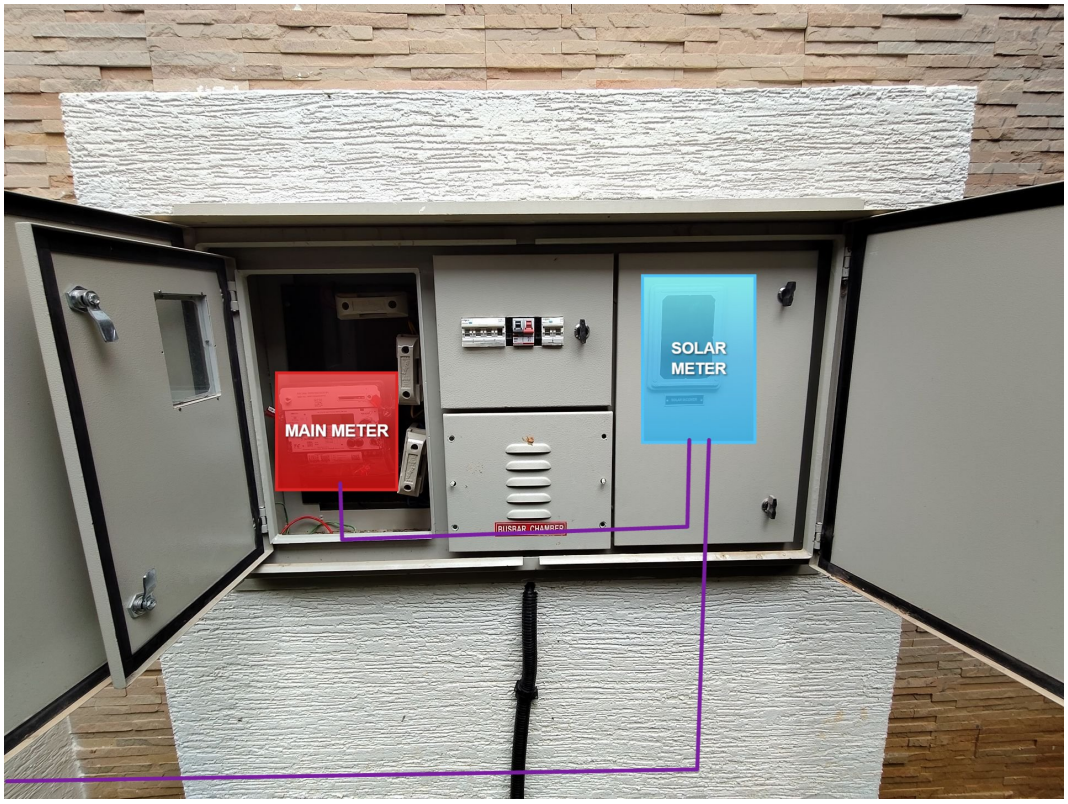

Solar meter and Main meter conncections.

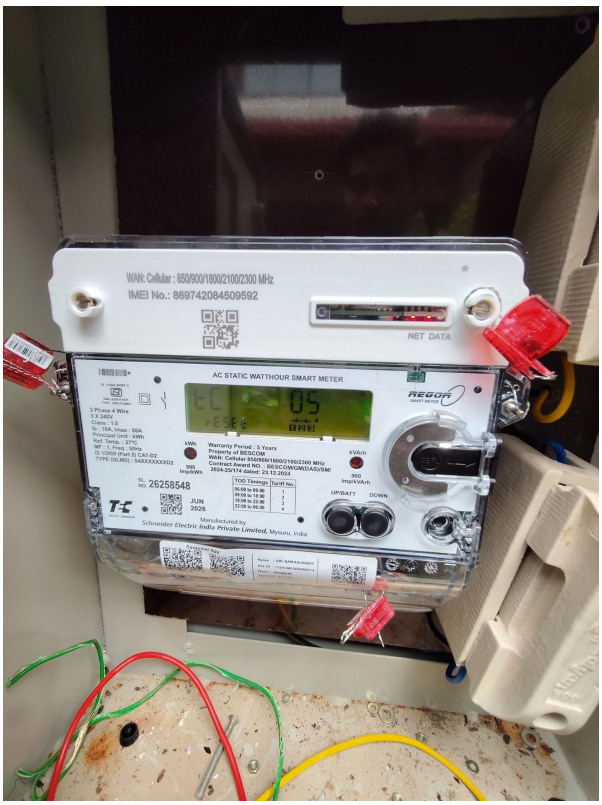

MAIN BESCOM METER.

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Installation and commissioning of 6.765 kWp On-grid solar power plant at the proposed premises.
2	The co-ordination and follow-up with BESCOM regarding solar connectivity till commissioning.

Customer Scope

#	Observation
1	Providing an active Wi-Fi or LAN cable connection up to the Enphase Accessories box location.
2	The customer is responsible for arranging the reliable ladder provision to get access to the proposed solar panel installation area prior to the project's execution.

THANK YOU

Dear Ganesh Krishnamurthy,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
