Technical Site Visit Report

Prepared for: Arulanandan Ponnivalavan_No.62, Woodsvale_Subsdiy_3.72kWp_Hybrid - #A322

PROJECT INFORMATION

Report Number	ESV-2026-0231
Project ID	C5VNRO3O
Project Name	Arulanandan Ponnivalavan_No.62, Woodsvale_Subsdiy_3.72kWp_Hybrid
Building Name	#A322
Billing Name	Arulanandan Ponnivalavan
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Mahantayya
Site Address	A322 , Vars Parkwood Apartment Near adarsh palm retreat, Doddakanelli, Bangalore - 560035
GPS Coordinates	12.8839733, 77.7916544
Google Maps	https://www.google.com/maps?q=12.8839733,77.7916544
Visit Date	2026-10-24
Visited By	K Naveen
Revision	Rev 0

CLIENT INFORMATION

Client Name	Arulanandan Ponnivalavan
Contact	+91 9741204938

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	3.72
Sanction Load (kW)	7

Module Make & Capacity	Premier DCR Bifacial 620
Module Length (mm)	2382
Module Width (mm)	1134
Number of Panels	6
Inverter Type	Hybrid (String)
Inverter Brand	Deye 5 kW 1phase String
Number of Inverters	1
Battery	Needed
Number of Batteries	1
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye Battery: SE-F5plus - 1
Mounting Structure Type	RCC Flat Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The existing building chajja are the obstructions that could affect the material lifting.	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter, DCDB, ACDB, Battery will be installed in ground floor which is backside of the meter location.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the ground floor which is located on the garden area.	-
6	Where is the Internet Router located?	Not Available	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-

#	Question	Answer	Notes
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	*RCC Flat roof with laid of tiles*
2	Are there any obstructions on the roof that could affect the solar installation?	**No**	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	-
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	**No**	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	Yes	*The existing conduit pipe is available for DC cabling up to the meter location*
13	What is the height of the building and how many floors does it have?	The height of the building is G+1+headroom is approximately 12 meters.	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-

#	Question	Answer	Notes
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	PVC chamber	-
13	In case of elevated structures, is an LA extension provided at the far end?	Yes	-
14	In case of elevated structures, is it with or without grouting?	With Grouting	-
15	Are there any challenges with respect to Installation and Maintenance activities?	details: While lifting the materials take care the glass to avoid the disturbances	-
16	Are there any safety risks associated with accessing the roof for installation?	Yes	-
17	Is space present in rooftop to store the panels?	Horizontally sleeping	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
19	Is ventilation available in the battery location?	Yes	-
20	Is Battery wall mounted or stand mounted?	Wall mounted	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall Mount	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 450, width: 500	-
23	Provide the dimension for earth pits location (L x W of available space).	length: 1250, width: 2498	-
24	Is LAN cable under customer scope?	**No**	-
25	Is there any shadow that affects the solar installation?	Yes	*The structure shadow will cast on the solar water heater.*
26	Is there any trench work to be done to carry the AC cable to the meter location?	**No**	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).









This route (using Staircase) will be followed to carry Small items.









Staircase Details



Meter Box



Material Storage




Proposed PV Area




Cable Routing



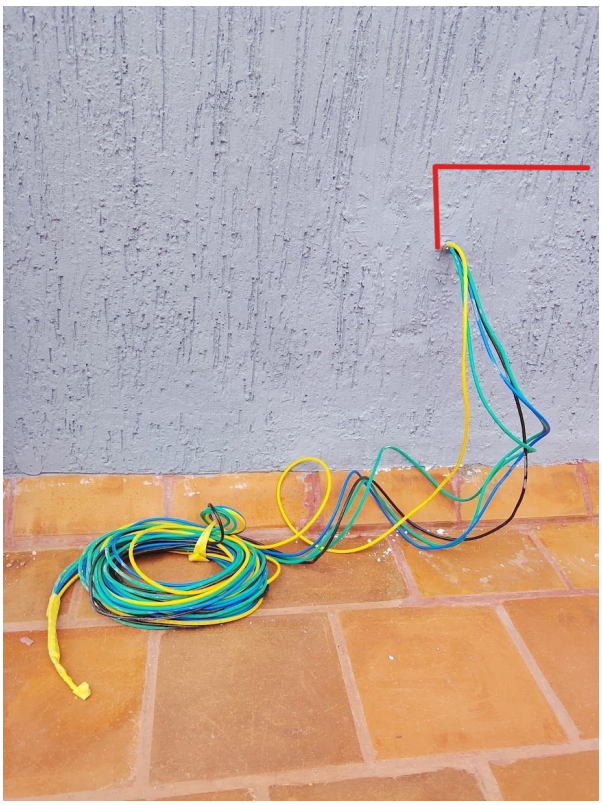


The DC Cable has to be run through this provision

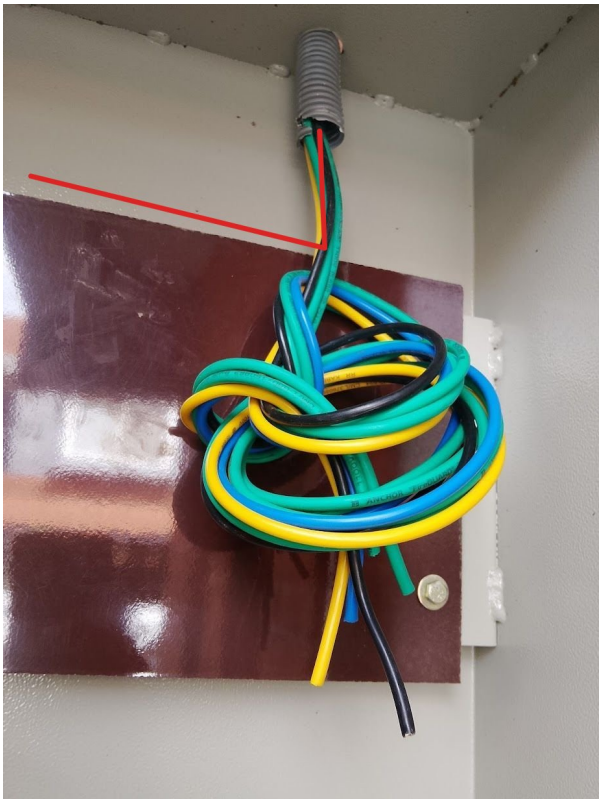


If the existing cable can be reused, we will use it; otherwise, we will run our own cable.




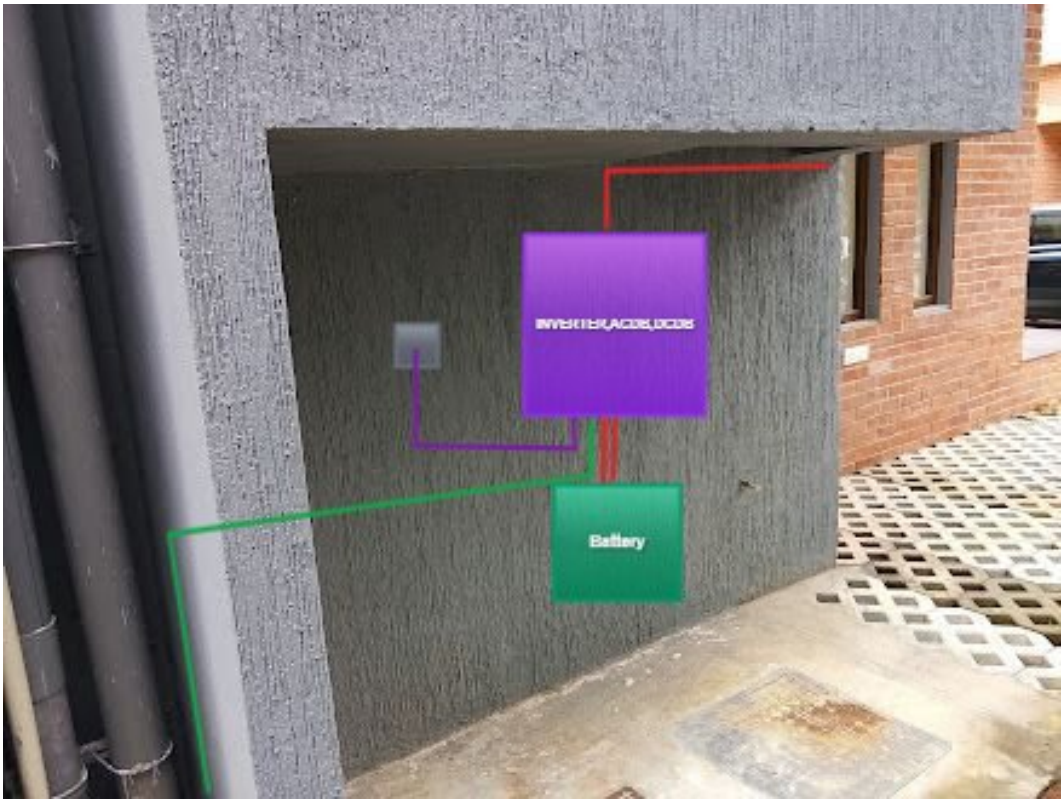

Make a hole to run the AC cable up to the UPS point

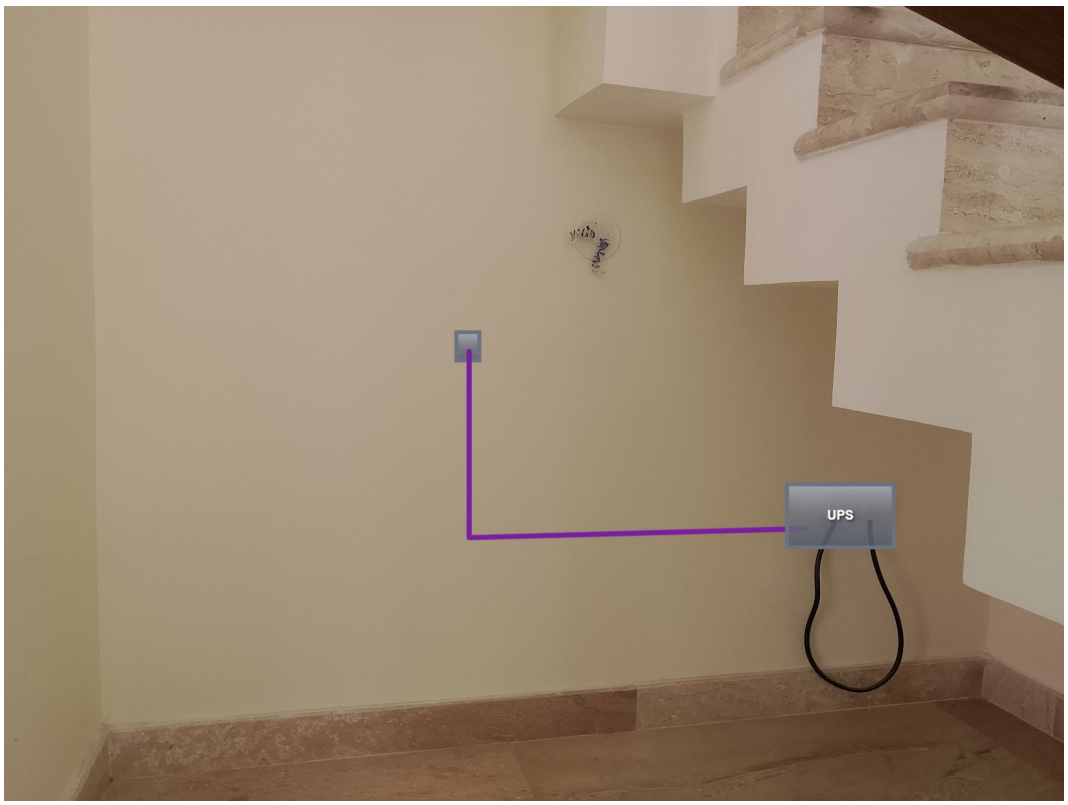
UPS




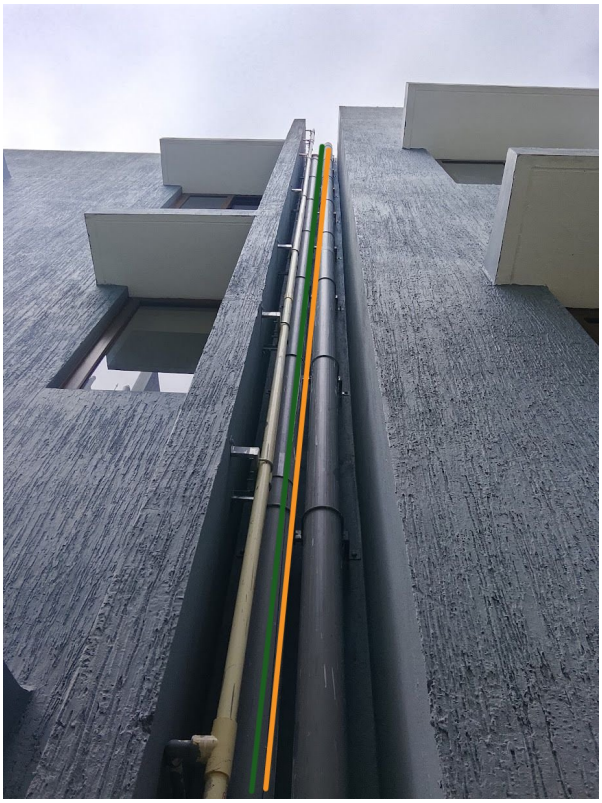





Equipment Location

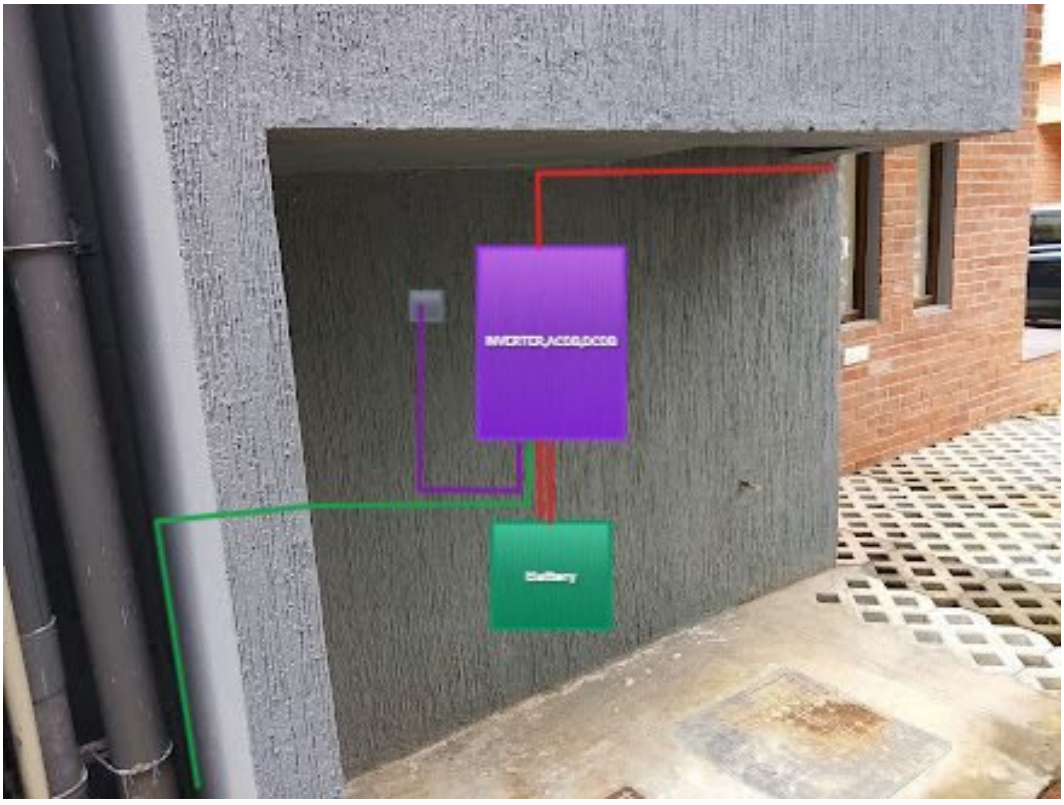


Client will provide protection box for inverter components.





Earth Pit Location




Site Layout - Top View

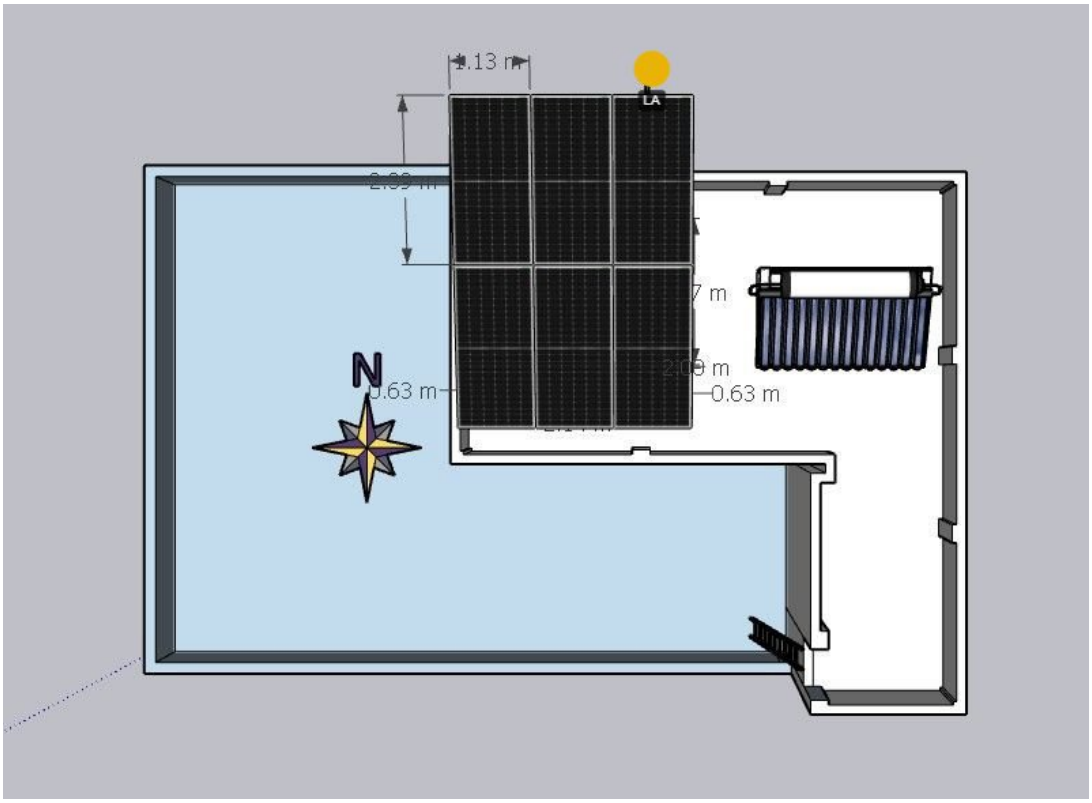


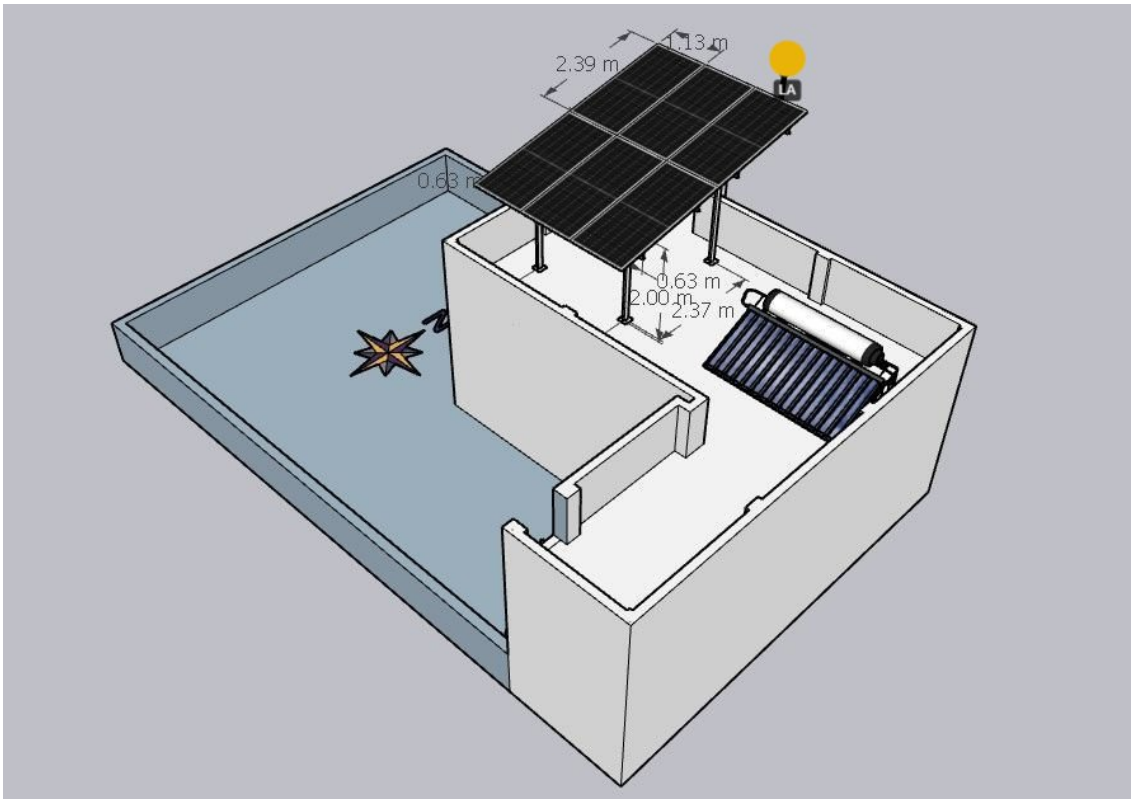

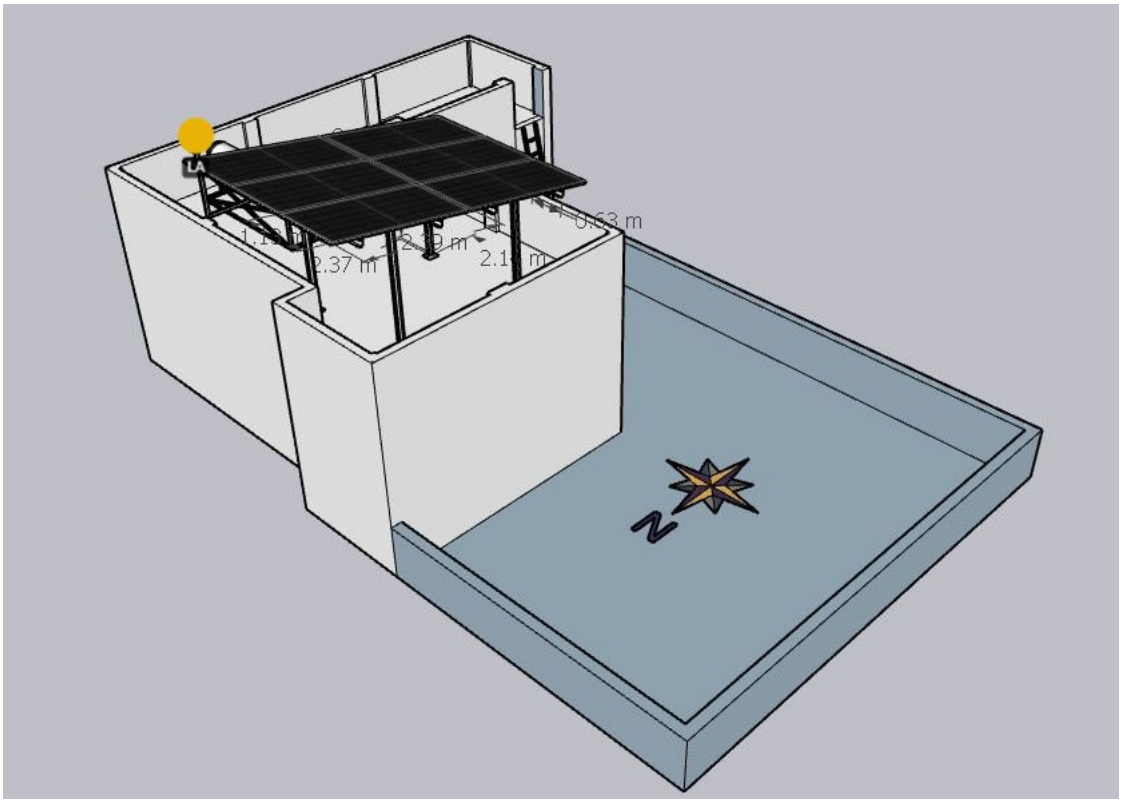

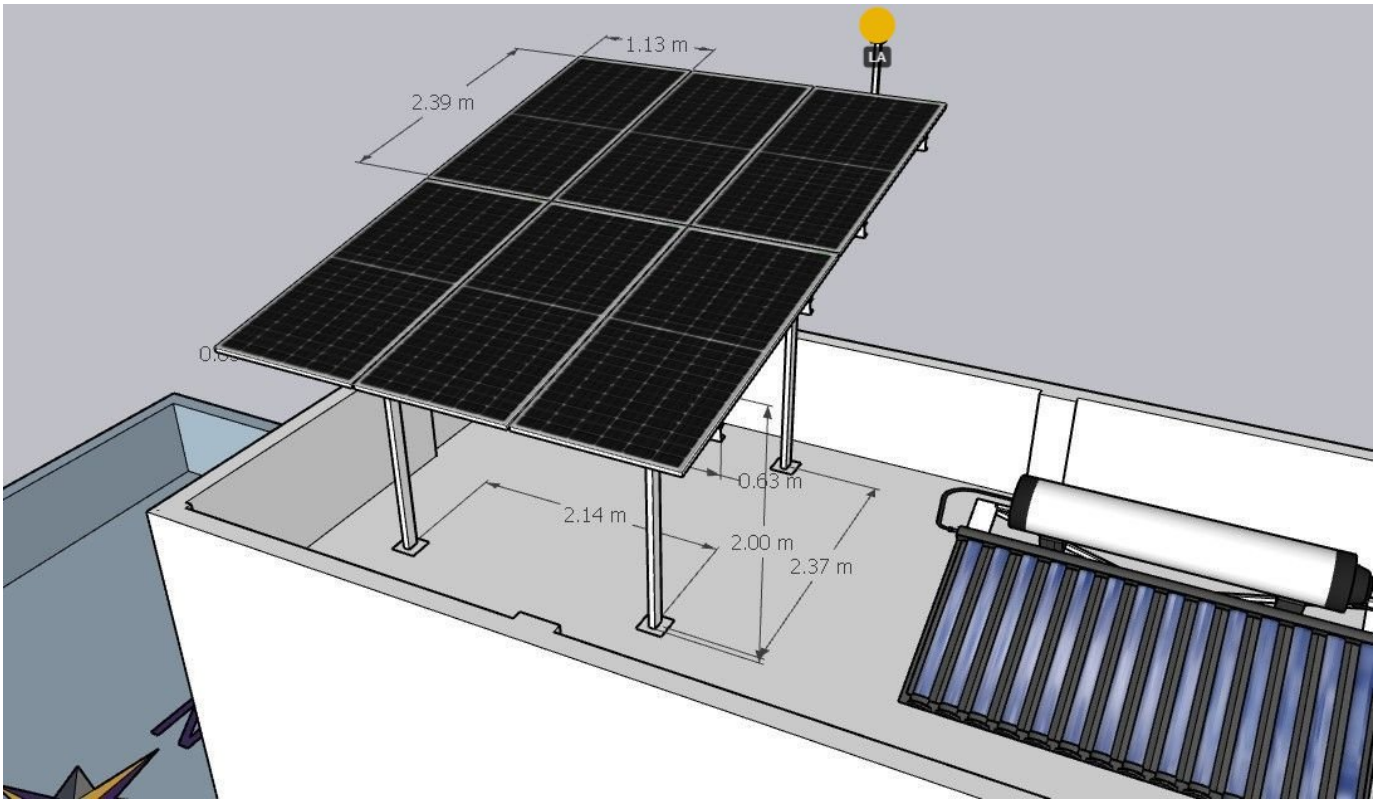

Shadow Analysis

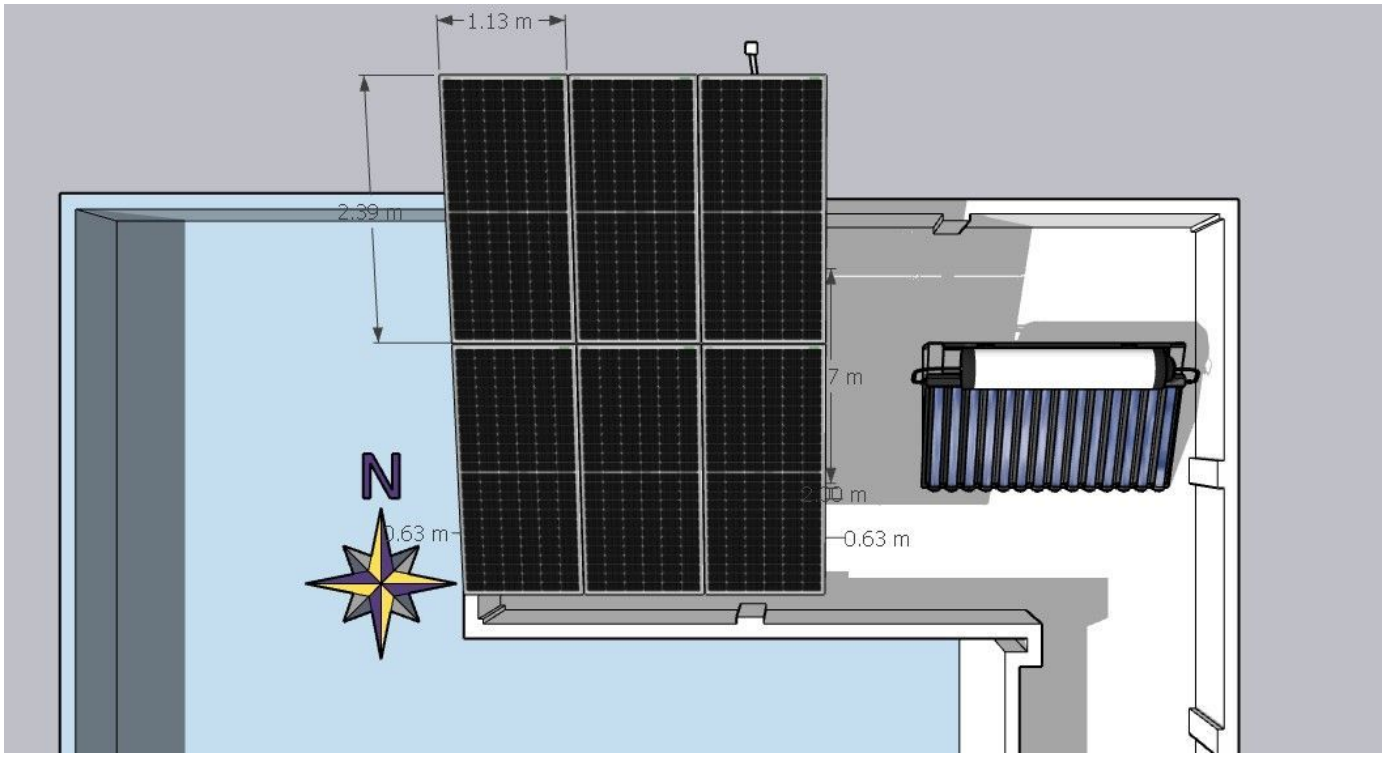

The structure shadow will cast on the solar water heater during 3.00 to 4.00 PM of every month.

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	While lifting the materials take care the glass elevation.
2	If the existing cable can be reused, we will use it; otherwise we will run our own cable.

Customer Scope

#	Observation
1	Wi-Fi up to the inverter location is under customer scope.
2	UPS near the inverter location is under customer scope.
3	As per the client suggestions only the panel layout, cable, earthing routing has been considered.
4	The existing panel shadow will cast on the solar water heater between 3.00 to 4.00 Pm of every month.
5	Client will made a protection box for inverter and battery compounds is under customer scope.

THANK YOU

Dear Arulanandan Ponnivalavan,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
