Technical Site Visit Report

Prepared for: Shyjan Joseph_Shakthi Enclave, 10th Main, 11th Cross Road, Kondappa Layout, Maruthi Nagar_4.96kWp_Hybrid - #350/

PROJECT INFORMATION

Report Number	ESV-2026-0246
Project ID	8OVHSO45
Project Name	Shyjan Joseph_Shakthi Enclave, 10th Main, 11th Cross Road, Kondappa Layout, Maruthi Nagar_4.96kWp_Hybrid
Building Name	#350/2
Billing Name	Shyjan Joseph
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Hariom
Site Address	#350/2, 10th Main, 11th Cross, Opp. Shakthi Enclave Apartment, Malleshpalya, New Thippasandra P.O, Bengaluru - 560075
GPS Coordinates	12.976662, 77.6773868
Google Maps	https://www.google.com/maps?q=12.976662,77.6773868
Visit Date	2026-11-07
Visited By	K Naveen
Revision	Rev 2

CLIENT INFORMATION

Client Name	Shyjan Joseph
Contact	+91 9845020414

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	4.96
Sanction Load (kW)	7

Module Make & Capacity	Premier DCR Bifacial 620
Module Length (mm)	2382
Module Width (mm)	11
Number of Panels	8
Inverter Type	Hybrid (String)
Inverter Brand	Deye 5 kW 1 Phase Hybrid
Number of Inverters	1
Battery	Needed
Number of Batteries	1
Capacity of each Battery (kWh)	5.12
Battery Model No.	Deye Battery: SE-F5plus - 1
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	details: The existing chajja are the obstacles that could hinder the material lifting.	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	The Inverter, ACDB, DCDB, Battery will be installed near the headroom which is near the terrace.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	**No**	-
5	Did you discuss the location of the earth pits with the customer?	The earth pits are located near the ground floor which is near to the garden area.	-
6	Where is the Internet Router located?	Ground floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	3 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	details: The solar water heater, ladder, are the obstructions that could affect the solar installation.	-
3	What is the angle of the panels? (in degrees)	7	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*AL Short Rail - Elevated Structure*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	**No**	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	**No**	*Not Available*
13	What is the height of the building and how many floors does it have?	The height of the building is G+2+headroom is approximately 15 meters	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	*To remove the obstacle in*

#	Question	Answer	Notes
			the existing meter box is under customer scope.
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	PVC chamber	-
13	In case of elevated structures, is an LA extension provided at the far end?	**No**	-
14	In case of elevated structures, is it with or without grouting?	With Grouting	-
15	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
16	Are there any safety risks associated with accessing the roof for installation?	**No**	-
17	Is space present in rooftop to store the panels?	Horizontally sleeping	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
19	Is ventilation available in the battery location?	Yes	-
20	Is Battery wall mounted or stand mounted?	Wall mounted	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 380, width: 350	-
23	Provide the dimension for earth pits location (L x W of available space).	length: 410, width: 1197	-
24	Is LAN cable under customer scope?	**No**	-
25	Is there any shadow that affects the solar installation?	N/A	-
26	Is there any trench work to be done to carry the AC cable to the meter location?	**No**	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit

Material Delivery Route



This route (using lifting) will be followed to carry large items (like Panels).










This route (using Staircase) will be followed to carry Small items.








Staircase Details

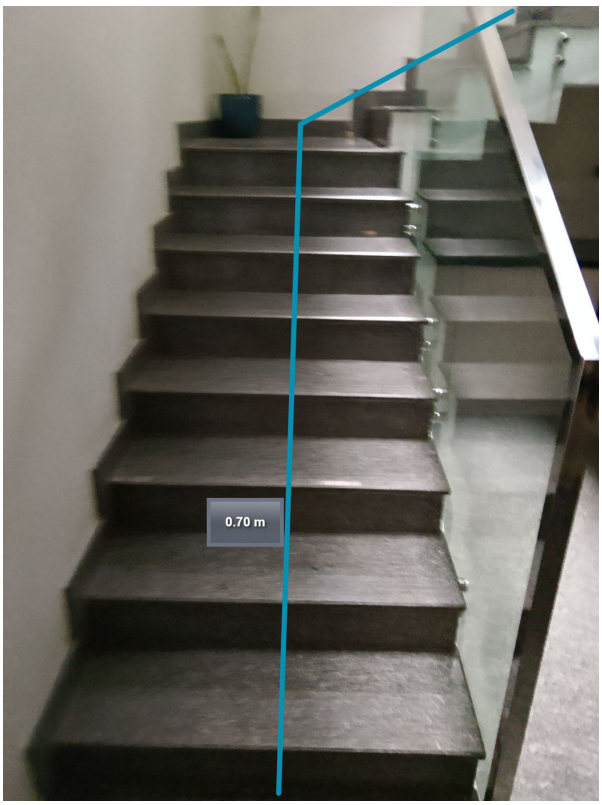

Meter Box



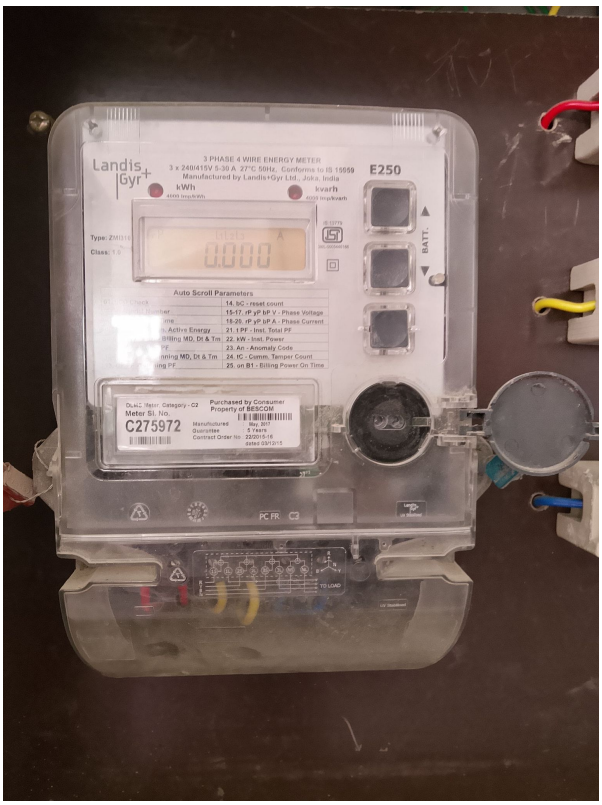

Material Storage



Proposed PV Area





Cable Routing












UPS Point near the inverter location is under customer scope.






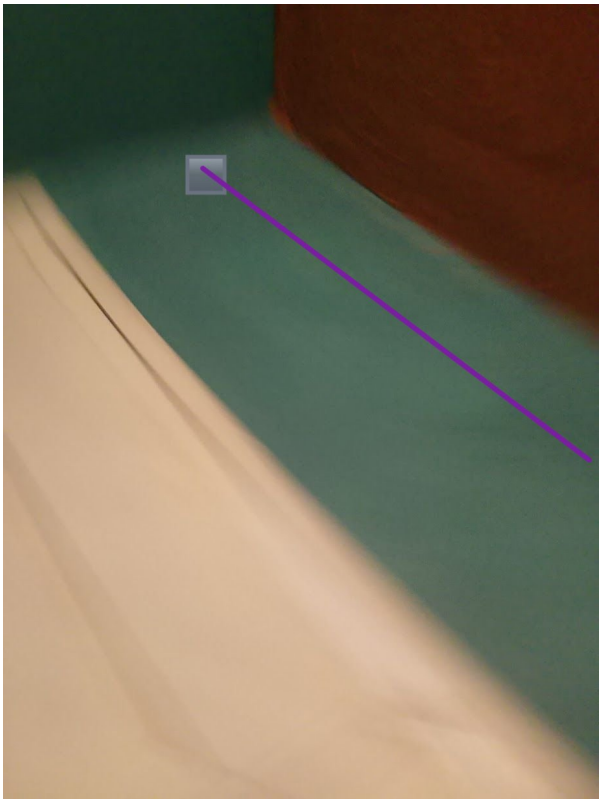

Make a hole to run the AC Cable up to the Main meter location.



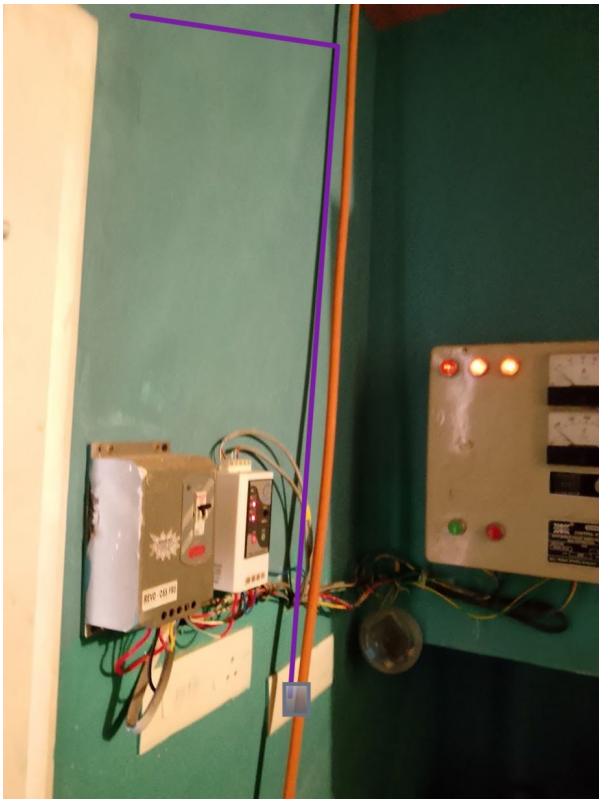

AC cable In near to the Main meter location












As per the customer suggestions the LA has to be placed here.








Equipment Location

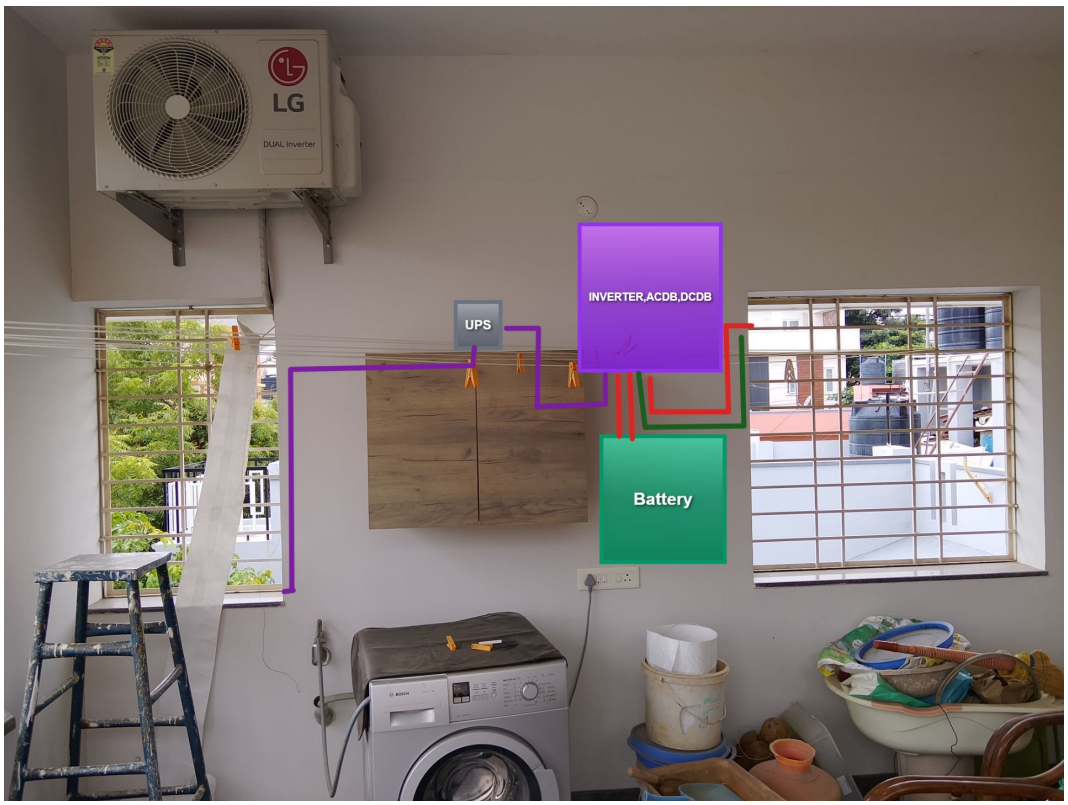

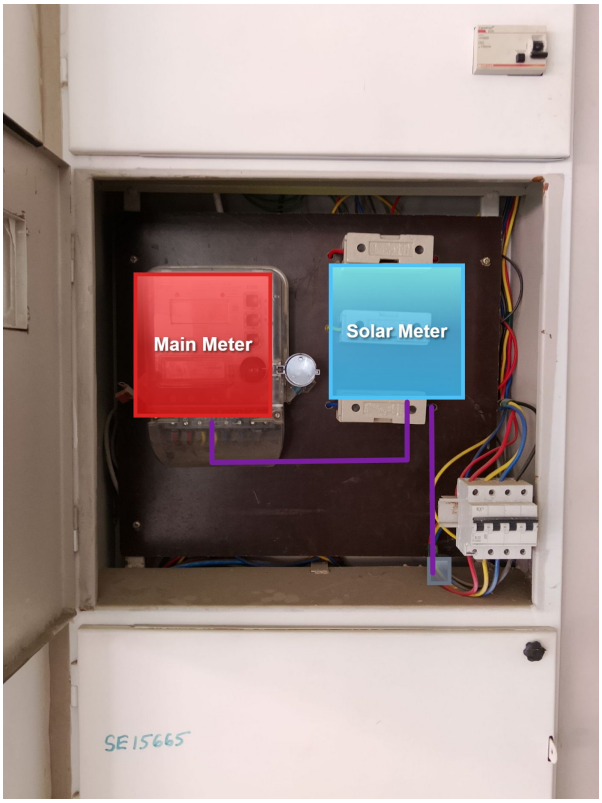


Client will relocate the fuses for placing solar meter to avoid the installation distrubances


Earth Pit Location







Site Layout - Top View

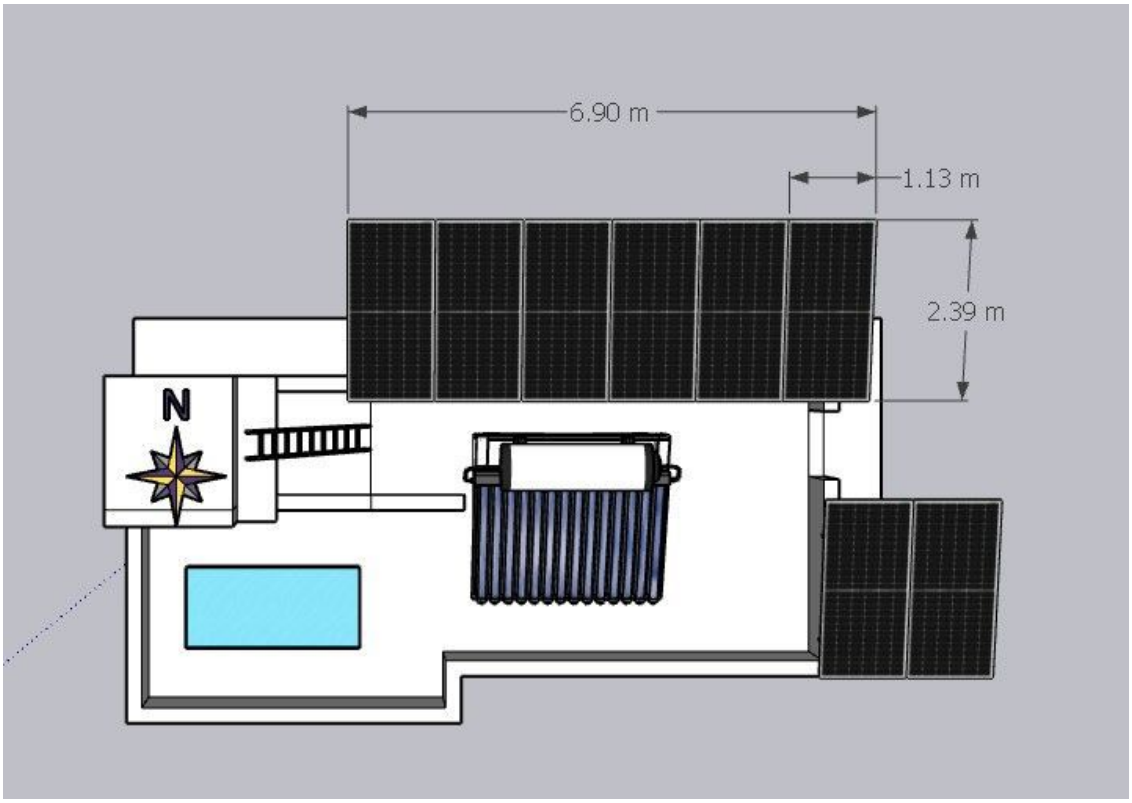

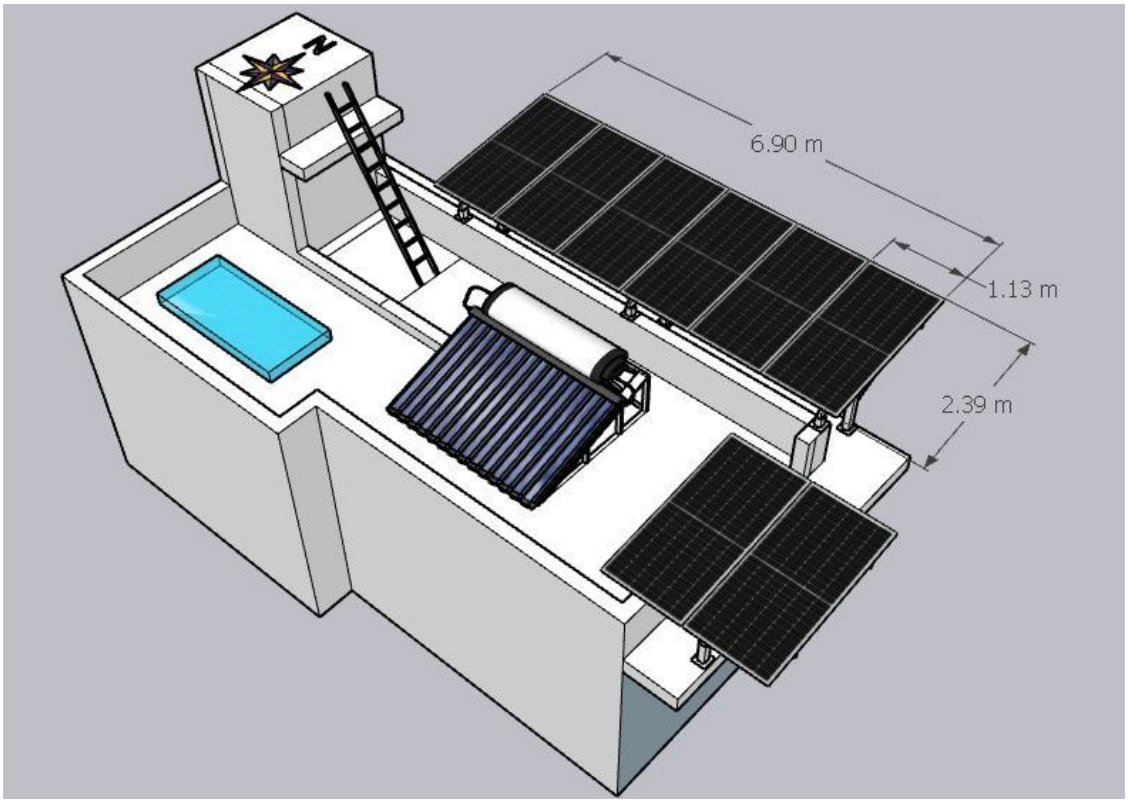

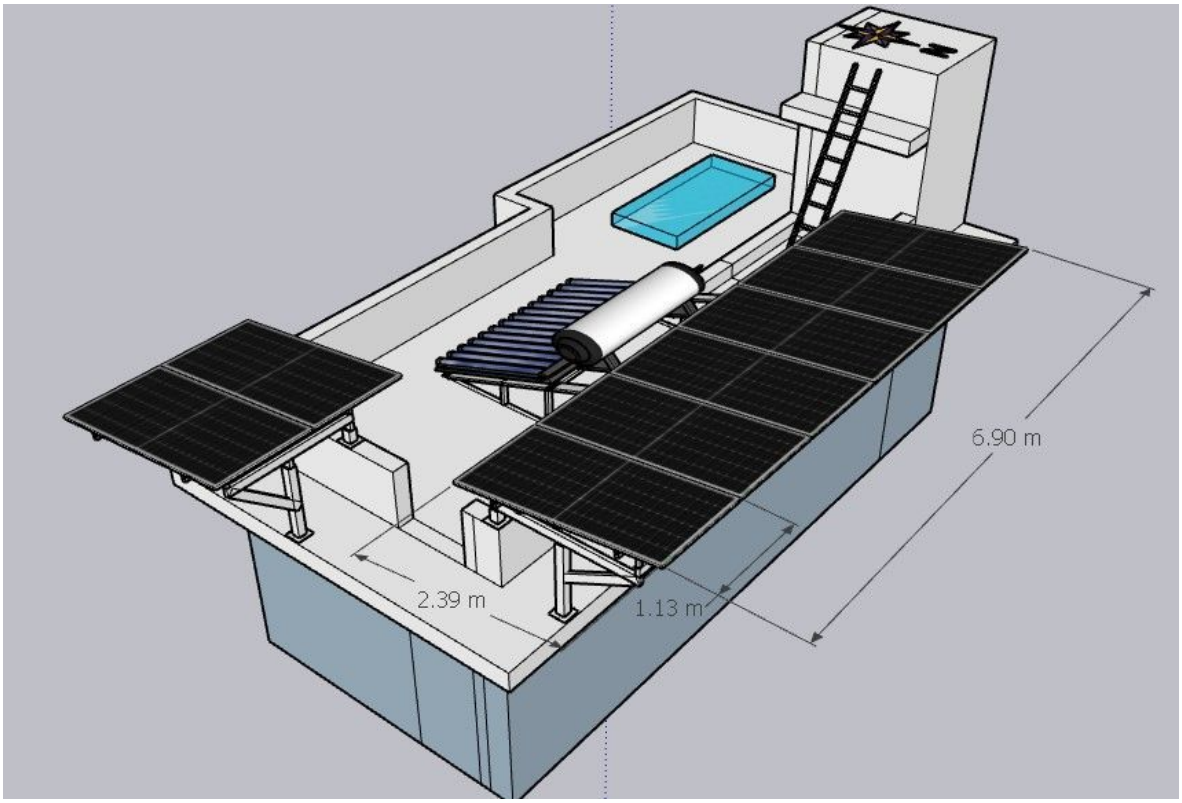

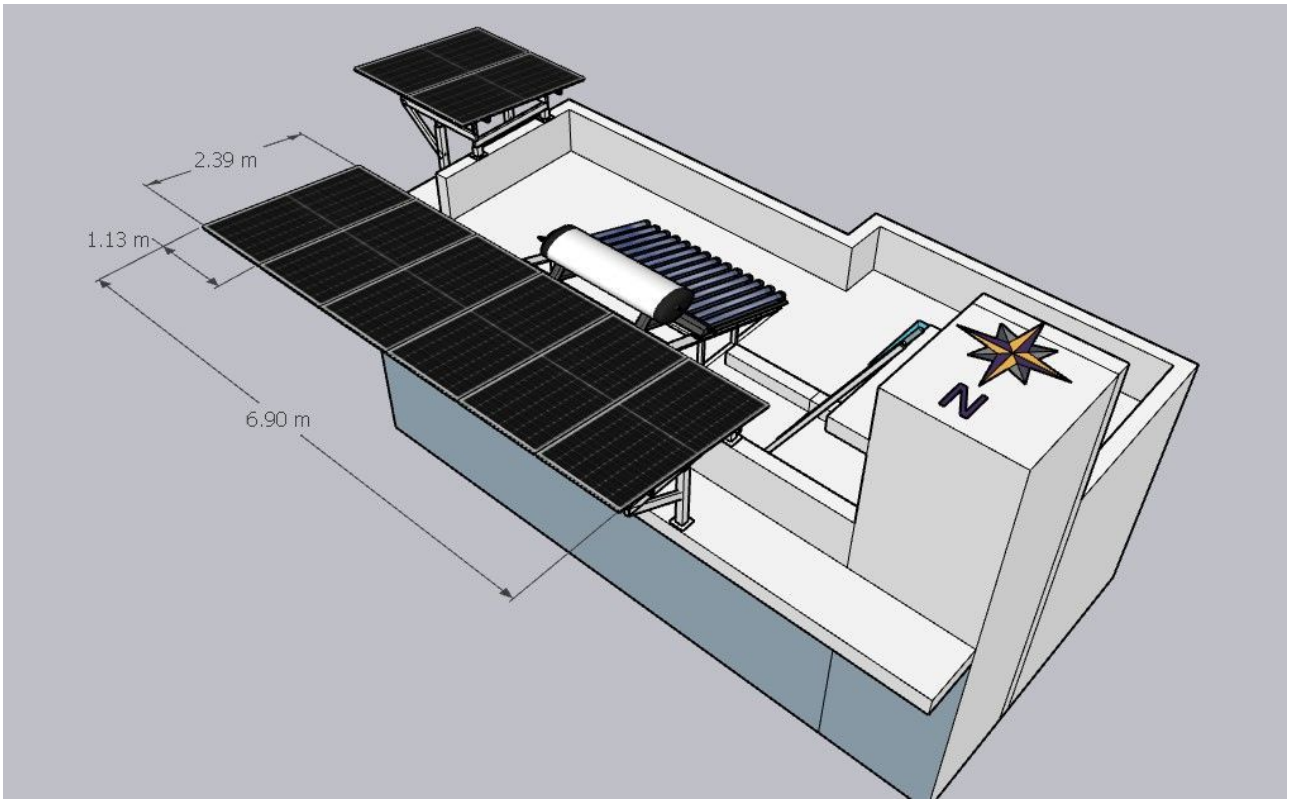

Building Exterior



OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	Power and water source to be provided by the client
2	Wi-Fi up to the inverter location is under customer scope.
3	UPS point near the inverter location is under customer scope
4	As per the customer suggestions only the panel layout, Inverter location cable, earthing routing has been considered.
5	MS Fabrication is under customer scope (MS Fabricator to ensure that the structure meets the required standards and is suitable for installing solar panels).).
6	In and Out (The inverter backup load point near the Inverter is under customer scope."). near the UPS point is under customer scope.

THANK YOU

Dear Shyjan Joseph,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
