Technical Site Visit Report

Prepared for: Vanishree TV_Whitefield_24.18kWp_Microinverter

PROJECT INFORMATION

Report Number	ESV-2026-0225
Project ID	7A61F957
Project Name	Vanishree TV_Whitefield_24.18kWp_Microinverter
Project Sector	Commercial
Project Type	Without Subsidy
Sales Lead	Gautam
Site Address	Plot No.7G, Council Khata 180/63 Vishveshwaraya Industrial Area Opp Graphite India Whitefield Bangalore 560048.
GPS Coordinates	12.96172581823214, 77.74519536926627
Google Maps	https://www.google.com/maps?q=12.961725818232141,77.74519536926627
Visit Date	2026-10-08
Visited By	Charan P
Revision	Rev 0

CLIENT INFORMATION

Client Name	Vanishree TV
Contact	98455 16259

PROJECT DETAILS

Solar Rooftop System Type	Hybrid
System Capacity (kWp)	24.18
Sanction Load (kW)	30
Module Make & Capacity	Waaree Bi-facial Non DCR and 620Wp
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	39
Inverter Type	Hybrid (Enphase)
Inverter Brand	Enphase IQ8P
Number of Inverters	39
Battery	Needed
Number of Batteries	8
Capacity of each Battery (kWh)	5
Battery Model No.	IQ 5P BatteryI with FlexPhase
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Below the sheet roof	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes, near the sheet roof on Southwest area.	-
6	Where is the Internet Router located?	Site under construction	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-

#	Question	Answer	Notes
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Mini-rails	-
9	What is the orientation of the solar panels?	["South","West"]	*South-westorientation*
10	How can the roof be accessed?	Ladder	-
11	Is the building currently under construction?	Yes	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	**No**	-
13	What is the height of the building and how many floors does it have?	10	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	**No**	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	**No**	-
4	Is the Termination Point easily visible or sealed?	Sealed	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	Yes	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	**No**	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	**No**	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	N/A	-
13	In case of elevated structures, is it with or without grouting?	N/A	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	**No**	-
16	Is space present in rooftop to store the panels?	No space	*The solar panels must be stored on the ground floor and lifted to the sheet roof using a crane during installation.*

#	Question	Answer	Notes
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	Yes	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1000, width: 1000	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 8000, width: 3000	-
22	Is LAN cable under customer scope?	No	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	No	-


PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout

TENNIS COURT - 23.98 kWp

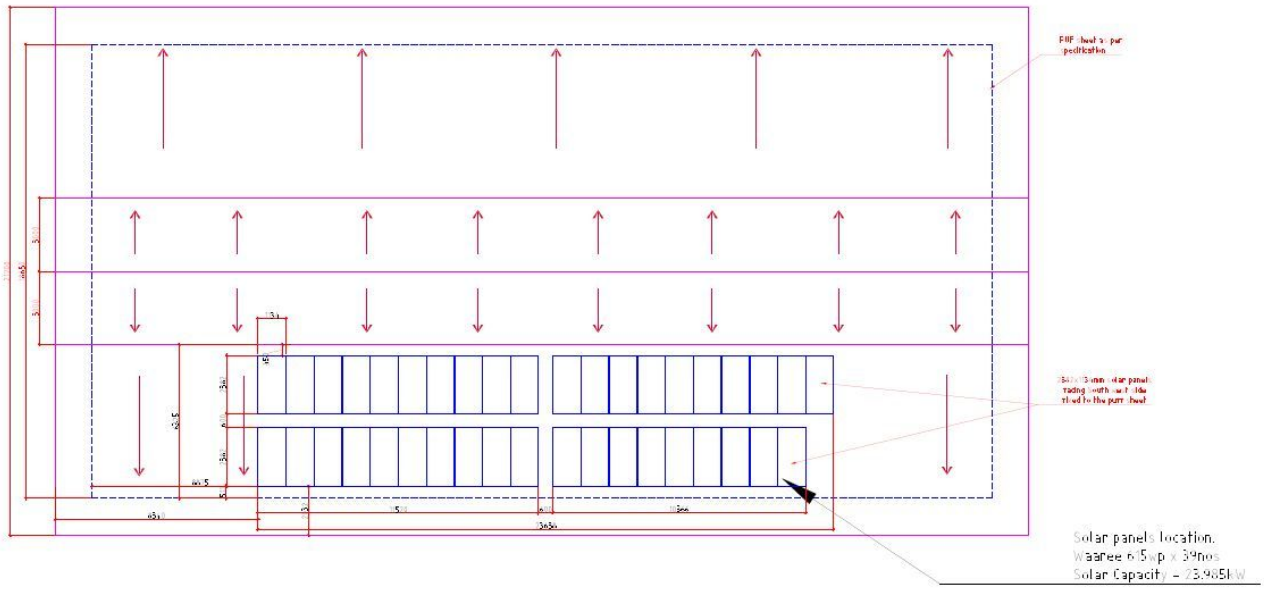

Building Exterior



Material Storage



This area can be used for storing the solar panels only. A separate room will be provided for the CC and batteries.

Material Delivery Route





This route will be followed to carry all items using Crane.




Proposed PV Area



Cable Routing






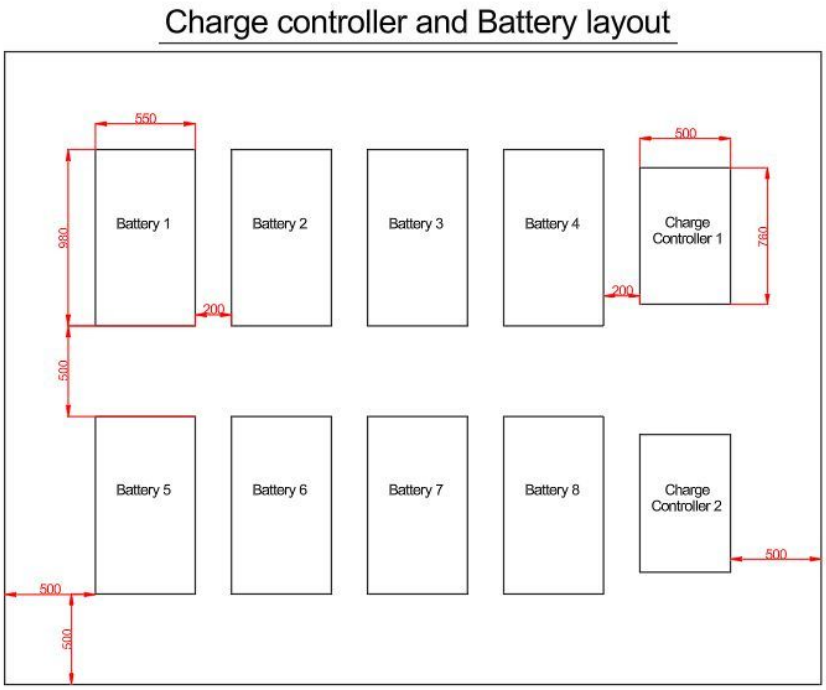

Required space to install Charge controllers and Batteries



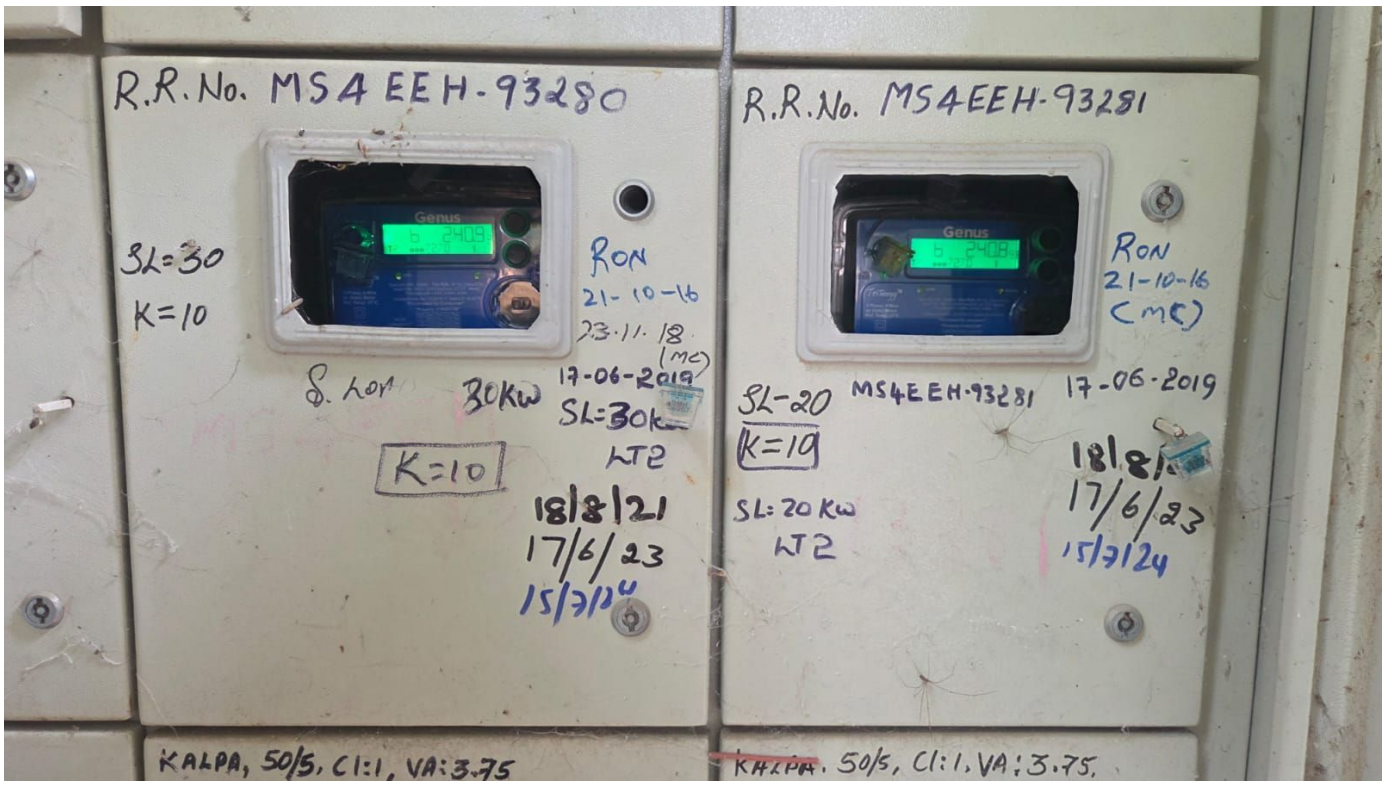

Earthing Routing











OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation

#	Observation
1	A crane will be used to lift and shift the solar panels to the terrace.
2	Installation and commissioning of the solar system.

Customer Scope

#	Observation
1	Wi-Fi up to Battery location.
2	UPS Point (Input/Output): Input – From the grid to the charge controller. Output – From the charge controller to the load.

THANK YOU

Dear Vanishree TV,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
