Technical Site Visit Report

Prepared for: ASHWA ENERGY PVT LTD - ASHWA ENERGY PVT LTD

PROJECT INFORMATION

Report Number	ESV-2026-0204
Project ID	3461B06C
Project Name	ASHWA ENERGY PVT LTD
Building Name	ASHWA ENERGY PVT LTD
Billing Name	ASHWA ENERGY PVT LTD
Project Sector	Commercial
Project Type	Without Subsidy
Sales Lead	Harsha
Site Address	B KIADB, Plot No.: 124, near SBI Bank, Belur Industrial Area, Belur, Karnataka 580011
GPS Coordinates	13.06510388673816, 77.57734768244833
Google Maps	https://www.google.com/maps?q=13.06510388673816,77.57734768244833
Visit Date	2026-09-04
Visited By	Kiran N
Revision	Rev 0

CLIENT INFORMATION

Client Name	Ashwa Energy Pvt Ltd
Contact	91 91481 98642

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	120.28
Sanction Load (kW)	270
Module Make & Capacity	Adani 620

Module Length (mm)	1134
Module Width (mm)	2382
Number of Panels	194
Inverter Type	SolarEdge
Inverter Brand	SolarEdge Inverter 2 nos 1. 100 kW 3phase 2.Optimizer S1200 99 nos
Number of Inverters	1
Number of Optimizers	99
Mounting Structure Type	Sheet Roof

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	In side of the Sheet roof	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Yes it's in the Garden Area	-
6	Where is the Internet Router located?	Customer will be provided	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Not Available / Under Construction	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	Corrugated Sheet Roof	*250 mm profile pinch*
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	7	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	7	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	MS Rafter	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-

#	Question	Answer	Notes
8	What type of mounting structure is planned?	Mini-rails	-
9	What is the orientation of the solar panels?	["East","West"]	-
10	How can the roof be accessed?	Other	*There is no ladder available at site for the roof access.*
11	Is the building currently under construction?	N/A	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-
13	What is the height of the building and how many floors does it have?	12 m	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	N/A	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital, If 3-phase: HT	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	**No**	-
6	Is space available for CT within Energy meter panel?	**No**	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Not Applicable	-
8	Provide details of the existing CT ratings (if applicable).	-	-
9	In Main meter panel, is empty space available for solar meter?	**No**	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	**No**	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	In case of elevated structures, is an LA extension provided at the far end?	**No**	-
13	In case of elevated structures, is it with or without grouting?	Not Applicable	-
14	Are there any challenges with respect to Installation and Maintenance activities?	**No**	-
15	Are there any safety risks associated with accessing the roof for installation?	details: No accessing	-
16	Is space present in rooftop to store the panels?	Vertically leaning against the wall	-
17	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
18	Is ventilation available in the battery location?	N/A	-
19	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	wall mounted	-

#	Question	Answer	Notes
20	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 1200, width: 1300	-
21	Provide the dimension for earth pits location (L x W of available space).	length: 1400, width: 5000	-
22	Is LAN cable under customer scope?	Yes	-
23	Is there any shadow that affects the solar installation?	No	-
24	Is there any trench work to be done to carry the AC cable to the meter location?	details: 40 m	-

PHOTO DOCUMENTATION

Cable Routing Legend

Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Material Delivery Route









Meter Box


Solar Meter Box
JCB



DANGER
440 VOLTS
INCOMER
CABLE ALLEY



Material Storage



Proposed PV Area

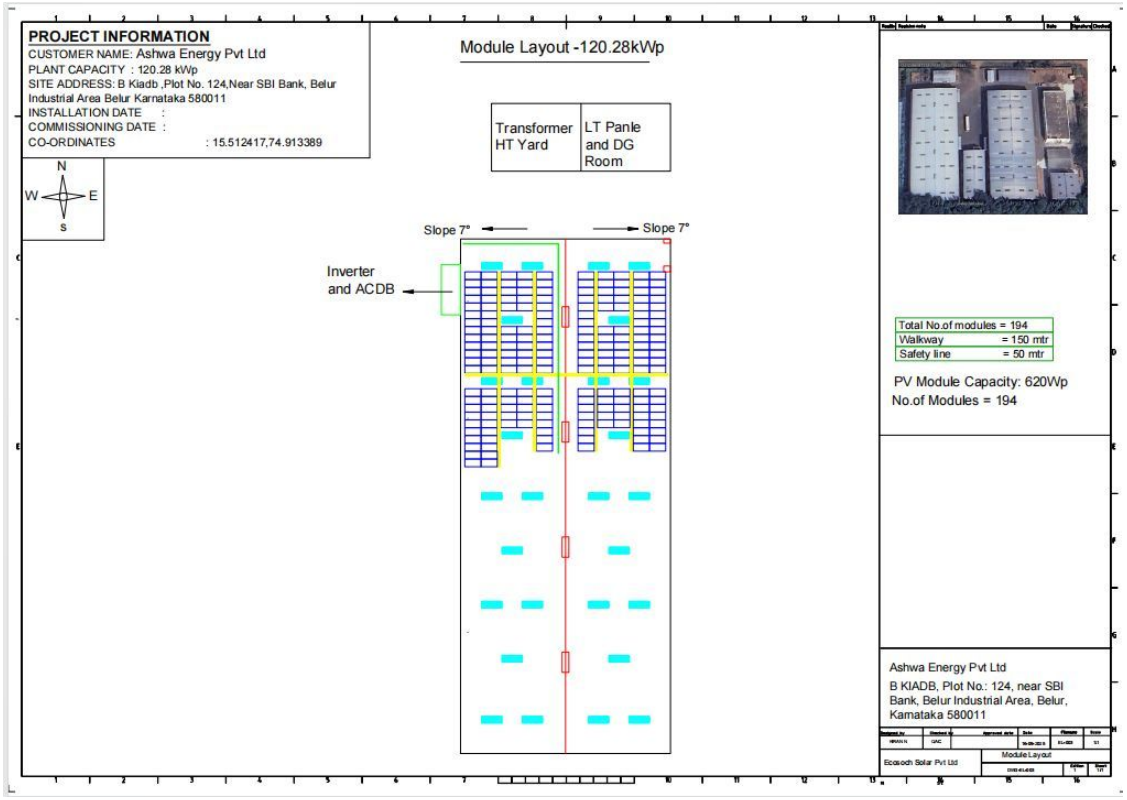

Cable Routing




KIRLOSKAR ELECTRIC






JCB
Solar meter Box


VAF
BUSBAR CHAMBER
1250A 3P ACB
DANGER
BUSBAR CHAMBER
INCOMER
CABLE ALLEY


DANGER
440 VOLTS
INCOMER
CABLE ALLEY



Equipment Location



Earth Pit Location











Main Meter Location


METER CHAMBER


METER CHAMBER
Reduction of load on dated
04.04.2025
RT-30.9.2025
RT 17.04.2026

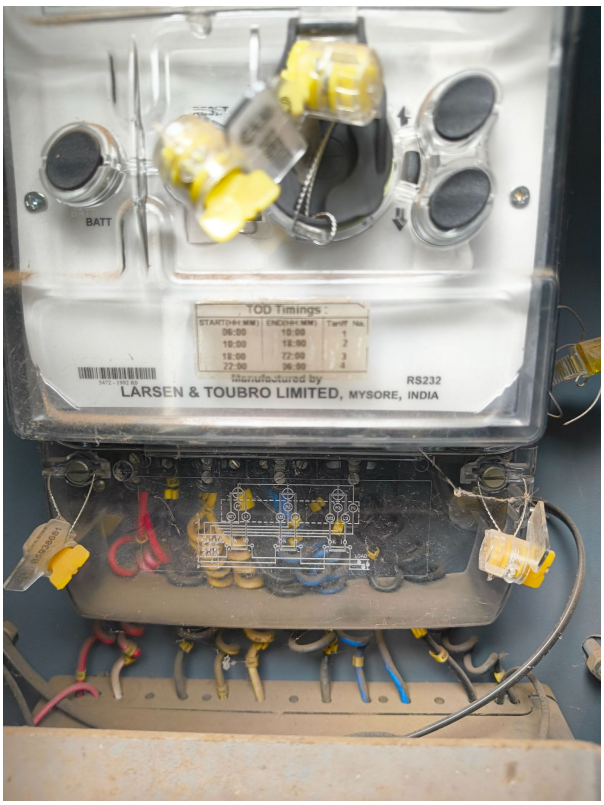

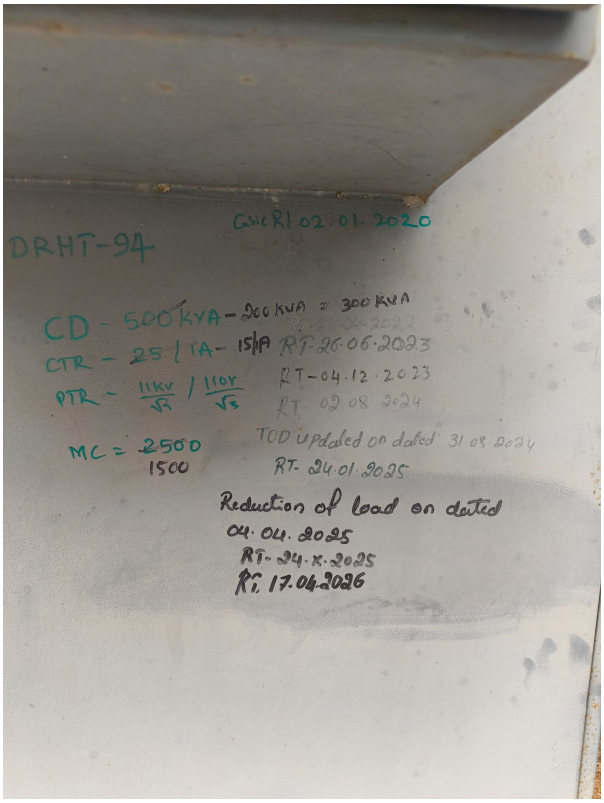

material lifting routing



Material shifting to the roof will required crane support

material lifting routing





Material shifting to the roof will be required crane



Material shifting to the roof will be required crane

CHECKLIST REFERENCE PHOTOS

Can the delivery van/truck reach the material unloading point?



Are there any obstacles at the site that could hinder material lifting?



Where will the Inverter, DCDB, ACDB, Battery, etc. be located?





Did you discuss the location of the earth pits with the customer?



What type of energy meter is currently installed?

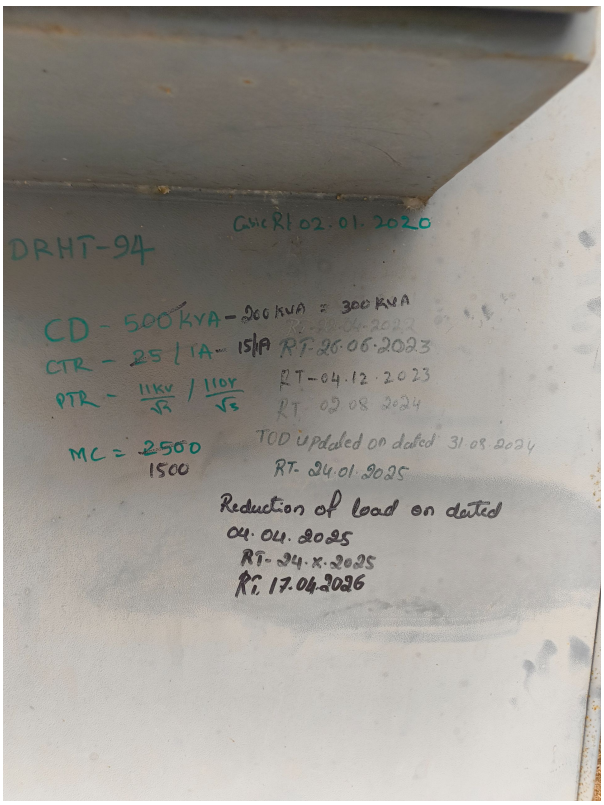


DRHT-94
CD - 500 KVA - 200 KVA = 300 KVA
CTR - 25 / 1A - 15/A
PTR - 11KV / 110V
MC = 2500 / 1500
RT-26.06.2023
RT-04.12.2023
RT 02.08.2024
TOD updated on dated 31.08.2024
RT- 24.01.2025
Reduction of load on dated
04.04.2025
RT-24.X.2025
RT 17.04.2026

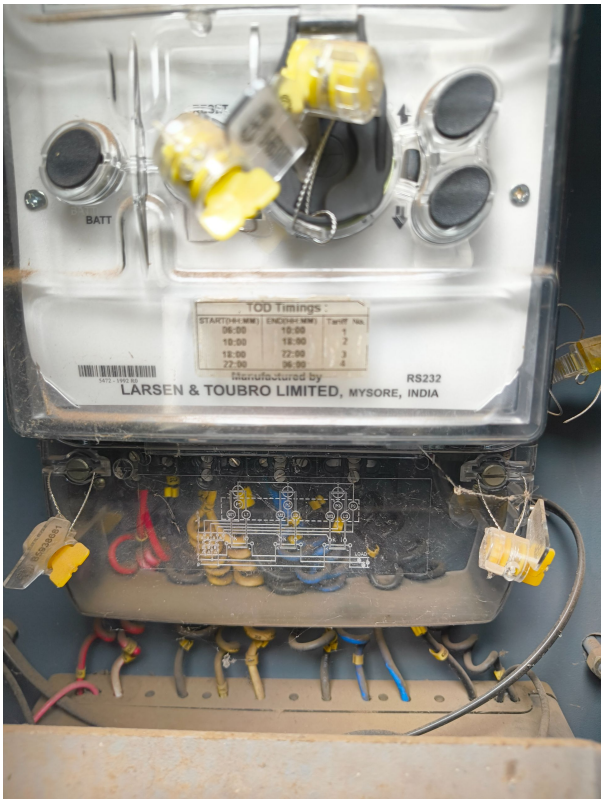
BATT
TOD Timings :
RS232
LARSEN & TOUBRO LIMITED, MYSORE, INDIA



Is the Meter cubicle photo matching with the previous answer?





OBSERVATIONS & RECOMMENDATIONS

Customer Scope

#	Observation
1	LAN Cable under Customer scope.

THANK YOU

Dear Ashwa Energy Pvt Ltd,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.

#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097

www.ecosoch.com | info@ecosoch.com
